



Government of India
Ministry of Statistics and
Programme Implementation



CMS

Ministry of Statistics & Programme Implementation

466th

Flash Report on Central Sector Infrastructure Projects



**(Rs. 150 crore
& above)**

(Part - I)*

Synopsis

September 2024

*Refer Part-II for tables comprising detailed project listing.

Flash Report - Central Sector Infrastructure Projects Costing Rs. 150 crore & above

Total Ongoing Projects (1792, Rs. 2756378.3 crore)

Mega*
(629 projects,
Rs. 2240975.4
crore)

Major*
(1163 projects,
Rs. 515402.9
crore)

Completed@
projects during
September
2024 (13
projects, Rs.
8422.2 crore)




**Newly Added/
elevated\$**
Projects during
September 2024
(21 projects,
Rs 24952.5
crore)

Note: @ Indicated legend is in format (Project Count, Cumulative Expenditure)
other Indicated legends are in format (Project count, Original Cost)

* Mega Project if having original cost $\geq$ 1000 crore

* Major Project if original cost < 1000 crore




\$ reported Anticipated cost more than 150 crore

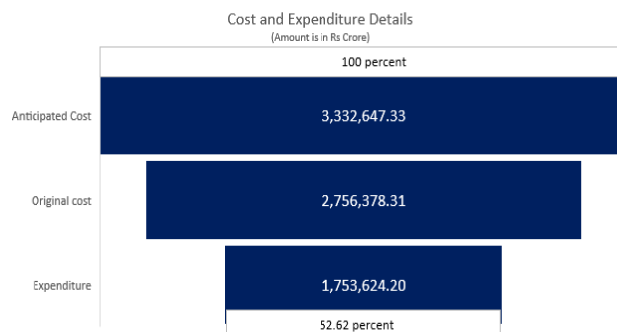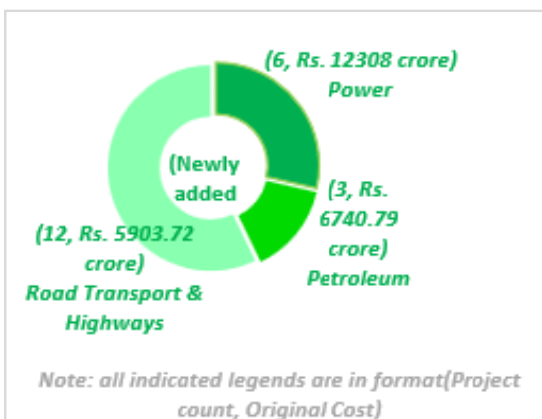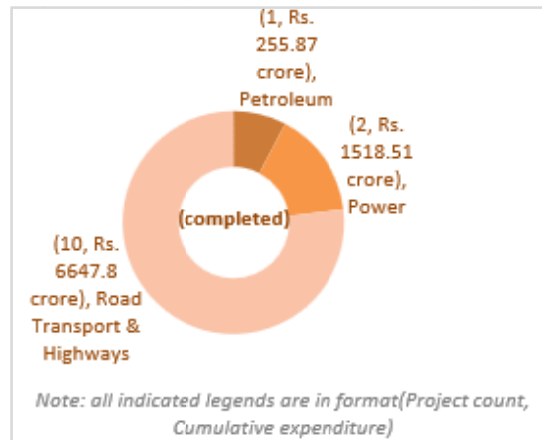


Total North East Region Ongoing Projects (229, Rs. 1,81,870.86 crore)

Mega*
(23 projects,
Rs. 1,00,224.07
crore)

Major*
(206 projects,
Rs. 81646.79
crore)

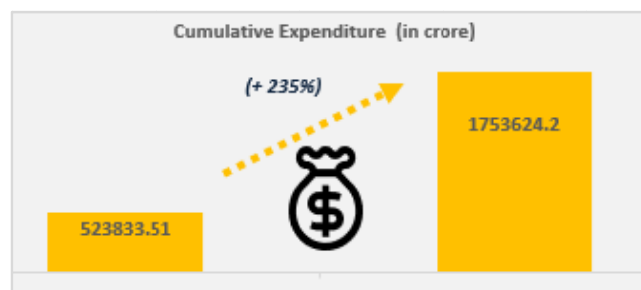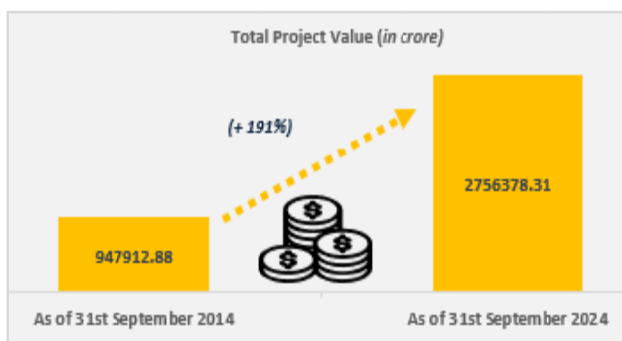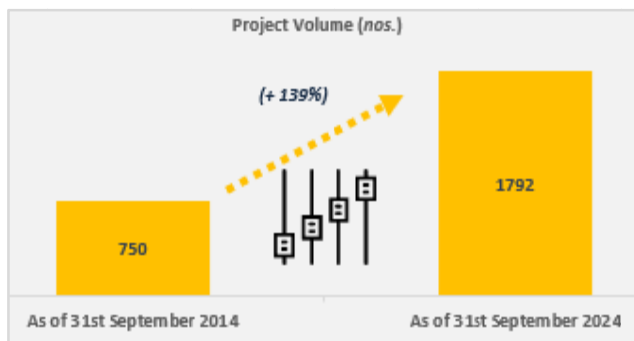


Sectoral Comparison : Major Sectors (as per count)
 [Outer Ring: Original Approved Cost in Rs. Crore] & [Inner Ring: Project Count]

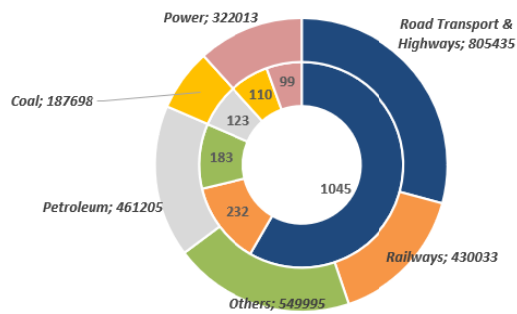


*Others include Water Resources, Civi Aviation, Urban Development, Department of Higher Education, Steel, Health & Family welfare, Mines, Telecommunications, Atomic energy, Home Affairs, Finance, DPIIT, DONER, Renewable Energy, Shipping & Ports, and Social Justice

State Comparison : Major States (as per count)
 [Outer Ring:Original Approved Cost in Rs. Crore] & [Inner Ring: Project Count]

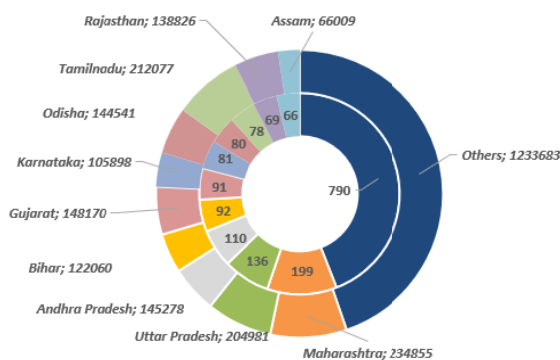

*Others include Jharkhand, Delhi , Chhattisgarh,Haryana, Jammu & Kashmir , West Bengal , Kerala ,Madhya Pradesh,Arunachal Pradesh , Punjab , Telangana , Uttarakhand , Himachal Pradesh , Manipur , Sikkim, Nagaland , Mizoram , Meghalaya,Tripura, Goa ,

Sectoral Distribution of total 641 projects with reported Physical Progress between 80-100%

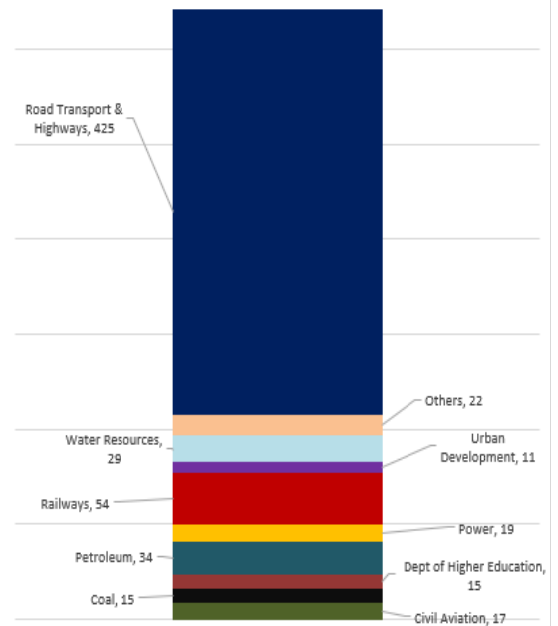

Note: This report is as of September 2024, based on the (non-exhaustive) list of projects and information as reported by Line Ministries/implementing agencies on the OCMS (www.cspm.gov.in) portal latest by 8th October 2024.



Government of India
Ministry of Statistics and
Programme Implementation



CMS

Ministry of Statistics & Programme Implementation

467th

Flash Report on Central Sector Infrastructure Projects



**(Rs. 150 crore
& above)**

(Part - II)*

List of Tables

September 2024

**Refer Part-I for Synopsis.*

CONTENTS

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution.....	1-2
Table:-2. Overview of Ongoing Projects: State-wise Distribution.....	3-5
Table:-3. Project List: Completed during September 2024.....	6-7
Table:-4. Project List: Added during September 2024.....	8-10
Table:-5. Project List: Ongoing Projects of North-East Region.....	11-34
Table:-6. Project List: Ongoing Projects as of 30 th September 2024.....	35-243

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	ATOMIC ENERGY	5	116,741.00 (167,447.00) {171,625.00}	111,309.72
2	CIVIL AVIATION	40	26,490.58 (27,450.90) {30,520.47}	15,686.81
3	COAL	110	187,698.23 (189,867.45) {192,440.13}	71,478.32
4	DEPARTMENT OF HIGHER EDUCATION	20	9,680.92 (10,294.08) {10,338.99}	7,197.74
5	DONER	1	151.33 (151.33) {151.33}	148.33
6	DPIIT	2	24,857.00 (24,857.00) {25,485.00}	14,507.93
7	FINANCE	2	577.27 (577.27) {569.04}	399.67
8	HEALTH AND FAMILY WELFARE	9	7,561.27 (7,730.18) {7,727.97}	4,451.07
9	HOME AFFAIRS	5	2,025.73 (2,946.02) {2,946.00}	2,387.61
10	MINES	8	7,559.78 (9,356.73) {9,833.57}	5,254.56
11	PETROLEUM	123	461,205.12 (515,909.97) {530,864.23}	247,336.35
12	POWER	99	322,012.86 (340,981.33) {386,448.98}	196,202.73
13	RAILWAYS	232	430,032.59 (545,694.16) {682,562.58}	421,826.32
14	ROAD TRANSPORT AND HIGHWAYS	1045	805,434.78 (840,238.09) {854,353.97}	405,118.81
15	SHIPPING AND PORTS	1	5,369.18 (4,633.81) {5,061.15}	3,078.56
16	SOCIAL JUSTICE	1	170.99 (170.99) {170.99}	73.80

Table:-1. Overview of Ongoing Projects: Sector-wise Distribution

Sl. No.	Sector	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
17	STEEL	12	11,337.99 (11,963.86) {11,963.86}	5,716.13
18	TELECOMMUNICATIONS	6	26,961.69 (26,949.89) {26,949.89}	4,464.75
19	URBAN DEVELOPMENT	30	287,043.72 (294,057.08) {312,556.91}	207,500.49
20	WATER RESOURCES	41	23,466.28 (23,420.50) {70,077.27}	29,484.50
	Total	1792	2,756,378.31 (3,044,697.64) {3,332,647.33}	1,753,624.20

*Either Revised or Original Cost

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	ANDAMAN AND NICOBAR ISLANDS	9	2,847.18 (3,137.68) {3,118.54}	1,999.74
2	ANDHRA PRADESH	110	145,278.32 (151,022.61) {208,776.75}	117,556.32
3	ARUNACHAL PRADESH	24	47,923.74 (47,987.27) {63,009.42}	30,317.80
4	ASSAM	66	66,008.78 (66,200.25) {75,741.21}	41,841.22
5	BIHAR	92	122,059.55 (142,870.31) {151,097.07}	96,299.32
6	CHHATTISGARH	53	82,054.75 (84,076.72) {84,743.01}	35,116.56
7	DELHI	27	92,995.74 (98,711.59) {97,290.55}	74,084.71
8	GOA	6	3,824.63 (3,824.63) {3,911.13}	3,111.62
9	GUJARAT	91	148,170.26 (163,593.21) {169,637.42}	89,546.57
10	HARYANA	33	74,759.15 (84,837.00) {85,586.95}	37,017.79
11	HIMACHAL PRADESH	29	27,418.92 (28,706.60) {43,798.61}	28,657.74
12	JAMMU AND KASHMIR	51	74,532.19 (110,182.74) {116,300.04}	71,734.70
13	JHARKHAND	65	104,141.01 (108,367.51) {112,048.93}	56,046.73
14	KARNATAKA	81	105,897.80 (109,351.01) {112,134.37}	50,780.39
15	KERALA	34	70,127.95 (77,210.27) {77,570.03}	37,794.48
16	LADAKH	6	2,474.97 (2,474.97) {2,634.64}	1,039.28

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
17	MADHYA PRADESH	65	107,647.91 (112,458.23) {120,982.58}	39,265.59
18	MAHARASHTRA	199	234,854.75 (239,999.85) {267,184.18}	132,776.05
19	MANIPUR	32	15,304.69 (23,160.75) {30,368.22}	18,676.01
20	MEGHALAYA	17	7,241.51 (7,528.40) {14,604.71}	3,767.66
21	MIZORAM	20	11,570.63 (16,703.71) {20,191.45}	16,513.45
22	MULTI STATE	58	286,178.20 (330,168.94) {352,634.33}	223,722.95
23	NAGALAND	34	12,315.74 (18,004.99) {17,703.96}	8,046.91
24	ODISHA	80	144,541.42 (146,515.62) {155,562.16}	62,695.71
25	PUNJAB	43	41,821.35 (41,909.94) {41,998.18}	16,007.81
26	RAJASTHAN	69	138,825.63 (179,080.31) {179,288.25}	98,394.37
27	SIKKIM	22	14,500.36 (14,896.52) {22,320.65}	12,260.74
28	TAMIL NADU	78	212,077.40 (251,549.09) {267,733.91}	126,542.20
29	TELANGANA	53	38,381.66 (38,840.81) {41,226.16}	23,527.75
30	TRIPURA	14	7,005.41 (7,127.78) {7,266.88}	1,397.89
31	UTTAR PRADESH	136	204,981.45 (211,135.81) {225,958.30}	102,943.96
32	UTTARAKHAND	33	36,816.79 (42,040.90) {59,857.18}	42,780.53

Table:-2. Overview of Ongoing Projects: State-wise Distribution

Sl. No.	State	Projects	Cost Original (Revised)* {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore
33	WEST BENGAL	62	71,798.47 (81,021.62) {100,367.56}	51,359.65
	Total	1792	2,756,378.31 (3,044,697.64) {3,332,647.33}	1,753,624.20

*Either Revised or Original Cost

Table:-3. Project List: Completed during September 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
<u>PETROLEUM</u>					
	1	DEVANGONTHI MARKETING TERMINAL (MANGALORE REFIN) (N16000401) (KARNATAKA)	200.00	6/1/2023	255.87
<u>POWER</u>					
	2	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000300) (RAJASTHAN)	1,184.88	9/1/2022	846.92
	3	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000305) (RAJASTHAN)	713.82	12/1/2022	671.59
<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	4	CHALLAKERE TO HARIYUR SECTION FROM KM 358.500 TO KM 414.205 OF NH150 A (NHAI) (N24001690) (KARNATAKA)	1,167.52	1/1/2023	946.42
	5	4L OF HARDA - BETUL (PKG-I) FROM KM.0 TO KM.30 [HARDA - TEMAGAON] (NHAI) (N24001763) (MADHYA PRADESH)	774.16	9/1/2023	463.85
	6	4L OF HARDA - BETUL (PKG-III) FROM KM. 81.00 TO KM.121.248 [CHICHOLI - BETUL] (NHAI) (N24001764) (MADHYA PRADESH)	814.04	9/1/2023	468.94
	7	UPGRADATION OF NH 930 JHALMALA TO SHERPER FROM NH KM 30.600 TO KM 67.800 TO TWOFOUR LANE WITH PAVED (MoRTH) (N24001918) (CHHATTISGARH)	222.86	8/1/2023	168.98
	8	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V (NHAI) (N24001212) (MADHYA PRADESH)	656.98	11/1/2022	1,058.34

Table:-3. Project List: Completed during September 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Original Cost in Rs. Crore	Date of Commissioning Original (MM/YYYY)	Cumulative Expenditure in Rs. Crore
	9	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM (NHA) (N24001214) (MADHYA PRADESH)	217.96	12/1/2022	2,298.00
	10	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION (MoRTH) (N24001218) (CHHATTISGARH)	335.32	6/1/2017	345.52
	11	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V (MoRTH) (N24001219) (CHHATTISGARH)	476.20	9/1/2016	502.91
	12	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) (NHIDCL) (N24001283) (MIZORAM)	281.78	7/1/2022	237.91
	13	MARIAM - PEREN PKG-2B (NHIDCL) (N24001351) (MANIPUR)	232.26	12/1/2022	156.93
		Total	7,277.78		8,422.18

Table:-4. Project List: Added during September 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
<u>PETROLEUM</u>	1	HP TRIJET UNIT IN VR (HPCL) (N16000535) (ANDHRA PRADESH)	7/2024	193.00 (N.A.) {193.00}	7/2027 (N.A.) {7/2027}
	2	DEMO PLANT FOR PRODUCTION OF BIO-ATF (MANGALORE REFIN) (N16000536) (KARNATAKA)	3/2024	364.00 (N.A.) {364.00}	3/2027 (N.A.) {3/2027}
	3	INTEGRATED DEVELOPMENT OF 4 CONTRACT AREAS UNDER DSF2 (ONGC) (N16000537) (MAHARASHTRA)	5/2023	6,183.79 (N.A.) {6,183.79}	4/2027 (N.A.) {4/2027}
<u>POWER</u>	4	TS FOR EVACUATION OF POWER FROM 7GW REZ IN KHAVDA AREA UNDER PHASE-IV PART E2 (PGCIL) (N18000390) (GUJARAT)	5/2024	679.00 (N.A.) {679.00}	5/2026 (N.A.) {5/2026}
	5	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) PART-B (JAISALMER/BARMER COMPLEX) (PGCIL) (N18000391) (RAJASTHAN)	8/2024	3,279.00 (N.A.) {3,279.00}	8/2026 (N.A.) {8/2026}
	6	TS FOR EVACUATION POWER RAJASTHAN REZ PH- IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX): PART-C (PGCIL) (N18000392) (MADHYA PRADESH)	8/2024	2,708.00 (N.A.) {2,708.00}	8/2026 (N.A.) {8/2026}
	7	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-C (PGCIL) (N18000393) (RAJASTHAN)	8/2024	2,227.00 (N.A.) {2,227.00}	8/2026 (N.A.) {8/2026}
	8	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-E (PGCIL) (N18000394) (RAJASTHAN)	8/2024	3,251.00 (N.A.) {3,251.00}	8/2026 (N.A.) {8/2026}

Table:-4. Project List: Added during September 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
ROAD TRANSPORT AND HIGHWAYS	9	AUGMENTATION OF 1500MVA 3RD 765/400KV TRANSFORMATION CAPACITY AT KURNOOL NEW SUBSTATION (PGCIL) (N18000395) (ANDHRA PRADESH)	5/2023	164.00 (N.A.) {164.00}	9/2025 (N.A.) {9/2025}
	10	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154) (ASSAM)	3/2023	728.97 (N.A.) {728.97}	2/2027 (N.A.) {2/2027}
	11	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155) (ASSAM)	3/2023	665.47 (N.A.) {665.47}	3/2027 (N.A.) {3/2027}
	12	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156) (MEGHALAYA)	3/2023	620.30 (N.A.) {620.30}	9/2026 (N.A.) {9/2026}
	13	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157) (MEGHALAYA)	3/2023	686.00 (N.A.) {686.00}	9/2026 (N.A.) {9/2026}
	14	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158) (MEGHALAYA)	3/2023	562.48 (N.A.) {562.48}	9/2026 (N.A.) {9/2026}
	15	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGTH: 11.210 KM) (NHIDCL) (N24002159) (TRIPURA)	2/2020	174.43 (N.A.) {174.43}	3/2026 (N.A.) {3/2026}

Table:-4. Project List: Added during September 2024

Sector	Sl. No.	Project Name (Agency Name) (Project Code) (State Name)	Date of Approval (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)
	16	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160) (TRIPURA)	1/2024	431.78 (N.A.) {431.78}	7/2026 (N.A.) {7/2026}
	17	KHOWAI TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-2 (NHIDCL) (N24002161) (TRIPURA)	1/2024	657.21 (N.A.) {657.21}	9/2026 (N.A.) {9/2026}
	18	KHOWAI TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-3 (NHIDCL) (N24002162) (TRIPURA)	1/2024	670.90 (N.A.) {670.90}	9/2026 (N.A.) {9/2026}
	19	CONSTRUCTION FOR MITIGATION MEASURES KM 368.00-UTTARAKHAND-TO KM 433.00 ON NH-07- PKG-1 (NHIDCL) (N24002163) (UTTARAKHAND)	12/2023	216.88 (N.A.) {216.88}	12/2025 (N.A.) {12/2025}
	20	CONSTRUCTION FOR MITIGATION MEASURES KM 450.00-UTTARAKHAND-TO KM 468.00 ON NH-07- PKG-3 (NHIDCL) (N24002164) (UTTARAKHAND)	12/2023	250.33 (N.A.) {250.33}	12/2025 (N.A.) {12/2025}
	21	CONSTRUCTION OF BYPASS TO MADURAI - ACHAMBATHU - VIRATIPATHU IN KM 6/850 - 10/382 OF NH 49 EXTN. (NE (MoRTH) (N24002165) (TAMIL NADU)	3/2022	238.97 (N.A.) {238.97}	8/2026 (N.A.) {8/2026}
Grand Total				24,952.51 (-) {24,952.51}	

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ARUNACHAL PRADESH	CIVIL AVIATION	1	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2/2019	8/2022 (Dec-24) {12/2024}	645.63 (N.A.) {712.15}	667.54	98.43
	POWER	2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9/2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {21,247.54}	22,026.82	93.88
		3	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2/2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	2,524.53	12.74
	ROAD TRANSPOR T AND HIGHWAYS	4	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2/2017	11/2023 (Mar-24) {11/2024}	180.57 (244.10) {180.57}	154.17	90.01
		5	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685)	2/2017	4/2022 (Nov-23) {11/2023}	167.28 (N.A.) {167.28}	144.91	100
		6	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3/2017	3/2022 (Jun-25) {6/2025}	1,718.59 (1,718.59) {1,718.59}	674.32	68.84
		7	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9/2016	12/2019 (Aug-24) {9/2024}	568.92 (568.92) {568.92}	508.65	100
		8	TWO-LANING OF HAYULIANG HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1/2017	5/2023 (May-23) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		9	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA- KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8/2020	4/2022 (Feb-25) {2/2025}	301.06 (N.A.) {301.06}	140.37	62.09
		10	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE- BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO (NHIDCL) (N24001245)	9/2020	5/2022 (Oct-22) {3/2024}	353.90 (N.A.) {353.90}	41.82	25.38
		11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE (MoRTH) (N24001291)	3/2019	3/2027 (N.A.) {3/2027}	421.48 (N.A.) {421.48}	365.83	100
		12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292)	3/2019	3/2027 (N.A.) {3/2027}	543.05 (N.A.) {600.00}	568.30	99.3
		13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE (MoRTH) (N24001293)	3/2019	3/2027 (N.A.) {3/2027}	486.70 (N.A.) {486.70}	474.23	100
		14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3/2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	371.45	91.71
		15	TADADEGE - HENKAR (NHIDCL) (N24001315)	2/2021	3/2023 (Jun-24) {9/2024}	550.45 (N.A.) {550.45}	113.92	44.05
		16	LADDA - BASAI (NHIDCL) (N24001316)	2/2021	4/2023 (Jan-25) {3/2025}	445.96 (N.A.) {445.96}	117.91	49.63
		17	DOGINALA - GAU (NHIDCL) (N24001320)	12/2020	9/2022 (N.A.) {12/2024}	242.30 (N.A.) {242.30}	21.47	17.81
		18	JORAM KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8/2020	4/2022 (Aug-24) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		19	JORAM KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8/2020	4/2022 (Feb-24) {9/2024}	294.04 (N.A.) {294.04}	147.13	100
		20	JORAM KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG-6) (NHIDCL) (N24001392)	8/2020	4/2022 (Jul-23) {7/2023}	199.03 (N.A.) {199.03}	102.85	100
		21	JORAM KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG-7) (NHIDCL) (N24001393)	8/2020	4/2022 (Feb-24) {11/2024}	184.88 (N.A.) {184.88}	95.64	93.83
		22	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372)	2/2021	3/2024 (Dec-24) {12/2024}	588.09 (N.A.) {588.09}	449.76	93.18
		23	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374)	6/2020	3/2027 (N.A.) {3/2027}	437.60 (N.A.) {437.60}	365.27	96.7
		24	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6/2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	142.05	34.41
ASSAM	CIVIL AVIATION	25	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12/2016	3/2021 (N.A.) {3/2025}	1,142.00 (N.A.) {2,333.00}	1,346.22	66.34
	HEALTH AND FAMILY WELFARE	26	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5/2017	5/2021 (Apr-23) {11/2024}	875.00 (873.92) {860.00}	769.30	98.94
	PETROLEU M	27	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9/2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	3.05	2.4
		28	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3/2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	56.33	71

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		29	DCU REVAMP PROJECT (NRL) (N16000511)	8/2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	152.65	34
		30	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1/2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	108.35	40.1
		31	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1/2018	2/2020 (Dec-23) {12/2024}	543.91 (N.A.) {670.90}	491.56	93.71
		32	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINERY (NRL) (N16000379)	1/2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	12,545.43	63.74
		33	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1/2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	8,192.36	77.65
		34	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5/2021	10/2023 (Feb-25) {2/2025}	412.00 (509.84) {509.84}	356.90	77.8
		35	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON (ONGC) (N16000433)	8/2021	2/2023 (Jun-24) {8/2024}	218.38 (N.A.) {218.38}	186.79	83.3
		36	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3/2022	7/2026 (Sep-26) {9/2026}	277.00 (N.A.) {277.00}	156.92	50.6
		37	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6/2021	12/2024 (N.A.) {12/2024}	860.00 (N.A.) {860.00}	399.50	86.5

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		38	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION, PROCESSING (OIL) (N16000450)	12/2020	7/2024 (Mar-24) {12/2024}	430.76 (N.A.) {430.76}	245.08	72.55
		39	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6/2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	59.42	7.4
		40	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3/2023	7/2027 (Jul-27) {7/2027}	156.36 (156.36) {156.36}	1.08	11
		41	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3/2023	7/2027 (Jul-27) {7/2027}	384.04 (N.A.) {384.04}	31.57	3.5
	RAILWAYS	42	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4/2015	3/2022 (N.A.) {3/2027}	2,232.32 (N.A.) {4,983.94}	3,451.65	92
	ROAD TRANSPORT AND HIGHWAYS	43	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2/2021	7/2025 (N.A.) {7/2025}	925.47 (N.A.) {925.47}	321.15	30.62
		44	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 (NHAI) (N24001432)	12/2021	8/2024 (Mar-24) {8/2024}	300.00 (N.A.) {300.00}	297.62	100
		45	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8/2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	292.37	57.74
		46	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3/2021	1/2023 (N.A.) {10/2024}	288.85 (N.A.) {288.85}	231.27	96.08
		47	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3/2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	78.65	30.81
		48	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9/2021	7/2024 (N.A.) {12/2024}	625.64 (N.A.) {625.64}	457.70	82.62

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		49	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3/2022	7/2024 (N.A.) {8/2024}	215.27 (N.A.) {215.27}	146.02	97.94
		50	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 (NHIDCL) (N24001452)	4/2022	7/2024 (N.A.) {8/2024}	170.95 (N.A.) {170.95}	125.71	100
		51	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11/2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,028.10	51.59
		52	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3/2020	6/2022 (May-25) {5/2025}	261.13 (N.A.) {261.13}	64.96	54.59
		53	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3/2020	6/2022 (Apr-25) {4/2025}	217.50 (N.A.) {217.50}	84.36	64.15
		54	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3/2020	12/2022 (N.A.) {8/2024}	220.20 (N.A.) {220.20}	215.69	97.76
		55	WIDENING/IMPROVEMENT TO 4- LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 (NHIDCL) (N24001248)	8/2020	4/2022 (N.A.) {7/2024}	208.84 (N.A.) {208.84}	191.18	100
		56	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3/2020	3/2022 (Dec-23) {12/2024}	216.49 (241.52) {216.49}	104.36	79.48
		57	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6/2015	8/2023 (N.A.) {12/2024}	437.39 (N.A.) {437.39}	321.54	24.35
		58	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6/2015	3/2024 (N.A.) {9/2025}	463.49 (N.A.) {463.49}	368.35	31.56

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		59	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1/1991	6/2019 (Jun-19) {10/2024}	520.01 (N.A.) {520.01}	304.78	90.01
		60	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12/2015	12/2018 (Jul-21) {10/2024}	289.99 (N.A.) {289.99}	232.66	87.62
		61	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1/2016	1/2016 (N.A.) {12/2024}	294.17 (N.A.) {294.17}	295.84	41.24
		62	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1/2016	12/2021 (N.A.) {3/2025}	252.00 (N.A.) {330.30}	146.28	0
		63	FOUR LANING OF BALACHERA- HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE (NHIDCL) (N24000902)	10/2017	6/2020 (Dec-23) {4/2024}	818.00 (887.68) {887.68}	873.61	100
		64	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11/2021	7/2024 (N.A.) {12/2024}	204.10 (N.A.) {204.10}	125.63	81.78
		65	FOUR LANING OF SRIRAMPUR- DHUBRI PKG-2 (NHIDCL) (N24001544)	3/2022	1/2025 (N.A.) {1/2025}	909.02 (N.A.) {909.02}	388.98	76.17
		66	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8/2022	12/2022 (Sep-24) {6/2024}	175.00 (N.A.) {175.00}	178.56	98.13
		67	BALANCE WORK OF 4L OF NARIMBANGLOJATINGA JUNCTION- HARANGAJAO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3/2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	394.71	48.37

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		68	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3/2022	6/2024 (N.A.) {12/2024}	457.72 (N.A.) {457.72}	252.91	85
		69	SHRIRAMPUR (KM. 0.000) TO KOCHUGAON (KM. 30.000) OF BIJNI TO ASSAM./WEST BENGAL BORDER SECTION OF NH (NHAI) (N24001549)	7/2017	4/2020 (Jul-24) {7/2024}	442.23 (N.A.) {442.23}	265.19	100
		70	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3/2022	2/2025 (N.A.) {12/2025}	613.89 (N.A.) {613.89}	17.09	9.23
		71	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1/2023	5/2025 (N.A.) {5/2025}	458.59 (N.A.) {458.59}	140.63	40.35
		72	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3/2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	4.07	10.6
		73	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) I (NHIDCL) (N24001969)	3/2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	281.73	37.01
		74	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001970)	3/2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	267.62	37.12
		75	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3/2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	326.53	33.78

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		76	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3/2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	182.45	51.25
		77	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3/2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	165.88	50.16
		78	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3/2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	349.64	23.67
		79	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3/2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	210.48	9.72
		80	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3/2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	269.25	11.97
		81	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1/2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	152.60	41.3
		82	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1/2023	12/2025 (N.A.) {12/2025}	356.65 (N.A.) {356.65}	115.18	5.05
		83	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3/2023	12/2025 (N.A.) {12/2025}	643.42 (N.A.) {643.42}	65.32	8.35
		84	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2/2020	3/2022 (N.A.) {10/2024}	592.06 (N.A.) {592.06}	291.85	97.9
		85	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2/2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	313.76	12.11

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		86	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3/2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	731.85	28.42
		87	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH- 6 (NHIDCL) (N24002129)	2/2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	172.77	18.3
		88	TAMENGLONG- MAHUR ROAD PKG- 7 (NHIDCL) (N24002130)	12/2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	278.53	29.35
		89	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH-53) AT KALIN (NHIDCL) (N24002154)	3/2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	88.64	0
		90	WIDENING/IMPROVEMENT TO 4- LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3/2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	73.01	0
MANIPUR	CIVIL AVIATION	91	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11/2021	7/2024 (Dec-25) {12/2025}	499.00 (N.A.) {499.00}	106.39	36.88
	RAILWAYS	92	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4/2003	3/2011 (Mar-28) {12/2028}	4,454.17 (12,274.06) {19,517.70}	14,774.02	79.8
	ROAD TRANSPOR T AND HIGHWAYS	93	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1/2023	12/2025 (N.A.) {3/2026}	760.16 (N.A.) {760.16}	63.80	27.83
		94	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3/2023	2/2026 (N.A.) {3/2026}	578.98 (N.A.) {578.98}	56.22	31.54
		95	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9/2021	1/2025 (N.A.) {1/2025}	315.56 (N.A.) {315.56}	60.70	49.44
		96	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12/2021	5/2024 (N.A.) {10/2025}	410.68 (N.A.) {410.68}	105.71	50.81

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		97	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12/2021	2/2025 (N.A.) {11/2025}	504.76 (N.A.) {504.76}	101.94	44.33
		98	AKASH BRIDGE - JESSAMI SECTION PKG-2 (NHIDCL) (N24001540)	3/2022	2/2025 (N.A.) {2/2025}	152.11 (N.A.) {152.11}	53.26	72.82
		99	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9/2021	2/2024 (N.A.) {4/2025}	310.76 (N.A.) {310.76}	116.81	76.8
		100	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3/2020	6/2022 (Dec-23) {12/2024}	292.24 (N.A.) {292.24}	127.86	85.33
		101	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6/2020	8/2022 (N.A.) {12/2024}	365.53 (N.A.) {365.53}	156.31	77.36
		102	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3/2020	6/2022 (N.A.) {12/2024}	167.95 (204.12) {167.95}	88.05	69.89
		103	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7/2020	8/2022 (N.A.) {12/2024}	177.76 (N.A.) {177.76}	89.67	80.53
		104	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8/2020	4/2022 (Jun-25) {8/2025}	379.39 (N.A.) {379.39}	189.86	45.88
		105	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO (NHIDCL) (N24001275)	8/2020	4/2022 (N.A.) {12/2025}	268.98 (N.A.) {268.98}	22.08	0
		106	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276)	8/2020	4/2022 (N.A.) {12/2025}	228.97 (N.A.) {228.97}	0.00	0

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		107	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2/2021	12/2022 (N.A.) {4/2025}	226.32 (N.A.) {226.32}	86.41	63.75
		108	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2/2021	12/2022 (Oct-24) {10/2024}	188.36 (N.A.) {188.36}	126.71	95.37
		109	IMPHAL MOREH PACKAGE- 3 (NHIDCL) (N24001352)	3/2021	12/2022 (N.A.) {6/2024}	259.31 (N.A.) {259.31}	144.94	100
		110	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3/2021	12/2022 (Nov-23) {6/2025}	195.14 (N.A.) {195.14}	59.99	50.75
		111	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3/2021	12/2022 (Jan-25) {1/2025}	234.08 (N.A.) {234.08}	139.45	90.34
		112	IMPHAL MOREH (PACKAGE 4) (NHIDCL) (N24001399)	3/2021	1/2023 (N.A.) {4/2024}	277.99 (N.A.) {277.99}	146.35	100
		113	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3/2021	1/2023 (N.A.) {5/2025}	211.70 (N.A.) {211.70}	35.16	34.86
		114	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7/2021	3/2023 (Feb-24) {3/2025}	467.00 (N.A.) {467.00}	183.55	75.23
		115	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7/2021	3/2023 (Jan-25) {1/2025}	185.80 (N.A.) {185.80}	112.31	92.65
		116	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7/2021	3/2023 (May-24) {2/2025}	483.87 (N.A.) {483.87}	278.89	91.03
		117	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7/2021	3/2023 (Feb-25) {2/2025}	198.77 (N.A.) {198.77}	110.09	85.12
		118	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7/2021	10/2023 (Feb-24) {6/2025}	673.27 (N.A.) {673.27}	357.47	72.74
		119	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8/2021	12/2023 (N.A.) {12/2025}	579.63 (N.A.) {579.63}	131.58	52.55
		120	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8/2021	5/2023 (N.A.) {10/2024}	467.41 (N.A.) {467.41}	243.19	92.18
		121	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8/2021	5/2023 (Jan-25) {2/2025}	477.86 (N.A.) {477.86}	235.67	80.3
		122	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9/2021	5/2023 (Oct-23) {4/2025}	311.18 (N.A.) {311.18}	171.57	72.7

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MEGHALAYA	DEPARTMENT OF HIGHER EDUCATION	123	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9/2013	9/2014 (Jul-24) {7/2024}	484.32 (429.70) {429.70}	274.05	72.5
	DONER	124	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR (HSCL FOR DONER) (N12000103)	4/2014	9/2017 (N.A.) {9/2017}	151.33 (N.A.) {151.33}	148.33	98.5
	RAILWAYS	125	NEW BG LINE FROM BYRNIHAT TO SHILLONG (NFR) (N22000205)	4/2010	3/2021 (N.A.) {3/2021}	906.46 (1,202.33) {8,324.28}	269.80	2
	ROAD TRANSPORT AND HIGHWAYS	126	RANIKOR-MAHESHKHOLA-BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10/2020	4/2022 (Jun-24) {12/2024}	157.86 (146.92) {157.86}	146.19	97.49
		127	RANIKOR-MAHESHKHOLA-BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3/2021	12/2022 (Jun-24) {11/2024}	260.21 (N.A.) {260.21}	202.19	89.14
		128	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11/2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	191.35	6.2
		129	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11/2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	45.46	1.5
		130	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM () (NHIDCL) (N24001313)	11/2020	12/2023 (Oct-25) {10/2025}	351.12 (N.A.) {351.12}	223.73	24.2
		131	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11/2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	384.55	13.5

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		132	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM (NHIDCL) (N24000903)	3/2019	3/2022 (Dec-23) {12/2023}	306.28 (N.A.) {306.28}	233.49	100
		133	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4/2017	9/2021 (Jul-23) {3/2025}	553.51 (610.09) {553.51}	343.73	67.31
		134	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9/2021	5/2024 (N.A.) {1/2025}	359.86 (N.A.) {359.86}	219.87	78.5
		135	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8/2020	2/2022 (Oct-24) {10/2024}	302.88 (N.A.) {302.88}	209.63	93
		136	RANIKOR- MAHESHKHOLA-BAGHMARA PKG-2 (NHIDCL) (N24001541)	11/2021	6/2024 (N.A.) {12/2024}	283.50 (N.A.) {283.50}	201.77	70.68
		137	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3/2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	168.64	0
		138	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3/2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	241.74	0
		139	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3/2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	263.14	0
MIZORAM	RAILWAYS	140	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4/2008	3/2014 (N.A.) {7/2025}	2,393.47 (5,021.45) {8,213.72}	7,520.14	93

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD</u> <u>TRANSPOR</u> <u>T AND</u> <u>HIGHWAYS</u>	141	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWLRANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9/2021	2/2025 (N.A.) {2/2026}	523.78 (N.A.) {523.78}	236.92	40
		142	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12/2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	137.25	36.31
		143	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4/2017	4/2023 (Mar-24) {1/2025}	519.09 (785.65) {785.65}	649.83	90
		144	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4/2017	7/2023 (May-24) {7/2024}	640.07 (990.88) {1,286.35}	1,217.65	99
		145	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4/2017	6/2023 (Mar-24) {3/2024}	642.96 (988.23) {988.23}	729.79	99.5
		146	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4/2017	4/2023 (Nov-23) {2/2025}	473.18 (688.25) {688.25}	520.26	83.66
		147	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4/2017	4/2023 (Oct-23) {2/2025}	537.82 (789.05) {789.05}	746.61	91.6
		148	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4/2017	6/2023 (Feb-24) {3/2025}	518.53 (906.76) {906.76}	784.80	88.5

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		149	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4/2017	4/2024 (Jul-24) {3/2025}	404.29 (750.32) {750.32}	589.53	83.2
		150	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4/2017	9/2023 (May-24) {3/2025}	428.11 (746.39) {746.39}	579.70	87.17
		151	CONSTRUCTION OF CHHIATHLANG-SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9/2020	10/2022 (Apr-24) {3/2024}	275.02 (247.25) {247.25}	231.19	99.73
		152	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3/2020	7/2022 (Jan-24) {6/2024}	206.88 (219.33) {219.33}	206.55	97.01
		153	DULTE- KWALKULH - CHAMPAI PKG.1 (NHIDCL) (N24001355)	3/2021	12/2022 (Mar-24) {3/2024}	374.39 (374.39) {374.39}	292.27	100
		154	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3/2021	12/2022 (Apr-24) {4/2024}	233.25 (233.25) {233.25}	178.37	100
		155	DULTE- KWALKULH - CHAMPAI PKG.3 (NHIDCL) (N24001357)	3/2021	6/2023 (Jan-24) {1/2024}	674.71 (674.71) {674.71}	589.25	100
		156	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3/2021	12/2022 (Dec-24) {12/2025}	698.44 (698.45) {698.45}	383.62	42.2
		157	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3/2021	1/2023 (Dec-24) {12/2025}	740.58 (740.58) {740.58}	276.77	41.5
		158	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3/2020	7/2022 (Mar-24) {7/2025}	292.24 (331.17) {331.17}	287.95	91.42
		159	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9/2021	5/2023 (Jun-24) {12/2024}	492.94 (492.94) {492.94}	355.00	84.7

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
NAGALAND	PETROLEUM	160	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8/2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	0.20	7.5
	RAILWAYS	161	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4/2006	3/2015 (N.A.) {12/2029}	2,326.52 (6,663.20) {6,663.20}	3,770.54	58
	ROAD TRANSPORT AND HIGHWAYS	162	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6/2020	9/2024 (Jun-26) {6/2026}	252.19 (N.A.) {252.19}	0.28	0
		163	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3/2021	7/2024 (Mar-25) {3/2025}	297.24 (N.A.) {297.24}	109.40	55.07
		164	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3/2021	2/2024 (Feb-25) {2/2025}	226.44 (N.A.) {226.44}	109.16	76.78
		165	MERANGKONG-TAMLU-MON (MTM) PKG-5 (NHIDCL) (N24001438)	7/2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	43.05	23.71
		166	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3/2020	6/2022 (Sep-22) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.4
		167	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7/2021	3/2023 (Sep-25) {9/2025}	258.52 (N.A.) {258.52}	62.78	57.55
		168	PEREN-DIMAPUR PKG-5 (NHIDCL) (N24001407)	2/2021	3/2023 (N.A.) {3/2023}	207.33 (N.A.) {207.33}	0.00	0
		169	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3/2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	109.24	60.93
		170	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) (NHIDCL) (N24001284)	3/2020	6/2022 (Jun-23) {6/2024}	361.53 (365.42) {365.42}	200.22	97.42

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		171	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG- I) (NHIDCL) (N24001286)	3/2020	6/2022 (Oct-22) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
		172	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4/2020	12/2021 (Nov-25) {11/2025}	330.80 (N.A.) {330.80}	110.22	58.59
		173	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8/2020	4/2022 (Nov-26) {11/2026}	232.29 (350.88) {232.29}	39.59	1.62
		174	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9/2020	10/2022 (Apr-24) {9/2024}	277.44 (N.A.) {277.44}	160.86	62.27
		175	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8/2020	10/2022 (Jun-25) {6/2025}	159.85 (342.29) {159.85}	76.99	15.94
		176	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA- BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8/2020	4/2022 (Apr-23) {2/2025}	202.36 (N.A.) {202.36}	71.92	26.96
		177	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9/2020	4/2022 (May-24) {2/2025}	315.63 (N.A.) {315.63}	95.84	74.23
		178	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) (NHIDCL) (N24001280)	3/2020	6/2022 (Mar-23) {9/2023}	320.97 (N.A.) {320.97}	182.21	100

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		179	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3/2017	11/2020 (Feb-23) {2/2023}	217.35 (N.A.) {217.35}	214.18	100
		180	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3/2019	12/2022 (Jan-23) {1/2023}	237.51 (N.A.) {237.51}	201.20	100
		181	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3/2016	9/2019 (Nov-22) {12/2024}	373.07 (534.41) {534.41}	382.50	99.81
		182	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3/2016	8/2022 (Sep-25) {9/2025}	429.52 (794.74) {794.74}	287.46	83.4
		183	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2/2017	9/2020 (Feb-23) {12/2024}	387.00 (688.12) {688.12}	387.50	99.32
		184	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3/2018	11/2022 (Aug-24) {12/2024}	500.09 (698.81) {698.81}	373.62	94.81
		185	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756)	3/2018	9/2022 (Jan-23) {7/2024}	285.68 (N.A.) {285.68}	174.28	99.9
		186	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3/2018	12/2021 (Aug-22) {8/2025}	215.79 (N.A.) {215.79}	107.40	27.45

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		187	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3/2018	9/2018 (Jun-23) {9/2025}	323.98 (N.A.) {323.98}	81.60	16.04
		188	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12/2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	35.44	20.02
		189	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12/2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	17.58	11.32
		190	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12/2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	68.58	29.41
		191	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3/2022	12/2024 (N.A.) {12/2024}	605.36 (N.A.) {605.36}	214.50	84.14
		192	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2/2021	6/2025 (Jun-25) {6/2025}	192.93 (N.A.) {192.93}	55.72	53.23
		193	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2/2021	6/2025 (N.A.) {6/2025}	177.77 (199.02) {199.02}	17.31	26.64
SIKKIM	CIVIL AVIATION	194	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11/2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	6.01	3

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	195	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim University) (N44000002)	8/2020	1/2025 (N.A.) {12/2024}	314.06 (N.A.) {303.55}	157.24	54
	<u>POWER</u>	196	TEESTA VI HE PROJECT (NHPC) (N18000325)	3/2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	3,731.76	63.39
		197	RANGIT IV HE PROJECT (NHPC) (N18000326)	3/2021	5/2024 (N.A.) {5/2025}	938.29 (N.A.) {1,871.23}	1,240.93	79.41
	<u>RAILWAYS</u>	198	SEVOK RANGPO, NEFR (NFR) (N22000102)	4/2008	12/2015 (N.A.) {12/2023}	1,339.48 (N.A.) {7,876.92}	3,290.96	39.8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	199	SPECIAL PROTECTION WORK ON REHABILITATION AND RESTORATION OF SLIDING AND SINKING ZONE FROM RANGPO TO (NHIDCL) (N24001913)	3/2017	6/2022 (N.A.) {6/2022}	165.56 (N.A.) {165.56}	0.00	71.74
		200	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10/2021	5/2024 (Jan-25) {1/2025}	385.15 (N.A.) {385.15}	167.49	75
		201	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3/2017	4/2022 (May-22) {12/2023}	375.80 (N.A.) {375.80}	287.54	95.26
		202	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11/2017	10/2020 (Aug-23) {4/2024}	290.05 (N.A.) {290.05}	218.36	96.98
		203	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3/2019	4/2022 (N.A.) {1/2025}	402.94 (N.A.) {402.94}	236.53	73.11

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		204	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8/2020	4/2023 (Nov-24) {3/2025}	295.97 (N.A.) {295.97}	243.68	93.39
		205	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3/2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	100
		206	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8/2020	4/2023 (N.A.) {10/2024}	311.00 (N.A.) {273.78}	240.56	93.88
		207	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7/2020	4/2023 (Aug-24) {3/2025}	345.38 (395.59) {395.59}	355.08	89.04
		208	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9/2020	5/2022 (Oct-23) {3/2025}	183.31 (439.56) {439.56}	351.16	46.26
		209	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9/2020	5/2023 (Aug-24) {3/2025}	262.84 (414.20) {414.20}	220.26	46.17
		210	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM 27.200 (END OF RO) (NHIDCL) (N24001336)	8/2020	4/2023 (Oct-24) {6/2025}	230.45 (244.91) {244.91}	200.82	77.2

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		211	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10/2020	11/2023 (Jul-25) {7/2025}	493.42 (478.79) {478.79}	269.79	40.05
		212	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10/2020	12/2023 (Jun-25) {12/2025}	816.79 (786.60) {786.60}	278.65	35.5
		213	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1/2021	9/2023 (Apr-25) {12/2025}	332.20 (N.A.) {332.20}	148.86	40.97
		214	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12/2020	2/2024 (Apr-25) {6/2025}	410.60 (379.30) {379.30}	188.53	43.19
		215	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8/2020	5/2022 (Oct-23) {3/2025}	292.80 (N.A.) {292.80}	179.62	49.25
TRIPURA	PETROLEUM	216	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6/2022	8/2025 (Sep-25) {9/2025}	656.00 (N.A.) {656.00}	301.82	64
	RAILWAYS	217	AGARTALA-AKHAURA NL (NFR) (N22000195)	4/2012	3/2020 (Jun-22) {9/2022}	569.63 (N.A.) {708.73}	380.92	84
	ROAD TRANSPORT AND HIGHWAYS	218	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3/2021	12/2022 (Jun-23) {1/2025}	354.79 (N.A.) {354.79}	34.08	17.2
		219	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT- KAILASHAHAR SECTION (NHIDCL) (N24001263)	6/2020	1/2022 (Feb-24) {10/2024}	277.50 (302.02) {302.02}	253.50	99.12
		220	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6/2020	1/2022 (Jul-24) {11/2024}	201.99 (287.47) {287.47}	144.07	95.4

Table:-5. Project List: Ongoing Projects of North-East Region

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		221	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 (NHIDCL) (N24001318)	9/2020	4/2022 (Oct-22) {10/2023}	173.17 (N.A.) {173.17}	93.35	100
		222	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11/2020	6/2022 (Oct-23) {10/2024}	159.13 (171.50) {171.50}	79.43	98.36
		223	REHABILITATION AND UP- GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGTH: 11.210 KM) (NHIDCL) (N24002159)	2/2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	0.00	0
		224	IMPROVEMENT AND WIDENING TO 2-LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1/2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	0.00	0
		225	KHOWAI TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1/2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	0.00	0
		226	KHOWAI TELIAMURA-AMARPUR- HARINA-SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1/2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	0.00	0
		227	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2/2022	1/2025 (N.A.) {1/2025}	456.88 (N.A.) {456.88}	95.50	39.4
		228	IMPROVEMENT AND WIDENING TO 2-LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5/2023	11/2024 (N.A.) {2/2025}	195.95 (N.A.) {195.95}	15.22	17.4
		229	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3/2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	0.00	0.48
			Total			181,870.86 (-) {251,206.50}	132,821.68	

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
<u>ANDAMAN AND NICOBAR ISLANDS</u>	<u>CIVIL AVIATION</u>	1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR (AAI) (N04000073)	10/2013	9/2018 (May-23) {6/2023}	417.23 (707.73) {707.73}	698.80	100
	<u>RAILWAYS</u>	2	LUDHIANA KILA RAIPUR (19 KMS) WITH FREIGHT LINE AT GILL STATION ON LDH- JHL SECTION (NR) (N22000584)	3/2019	3/2025 (N.A.) {3/2025}	235.72 (N.A.) {235.72}	0.00	0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	3	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 () (NHIDCL) (N24000744)	3/2015	1/2022 (N.A.) {2/2026}	262.97 (N.A.) {262.97}	92.73	41.55
		4	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N (NHIDCL) (N24000745)	3/2017	12/2019 (Mar-23) {7/2024}	409.85 (N.A.) {409.85}	214.23	89.07
		5	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM (NHIDCL) (N24000748)	2/2018	9/2020 (Jan-23) {8/2025}	391.00 (N.A.) {391.00}	170.37	57.55
		6	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O (NHIDCL) (N24000749)	3/2018	9/2020 (Nov-22) {9/2024}	234.27 (N.A.) {234.27}	126.50	76.86
		7	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 (MoRTH) (N24000820)	11/2017	11/2019 (N.A.) {11/2019}	237.80 (N.A.) {238.00}	222.13	97.46
		8	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000821)	11/2017	11/2019 (N.A.) {11/2019}	257.34 (N.A.) {238.00}	214.90	100

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		9	AJANTHA TO BULDHANA (MoRTH) (N24001008)	2/2017	7/2019 (N.A.) {12/2023}	401.00 (401.00) {401.00}	260.08	97
ANDHRA PRADESH	CIVIL AVIATION	10	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT (AAI) (N04000089)	8/2017	2/2020 (Dec-21) {1/2024}	177.10 (N.A.) {177.10}	143.08	100
		11	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT (AAI) (N04000091)	4/2020	3/2023 (N.A.) {6/2025}	611.80 (N.A.) {611.80}	330.74	56
		12	RAJAHMUNDRI AIRPORT: CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUD (AAI) (N04000103)	12/2022	8/2025 (N.A.) {8/2025}	347.15 (N.A.) {347.15}	41.88	26
		13	KADAPPA AIRPORT- CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS INCLUDING MA (AAI) (N04000106)	3/2023	1/2026 (N.A.) {1/2026}	265.91 (N.A.) {265.91}	22.98	15
	DEPARTMENT OF HIGHER EDUCATION	14	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE (CPWD EDUCATION) (N42000005)	2/2019	6/2020 (N.A.) {6/2020}	655.34 (N.A.) {655.34}	366.21	95
		15	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT (CPWD EDUCATION) (N42000007)	9/2019	9/2022 (N.A.) {6/2024}	588.72 (656.39) {656.39}	666.18	100
	PETROLEUM	16	VISAKH REFINERY MODERNISATION PROJECT (HPCL) (N16000235)	7/2016	7/2020 (Jul-22) {10/2024}	20,928.00 (26,264.00) {30,609.00}	26,121.72	98.5

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		17	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT (ONGC) (N16000247)	3/2016	6/2020 (Mar-25) {3/2025}	34,012.00 (N.A.) {34,012.00}	30,729.58	93.3
		18	REVAMPING OF FACILITIES AT VIZAG TERMINAL (IOCL) (N16000343)	4/2018	4/2022 (Mar-25) {3/2025}	355.00 (N.A.) {355.00}	241.37	77.1
		19	SWRO II WITH LLPH FACILITIES (HPCL) (N16000378)	9/2019	7/2020 (N.A.) {3/2025}	196.26 (196.26) {196.26}	147.53	87.1
		20	HP CRUDE TO OLEFINS AND AROMATICS TECHNOLOGY DEMO UNIT AT VISAKH REFINERY (HPCL) (N16000432)	9/2021	6/2024 (N.A.) {6/2025}	160.00 (N.A.) {160.00}	13.20	41
		21	CGD PROJECT AT KURNOOL, GUNTUR AND PRAKASAM DISTRICTS (IOCL) (N16000485)	3/2022	3/2030 (N.A.) {3/2030}	1,420.00 (N.A.) {1,420.00}	113.61	4.8
		22	MULTI-PRODUCT PIPELINE FROM KRISHNAPATNAM COASTAL INSTALLATION TO THE PROPOSED INSTALLATION AT HYDER (BPCL) (N16000499)	9/2019	3/2025 (N.A.) {10/2025}	1,932.00 (N.A.) {1,932.00}	1,491.58	67.3
		23	HP TRIJET UNIT IN VR (HPCL) (N16000535)	7/2024	7/2027 (N.A.) {7/2027}	193.00 (N.A.) {193.00}	0.08	6
		24	TRANSMISSION SCHEME FOR SOLAR ENERGY ZONE IN ANANTHPURAM (2500MW) AND KURNOOL (1000MW) (PGCIL) (N18000380)	9/2023	3/2025 (N.A.) {9/2025}	1,249.00 (N.A.) {1,249.00}	93.81	15
	POWER	25	AUGMENTATION OF 1500MVA 3RD 765/400KV TRANSFORMATION CAPACITY AT KURNOOL NEW SUBSTATION (PGCIL) (N18000395)	5/2023	9/2025 (N.A.) {9/2025}	164.00 (N.A.) {164.00}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
RAILWAYS		26	KOTLPALLI-NARASAPUR (NL) (SCR) (SCR) (220100265)	12/2001	3/2009 (N.A.) {3/2027}	1,045.20 (N.A.) {2,500.98}	1,150.74	0
		27	NADIKUDE-SRI KALAHASTI (SCR) (N22000286)	4/2011	3/2021 (N.A.) {5/2027}	2,288.70 (N.A.) {3,122.35}	1,681.90	0
		28	GUNTUR-GUNTAKAL (SCR) (N22000368)	4/2016	3/2022 (N.A.) {12/2025}	3,631.00 (N.A.) {3,887.48}	3,125.17	0
		29	VIJAYAWADA-GUDUR (RVNL) (N22000369)	4/2015	12/2023 (N.A.) {12/2024}	3,246.26 (N.A.) {6,238.67}	5,614.60	84
		30	KOTTAVALSA - KORAPUT DOUBLING (ECOR) (N22000377)	4/2015	3/2022 (N.A.) {3/2022}	2,499.71 (N.A.) {2,499.71}	1,723.47	68
		31	PENUKONDA-DHARMAVARAM, EXCL. DHARMAVARAM (41.5 KM) (SWR) (N22000555)	4/2019	3/2026 (N.A.) {2/2025}	294.67 (307.66) {307.66}	125.30	41
		32	MALUGUR-PALASAMUDRAM (17.98 KM) (PB#29/NR/2022-23) (SWR) (N22000556)	9/2022	12/2025 (N.A.) {12/2026}	323.14 (342.41) {342.41}	39.46	12
		33	DOUBLING BETWEEN GOOTY- PENDAKALLU (29.225) (SCR) (N22000585)	3/2023	3/2027 (N.A.) {3/2027}	351.83 (N.A.) {351.83}	0.00	0
		34	VIJAYAWADA KAZIPET BYEPASS LINE (SCR) (N22000586)	4/2016	12/2025 (N.A.) {12/2025}	226.72 (N.A.) {226.72}	161.84	55
		35	RENIGUNTA WADI GOOTY - BYPASS (SCR) (N22000587)	4/2016	12/2025 (N.A.) {12/2025}	302.00 (N.A.) {302.00}	154.50	50
	ROAD TRANSPORT AND HIGHWAYS	36	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T (MoRTH) (N24000282)	1/2014	11/2014 (N.A.) {5/2024}	195.45 (N.A.) {385.97}	294.95	97

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		37	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES (MoRTH) (N24000301)	3/2015	10/2015 (May-21) {5/2021}	271.45 (N.A.) {271.45}	238.23	100
		38	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4-350 TO KM 75-600 (MoRTH) (N24000422)	3/2015	9/2015 (Aug-17) {5/2018}	309.01 (N.A.) {309.01}	0.00	100
		39	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 (NHAI) (N24000811)	3/2018	12/2020 (Dec-22) {12/2024}	314.43 (N.A.) {348.72}	85.61	64.44
		40	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) TO KM 275/622(DESIGN CH 5.12 (MoRTH) (N24000928)	10/2015	12/2015 (Dec-19) {1/2021}	333.21 (N.A.) {353.43}	342.71	100
		41	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU (MoRTH) (N24000929)	9/2016	2/2017 (Jan-22) {2/2022}	372.68 (N.A.) {309.37}	274.76	100
		42	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 (MoRTH) (N24000931)	11/2016	5/2017 (N.A.) {11/2024}	290.15 (N.A.) {236.16}	205.02	90
		43	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD (MoRTH) (N24000932)	1/2017	8/2017 (Jul-22) {7/2022}	319.28 (N.A.) {319.28}	241.94	100

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		44	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG (MoRTH) (N24000937)	3/2018	8/2018 (N.A.) {8/2024}	289.67 (290.00) {285.29}	254.19	97
		45	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P (MoRTH) (N24000963)	1/2018	8/2018 (Dec-21) {12/2021}	418.03 (386.99) {386.99}	365.55	100
		46	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH- 214(NH216)(KAKINAD (MoRTH) (N24000964)	8/2016	1/2017 (N.A.) {5/2025}	350.61 (N.A.) {411.18}	457.55	98
		47	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 (MoRTH) (N24000969)	1/2017	9/2017 (N.A.) {3/2025}	263.45 (N.A.) {263.45}	241.95	84
		48	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) (NHAI) (N24001301)	11/2019	1/2024 (N.A.) {7/2024}	1,601.10 (N.A.) {1,601.10}	1,180.71	75.27
		49	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU- GONDIGUDA SECT (MoRTH) (N24001386)	8/2020	3/2021 (N.A.) {8/2024}	222.61 (N.A.) {222.61}	143.53	76
		50	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH 365BG FROM RECHARLA VI (NHAI) (N24001476)	9/2021	9/2022 (Sep-24) {3/2025}	517.05 (N.A.) {655.06}	517.26	60.6

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		51	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED NEW GREENFIELD HIGHWAY SECTION OF NH-365BG (KHAMMAM-DEVARAP (NHAI) (N24001477)	9/2021	9/2022 (Sep-24) {5/2025}	622.00 (N.A.) {817.91}	502.15	53.09
		52	6L OF CHILKARARUPET BYPASS FROM KM. 357.400 TO KM. 371.920 OF NH-16 (NHAI) (N24001817)	2/2019	3/2023 (Oct-24) {10/2024}	757.45 (N.A.) {757.45}	484.16	81.07
		53	6L OF PONDAVAKKAM TO KANNIGAIPAI FROM KM 96.040 TO KM 116.100 OF NH 716B (PKG-IV) (NHAI) (N24001818)	2/2021	1/2025 (N.A.) {1/2025}	818.73 (N.A.) {1,105.00}	335.42	17.52
		54	6L OF VEERA KAVERI RAJA PURAM TO PONDAVAKKAM FROM KM 61.380 TO KM 96.040 OF NH 716B (PKG-III) (NHAI) (N24001819)	3/2021	1/2025 (N.A.) {1/2025}	1,102.63 (N.A.) {1,303.00}	784.25	75.3
		55	6L OF VARADHARAJULA TO KUMARAJAPET FROM KM 0.000 TO KM 43.800 OF NH-716B (PKG-I) (NHAI) (N24001820)	2/2021	12/2024 (N.A.) {12/2024}	1,484.83 (N.A.) {1,768.00}	1,028.89	60.77
		56	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-III) FROM KM.127.000 TO KM 156.000 (BANGARUPALEM TO GUDIP (NHAI) (N24001821)	11/2020	10/2024 (N.A.) {10/2024}	1,137.74 (N.A.) {1,289.00}	907.36	81.7
		57	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-I) FROM KM.71.000 TO KM 96.000 (BETHAMANGALA IN THE STATE (NHAI) (N24001822)	12/2020	10/2024 (N.A.) {10/2024}	1,075.27 (N.A.) {1,307.00}	775.28	63.8
		58	4L OF MADANAPALLE TO PILERU SECTION FROM KM 0.000 TO KM 55.900 OF NH-71(PACKAGE-I) - N/05060/01002/A (NHAI) (N24001823)	1/2022	1/2025 (Jan-23) {1/2025}	1,852.12 (N.A.) {1,787.00}	525.31	67

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		59	RENIGUNTA - POYYA - NAIDUPETA KM 124.60 TO KM 183.4 OF NH 71 - N/04027/06001/AP (NHAI) (N24001824)	3/2020	1/2024 (Dec-24) {12/2024}	1,863.09 (N.A.) {2,238.00}	1,227.61	92.36
		60	6L KANTAKAPALLE SABBAVARAM SECTION OF NH-130CD ROAD FROM KM 445.100 TO KM 464.662 (PKG-4) (NHAI) (N24001836)	2/2021	10/2024 (N.A.) {10/2024}	824.29 (N.A.) {924.00}	388.86	61
		61	6L JAKKUVA KORLAM SECTION OF NH- 130CD ROAD FROM KM 396.800 TO KM 421.100 (PKG 2) (NHAI) (N24001837)	2/2021	3/2024 (Jul-24) {9/2024}	663.60 (N.A.) {768.00}	305.59	90.69
		62	6L ALURU - JAKKUVA SECTION OF NH- 130CD ROAD FROM KM 365.033 TO KM 396.800 (PKG. 1) (NHAI) (N24001838)	2/2021	3/2024 (N.A.) {3/2025}	922.50 (N.A.) {1,128.68}	361.56	69.9
		63	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KODUR 0.000 KMS TO VANAVOLU 24.300 KMS OF NH 544G PACKA (NHAI) (N24001841)	12/2022	9/2025 (N.A.) {2/2026}	912.94 (N.A.) {912.94}	148.88	24.73
		64	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANAVOLU 24.300 KM. TO VANKARAKUNTA 45.700 KM. OF NH 5 (NHAI) (N24001842)	12/2022	11/2025 (N.A.) {11/2025}	750.81 (N.A.) {750.81}	99.64	24.5
		65	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM VANKARAKUNTA 45.700 KM. TO ODULAPALLE 72.000 KM. OF NH (NHAI) (N24001843)	12/2022	11/2025 (N.A.) {11/2025}	992.89 (N.A.) {992.89}	94.42	11.5

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		66	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM ODULAPALLE 72.000 KM. TO NALLACHERUVUPALLI 96.300 KM. (NHAI) (N24001844)	12/2022	10/2025 (N.A.) {10/2025}	1,058.90 (N.A.) {1,058.90}	131.39	10.77
		67	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NALLACHERUVU PALLI 96.300 KM. TO YERRAGUDIPADU 129.000 (NHAI) (N24001845)	2/2023	10/2025 (N.A.) {10/2025}	1,253.24 (N.A.) {1,253.24}	70.84	3.5
		68	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM YERRAGUDIPADU 129.000 KM. TO AUDIREDDIPALLE 160.000 KM. (NHAI) (N24001846)	2/2023	10/2025 (N.A.) {10/2025}	1,200.42 (N.A.) {1,200.42}	57.64	1.5
		69	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM AUDIREDDIPALLE 160.000 KM. TO MALLAPALLE 176.000 KM. PA (NHAI) (N24001847)	1/2023	11/2025 (N.A.) {11/2025}	956.14 (N.A.) {956.14}	95.51	14.72
		70	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MALLAPALLE 176.000 KM. TO KAVULAKUNTALA 196.000 KM. PACK (NHAI) (N24001848)	2/2023	10/2025 (N.A.) {10/2025}	909.02 (N.A.) {909.02}	60.01	6.65
		71	4L PS MYDUKUR BADVEL FROM KM 585.820 TO KM 630.960 SECTION OF NH 67 (NHAI) (N24001849)	5/2022	7/2025 (N.A.) {9/2025}	1,063.72 (N.A.) {1,063.72}	346.39	40.97
		72	CONSTRUCTION OF 4-LANE HIGHWAY FROM SAMARLAKOTA TO ACHAMPETA JUNCTION (FROM KM. 0.000 TO KM. 12.250 (NHAI) (N24001856)	5/2023	8/2025 (N.A.) {8/2025}	648.75 (N.A.) {648.75}	107.33	31.8

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		73	4 LANING OF BATHALAPALLI TO MUDIGUBBA SECTION (DESIGN CHAINAGE KM. 96.300 TO 129.300) INCLUDING BATH (MoRTH) (N24001931)	3/2022	2/2025 (N.A.) {2/2025}	536.00 (N.A.) {536.00}	393.81	43
		74	2L+PS FROM KM. 0+000 TO KM. 32+000 (MUDIGUBBA TO PUTTAPARTHI) OF NH- 342 (MoRTH) (N24001932)	3/2022	9/2024 (N.A.) {9/2024}	401.72 (N.A.) {401.72}	162.11	65
		75	MULAKALACHERUVU TO MADANAPALLE SECTION OF NH42 FROM KM 202.050 TO KM 245.640 EXCLUDING RETAINED STRE (MoRTH) (N24001933)	12/2021	12/2024 (N.A.) {12/2024}	480.10 (N.A.) {480.10}	443.87	78
		76	NH440 RAYACHOTY TOVEMPALLI 2LPS (MoRTH) (N24001934)	12/2021	5/2024 (N.A.) {5/2024}	439.82 (N.A.) {439.82}	193.63	27
		77	4 LANE WITH PAVED SHOULDER FROM KM 0.000 TO KM 51.119 OF TADIPATRI TO MUDDANUR OF NH67 (MoRTH) (N24001935)	3/2022	8/2025 (N.A.) {8/2025}	724.17 (N.A.) {724.17}	321.81	60
		78	NH165 FROM KM 0.000 TO KM 64.020 PAMARRU TO AKIVEEDU SECTION TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001939)	3/2020	9/2023 (N.A.) {12/2025}	529.24 (N.A.) {529.24}	312.17	51.78
		79	2LPS FROM KM36.400 TO KM. 107.224 OF NH167BG FROM DUTTALUR TO KAVALI SECTION (MoRTH) (N24001942)	3/2021	7/2024 (N.A.) {7/2024}	423.67 (N.A.) {423.67}	228.15	58
		80	NH167B FROM KM 99.103 CS PURAM TO KM 143.320 MALAKONDA TO 2LPS (MoRTH) (N24001949)	12/2021	3/2024 (N.A.) {12/2025}	277.30 (N.A.) {277.30}	168.68	91.04

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		81	NH167B FROM KM.143.320 MALAKONDA TO 189.050 SINGARAYAKONDA ON NH 16 TO TWO LANE WITH PAVED SHOULDERS (MoRTH) (N24001950)	3/2021	2/2025 (N.A.) {2/2025}	369.81 (N.A.) {369.81}	244.60	83.85
		82	NH167AD FROM MACHERLA TO DACHEPALLI FROM KM.0.000 TO 43.659 TO 2LPS (MoRTH) (N24001951)	1/2022	1/2025 (N.A.) {1/2025}	403.22 (N.A.) {403.22}	262.08	71
		83	NH 167 B KADAPA NELLORE BORDER TO CSPURAM I.E. FROM KM 58.635 TO KM 99.409 (MoRTH) (N24001952)	3/2022	8/2025 (N.A.) {8/2025}	285.50 (N.A.) {285.50}	108.03	55.3
		84	NH-30-BHADRACHALAM TO KONTA SECTION 2LPS (MoRTH) (N24001953)	12/2021	9/2024 (N.A.) {9/2024}	388.71 (N.A.) {388.71}	181.43	67.2
		85	WIDENING TO 2LPS OF RAMPACHODAVARAM - KOYYURU SECTION OF NH516E FROM KM.43.700 TO KM 113.820 (MoRTH) (N24001954)	3/2022	1/2025 (N.A.) {1/2025}	568.12 (N.A.) {568.12}	295.33	79.81
		86	GUDIWADA TOWN 2 LANE ROB AND ROAD IMPROVEMENT OF NH165 IN REPLACEMENT OF LC NO 3ESPL3 AT KM 231.700 (MoRTH) (N24001955)	3/2022	5/2025 (N.A.) {5/2025}	317.22 (N.A.) {317.22}	136.76	42.66
		87	2LPS FROM GONDIGUDA TO ARAKU BHALLAGUDA KM 27.480 TO KM 51.772 SECTION OF NH 516E (MoRTH) (N24001956)	8/2020	9/2023 (N.A.) {12/2024}	296.66 (N.A.) {296.66}	216.41	79
		88	2LPS OF KOYYURU TO CHAPRATHIPALEM SECTION OF NH 516E (MoRTH) (N24001957)	8/2020	7/2024 (N.A.) {7/2024}	349.29 (N.A.) {349.29}	138.22	49

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		89	2LPS OF CHAPRATHIPALEM TO LAMBASINGI SECTION OF NH 516E (MoRTH) (N24001958)	8/2020	10/2024 (N.A.) {10/2024}	311.22 (N.A.) {311.22}	100.84	40
		90	4 LANE FROM KM 56.400 TO KM 120.300 FROM B.KOTHAPALLI JUNCTION TO GORANTLA OF NH 716G (MoRTH) (N24001959)	3/2022	9/2025 (N.A.) {9/2025}	839.98 (N.A.) {839.98}	247.82	44.59
		91	4L GREENFIELD ROAD CONNECTING NORTH AND SOUTH INDUSTRIAL CLUSTER OF KHANDALERU CREEK NEAR KRISHNAPAT (NHAI) (N24001979)	8/2022	9/2025 (N.A.) {9/2025}	609.43 (N.A.) {609.43}	25.24	23.72
		92	4 LANING OF NH 544D FROM EXISTING KM 346.300 OF NH 44 (DESIGN CHAINAGE KM 0.000) TO KM 39.380 (DESIG (NHAI) (N24001980)	10/2022	7/2025 (N.A.) {7/2025}	907.76 (N.A.) {907.76}	238.14	50.18
		93	CONSTRUCTION OF SIX LANING OF NAIDUPETA JUNCTION - TURPUKANUPUR SECTION FROM KM.57+046 TO KM.91+927 (NHAI) (N24001981)	7/2022	10/2025 (N.A.) {10/2025}	1,398.84 (N.A.) {1,398.84}	58.68	5.92
		94	4L PS FROM KURNOOL (EXISTING KM. 5.400 OF NH-40/DESIGN KM.0.000) TO MANDLEM (EXISTING KM.38.000/DESI (NHAI) (N24001982)	3/2023	10/2025 (N.A.) {10/2025}	827.39 (N.A.) {827.39}	242.65	71.07
		95	4 LANING FROM EXISTING KM 39.380 (DESIGN CH. 37.000) TO KM 74.450 (DESIGN CH. 69.000) OF MUCHUKOTA (NHAI) (N24001983)	10/2022	8/2025 (N.A.) {8/2025}	972.63 (N.A.) {1,055.23}	192.22	32.99

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		96	4L PS FROM MANDLEM (EXISTING KM. 38.000/DESIGN KM.30.600) TO ATMAKUR (EXISTING KM.73.000/DESIGN KM 6 (NHAI) (N24001984)	3/2023	10/2025 (N.A.) {10/2025}	887.28 (N.A.) {887.28}	107.97	23.24
		97	BANGALORE CHENNAI EXPRESSWAY (PHASE-II PKG-II) FROM KM.96.000 TO KM 127.000 (BAIREDDYPALLE TO BANGAR (NHAI) (N24001985)	3/2021	6/2025 (N.A.) {6/2025}	1,942.94 (2,171.00) {2,171.00}	961.35	40.3
		98	4L OF PILERU TO KALUR SECTION FROM KM 55.900 TO KM 92.800 AND KM 94.500 TO KM 95.717 (NHAI) (N24001986)	10/2023	4/2025 (N.A.) {4/2025}	1,047.32 (N.A.) {1,047.32}	240.43	59
		99	CONSTRUCTION OF 1 NOS ROB, 2 NOS VUPS, SERVICE ROADS, PROVISION OF LIGHTING AND CONSTRUCTION OF OTHE (NHAI) (N24001987)	6/2023	12/2024 (N.A.) {12/2024}	152.05 (N.A.) {152.05}	92.60	54.85
		100	6L OF CHITTOOR TO THATCHUR FROM KUMARAJAPET TO VEERA KAVERI RAJA PURAM FROM KM 43.800 TO KM 61.380 O (NHAI) (N24001988)	2/2021	10/2025 (N.A.) {10/2025}	591.99 (703.00) {703.00}	256.19	39.03
		101	CONSTRUCTION OF 4 LANE ACCESS CONTROLLED HIGHWAY FROM CHILLAKURU CROSS ROAD TO TURPUKANUPUR KM 0+000 (NHAI) (N24002033)	7/2022	12/2025 (N.A.) {12/2025}	909.47 (N.A.) {909.47}	97.03	12.57
		102	COMPLETION OF BALANCE WORKS PENDING IN BIT AND PIECES (INCOMPLETE STRETCH AT 7 LOCATIONS) AND LISTED (NHAI) (N24002103)	9/2022	1/2025 (N.A.) {1/2025}	166.52 (N.A.) {166.52}	43.74	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		103	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM NARAYANMPET (CH. 203+500) TO CHANDRASEKHARPURAM (CH. 22 (NHAI) (N24002122)	2/2024	2/2026 (N.A.) {2/2026}	813.66 (N.A.) {813.66}	12.51	1.49
		104	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM CHANDRASEKHARPURAM (CH. 228+000) TO POLAVARAM (CH. 260 (NHAI) (N24002123)	2/2024	2/2026 (N.A.) {2/2026}	1,292.65 (N.A.) {1,292.65}	49.30	1.91
		105	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM POLAVARAM (CH. 260+000) TO MARRIPUDI (CH. 285+500) OF [(NHAI) (N24002124)	2/2024	2/2026 (N.A.) {2/2026}	747.29 (N.A.) {747.29}	54.44	2.71
		106	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM MARRIPUDI (CH. 285+500) TO SOMAVARAPPADU (CH. 314+600) (NHAI) (N24002125)	2/2024	2/2026 (N.A.) {2/2026}	976.40 (N.A.) {976.40}	89.70	12
		107	6L ACCESS CONTROLLED GREENFIELD HIGHWAY FROM SOMAVARAPPADU (CH.314.600) TO MUPPAVARAM (CH.343+240) O (NHAI) (N24002126)	2/2024	2/2026 (N.A.) {2/2026}	1,103.89 (N.A.) {1,103.89}	54.54	0
		108	4-LANE WITH PAVED SHOULDERS FROM KM 32/0 TO KM 79/650 (DESIGN CHAINAGE KM 32+000 TO KM 78+760) PUTTA (MoRTH) (N24002139)	3/2023	12/2025 (N.A.) {11/2025}	1,318.57 (N.A.) {1,318.57}	253.37	30
		109	SOMAYAJULAPALLI DHONE SECTION OF NH 340B FROM KM.0/0 TO 56/200 [DESIGN CH. KM 0/00 TO KM 53/33] (MoRTH) (N24002140)	4/2023	12/2025 (N.A.) {12/2025}	629.73 (N.A.) {629.73}	185.00	38

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		110	2 LANE WITH PAVED SHOULDER CONFIGURATION FROM SEETHARAMAPURAM TO DUTTALURU SECTION OF NH-167 BG FROM (MoRTH) (N24002141)	6/2023	7/2025 (N.A.) {7/2025}	364.07 (N.A.) {364.07}	132.87	69.1
		111	2-LANE WITH PAVED SHOULDER CONFIGURATION OF LAMBASINGI TO PADERU SECTION (KM 205+000 TO KM 253+974) (MoRTH) (N24002142)	8/2023	11/2025 (N.A.) {11/2025}	361.24 (N.A.) {361.24}	24.93	8.26
		112	BYPASS ROAD TO ADONI TOWN CONNECTING NH-167 (HAGARI - JADCHARLA ROAD) FROM KM.62/700 TO 71/400 IN KU (MoRTH) (N24002143)	8/2023	2/2026 (N.A.) {2/2026}	361.24 (N.A.) {361.24}	29.08	20
		113	VODAREVU-CHILAKALURIPET SECTION (DESIGN CHAINAGE 0+00 TO 47+000) OF NH-167A (PACKAGE-I) (MoRTH) (N24002144)	8/2023	2/2026 (N.A.) {2/2026}	1,064.24 (N.A.) {1,064.24}	203.83	15.95
		114	TADIPATRI BYPASS (KM 0+000 TO KM 6+285) OF 4-LANE ON NH-67 IN ANANTAPURAMU (MoRTH) (N24002145)	11/2023	3/2026 (N.A.) {3/2026}	159.66 (N.A.) {159.66}	50.76	48.16
		115	KURNOOL/KADAPA BORDER- JAMMALAMADUGU SECTION OF NH-167K I.E. DESIGN CH. KM 248+010 TO KM 269+900 (MoRTH) (N24002146)	11/2023	11/2025 (N.A.) {11/2025}	292.63 (N.A.) {292.63}	0.00	0
		116	DORNALA TO KUNTA JUNCTION FROM DESIGN CHAINAGE KM 244+000 TO 267+990 SECTION OF NH-765 (PACKAGE- 2) (MoRTH) (N24002147)	12/2022	1/2024 (N.A.) {3/2026}	244.83 (N.A.) {244.83}	34.83	14

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ARUNACHAL PRADESH		117	PADERU BYPASS (KM 0+000 TO KM 13+000) OF 2- LANE WITH PAVED SHOULDER ON NH-516E (MoRTH) (N24002148)	3/2023	3/2024 (N.A.) {2/2026}	244.43 (N.A.) {244.43}	0.00	0
		118	DAVUALAPALLY TO MALLAPALEM SECTION {DESIGN CH. KM 133+922 TO KM 154+216 (EXISTING CH. KM 133+922 TO (MoRTH) (N24002149)	1/2024	2/2024 (N.A.) {2/2026}	393.61 (N.A.) {393.61}	41.66	0
	WATER RESOURCES	119	POLAVARAM IRRIGATION PROJECT (PPA) (N30000002)	2/2009	3/2020 (N.A.) {3/2024}	10,151.04 (N.A.) {55,548.87}	21,644.53	77
	CIVIL AVIATION	120	CONSTRUCTION OF NEW GREEN FIELD AIRPORT AT HOLLONGI ITANAGAR ARUNACHAL PRADESH (AAI) (N04000092)	2/2019	8/2022 (Dec-24) {12/2024}	645.63 (N.A.) {712.15}	667.54	98.43
	POWER	121	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) (NHPC) (180100221)	9/2003	9/2010 (N.A.) {5/2026}	6,285.33 (N.A.) {21,247.54}	22,026.82	93.88
		122	DIBANG MULTIPURPOSE PROJECT 2880 MW ARUNACHAL PRADESH (NHPC) (N18000362)	2/2023	2/2032 (N.A.) {2/2032}	31,876.39 (N.A.) {31,876.39}	2,524.53	12.74
	ROAD TRANSPORT AND HIGHWAYS	123	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX (NHIDCL) (N24000683)	2/2017	11/2023 (Mar-24) {11/2024}	180.57 (244.10) {180.57}	154.17	90.01
		124	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI (NHIDCL) (N24000685)	2/2017	4/2022 (Nov-23) {11/2023}	167.28 (N.A.) {167.28}	144.91	100
		125	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF (NHIDCL) (N24000946)	3/2017	3/2022 (Jun-25) {6/2025}	1,718.59 (1,718.59) {1,718.59}	674.32	68.84

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		126	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 (NHIDCL) (N24000948)	9/2016	12/2019 (Aug-24) {9/2024}	568.92 (568.92) {568.92}	508.65	100
		127	TWO-LANING OF HAYULIANG HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI (NHIDCL) (N24000979)	1/2017	5/2023 (May-23) {3/2025}	256.66 (N.A.) {256.66}	0.00	63.59
		128	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA- HAYULIANG SECTION OF NH-113 FROM CH.68. (NHIDCL) (N24001244)	8/2020	4/2022 (Feb-25) {2/2025}	301.06 (N.A.) {301.06}	140.37	62.09
		129	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE- BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO (NHIDCL) (N24001245)	9/2020	5/2022 (Oct-22) {3/2024}	353.90 (N.A.) {353.90}	41.82	25.38
		130	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE (MoRTH) (N24001291)	3/2019	3/2027 (N.A.) {3/2027}	421.48 (N.A.) {421.48}	365.83	100
		131	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE (MoRTH) (N24001292)	3/2019	3/2027 (N.A.) {3/2027}	543.05 (N.A.) {600.00}	568.30	99.3
		132	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE (MoRTH) (N24001293)	3/2019	3/2027 (N.A.) {3/2027}	486.70 (N.A.) {486.70}	474.23	100

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		133	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE (MoRTH) (N24001297)	3/2019	3/2027 (N.A.) {3/2027}	450.65 (N.A.) {450.65}	371.45	91.71
		134	TADADEGE - HENKAR (NHIDCL) (N24001315)	2/2021	3/2023 (Jun-24) {9/2024}	550.45 (N.A.) {550.45}	113.92	44.05
		135	LADDA - BASAI (NHIDCL) (N24001316)	2/2021	4/2023 (Jan-25) {3/2025}	445.96 (N.A.) {445.96}	117.91	49.63
		136	DOGINALA - GAU (NHIDCL) (N24001320)	12/2020	9/2022 (N.A.) {12/2024}	242.30 (N.A.) {242.30}	21.47	17.81
		137	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH (MoRTH) (N24001372)	2/2021	3/2024 (Dec-24) {12/2024}	588.09 (N.A.) {588.09}	449.76	93.18
		138	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC (MoRTH) (N24001374)	6/2020	3/2027 (N.A.) {3/2027}	437.60 (N.A.) {437.60}	365.27	96.7
		139	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC (MoRTH) (N24001375)	6/2020	3/2027 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	142.05	34.41
		140	JORAM KOLORIANG ROAD FROM EXISTING KM 50.050 TO KM 70.00 (PKG-3) (NHIDCL) (N24001390)	8/2020	4/2022 (Aug-24) {9/2024}	228.71 (N.A.) {228.71}	98.86	99.52
		141	JORAM KOLORIANG ROAD FROM EXISTING KM 70.00 TO KM 88.700 (PKG-4) (NHIDCL) (N24001391)	8/2020	4/2022 (Feb-24) {9/2024}	294.04 (N.A.) {294.04}	147.13	100

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
ASSAM		142	JORAM KOLORIANG ROAD FROM EXISTING KM104.850 TO KM 122.60 (PKG- 6) (NHIDCL) (N24001392)	8/2020	4/2022 (Jul-23) {7/2023}	199.03 (N.A.) {199.03}	102.85	100
		143	JORAM KOLORIANG ROAD FROM EXISTING KM122.600 TO KM138.00 (PKG- 7) (NHIDCL) (N24001393)	8/2020	4/2022 (Feb-24) {11/2024}	184.88 (N.A.) {184.88}	95.64	93.83
	CIVIL AVIATION	144	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI (AAI) (N04000083)	12/2016	3/2021 (N.A.) {3/2025}	1,142.00 (N.A.) {2,333.00}	1,346.22	66.34
	HEALTH AND FAMILY WELFARE	145	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM (HITES) (N21000027)	5/2017	5/2021 (Apr-23) {11/2024}	875.00 (873.92) {860.00}	769.30	98.94
	PETROLEUM	146	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA (OIL) (N16000331)	1/2018	2/2020 (Dec-23) {12/2024}	543.91 (N.A.) {670.90}	491.56	93.71
		147	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY (NRL) (N16000379)	1/2019	10/2024 (N.A.) {12/2025}	12,366.00 (N.A.) {18,968.00}	12,545.43	63.74
		148	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES (NRL) (N16000394)	1/2019	10/2024 (N.A.) {9/2025}	10,228.00 (N.A.) {9,058.00}	8,192.36	77.65
		149	EXPANSION OF GUWAHATI REFINERY FROM 1 TO 1.2 MMTPA ALONG WITH INSTALLATION OF CATALYTIC REFORMING UN (IOCL) (N16000414)	5/2021	10/2023 (Feb-25) {2/2025}	412.00 (509.84) {509.84}	356.90	77.8
		150	GAS ASSISTED GRAVITY DRAINAGE SCHEME, KASOMARIGAON (ONGC) (N16000433)	8/2021	2/2023 (Jun-24) {8/2024}	218.38 (N.A.) {218.38}	186.79	83.3

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		151	REVAMPING OF FACILITIES AT EXISTING GUWAHATI TERMINAL, ASSAM (IOCL) (N16000441)	3/2022	7/2026 (Sep-26) {9/2026}	277.00 (N.A.) {277.00}	156.92	50.6
		152	UPGRADATION OF FACILITIES OF NUMALIGARH-SILIGURI PRODUCT PIPELINE (NSPL) FOR TRANSPORTATION OF ADDIT (OIL) (N16000449)	6/2021	12/2024 (N.A.) {12/2024}	860.00 (N.A.) {860.00}	399.50	86.5
		153	PROJECT TO CONSTRUCT A FIELD GAS GATHERING STATION AT BAGHJAN AREA FOR COLLECTION,PROCESSING (OIL) (N16000450)	12/2020	7/2024 (Mar-24) {12/2024}	430.76 (N.A.) {430.76}	245.08	72.55
		154	CAPACITY EXPANSION OF DIGBOI REFINERY FROM 0.65 TO 1.0 MMTPA (IOCL) (N16000457)	6/2022	10/2025 (N.A.) {3/2026}	768.00 (N.A.) {768.00}	59.42	7.4
		155	CONSTRUCTION OF LPG FACILITIES AT KAMARDANGA, ASSAM (HPCL) (N16000484)	3/2023	7/2027 (Jul-27) {7/2027}	156.36 (156.36) {156.36}	1.08	11
		156	SETTING UP OF NEW RAIL FED POL FACILITY AT KAMARDANGA, ASSAM (HPCL) (N16000494)	3/2023	7/2027 (Jul-27) {7/2027}	384.04 (N.A.) {384.04}	31.57	3.5
		157	POWER RECOVERY TURBINE IN PFCCU (NRL) (N16000510)	3/2023	7/2025 (N.A.) {7/2025}	293.50 (N.A.) {293.50}	56.33	71
		158	DCU REVAMP PROJECT (NRL) (N16000511)	8/2021	3/2025 (N.A.) {10/2025}	370.00 (N.A.) {370.00}	152.65	34
		159	PIPELINE NETWORK PROJECT RUDRASAGAR (ONGC) (N16000528)	1/2023	4/2026 (N.A.) {4/2026}	344.99 (N.A.) {344.99}	108.35	40.1

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		160	BORHOLLA GGS LIFE EXTENSION PROJECT (ONGC) (N16000532)	9/2023	5/2026 (N.A.) {5/2026}	198.70 (N.A.) {198.70}	3.05	2.4
	<u>RAILWAYS</u>	161	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) (NFR) (N22000388)	4/2015	3/2022 (N.A.) {3/2027}	2,232.32 (N.A.) {4,983.94}	3,451.65	92
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	162	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) (NHIDCL) (N24000319)	6/2015	8/2023 (N.A.) {12/2024}	437.39 (N.A.) {437.39}	321.54	24.35
		163	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 (NHIDCL) (N24000320)	6/2015	3/2024 (N.A.) {9/2025}	463.49 (N.A.) {463.49}	368.35	31.56
		164	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 (NHIDCL) (N24000431)	1/1991	6/2019 (Jun-19) {10/2024}	520.01 (N.A.) {520.01}	304.78	90.01
		165	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. (NHIDCL) (N24000438)	12/2015	12/2018 (Jul-21) {10/2024}	289.99 (N.A.) {289.99}	232.66	87.62
		166	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O (NHIDCL) (N24000582)	1/2016	1/2016 (N.A.) {12/2024}	294.17 (N.A.) {294.17}	295.84	41.24
		167	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 (NHIDCL) (N24000583)	1/2016	12/2021 (N.A.) {3/2025}	252.00 (N.A.) {330.30}	146.28	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		168	FOUR LANING OF BALACHERA- HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE (NHIDCL) (N24000902)	10/2017	6/2020 (Dec-23) {4/2024}	818.00 (887.68) {887.68}	873.61	100
		169	4-LANING OF HAPACHARA - TULUNGIA SECTION (NHIDCL) (N24001246)	3/2020	12/2022 (N.A.) {8/2024}	220.20 (N.A.) {220.20}	215.69	97.76
		170	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 (NHIDCL) (N24001248)	8/2020	4/2022 (N.A.) {7/2024}	208.84 (N.A.) {208.84}	191.18	100
		171	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) (NHIDCL) (N24001269)	3/2020	3/2022 (Dec-23) {12/2024}	216.49 (241.52) {216.49}	104.36	79.48
		172	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD (NHIDCL) (N24001326)	11/2020	9/2028 (N.A.) {9/2028}	4,997.04 (N.A.) {4,997.04}	2,028.10	51.59
		173	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) (NHIDCL) (N24001331)	3/2020	6/2022 (May-25) {5/2025}	261.13 (N.A.) {261.13}	64.96	54.59
		174	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) (NHIDCL) (N24001332)	3/2020	6/2022 (Apr-25) {4/2025}	217.50 (N.A.) {217.50}	84.36	64.15
		175	DABOKA KATHKATI PACKAGE-5 (NHIDCL) (N24001366)	3/2021	1/2023 (N.A.) {10/2024}	288.85 (N.A.) {288.85}	231.27	96.08
		176	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 (NHIDCL) (N24001368)	3/2021	1/2024 (N.A.) {10/2025}	286.72 (N.A.) {286.72}	78.65	30.81

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		177	CONSTRUCTION OF 2-LANE MAJOR BRIDGE INCLUDING APPROACHES OVER BRAHMAPUTRA BETWEEN MAJULI ON NORTH BAN (MoRTH) (N24001408)	2/2021	7/2025 (N.A.) {7/2025}	925.47 (N.A.) {925.47}	321.15	30.62
		178	6L FLYOVER AT BORAGAON, GORCHUK, LOKHRA AND BASISTHA JUNCTION ON GUWAHATI BYPASS SECTION FROM KM 146 (NHAI) (N24001432)	12/2021	8/2024 (Mar-24) {8/2024}	300.00 (N.A.) {300.00}	297.62	100
		179	JOGIGHOPA BRIDGE (NHIDCL) (N24001434)	8/2021	11/2024 (N.A.) {12/2026}	746.76 (N.A.) {746.76}	292.37	57.74
		180	DABOKA KATHKATI PACKAGE-6 (NHIDCL) (N24001450)	9/2021	7/2024 (N.A.) {12/2024}	625.64 (N.A.) {625.64}	457.70	82.62
		181	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-1 (NHIDCL) (N24001451)	3/2022	7/2024 (N.A.) {8/2024}	215.27 (N.A.) {215.27}	146.02	97.94
		182	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-2 (NHIDCL) (N24001452)	4/2022	7/2024 (N.A.) {8/2024}	170.95 (N.A.) {170.95}	125.71	100
		183	DABOKA KATHKATI PACKAGE-7 (NHIDCL) (N24001537)	11/2021	7/2024 (N.A.) {12/2024}	204.10 (N.A.) {204.10}	125.63	81.78
		184	FOUR LANING OF SRIRAMPUR-DHUBRI PKG-2 (NHIDCL) (N24001544)	3/2022	1/2025 (N.A.) {1/2025}	909.02 (N.A.) {909.02}	388.98	76.17
		185	6L STANDALONE FLYOVERS AT RAHA, DEMOW, BORGHAT, KATHIATALI JUNCTIONS AND ROB AT JAGIROAD ON STRETCH (NHAI) (N24001545)	8/2022	12/2022 (Sep-24) {6/2024}	175.00 (N.A.) {175.00}	178.56	98.13

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		186	BALANCE WORK OF 4L OF NARIMBANGLOJATINGA JUNCTION- HARANGAJO ROAD SECTION FROM KM 0.000 TO KM 49.23 (NHAI) (N24001547)	3/2022	1/2026 (N.A.) {1/2026}	1,909.98 (N.A.) {1,909.98}	394.71	48.37
		187	6L STANDALONE FLYOVERS AT BONGAIGAON, CHAPAGURI, PATHSALA, SIMLAGURI CHOWK AND BAIHATA BYPASS JUNCTI (NHAI) (N24001548)	3/2022	6/2024 (N.A.) {12/2024}	457.72 (N.A.) {457.72}	252.91	85
		188	SHRIRAMPUR (KM. 0.000) TO KOCHUGAON (KM. 30.000) OF BIJNI TO ASSAM./WEST BENGAL BORDER SECTION OF NH (NHAI) (N24001549)	7/2017	4/2020 (Jul-24) {7/2024}	442.23 (N.A.) {442.23}	265.19	100
		189	SRIRAMPUR - DHUBRI PKG-1 (NHIDCL) (N24001831)	3/2022	2/2025 (N.A.) {12/2025}	613.89 (N.A.) {613.89}	17.09	9.23
		190	DIBRUGARH-LAHOAL-CHABUA BYPASS PACKAGE-3 (NHIDCL) (N24001832)	1/2023	5/2025 (N.A.) {5/2025}	458.59 (N.A.) {458.59}	140.63	40.35
		191	CONSTRUCTION OF MANGALDOI BYPASS (NH-15) STARTING AT CH 26+400 AND TERMINATING AT CH 41+505 UNDER RA (MoRTH) (N24001840)	3/2022	4/2025 (N.A.) {4/2025}	535.03 (N.A.) {535.03}	4.07	10.6
		192	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH- 137) I (NHIDCL) (N24001969)	3/2023	8/2025 (N.A.) {8/2025}	904.04 (N.A.) {904.04}	281.73	37.01
		193	WIDENING AND UPGRADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH- 137) IN (NHIDCL) (N24001970)	3/2023	8/2025 (N.A.) {8/2025}	860.37 (N.A.) {860.37}	267.62	37.12

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		194	WIDENING AND UPGADATION TO TWO LANES WITH PAVED SHOULDERS ROAD FROM TAMENGLONG TO MAHUR (NH-137) IN (NHIDCL) (N24001971)	3/2023	8/2025 (N.A.) {8/2025}	890.33 (N.A.) {890.33}	326.53	33.78
		195	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 0+800 (KANDULIJAN GAON) TO KM 27+701 (SI (NHIDCL) (N24001972)	3/2023	4/2026 (N.A.) {4/2026}	609.16 (N.A.) {609.16}	182.45	51.25
		196	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 27+701 (SIMEN CHAPORI) TO KM 55+000 (NAG (NHIDCL) (N24001973)	3/2023	2/2026 (N.A.) {2/2026}	562.05 (N.A.) {562.05}	165.88	50.16
		197	BILASIPURA-GUWAHATI ROAD PKG-8 (NHIDCL) (N24002021)	3/2023	12/2026 (N.A.) {12/2026}	1,457.59 (N.A.) {1,457.59}	349.64	23.67
		198	BILASIPURA-GUWAHATI ROAD PKG-9 (NHIDCL) (N24002022)	3/2023	6/2026 (N.A.) {6/2026}	1,000.27 (N.A.) {1,000.27}	210.48	9.72
		199	BILASIPURA-GUWAHATI ROAD PKG-10 (NHIDCL) (N24002023)	3/2023	6/2026 (N.A.) {6/2026}	1,264.90 (N.A.) {1,264.90}	269.25	11.97
		200	DABOKA BYPASS OF DABOKA - PAROKHAOWA PKG -1 (NHIDCL) (N24002024)	1/2023	11/2025 (N.A.) {11/2025}	516.88 (N.A.) {516.88}	152.60	41.3
		201	2 LANE WITH PAVED SHOULDER FROM KM 16+900 (BOGAPANI) TO KM 27+150 (GOLAI GAON) ON EXISTING DIBRUGARH (NHIDCL) (N24002025)	1/2023	12/2025 (N.A.) {12/2025}	356.65 (N.A.) {356.65}	115.18	5.05

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		202	2 LANE WITH PAVED SHOULDER FROM KM 27+150 (GOLAI GAON) TO KM 47+682 (LEDO) ON EXISTING DIBRUGARH TO (NHIDCL) (N24002026)	3/2023	12/2025 (N.A.) {12/2025}	643.42 (N.A.) {643.42}	65.32	8.35
		203	DEVELOPMENT OF EXTERNAL TRUNK CONNECTIVITY AND INTERNAL INFRASTRUCTURE WORKS AT MULTI MODEL LOGISTIC (NHIDCL) (N24002030)	2/2020	3/2022 (N.A.) {10/2024}	592.06 (N.A.) {592.06}	291.85	97.9
		204	SILCHAR VAIRENGTE SAIRANG ROAD PKG-1 (NHIDCL) (N24002127)	2/2023	7/2026 (N.A.) {7/2026}	1,256.90 (N.A.) {1,256.90}	313.76	12.11
		205	SILCHAR VAIRENGTE SAIRANG ROAD PKG-2 (NHIDCL) (N24002128)	3/2023	8/2026 (N.A.) {8/2026}	1,716.21 (N.A.) {1,716.21}	731.85	28.42
		206	FOUR LANNING OF BADARPUR BYPASS FROM DESIGN CHAINAGE KM 27+300 AT CROSSING WITH NH-6 (NHIDCL) (N24002129)	2/2023	8/2026 (N.A.) {8/2026}	574.26 (N.A.) {574.26}	172.77	18.3
		207	TAMENGLONG- MAHUR ROAD PKG-7 (NHIDCL) (N24002130)	12/2023	3/2026 (N.A.) {3/2026}	846.82 (N.A.) {846.82}	278.53	29.35
		208	CONSTRUCTION OF 4-LANE PANCHGRAM BYPASS FROM DESIGN CHAINAGE KM 15+500 ON NH-37 (OLD NH- 53) AT KALIN (NHIDCL) (N24002154)	3/2023	2/2027 (N.A.) {2/2027}	728.97 (N.A.) {728.97}	88.64	0
		209	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 55+000 (NAGABANG GAMSUK) TO KM 82+514 (OY (NHIDCL) (N24002155)	3/2023	3/2027 (N.A.) {3/2027}	665.47 (N.A.) {665.47}	73.01	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
BIHAR	CIVIL AVIATION	210	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II (AAI) (N04000082)	5/2018	10/2022 (Dec-24) {12/2024}	1,216.90 (N.A.) {1,216.90}	797.98	72.62
		211	DARBHANGA:DEVELOPMENT OF NEW CIVIL ENCLAVE AT DARBHANGA, BIHAR. SH- CONSTRUCTION OF NEW TERMINAL BUI (AAI) (N04000112)	7/2024	7/2026 (N.A.) {7/2026}	911.66 (N.A.) {911.66}	0.00	0
	DEPARTMEN T OF HIGHER EDUCATION	212	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE- II FOR THE CAMPUS OF IIT PATNA (CPWD EDUCATION) (N28000100)	2/2016	6/2017 (Jan-24) {1/2024}	496.18 (496.00) {460.00}	390.15	100
		213	PERMANENT CAMPUS FOR IIM BODH GAYA (CPWD EDUCATION) (N42000009)	9/2018	9/2020 (N.A.) {9/2020}	375.00 (N.A.) {375.00}	327.75	98.9
	PETROLEUM	214	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA (IOCL) (N16000386)	1/2020	4/2023 (Dec-24) {12/2025}	14,810.00 (N.A.) {14,810.00}	9,640.59	79.6
		215	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA (IOCL) (N16000423)	6/2019	12/2029 (Mar-30) {3/2030}	163.00 (N.A.) {163.00}	83.69	23.5
		216	INSTALLATION OF BITUMEN MANUFACTURING UNIT ALONG WITH ALLIED FACILITIES AT BARAUNI (IOCL) (N16000453)	1/2022	4/2025 (N.A.) {4/2025}	389.00 (N.A.) {389.00}	22.13	18.7
		217	CITY GAS DISTRIBUTION PROJECTS AT GOPALGANJ SIWAN WEST CHAMPARAN EAST CHAMPARAN AND DEORIA DISTRICTS (BPCL) (N16000523)	12/2022	6/2030 (N.A.) {6/2030}	3,919.00 (N.A.) {3,919.00}	186.17	12.5

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		218	CITY GAS DISTRIBUTION PROJECTS AT DARBHANGA, MADHUBANI, SUPAUL, SITAMARHI AND SHEOHAR DISTRICTS (BPCL) (N16000524)	12/2022	3/2030 (N.A.) {3/2030}	3,638.00 (N.A.) {3,638.00}	210.71	12.9
	POWER	219	BARH STPP(3X660MW) NTPC (NTPC) (180100242)	2/2005	10/2011 (Jul-23) {11/2024}	8,692.97 (21,312.11) {21,312.11}	22,311.28	90
		220	BUXAR THERMAL POWER PLANT (1320 MW) (SJVN) (N18000194)	3/2019	1/2024 (N.A.) {6/2025}	10,439.09 (N.A.) {10,439.09}	10,254.77	82
	RAILWAYS	221	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR (ECR) (220100240)	4/1997	3/2012 (N.A.) {12/2023}	324.73 (967.29) {1,250.00}	1,236.75	99
		222	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) (ECR) (220100257)	4/1997	(N.A.) {12/2026}	162.87 (614.45) {614.45}	454.81	50
		223	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR (ECR) (220100303)	4/2003	(N.A.) {12/2024}	528.65 (2,087.36) {2,087.36}	2,010.32	48
		224	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR (NFR) (N22000087)	9/2006	3/2019 (N.A.) {6/2025}	532.87 (2,132.03) {4,415.08}	2,832.81	81
		225	SAKRI-HASANPUR ROAD (NL) (ECR) (N22000171)	4/1999	(N.A.) {3/2027}	325.00 (735.20) {735.20}	578.17	78
		226	ARARIA-SUPAUL (NL) (ECR) (N22000177)	4/2008	(N.A.) {1/2025}	1,605.17 (1,605.17) {1,605.17}	1,390.28	26
		227	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) (ECR) (N22000180)	4/2004	(N.A.) {6/2024}	372.14 (1,470.50) {2,350.00}	2,510.86	97
		228	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC (ECR) (N22000181)	4/2009	3/2020 (N.A.) {3/2026}	548.00 (548.00) {783.83}	544.31	78

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		229	SAMASTIPUR-DARBANGHA (ECR) (N22000329)	5/2015	(N.A.) {3/2025}	380.00 (519.33) {519.33}	543.01	62
		230	KIUL - GAYA DOUBLING PROJECT (ECR) (N22000349)	12/2015	3/2020 (N.A.) {9/2024}	1,200.20 (1,200.20) {1,771.07}	1,719.05	96
		231	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE (ECR) (N22000350)	12/2015	3/2020 (N.A.) {5/2025}	1,491.47 (1,491.47) {1,600.00}	1,647.46	77
		232	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM (ECR) (N22000472)	4/2016	3/2021 (N.A.) {12/2024}	744.04 (1,215.54) {1,215.54}	1,415.30	85
		233	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM (ECR) (N22000473)	4/2016	3/2021 (N.A.) {9/2024}	731.64 (1,185.73) {1,300.00}	1,393.52	80
		234	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN- BIHARSHARIF, (ECR) (N22000476)	4/1991	(N.A.) {12/2024}	329.39 (803.09) {2,722.16}	2,583.23	90
		235	DARBHANGA - BYPASS LINE CONNECTING SHISHO HALT AND KAKARGHATI EXCL DARBHANGA YARD (7.64 KM) (ECR) (N22000523)	6/2019	6/2025 (N.A.) {9/2024}	983.62 (253.23) {415.00}	382.48	80
		236	BARAUNI- BACHWARA 3RD AND 4TH LINE (ECR) (N22000524)	7/2022	7/2027 (N.A.) {6/2025}	486.00 (N.A.) {486.00}	97.60	30
		237	JHAJHA - BATIA (UMBRELLA WORK PB#23/2018-19/NR) (ECR) (N22000526)	2/2019	6/2028 (N.A.) {3/2027}	496.47 (N.A.) {496.47}	2.53	0
		238	SONENAGAR BYE PASS LINE FROM CHIRALAPOTHU TO BAGHA BISHUNPUR (ECR) (N22000528)	10/2022	10/2027 (N.A.) {6/2025}	234.00 (223.69) {223.69}	15.16	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		239	KATIHAR-KUMEDPUR & KATIHAR-MUKURIA (64.5 KM) (UMBRELLA WORK PB#57/2019-20/NR) (NFR) (N22000570)	8/2022	8/2027 (N.A.) {8/2027}	745.00 (N.A.) {745.00}	0.00	0
	ROAD TRANSPORT AND HIGHWAYS	240	PATNA-MUZZAFFARPUR (NHAI) (N24000165)	8/2010	2/2013 (N.A.) {12/2024}	671.30 (N.A.) {671.30}	1,830.13	97.15
		241	4-LANNING OF CHAPRA-HAJIPUR (NHAI) (N24000187)	1/2011	7/2013 (Dec-24) {12/2024}	575.00 (N.A.) {575.00}	550.60	85.97
		242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR (MoRTH) (N24000382)	1/2014	10/2019 (Dec-24) {12/2024}	675.00 (780.77) {780.77}	702.20	87.82
		243	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 (NHAI) (N24000480)	12/2015	4/2019 (Jul-22) {3/2025}	1,041.10 (567.00) {639.58}	553.73	97.27
		244	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 (NHAI) (N24000507)	12/2015	12/2019 (N.A.) {12/2024}	1,167.45 (N.A.) {1,182.94}	735.99	94.25
		245	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 (MoRTH) (N24000531)	2/2016	11/2018 (Sep-24) {9/2024}	319.68 (503.28) {503.28}	430.14	99
		246	CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-I-KM 40.00 TO KM 65.400 AND K (MoRTH) (N24000576)	2/2016	5/2016 (Sep-24) {9/2024}	178.85 (225.06) {278.54}	232.61	98
		247	PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2 LANES/2 LANE(FOR LOT-III-KM 156.5 (MoRTH) (N24000578)	2/2016	5/2016 (Sep-24) {9/2024}	553.30 (706.39) {706.39}	607.49	98

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		248	FOUR LANING OF GAYA-HISUA-RAJGIRI- NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR (MoRTH) (N24000579)	1/2014	10/2016 (Dec-24) {12/2024}	1,408.85 (2,138.16) {2,138.16}	1,703.04	96
		249	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN (NHAI) (N24000665)	3/2017	3/2020 (Mar-25) {3/2025}	672.89 (736.01) {830.31}	566.83	75.14
		250	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 (NHAI) (N24000696)	8/2017	2/2022 (Aug-23) {3/2025}	950.64 (1,161.00) {1,168.33}	980.81	83.95
		251	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 (NHAI) (N24000714)	12/2017	10/2024 (Apr-25) {6/2025}	2,598.00 (N.A.) {1,962.50}	1,249.32	68.33
		252	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I (NHAI) (N24000723)	1/2018	12/2021 (Dec-19) {3/2025}	573.70 (644.50) {726.99}	468.93	75.58
		253	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER (NHAI) (N24000813)	3/2018	11/2021 (Dec-24) {12/2024}	496.20 (470.18) {537.17}	368.86	94.37
		254	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND (MoRTH) (N24000943)	9/2018	6/2024 (Feb-26) {2/2026}	1,478.40 (N.A.) {1,478.40}	806.35	58.15

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		255	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 (MoRTH) (N24001201)	2/2019	9/2024 (N.A.) {2/2026}	2,926.42 (N.A.) {2,926.42}	970.95	47
		256	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT (NHAI) (N24001303)	10/2013	12/2020 (Dec-24) {12/2024}	649.90 (N.A.) {750.00}	711.53	98.3
		257	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE (NHAI) (N24001304)	10/2013	11/2020 (Dec-24) {12/2024}	446.97 (598.48) {740.50}	638.80	96.3
		258	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA (NHAI) (N24001305)	10/2013	11/2020 (Dec-24) {12/2024}	464.09 (605.53) {765.12}	698.25	97.3
		259	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N (NHAI) (N24001371)	10/2019	8/2023 (Dec-24) {12/2024}	1,101.99 (N.A.) {1,101.99}	772.33	66.12
		260	4L GREENFIELD ALIGNMENT FROM KALYANAPUR TO TAL DASHRAHA OF NH- 119D (PKG-III) (NHAI) (N24001697)	2/2023	2/2025 (N.A.) {12/2025}	1,358.00 (N.A.) {1,358.00}	146.66	11.5
		261	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM NEAR RASULPUR TO MIRZACHAUKI (DESIGN CH (NHAI) (N24001698)	8/2022	8/2024 (N.A.) {8/2024}	1,198.02 (N.A.) {1,198.02}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		262	CONSTRUCTION OF 4 LANE ELEVATED SECTION AND AT- GRADE IMPROVEMENTS AT BEGUSARAI TOWN SECTION OF NH-3 (NHAI) (N24001699)	3/2022	12/2024 (N.A.) {3/2025}	312.58 (N.A.) {312.58}	135.11	57.4
		263	SIX LANNING OF AURANGABAD TO BIHAR/JHARKHAND BORDER SECTION OF NH-19 (OLD NH-2) FROM KM. 209.827 TO (NHAI) (N24001700)	12/2021	3/2024 (Dec-24) {12/2024}	552.55 (553.00) {553.00}	414.79	54.95
		264	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM START OF EXISTING BHAGALPUR BYPASS TO RASU (NHAI) (N24001701)	4/2022	4/2024 (N.A.) {4/2024}	1,769.50 (N.A.) {1,769.50}	0.00	0
		265	CONSTRUCTION OF 4 LANE ELEVATED HIGHWAY AND AT-GRADE IMPROVEMENTS AT GOPALGANJ TOWN FROM DESIGN CH: (NHAI) (N24001702)	12/2021	9/2024 (N.A.) {9/2024}	184.90 (185.00) {185.00}	163.01	86.8
		266	6 L OF AURANGABAD TO BIHAR-JHARKHAND BORDER (CHORDAHA) SECTION FROM KM. 180.000 TO KM. 209.827 OF N (NHAI) (N24001703)	2/2022	5/2025 (N.A.) {5/2025}	786.81 (787.00) {787.00}	0.00	0
		267	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM KHARIA VILLAGE JUNCTION TO START OF EXISTI (NHAI) (N24001704)	3/2021	3/2024 (Dec-24) {12/2024}	1,020.84 (N.A.) {1,020.84}	84.78	0
		268	FOUR LANING OF MUNGER TO MIRZACHAUKI (NH-80) SECTION FROM MUNGER TO KHARIA VILLAGE JUNCTION DESIGN C (NHAI) (N24001705)	3/2022	3/2024 (Dec-24) {12/2024}	1,485.66 (N.A.) {1,485.66}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		269	4 LANING OF GALGALIA - BAHADURGANJ SECTION FROM KM 0.000 TO KM 49.000 (PACKAGE-I) OF NH-327E. (NHAI) (N24001706)	3/2021	1/2024 (Dec-24) {12/2024}	1,097.18 (1,097.00) {1,097.00}	518.04	99.79
		270	4 LANING OF BAHADURGANJ ARARIA SECTION FROM KM 49.000 TO KM 94.000 (PACKAGE-II) OF NH-327E (NHAI) (N24001707)	3/2021	1/2024 (Dec-24) {12/2024}	1,143.46 (1,143.46) {1,143.46}	487.45	97.8
		271	BAKHTIYARPUR RAJAULI PKG-III FROM KM 101.630 TO KM 152.520 NH20 (NHAI) (N24001708)	9/2020	6/2024 (N.A.) {12/2024}	2,156.22 (N.A.) {2,156.22}	2,134.67	96.57
		272	BAKHTIYARPUR RAJAULI PKG-II FROM KM 54.405 TO KM 101.630 NH20 (NHAI) (N24001709)	9/2020	4/2023 (Dec-24) {12/2024}	897.45 (N.A.) {1,090.00}	1,037.63	97.85
		273	4 LANING FROM KM. 34.600 TO KM. 79.970 and 2LPS FROM KM. 79.970 TO KM. 82.000 OF NARENPUR - PURNEA S (NHAI) (N24001710)	9/2020	3/2023 (Dec-24) {12/2024}	2,334.68 (2,494.20) {2,494.20}	913.70	99.2
		274	6L OF KANHAULI RAMNAGAR PATNA RING ROAD PKG I FROM KM 0.000 TO KM 39.160 OF SH78 NEW NH131G (NHAI) (N24001711)	9/2020	3/2023 (Dec-24) {12/2024}	939.43 (N.A.) {939.43}	370.62	100
		275	FOUR LANING OF PARARIA TO MOHANIA SECTION OF NH 319 (OLD NH 30) FROM KM. 54+530 (DESIGN CHAINAGE) TO (NHAI) (N24001712)	8/2020	7/2023 (Dec-24) {12/2024}	690.00 (N.A.) {690.00}	770.73	98.65

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		276	BALANCE WORK OF TWO LANING WITH PAVED SHOULDER OF PIPRAKOTHIMOTIHARI- RAXAUL SECTION OF NH-28A FRO (NHAI) (N24001715)	12/2018	10/2020 (N.A.) {1/2024}	333.60 (466.59) {461.41}	460.38	100
		277	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH 122B FROM KM 29.730 TO KM 72.348 IN STATE OF BIH (MoRTH) (N24001870)	2/2022	11/2024 (Mar-25) {3/2025}	624.43 (N.A.) {624.43}	188.90	68
		278	WIDENING AND STRENGTHENING FROM KM 70.15 TO KM 121.025 OF NH-80 (MoRTH) (N24001875)	3/2021	1/2025 (Mar-25) {3/2025}	477.54 (N.A.) {477.54}	215.22	56.92
		279	WIDENING and STRENGTHENING FROM KM132.895 TO KM 190.15 NH-80 (MoRTH) (N24001876)	3/2021	3/2024 (Jun-25) {6/2025}	566.15 (N.A.) {566.15}	159.74	35.1
		280	CONSTRUCTION OF NEW 4-LANE BRIDGE (PARALLEL TO EXISTING VIKRAMASHILA SETU)FROM KM 8+920 TO KM 13+375 (MoRTH) (N24001877)	7/2020	5/2027 (N.A.) {5/2027}	1,110.23 (N.A.) {1,110.23}	263.84	28.5
		281	IMPROVEMENT TO TWO LANE WITH PAVED SHOULDERS OF NH-319A FROM KM 0 TO KM 45 IN STATE OF BIHAR UNDER (MoRTH) (N24001878)	2/2022	12/2024 (Mar-25) {3/2025}	427.29 (N.A.) {427.29}	166.86	55.9
		282	CONSTRUCTION OF PROPOSED 4_LANE REVELGUNJ BYPASS NH-19 IN THE STATE OF BIHAR ON EPC MODE CONNECTING (MoRTH) (N24001879)	3/2022	7/2025 (N.A.) {7/2025}	295.24 (N.A.) {295.24}	31.83	27.4

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		283	CONSTRUCTION OF 6- LANE BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD (NH- (NHAI) (N24002062)	3/2023	9/2027 (N.A.) {9/2027}	3,012.27 (N.A.) {3,012.27}	0.00	0
		284	BALANCE WORK - WB-10 (GANDAK BRIDGE) KM 402.00 TO KM 440.00 (DEVANPUR - KOTWA) (NHAI) (N24002063)	12/2021	1/2024 (N.A.) {6/2025}	210.05 (N.A.) {210.05}	100.28	68.58
		285	PERMANENT RECTIFICATION OF 3 NOS. OF BLACK SPOTS IN PROJECT HIGHWAY NH-27 OF U.P BORDER - DEWAPUR - (NHAI) (N24002064)	12/2022	12/2025 (N.A.) {12/2025}	381.80 (N.A.) {381.80}	32.97	16.01
		286	4L GREENFIELD ALIGNMENT OF AMAS TO SHIVRAMPUR FROM 0.000 KM. TO 55.002 KM. OF NH 119 D (PKG-I) (NHAI) (N24002065)	2/2022	3/2025 (N.A.) {3/2025}	1,390.92 (N.A.) {1,390.92}	150.71	8.17
		287	4L GREENFIELD ALIGNMENT OF SHIVRAMPUR TO RAMNAGAR FROM KM. 55.002 TO KM. 109.300 OF NH 119 D (PKG-I) (NHAI) (N24002066)	2/2022	7/2025 (N.A.) {7/2025}	1,494.31 (N.A.) {1,494.31}	38.28	4.59
		288	IMPROVEMENT OF 2 LANE WITH PAVED SHOULDER OF STRETCH FROM BIKRAMGANJ DAWATH MELAYABAGH NAWANAGR -DUM (MoRTH) (N24002133)	3/2021	3/2025 (N.A.) {6/2025}	178.63 (N.A.) {178.63}	54.73	46
	URBAN DEVELOPMENT	289	PATNA METRO RAIL CORPORATION LIMITED (PATNA METRO RAI) (N28000148)	2/2019	6/2024 (N.A.) {9/2024}	13,365.77 (N.A.) {13,925.50}	2,710.21	38.67
	WATER RESOURCES	290	SEWER NETWORK SPS AND STP BEGUSARAI (BUIDCO) (N30000026)	3/2018	7/2021 (Dec-19) {9/2024}	230.06 (N.A.) {230.06}	234.00	96

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		291	I AND D AND STP WORKS FOR BHAGALPUR (BUIDCO) (N30000027)	10/2017	9/2020 (Nov-20) {10/2024}	254.13 (413.29) {413.29}	120.95	83
		292	I AND D AND STP AT CHAPPRA (BUIDCO) (N30000028)	11/2018	12/2020 (N.A.) {2/2024}	236.15 (N.A.) {236.15}	142.08	100
		293	SEWER NETWORKS SPS AND STP HAJIPUR (BUIDCO) (N30000035)	3/2018	8/2021 (Mar-18) {9/2024}	305.19 (N.A.) {305.19}	311.42	90
		294	SEWER NETWORKS, SPS AND STP, MUNGER (BUIDCO) (N30000036)	3/2018	10/2021 (Mar-18) {6/2024}	294.02 (350.79) {522.85}	406.16	100
		295	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR (BUIDCO) (N30000037)	12/2014	3/2020 (N.A.) {6/2022}	225.77 (N.A.) {398.90}	363.79	100
		296	SAIDPUR SEWER NETWORK PATNA (BUIDCO) (N30000039)	4/2015	1/2021 (N.A.) {6/2022}	268.63 (N.A.) {493.85}	489.65	100
		297	SEWERAGE SCHEME AT PAHARI ZONE V PATNA (BUIDCO) (N30000040)	5/2017	4/2021 (May-17) {2/2023}	356.37 (364.00) {356.37}	312.11	100
		298	SEWERAGE TREATMENT PLANT AT PAHARI PATNA (BUIDCO) (N30000043)	5/2017	11/2020 (May-17) {5/2022}	191.62 (N.A.) {191.62}	123.27	100
		299	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK (BUIDCO) (N30000044)	3/2017	5/2021 (Mar-17) {2/2023}	277.42 (253.98) {277.42}	355.31	100
		300	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA (BUIDCO) (N30000050)	8/2017	6/2022 (N.A.) {9/2024}	578.89 (453.83) {578.89}	150.50	46
		301	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA (BUIDCO) (N30000051)	8/2017	6/2022 (N.A.) {9/2024}	824.00 (734.09) {824.00}	377.18	48

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
CHHATTISGARH	COAL	302	GEVRA EXPANSION OCP (SECL) (35-70) MTY (SECL) (060100093)	6/2010	3/2023 (N.A.) {3/2025}	11,816.40 (N.A.) {11,816.40}	6,152.08	77
		303	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY (SECL) (N06000008)	8/2013	3/2023 (N.A.) {3/2025}	7,612.33 (N.A.) {7,612.33}	4,587.59	81
		304	PELMA OCP(15.00MTY) (SECL) (N06000045)	11/2014	3/2023 (N.A.) {3/2030}	1,624.59 (N.A.) {1,624.59}	13.65	16
		305	CHHAL OC SEAM -III (6.00 MTY) (SECL) (N06000104)	12/2013	3/2022 (Mar-25) {3/2025}	610.63 (N.A.) {610.63}	568.33	85
		306	AMERA OC RCE (SECL) (N06000123)	2/2015	3/2018 (Mar-26) {3/2026}	335.97 (N.A.) {335.97}	173.32	42
		307	AMGAON OPENCAST PROJECT RCE (SECL) (N06000135)	7/2015	3/2020 (Mar-26) {3/2026}	316.10 (N.A.) {316.10}	187.50	65
		308	MAHAMAYA OPENCAST PROJECT (SECL) (N06000164)	5/2018	3/2026 (N.A.) {3/2026}	410.26 (N.A.) {410.26}	178.90	38
		309	JHIRIA WEST OPENCAST PROJECT (SECL) (N06000166)	11/2018	3/2026 (N.A.) {3/2026}	366.94 (N.A.) {366.94}	30.01	36
		310	BAROUD OC EXPANSION (3-10 MTY) (SECL) (N06000197)	8/2020	3/2029 (N.A.) {3/2029}	2,309.80 (N.A.) {2,309.80}	844.94	38
		311	JAMPALI OCP RCE (SECL) (N06000198)	5/2020	3/2024 (Mar-25) {3/2025}	278.64 (N.A.) {278.64}	207.81	73
		312	PORDA CHINTAPANI OCP (10 MTY) (SECL) (N06000199)	12/2020	3/2029 (N.A.) {3/2029}	2,310.12 (N.A.) {2,310.12}	42.64	10
		313	DIPKA OC EXPANSION 40 MTY (SECL) (N06000200)	12/2020	3/2029 (N.A.) {3/2029}	5,241.40 (N.A.) {5,241.40}	2,688.16	30
		314	JAGANNATHPUR OC RCE (3.0 MTY) (SECL) (N06000232)	7/2016	3/2020 (Mar-05) {3/2025}	459.49 (N.A.) {459.49}	256.58	92

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		315	KATKONA RO UG PROJECT (1.74 MTY) (SECL) (N06000274)	1/2023	3/2029 (N.A.) {3/2029}	329.22 (N.A.) {329.22}	0.00	2
	DEPARTMENT OF HIGHER EDUCATION	316	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. (CPWD EDUCATION) (N28000141)	3/2020	7/2022 (N.A.) {7/2022}	808.62 (N.A.) {808.62}	640.70	93
	PETROLEUM	317	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT (HPCL) (N16000413)	3/2021	3/2024 (Mar-25) {3/2025}	456.00 (N.A.) {456.00}	336.90	82.6
	POWER	318	WESTERN REGION EXPANSION SCHEME XXV (PGCIL) (N18000350)	2/2023	11/2023 (N.A.) {1/2025}	385.84 (N.A.) {385.84}	136.71	50
		319	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME XXVII (PGCIL) (N18000354)	3/2023	9/2024 (N.A.) {12/2024}	271.69 (N.A.) {271.69}	117.04	54
		320	TRANSMISSION SYSTEM ASSOCIATED WITH WESTERN REGION EXPANSION SCHEME-XXVIII AND XXIX (PGCIL) (N18000355)	3/2023	3/2025 (N.A.) {3/2025}	260.30 (N.A.) {260.30}	106.79	78
		321	LARA SUPER THERMAL POWER PROJECT, STAGE-II (2X800 MW) (BHEL) (N18000381)	8/2023	6/2028 (N.A.) {6/2028}	15,530.00 (N.A.) {15,530.00}	709.38	0
	RAILWAYS	322	KIRANDUL - JAGDALPUR DOUBLING (ECOR) (N22000318)	12/2012	3/2020 (N.A.) {3/2024}	1,160.00 (N.A.) {1,440.00}	1,434.16	88.5
		323	JHARSUGUDA-BILASPUR 4TH LINE (SECR) (N22000484)	4/2015	3/2021 (Dec-23) {12/2024}	1,973.00 (2,135.34) {2,135.34}	2,040.25	80
		324	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I (IRCON) (N22000489)	4/2013	9/2018 (N.A.) {12/2024}	3,055.00 (3,438.39) {3,438.39}	3,041.21	93

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		325	Gauge conversion of Raipur(Kendri)- Dhamtari and Abhanpur-Rajim branch (67.20 km) (SECR) (N22000572)	7/2011	10/2024 (N.A.) {2/2025}	1,171.30 (N.A.) {1,171.30}	469.63	45
		326	NIPANIA-BHATAPRA (14.4 KM) 4TH LINE (PB#72/NR/2022-23) (SECR) (N22000573)	9/2022	12/2026 (N.A.) {12/2026}	170.49 (N.A.) {170.49}	0.10	0
		327	4TH LINE - BHATAPARA-HATHBAND (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000574)	12/2022	12/2026 (N.A.) {12/2026}	177.03 (N.A.) {177.03}	0.21	0
		328	4TH LINE - BHILAI-BHILAI NAGAR (8.8 KM) (PB#72/NR/2022-23) (SECR) (N22000575)	9/2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {177.34}	0.63	0
		329	4TH LINE - DADHAPARA-BELHA (9.2 KM) (PB#72/NR/2022-23) (SECR) (N22000576)	9/2022	9/2026 (N.A.) {9/2026}	169.06 (N.A.) {169.06}	0.22	0
		330	4TH LINE - RAJNANDGAON- DONGARHGARH (31.2 KM) (PB#72/NR/2022-23) (SECR) (N22000577)	9/2022	9/2026 (N.A.) {9/2026}	328.34 (N.A.) {328.34}	0.37	0
		331	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (N22000579)	9/2022	9/2026 (N.A.) {9/2026}	167.64 (N.A.) {167.64}	0.00	0
		332	DOUBLING OF BORIDAND - AMBIKAPUR (SURAJPUR) (SECR) (N22000580)	6/2022	6/2030 (N.A.) {6/2030}	1,376.20 (N.A.) {775.82}	48.71	5
		333	DALLIRAJHARA - ROWGHAT (95 KM) {PART OF DALLIRAJHARA-JAGDALPUR (235 KM)} (RVNL) (N22000602)	3/2008	6/2025 (N.A.) {6/2025}	631.78 (N.A.) {1,627.56}	1,323.64	84
		334	CHIRIMIRI-NAGPUR HALT (SECR) (N22000616)	10/2018	6/2030 (N.A.) {6/2030}	241.00 (N.A.) {241.00}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	335	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 (MoRTH) (N24001217)	1/2016	8/2016 (N.A.) {12/2024}	497.14 (572.66) {572.66}	363.29	57.37
		336	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION (MoRTH) (N24001221)	1/2016	10/2016 (N.A.) {9/2024}	624.98 (731.50) {731.50}	604.79	99
		337	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI (MoRTH) (N24001222)	3/2016	7/2016 (N.A.) {3/2025}	452.94 (N.A.) {435.61}	292.28	63.04
		338	CONSTRUCTION OF 4 NOS GRADE SEPARATOR BETWEEN KM. 281.000 TO KM 307.600 KM. 286.400 KUMHARI KM. 299. (MoRTH) (N24001227)	3/2018	1/2019 (N.A.) {9/2024}	349.03 (N.A.) {349.03}	316.52	97.9
		339	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH- 130A (MoRTH) (N24001228)	11/2017	5/2019 (N.A.) {12/2024}	188.80 (N.A.) {188.80}	136.81	97
		340	DEVELOPMENT OF SIX LANE SARGI- BASANWAHI OF NH 130 CD FROM KM.42+800 TO 99+500 UNDER RAIPUR VISAKHAPA (NHAI) (N24001588)	12/2021	1/2025 (N.A.) {9/2025}	1,470.73 (N.A.) {1,470.73}	504.46	52.1
		341	DEVELOPMENT OF SIX LANE JHANKI SARGI OF NH 130 CD FROM KM.0+000 TO 42+800 UNDER RAIPUR VISAKHAPATTNA (NHAI) (N24001593)	11/2021	9/2024 (N.A.) {6/2025}	1,368.19 (N.A.) {1,368.19}	782.50	76.53

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		342	4 LANE OF BILASPUR TO URGAL PROJECT (KM 0.00 TO KM 70.2) OF NH-130A (NHAI) (N24001611)	4/2020	3/2024 (N.A.) {9/2025}	1,855.59 (2,523.86) {2,523.86}	388.19	70.92
		343	UP GRADATION OF NH 930 SHERPAR TO KOHKA FROM KM 67.880 TO KM 114.860 TO TWO LANE WITH PAVED SHOULDER (MoRTH) (N24001917)	3/2020	5/2024 (N.A.) {11/2024}	278.97 (N.A.) {278.97}	169.62	71.26
		344	UP GRADATION OF NH 130C ABHANPUR TO PAUND FROM NK KM 0.000 TO KM. 40.380 TO TWO LANE WITH PAVED SHOULDER (MoRTH) (N24001919)	12/2020	9/2023 (Nov-24) {11/2024}	193.16 (N.A.) {193.16}	79.16	61.3
		345	UPGRADATION OF NH 130A MUNGELI TO PONDHI FROM NH KM. 51.600 TO KM. 77.870 KM. 80.970 TO 96.970 TO 2 (MoRTH) (N24001920)	3/2021	9/2024 (N.A.) {1/2025}	218.57 (N.A.) {218.57}	91.72	77.12
		346	DEVELOPMENT OF SIX LANE BASANWAHI-MARANGPURI OF NH 130 CD FROM KM.99+500 TO 124+661 UNDER RAIPUR VIS (NHAI) (N24002017)	3/2022	10/2025 (N.A.) {9/2026}	1,307.16 (N.A.) {1,307.16}	82.01	9.8
		347	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 1 SECTION OF NH 53 FROM CH 0.000 TO CH 44.50 (NHAI) (N24002045)	6/2022	7/2025 (N.A.) {7/2025}	1,828.00 (N.A.) {1,828.00}	318.96	11.76
		348	CONSTRUCTION OF 6 LANE DURG RAIPUR ARANG BYPASS PKG 2 SECTION OF NH 53 FROM CH 44+500 TO CH.92+230 I (NHAI) (N24002046)	6/2022	5/2025 (N.A.) {5/2025}	1,958.94 (1,959.00) {1,958.94}	585.16	22.1
	STEEL	349	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 (NMDC) (N12000124)	11/2015	6/2023 (Jul-24) {12/2025}	2,907.00 (N.A.) {2,907.00}	2,179.24	59.2

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		350	SCREENING PLANT-III AT KIRANDUL (NMDC) (N12000127)	3/2021	8/2024 (N.A.) {1/2026}	2,092.97 (2,718.84) {2,718.84}	1,243.56	63.5
		351	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (NMDC) (N12000130)	7/2021	11/2024 (N.A.) {12/2025}	282.44 (N.A.) {282.44}	120.40	45
		352	REPLACEMENT OF CONVERTER VESSELS, TRUNNION RINGS, SUPPORT SYSTEM AND INSTALLATION OF SECONDARY EMISS (SAIL) (N12000131)	10/2023	6/2026 (N.A.) {6/2026}	471.83 (N.A.) {471.83}	38.21	1.9
		353	REBUILDING OF COKE OVEN BATTERY NO.7 AND 8 OF BHILAI STEEL PLANT (SAIL) (N12000134)	11/2023	10/2025 (N.A.) {10/2025}	884.10 (N.A.) {884.10}	235.69	43.8
	URBAN DEVELOPME NT	354	CONSTRUCTION 729 QUARTERS (TYPE II- 180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI (CPWD) (N28000149)	5/2019	9/2020 (Oct-24) {10/2024}	299.97 (299.97) {299.97}	245.83	81
DELHI	CIVIL AVIATION	355	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR (AAI) (N04000076)	11/2016	4/2020 (Apr-24) {4/2024}	303.80 (374.98) {374.98}	327.64	100
	DPIIT	356	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE (IICC FOR DPIIT) (N40000002)	11/2017	12/2019 (N.A.) {10/2024}	4,773.00 (N.A.) {5,401.00}	4,789.71	97.3
	FINANCE	357	C/O RESIDENTIAL COMPLEX BUILDING FOR CENTRAL BOARD OF INDIRECT TAXES AND CUSTOMS AT SECTOR-9, DWARKA (NPCC) (N07000001)	7/2018	4/2022 (N.A.) {4/2022}	228.50 (N.A.) {220.27}	176.28	85

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>HOME AFFAIRS</u>	358	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI (CPWD FOR MHA) (N28000071)	10/2013	10/2019 (N.A.) {9/2024}	1,219.21 (2,091.53) {2,091.53}	1,914.49	100
		359	CONSTRUCTION OF HEADQUARTER BUILDING OF CRPF AT LODHI ROAD NEW DELHI (CPWD FOR MHA) (N45000002)	6/2019	7/2022 (N.A.) {5/2025}	277.35 (N.A.) {277.35}	90.58	54
	<u>RAILWAYS</u>	360	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE (NR) (N22000281)	4/2012	(N.A.) {9/2023}	295.68 (N.A.) {419.00}	133.78	30
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	361	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM AKSHARDHAM NH 9 JUNCTION TO DELHI UP BOR (NHAI) (N24001771)	6/2020	12/2024 (N.A.) {12/2024}	1,479.22 (N.A.) {1,479.22}	1,491.26	98
		362	6L ACCESS CONTROLLED HIGHWAY FROM DND MAHARANI BAGH JN. WITH JAITPUR PUSHTA ROAD OF NH 148NA FROM (NHAI) (N24001773)	5/2020	7/2024 (N.A.) {1/2026}	1,467.44 (N.A.) {1,942.89}	913.85	78.48
		363	DEVELOPMENT OF 6L UER-II (PACKAGE- I) (NH-1 NEAR BAKOLI TILL KARALA KANJHAWALA ROAD) FROM KM. (-)0.70 (NHAI) (N24001777)	7/2020	10/2023 (N.A.) {9/2024}	2,171.80 (N.A.) {2,171.80}	958.13	99
		364	DEVELOPMENT OF 4L UER II [PACKAGE - V] (SPUR TO BAHADURGARH BYPASS) (NH-10) FROM KM. 0.00 TO KM.7.30 (NHAI) (N24001778)	7/2020	10/2023 (N.A.) {10/2024}	801.46 (N.A.) {801.46}	382.03	99.33
		365	DWARKA EXPRESSWAY FROM KM -0.600 TO KM 5.300 - PKG-I (SHIVMURTI CHOWK- RUB NEAR DWARKA SECTOR 21) (NHAI) (N24001779)	3/2018	9/2022 (N.A.) {10/2024}	2,507.00 (N.A.) {3,030.73}	1,155.70	85.07

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		366	8L OF DWARKA EXPRESSWAY PKG-II (RUB NEAR DWARKA SECTOR 21-DL/HR BORDER) FROM 5.300 KM.TO 9.500 KM. O (NHAI) (N24001781)	1/2018	10/2021 (N.A.) {10/2024}	2,067.67 (N.A.) {2,160.00}	1,496.49	95.65
		367	DEVELOPMENT OF 6L UER II [PACKAGE - II] (KARALA KANJHAWALA ROAD TILL NANGLOI - NAJAFGARH ROAD) FROM (NHAI) (N24001825)	7/2020	10/2023 (N.A.) {11/2024}	1,894.96 (N.A.) {1,894.96}	741.88	83.63
	TELECOMMUNICATIONS	368	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT (CPWD FOR TELECO) (N28000115)	10/2014	3/2018 (N.A.) {3/2025}	248.20 (N.A.) {248.20}	213.22	98
	URBAN DEVELOPMENT	369	DELHI MRTS PHASE-III (DMRC) (N28000056)	9/2011	3/2016 (Aug-21) {8/2021}	38,585.00 (43,095.35) {40,180.91}	40,529.39	99.99
		370	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR (NBCC) (N28000105)	7/2016	(N.A.) {10/2024}	2,694.00 (N.A.) {2,694.00}	2,402.68	0
		371	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I (CPWD) (N28000128)	10/2016	7/2021 (N.A.) {6/2024}	1,180.00 (N.A.) {1,100.80}	36.69	2
		372	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I (CPWD) (N28000129)	10/2016	3/2022 (N.A.) {6/2024}	1,128.00 (N.A.) {1,128.00}	550.45	46
		373	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS (DMRC) (N28000135)	7/2019	3/2025 (N.A.) {3/2026}	24,948.65 (N.A.) {24,948.65}	13,014.06	54.5
		374	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND (DMRC) (N28000136)	5/2017	12/2020 (Nov-22) {11/2022}	565.00 (739.49) {565.00}	521.75	100

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		375	CONSTRUCTION OF 184 MULTI STORIED FLATS FOR HON'BLE MPS AT BKS MARG, NEW DELHI (CPWD) (N28000153)	1/2022	11/2024 (May-25) {5/2025}	646.52 (N.A.) {646.52}	291.91	62
		376	REDEVELOPMENT OF GPRA AT NETAJI NAGAR NEW DELHI PACKAGE 2 (NBCC) (N28000156)	10/2016	3/2024 (N.A.) {3/2025}	1,536.72 (N.A.) {1,536.72}	305.31	76
	<u>WATER RESOURCES</u>	377	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD 10MG/L (DJB) (N30000014)	3/2017	12/2022 (N.A.) {9/2024}	665.78 (N.A.) {665.78}	782.51	96
		378	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 (DJB) (N30000015)	5/2016	12/2021 (N.A.) {2/2024}	211.79 (223.70) {211.79}	208.71	100
		379	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S (DJB) (N30000016)	5/2016	2/2022 (Sep-23) {7/2023}	239.11 (314.71) {239.11}	268.13	100
		380	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI (DJB) (N30000017)	12/2018	1/2021 (N.A.) {3/2022}	515.07 (N.A.) {515.07}	388.08	100
		381	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO (DJB) (N30000018)	5/2017	5/2020 (N.A.) {5/2020}	344.81 (N.A.) {344.81}	0.00	0
<u>GOA</u>	<u>CIVIL AVIATION</u>	382	EXTENSION OF EXISTING INTEGRATED TERMINAL BUILDING AND ALLIED WORKS AT GOA AIRPORT. (AAI) (N04000095)	11/2017	9/2021 (N.A.) {3/2025}	255.69 (N.A.) {255.69}	75.31	56

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	383	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. (CPWD EDUCATION) (N42000002)	5/2019	8/2021 (N.A.) {12/2024}	303.90 (N.A.) {390.40}	364.00	99.3
	<u>PETROLEUM</u>	384	UPGRADING IPSHEM TO WORLD CLASS FACILITY OF ONGC, GOA (ONGC) (N16000502)	3/2023	6/2024 (N.A.) {11/2024}	325.53 (N.A.) {325.53}	290.46	99.1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	385	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE (MoRTH) (N24000444)	10/2015	(Sep-23) {9/2023}	936.40 (N.A.) {936.40}	770.90	100
		386	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR (MoRTH) (N24000516)	12/2015	(N.A.) {12/2023}	819.95 (N.A.) {819.95}	504.65	99
		387	MOPA AIRPORT (MoRTH) (N24001458)	12/2021	4/2022 (Sep-24) {9/2024}	1,183.16 (N.A.) {1,183.16}	1,106.30	97
	<u>ATOMIC ENERGY</u>	388	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 (NPCIL) (N02000010)	10/2009	12/2015 (N.A.) {3/2024}	11,459.00 (22,517.00) {22,517.00}	21,479.00	100
GUJARAT	<u>CIVIL AVIATION</u>	389	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT (AAI) (N04000088)	1/2018	8/2022 (May-24) {10/2024}	1,405.00 (N.A.) {1,405.00}	1,278.77	99.9
		390	EXTENSION OF TERMINAL BUILDING, PTT, APRON AND CAR PARK AT SURAT AIRPORT. (AAI) (N04000093)	8/2018	2/2021 (N.A.) {10/2024}	353.25 (N.A.) {353.25}	341.37	98
		391	DEVELOPMENT OF NEW GREENFIELD AIRPORT AT DHOLERA, AHMEDABAD (GUJARAT). PHASE-1. (AAI) (N04000099)	6/2022	12/2025 (N.A.) {12/2025}	1,305.00 (1,143.95) {1,143.95}	237.55	32

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	392	REDEVELOPMENT OF SANTHAL FIELD (ONGC) (N16000279)	2/2017	3/2026 (N.A.) {3/2026}	1,162.56 (N.A.) {1,162.56}	1,093.53	89.4
		393	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY (IOCL) (N16000382)	11/2019	5/2023 (Mar-24) {12/2024}	5,251.00 (5,894.00) {5,894.00}	4,343.11	98.4
		394	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY (IOCL) (N16000409)	9/2020	8/2024 (Dec-25) {12/2025}	18,936.00 (N.A.) {18,936.00}	8,884.89	75.3
		395	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM (IOCL) (N16000411)	10/2020	8/2023 (Nov-24) {11/2024}	1,614.00 (N.A.) {1,614.00}	1,003.59	90.19
		396	REDEVELOPMENT OF LINCH FIELD (ONGC) (N16000428)	4/2021	3/2025 (N.A.) {7/2025}	631.03 (860.04) {860.04}	270.34	52.2
		397	REDEVELOPMENT OF SOBHASAN COMPLEX (ONGC) (N16000431)	8/2021	2/2026 (N.A.) {2/2026}	885.63 (1,286.67) {1,286.67}	395.83	37.4
		398	COMMERCIAL POLYMER FLOODING PROJECT IN BECHRAJI FIELD (ONGC) (N16000444)	1/2022	11/2024 (N.A.) {11/2024}	621.40 (N.A.) {621.40}	101.03	19.8
		399	INSTALLATION OF NEW BITUMEN UNIT ALONG WITH ALLIED FACILITIES AT GUJARAT (IOCL) (N16000454)	1/2022	9/2024 (N.A.) {8/2025}	328.00 (N.A.) {328.00}	27.86	20.9
		400	RESTORATION OF GAS TERMINAL, PHASE-I (PART-A), HAZIRA PLANT (ONGC) (N16000477)	5/2022	2/2025 (N.A.) {2/2025}	249.43 (N.A.) {249.43}	98.17	78.4
		401	KALOL REDEVELOPMENT PROJECT (ONGC) (N16000481)	8/2022	3/2027 (N.A.) {3/2027}	1,487.41 (N.A.) {1,487.41}	733.89	52

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		402	CONSTRUCTION OF TWO PRODUCED WATER TREATMENT PLANTS (PWTP) AT BECHARAJI AND SOBHASAN INSTALLATION OF (ONGC) (N16000482)	7/2021	7/2024 (N.A.) {9/2024}	320.20 (N.A.) {187.61}	176.01	100
		403	OLD PIPE LINE REPLACEMENT (OPRP) GROUP-A (ONGC) (N16000483)	7/2021	7/2025 (N.A.) {7/2025}	173.03 (N.A.) {169.84}	120.79	75.7
		404	REVAMPING OF SV STATIONS, GAS TERMINAL AND KRIBHCO TERMINAL (ONGC) (N16000514)	11/2022	8/2026 (N.A.) {8/2026}	837.34 (N.A.) {837.34}	39.93	21
	POWER	405	GUJARAT 200 MW (GUVNL TENDER) (NTPC) (N18000295)	1/2021	7/2022 (N.A.) {7/2022}	842.27 (N.A.) {842.27}	494.80	0
		406	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA AND RADHANPUR) (NTPC) (N18000296)	5/2021	9/2022 (N.A.) {9/2022}	674.92 (N.A.) {674.92}	457.90	0
		407	Bagodara Solar Power Project (SJVN) (N18000297)	5/2021	10/2022 (N.A.) {3/2025}	339.35 (N.A.) {339.35}	330.05	51
		408	DAYAPAR WIND ENERGY PROJECT 150MW (NTPC) (N18000319)	11/2021	5/2023 (N.A.) {6/2024}	937.80 (N.A.) {937.80}	690.34	0
		409	DAYAPAR WIND ENERGY PROJECT 200MW (NTPC) (N18000345)	7/2022	3/2025 (N.A.) {3/2025}	1,316.02 (N.A.) {1,316.02}	207.34	0
		410	KHAWDA 1255MW SOLAR PROJECT (KHAWDA SOLAR PARK) (NTPC) (N18000346)	9/2022	9/2024 (N.A.) {9/2024}	7,179.54 (N.A.) {7,179.54}	916.13	0
		411	BHUJ SOLAR 300MW (TRANCHE-IV WIND SOLAR HYBRID) (NTPC) (N18000349)	11/2022	3/2024 (N.A.) {6/2024}	1,442.60 (N.A.) {1,442.60}	80.60	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		412	ESTABLISHMENT OF KHAVDA POOLING STATION 3 (KPS3) IN KHAVDA RE PARK (PGCIL) (N18000357)	3/2023	12/2024 (N.A.) {2/2025}	922.30 (N.A.) {922.30}	259.67	30
		413	TRANSMISSION NETWORK EXPANSION IN GUJARAT ASSOCIATED WITH INTEGRATION OF RE PROJECTS FROM KHAVDA POT (PGCIL) (N18000358)	3/2023	3/2025 (N.A.) {3/2025}	815.12 (N.A.) {815.12}	7.99	26
		414	KHAVDA-2, GUJARAT- ESTABLISHMENT OF KHAVDA POOLING STATION-2 (KPS2) IN KHAVDA RE PARK (PGCIL) (N18000359)	3/2023	12/2024 (N.A.) {2/2025}	966.79 (N.A.) {966.79}	133.22	37
		415	KHAVDA PHASE-II-PART B, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000360)	3/2023	3/2025 (N.A.) {3/2025}	1,167.55 (N.A.) {1,167.55}	509.14	22
		416	KHAVDA PHASE-II-PART C, GUJARAT- TRANSMISSION SCHEME FOR EVACUATION OF 4.5 GW RE INJECTION AT KHAVDA (PGCIL) (N18000361)	3/2023	3/2025 (N.A.) {3/2025}	2,820.99 (N.A.) {2,820.99}	336.10	19
		417	KHAVDA 1200MW (4X300MW) IN KHAVDA RE PARK (NTPC) (N18000365)	6/2023	12/2024 (N.A.) {12/2024}	6,283.81 (N.A.) {6,283.81}	383.77	0
		418	DAYAPAR WIND- III (HYBRID TRANCHE-V) (NTPC) (N18000366)	5/2023	1/2025 (N.A.) {5/2025}	1,095.01 (N.A.) {1,095.01}	119.46	0
		419	TS FOR EVACUATION OF POWER FROM POTENTIAL RE ZONE IN KHAVDA AREA OF GUJARAT UNDER PH-IV PART E3 (PGCIL) (N18000383)	7/2023	7/2025 (N.A.) {7/2025}	334.00 (N.A.) {334.00}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		420	TS FOR EVACUATION OF ADDITIONAL 7GW RE POWER FROM KHAVDA RE PARK UNDER PHASE-III PART B [VATAMAN TRA (PGCIL) (N18000384)	12/2023	12/2025 (N.A.) {12/2025}	3,752.00 (N.A.) {3,752.00}	187.02	1
		421	TS FOR EVACUATION OF POWER FROM 7GW REZ IN KHAVDA AREA UNDER PHASE-IV PART E2 (PGCIL) (N18000390)	5/2024	5/2026 (N.A.) {5/2026}	679.00 (N.A.) {679.00}	0.00	0
	RAILWAYS	422	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) (WR) (N22000123)	4/2008	3/2012 (Sep-26) {9/2026}	318.24 (1,531.55) {1,531.55}	1,317.64	86
		423	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) (WR) (N22000142)	4/2011	(Oct-25) {10/2025}	844.10 (844.10) {844.10}	540.46	41
		424	ANAND GODHRA DOUBLING PROJECT 79 KMS (WR) (N22000504)	4/2017	3/2020 (Dec-24) {12/2024}	692.25 (692.26) {692.26}	540.99	90
		425	MEHSANA PALANPUR DOUBLING PROJECT 65.10 KMS (WR) (N22000505)	4/2018	3/2024 (N.A.) {12/2024}	537.31 (537.31) {537.31}	564.48	96
		426	4TH LINE BETWEEN BAREJADI NANDEJ (GERATPUR)- SANAND (38.20 KM) (AHMEDABAD BYPASS). (WR) (N22000532)	2/2023	3/2027 (Feb-27) {2/2027}	961.67 (961.67) {961.67}	23.10	1
		427	QUADRUPLING BETWEEN GANDHIDHAM - ADIPUR WITH Y CONNECTION AT ADIPUR FOR PROVIDING DIRECT ENTRY TOWAR (WR) (N22000533)	2/2023	12/2025 (Oct-25) {10/2025}	152.44 (152.44) {152.44}	23.19	5
		428	MEHSANA-PALANPUR (65.1 KM) (WR) (N22000534)	9/2020	9/2026 (Oct-24) {10/2024}	529.30 (N.A.) {537.31}	371.32	97
		429	RAJKOT-KANALUS (111.20 KM) (WR) (N22000535)	10/2021	10/2026 (Dec-25) {12/2025}	1,011.72 (1,080.58) {1,080.58}	841.26	61

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		430	HIMMATNAGAR-KHEDBRAHMA (54.83 KM) (WR) (N22000537)	6/2022	2/2030 (Feb-25) {2/2025}	354.99 (482.42) {482.42}	431.70	53
		431	PETLAD-BHADLAN (22.5 KM) (WR) (N22000538)	5/2022	5/2030 (N.A.) {12/2025}	202.50 (307.12) {307.12}	47.30	7
		432	NADIAD-PETLAD (37.26 KM) (WR) (N22000539)	5/2022	6/2030 (N.A.) {12/2025}	335.34 (461.91) {461.91}	47.40	7
		433	SAMLAYA-TIMBA ROAD (53.53 KM) (WR) (N22000540)	2/2023	3/2030 (N.A.) {1/2027}	401.48 (670.17) {670.17}	71.95	9
		434	SAMNI-JAMBUSAR (24.08 KM) (WR) (N22000541)	5/2022	3/2030 (Apr-26) {4/2026}	216.72 (349.93) {349.93}	62.36	25
		435	VIJAPUR-AMBLIYASAN (41.53 KM) (WR) (N22000547)	5/2022	3/2030 (Feb-25) {2/2025}	309.81 (415.38) {415.38}	341.43	70
		436	ADRAJ MOTI-VIAJAPUR (39.75 KM) (WR) (N22000548)	5/2022	5/2030 (N.A.) {5/2030}	296.54 (N.A.) {296.54}	0.00	0
		437	KALOL-KADI-KATOSAN ROAD (37.23 KM) (WR) (N22000549)	6/2022	6/2027 (Oct-24) {10/2024}	279.23 (346.94) {346.94}	397.87	90
		438	NEW BG LINE BETWEEN NALIYA-JAKHAU PORT (WR) (N22000550)	2/2023	1/2028 (Sep-26) {9/2026}	410.46 (410.46) {410.46}	21.58	2
		439	NEW BG LINE INTERSECTION (5 NOS) BETWEEN GERATPUR-SANAND & BOTAD- AHMEDABAD (16.51 KM) (PB#29/NR/202 (WR) (N22000551)	10/2022	10/2027 (N.A.) {10/2027}	437.21 (N.A.) {437.21}	0.00	0
		440	TARANGA HILL ABU ROAD VIA AMBAJI NEW LINE (NWR) (N22000592)	7/2022	7/2030 (N.A.) {12/2026}	1,695.82 (N.A.) {2,798.16}	706.51	10
		441	JUNAGARH -VISAVADAR (42.28) KM (RVNL) (N22000600)	6/2022	12/2026 (N.A.) {12/2026}	492.83 (N.A.) {492.83}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		442	MODASA- SHAMLAJI NEW LINE (MM OF AHMEDABAD-HIMMATNAGAR-UDAIPUR (299.2 KM)) (WR) (N22000622)	9/2012	3/2027 (Mar-26) {3/2026}	261.68 (261.68) {261.68}	367.54	40
		443	NATHDWARA-NEW NATHDWARA NEW LINE (MM OF AJMER-CHITTAURGARH-UDAIPUR) (WR) (N22000623)	6/2013	6/2025 (N.A.) {6/2025}	166.33 (N.A.) {166.33}	55.81	8
	ROAD TRANSPORT AND HIGHWAYS	444	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. (NHAI) (N24000567)	5/2016	8/2019 (N.A.) {2/2024}	998.18 (N.A.) {998.18}	802.04	100
		445	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST (NHAI) (N24000569)	5/2016	9/2019 (May-24) {10/2024}	723.64 (N.A.) {723.64}	559.55	95.98
		446	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU (NHAI) (N24000570)	5/2016	8/2019 (N.A.) {10/2024}	763.08 (N.A.) {763.08}	507.35	95.18
		447	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 (NHAI) (N24000592)	7/2016	7/2020 (N.A.) {10/2024}	829.97 (N.A.) {829.97}	457.75	92.2
		448	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. (NHAI) (N24000649)	1/2017	12/2020 (Jun-25) {6/2025}	1,251.11 (1,527.75) {1,527.75}	683.63	83.84
		449	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR (NHAI) (N24000834)	3/2018	10/2021 (Sep-24) {9/2024}	1,161.39 (1,404.00) {1,404.00}	418.51	39.17

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		450	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA (MoRTH) (N24000925)	10/2018	11/2020 (Sep-24) {9/2024}	400.76 (394.44) {394.44}	287.39	87
		451	CONSTRUCTION OF ROB WITH APPROACHES IN LIEU OF L C NO 165 OF AHMEDABAD PALANPUR BETWEEN RAILWAY STAT (MoRTH) (N24001427)	6/2020	4/2023 (Sep-24) {9/2024}	166.21 (N.A.) {166.21}	98.65	93
		452	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SARDAR PATEL RING ROAD TO SINDHREJ VILLAGE (CH. 0 (NHAI) (N24001443)	5/2020	3/2024 (Oct-24) {11/2024}	690.30 (929.95) {929.95}	693.41	79
		453	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF SINDHREJ VILLAGE (CH. 22.00 TO CH. 48.52) SECTION (NHAI) (N24001444)	5/2020	1/2024 (Oct-24) {11/2024}	882.00 (N.A.) {882.00}	737.57	71.96
		454	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF VEJALLKA VILLAGE TO START OF DSIR ZONE OF AHMEDAB (NHAI) (N24001445)	5/2020	7/2023 (Oct-24) {11/2024}	691.52 (903.85) {903.85}	728.37	85.1
		455	CONSTRUCTION OF FOUR LANE EXPRESSWAY FROM START OF DSIR ZONE OF AHMEDABAD DISTRICT TO ADHELAI VILLAG (NHAI) (N24001446)	5/2020	12/2023 (Oct-24) {11/2024}	894.00 (1,210.06) {1,210.06}	878.86	81.08
		456	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 26 (NHAI) (N24001515)	9/2020	2/2024 (N.A.) {1/2025}	1,542.02 (N.A.) {1,542.02}	778.07	50.51

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		457	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 27 (NHAI) (N24001516)	9/2020	2/2024 (Aug-24) {8/2024}	1,185.69 (N.A.) {1,185.69}	845.32	82.3
		458	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 30 (NHAI) (N24001518)	11/2019	9/2023 (N.A.) {10/2024}	1,669.56 (N.A.) {1,669.56}	967.79	88.12
		459	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 28 (NHAI) (N24001519)	9/2020	11/2023 (N.A.) {9/2024}	1,198.55 (N.A.) {1,198.55}	802.45	85.29
		460	DELHI VADODARA GREENFIELD ALIGNMENT SECTION OF NH 148N PACKAGE 31 (NHAI) (N24001520)	11/2019	5/2024 (N.A.) {11/2024}	1,604.06 (N.A.) {1,604.06}	1,219.52	95.73
		461	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF BHIMASAR JUNCTION OF NH-41 TO ANJAR BHUJ UPTO AIRPORT (NHAI) (N24001785)	3/2022	6/2025 (N.A.) {6/2025}	1,373.06 (1,085.00) {1,373.06}	491.22	61.03
		462	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 103.400 TO KM 128.000 OF VADODARA MU (NHAI) (N24001786)	3/2021	3/2024 (N.A.) {3/2025}	1,259.00 (N.A.) {1,910.00}	137.93	15.02
		463	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY FROM KM 217.500 TO KM 254.430 OF VADODARA MU (NHAI) (N24001788)	7/2020	12/2023 (N.A.) {6/2024}	2,271.86 (N.A.) {3,916.00}	518.25	74.55
		464	CONSTRUCTION OF EIGHT LANE EXPRESSWAY FROM KM 190.000 TO KM 217.500 GANDEVA TO ENA SECTION OF VADODA (NHAI) (N24001789)	7/2020	8/2023 (N.A.) {6/2024}	1,710.30 (N.A.) {1,927.00}	362.81	68.11

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		465	SANCHORE - SANTALPUR FROM KM 67.000- KM 99.000 OF NH-754K (AJ-RGBS-PACKAGE-3) (NHAI) (N24001790)	2/2020	8/2023 (Dec-24) {10/2024}	752.30 (N.A.) {766.20}	451.11	98.14
		466	SANCHORE - SANTALPUR FROM KM 4.888 - KM 35.000 OF NH-754K (AJ-RGBS-PACKAGE-1) (NHAI) (N24001791)	2/2020	6/2023 (Mar-24) {5/2024}	606.51 (N.A.) {657.00}	453.89	98.99
		467	4L OF BAL WORKS OF TALAJA - MAHUVA FROM 54.990 KM. TO 100.450 KM. OF OLD NH-8E (PACKAGE-II) (NHAI) (N24001792)	3/2021	9/2022 (N.A.) {9/2024}	536.03 (N.A.) {536.03}	445.87	98.87
		468	4L OF BAL WORKS OF MAHUVA TO KAGVADAR FROM 100.450 KM. TO 140.470 KM. OF NH-8E (PKG- III) (NHAI) (N24001793)	3/2021	9/2022 (N.A.) {9/2024}	485.75 (N.A.) {485.75}	383.09	97.71
		469	SANCHORE - SANTALPUR FROM KM 99.000- KM 130.073 OF NH-754K (AJ-RGBS-PACKAGE-4) (NHAI) (N24001794)	2/2020	3/2023 (Dec-24) {10/2024}	778.15 (N.A.) {785.67}	539.42	99.61
		470	4L KODINAR - VERAVAL (PACKAGE VI) FROM KM. 222.400 TO KM. 230.00 (KODINAR BYPASS) OF NH-8E (NH 51 NE) (NHAI) (N24001827)	3/2022	3/2023 (N.A.) {7/2024}	162.73 (N.A.) {162.73}	131.79	95.3
		471	UPGRADATION AND STRENGTHENING TO 2 LANE PS FROM KM 95/500 TO KM 129/775 OF NH 168 G IDAR BHILODA SA (MoRTH) (N24002014)	9/2022	12/2023 (Dec-25) {12/2025}	237.28 (N.A.) {237.28}	0.59	0
		472	UPGRADATION TO 4L PS DIVIDED CARRIAGEWAY FROM PATAN (NEAR RAJPUR) TO GOJARIYA FROM KM 52.000 TO KM 1 (NHAI) (N24002034)	12/2021	3/2025 (N.A.) {3/2025}	1,181.34 (1,181.00) {1,181.34}	329.33	49.3

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		473	WIDENING TO 6L OF EXISTING 4L JETPUR - GONDAL - RAJKOT SECTION FROM KM. 117.600 TO KM. 185.00 ON NH- (NHA)) (N24002035)	9/2023	9/2025 (N.A.) {9/2025}	2,070.44 (N.A.) {2,070.44}	169.27	11.45
		474	UPGRADATION OF DHORAJI JAMKANDORNA KALAVAD SECTION OF NH 927D FROM DESIGN CHAINAGE KM 00 TO KM 58.11 (MoRTH) (N24002117)	10/2022	2/2024 (Feb-26) {2/2026}	246.60 (291.00) {291.00}	29.33	15
		475	UPGRADATION TO TWO LANE WITH PAVED SHULDER CONFIGURATION FROM KM 00 TO 47 OF NH 351 MAHUVA TO BADHA (MoRTH) (N24002118)	12/2022	2/2024 (Aug-25) {8/2025}	173.06 (N.A.) {219.00}	0.15	0
	URBAN DEVELOPME NT	476	AHMEDABAD METRO RAIL PROJECT PHASE I (MEGA) (N28000122)	11/2014	12/2018 (N.A.) {12/2024}	10,773.00 (N.A.) {12,924.55}	12,295.84	99.79
		477	AHMEDABAD METRO RAIL PROJECT PHASE II (MEGA) (N28000137)	3/2019	3/2024 (N.A.) {6/2025}	5,384.17 (N.A.) {5,384.17}	3,411.86	73.45
		478	SURAT METRO RAIL PROJECT (MEGA) (N28000138)	3/2019	3/2024 (N.A.) {10/2025}	12,020.32 (N.A.) {12,020.32}	5,415.51	52.8
HARYANA	HEALTH AND FAMILY WELFARE	479	ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT MANETHI, HARYANA. (HITES) (N21000032)	3/2019	3/2023 (Mar-26) {3/2026}	1,294.34 (1,294.34) {1,294.34}	117.69	3.5
	HOME AFFAIRS	480	C/o separate family accommodation (Phase- I) on EPC basis for SSB at Faridabad (Haryana)" (CPWD FOR MHA) (N28000147)	1/2020	10/2023 (Jan-25) {1/2025}	166.98 (167.00) {166.98}	108.99	89
	PETROLEUM	481	R and D CAMPUS II AT FARIDABAD (IOCL) (N16000375)	6/2019	12/2022 (Jul-25) {7/2025}	2,281.94 (3,219.94) {3,219.94}	1,569.66	60.7

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		482	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA (IOCL) (N16000412)	2/2021	9/2024 (Dec-25) {12/2025}	34,627.00 (38,231.00) {38,231.00}	13,973.41	72.6
		483	POLY BUTADIENE RUBBER PLANT AT PANIPAT (IOCL) (N16000458)	3/2022	3/2025 (N.A.) {12/2025}	1,459.00 (2,102.79) {2,102.79}	443.17	40.2
	RAILWAYS	484	DOUBLING BETWEEN BHIWANI-DOBH BAHALI (NWR) (N22000604)	2/2023	2/2028 (N.A.) {2/2026}	471.06 (N.A.) {471.06}	38.90	27
		485	DOUBLING BETWEEN REWARI- KATHUWAS (27.73 KM) (NWR) (N22000606)	2/2023	6/2027 (N.A.) {6/2025}	352.41 (N.A.) {352.41}	35.70	15
	ROAD TRANSPORT AND HIGHWAYS	486	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P (NHAI) (N24000835)	3/2018	12/2020 (Dec-24) {3/2024}	1,484.30 (N.A.) {2,182.41}	1,237.02	100
		487	CONSTRUCTION OF 4-LANE NH-344P- PACKAGE-4 (FROM KM 0+000 TO KM 29+600, 29.6KM), STARTING FROM BAWANA (NHAI) (N24001532)	11/2021	11/2023 (Jan-24) {8/2024}	694.00 (1,918.00) {1,500.00}	1,682.82	100
		488	CONSTRUCTION OF 4-LANE GREEN FIELD DELHI-AMRITSAR-KATRA EXPRESSWAY (NE-05) FROM JUSSUR KHERI ON KMP (NHAI) (N24001533)	11/2020	12/2023 (N.A.) {10/2024}	1,690.23 (N.A.) {2,010.17}	1,311.87	96.1
		489	CONSTRUCTION OF FOUR-LANE GREENFIELD DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH ROHTAK-PANIP (NHAI) (N24001534)	12/2020	1/2024 (Apr-24) {9/2024}	1,334.04 (N.A.) {1,334.00}	974.53	93.55

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		490	4-LANING OF GOHANA-SONIPAT (PKG-2) SECTION FROM KM 40.601 TO KM 78.837 (LENGTH = 38.236KM) OF NH-352 (NHA) (N24001535)	7/2020	7/2022 (May-24) {10/2024}	899.00 (1,882.46) {1,882.46}	1,123.98	91.76
		491	FOUR LANING OF JIND GOHANA GREENFIELD ALIGNMENT PACKAGE 1 IN THE STATE OF HARYANA UNDER HYBRID ANNUI (NHA) (N24001536)	7/2020	7/2022 (N.A.) {10/2024}	817.00 (1,605.00) {1,605.00}	1,025.56	97.1
		492	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE- I PKG-III) F (NHA) (N24001633)	12/2020	12/2023 (Feb-24) {10/2024}	1,430.88 (N.A.) {1,430.88}	1,035.60	95.72
		493	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE- I PKG-IV) FRO (NHA) (N24001634)	1/2021	12/2023 (Mar-24) {10/2024}	1,306.95 (N.A.) {1,306.95}	942.46	94.83
		494	4 LANING OF JAGADHRI TAJEWALA ROAD SECTION OF NH 907 (OLD NH 73A) UNDER NH(O) (PKG 1) IN THE STATE O (NHA) (N24001635)	3/2022	2/2025 (N.A.) {2/2025}	1,269.50 (N.A.) {1,269.50}	182.00	46
		495	SIX LANNING OF MANDI DABWALI (PUNJAB/HARYANA BORDER)- CHAUTALA ROAD SECTION FROM PROPOSED MANDI DABW (NHA) (N24001672)	1/2021	1/2024 (Sep-24) {9/2024}	864.27 (864.00) {864.27}	586.82	99.96
		496	4- LANING OF ROHTAK-JIND SECTION FROM KM. 307+000 TO KM. 347+800 OF NH-71 AND CONNECTING LINK FROM K (NHA) (N24001673)	3/2020	3/2023 (Nov-24) {11/2024}	510.97 (N.A.) {510.97}	529.00	88

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		497	CONSTRUCTION OF GURGAON - PATAUDI - REWARI SECTION OF NH- 352W (DESIGN LENGTH 46.11 KM) AS FEEDER ROU (NHAI) (N24001774)	12/2020	11/2023 (N.A.) {6/2024}	1,524.03 (N.A.) {1,524.03}	1,075.15	58.09
		498	CONSTRUCTION OF PROPOSED REWARI BYPASS (DESIGN LENGTH 14.4 KM) NH- 11 AS A FEEDER ROUTE IN THE STATE (NHAI) (N24001775)	2/2020	1/2023 (Dec-24) {12/2024}	808.31 (N.A.) {958.00}	805.10	99.51
		499	DWARKA EXPRESSWAY PKG-III (DELHI/HR BORDER TO START OF ROB GURUGRAM) (NHAI) (N24001780)	1/2018	11/2020 (Dec-24) {3/2024}	2,228.00 (N.A.) {2,228.00}	1,411.27	100
		500	CONSTRUCTION OF 8LANE EXPRESSWAY NE4 STARTING BEFORE KMP EXPRESSWAY AND ENDS AT CH. 47+000 NEAR KHAN (NHAI) (N24001783)	11/2018	9/2021 (N.A.) {10/2024}	2,252.75 (N.A.) {2,252.75}	1,223.07	99.95
		501	CONSTRUCTION OF EIGHT LANE EXPRESSWAY STARTING AT CH. 47+000 NEAR KHANPUR GHATI AND ENDS AT HARYANA (NHAI) (N24001784)	11/2018	9/2021 (N.A.) {10/2024}	1,935.61 (N.A.) {1,935.61}	856.41	99.9
		502	UPGRADATION OF EXISTING 4 LANE ISMAILABAD-AMBALA SECTION (KM. 0+000 TO KM 42+500) (PART OF AMBALA- KO (NHAI) (N24002037)	1/2023	12/2025 (N.A.) {12/2025}	609.32 (609.00) {609.00}	58.37	19
		503	CONSTRUCTION OF 6-LANE GREENFIELD KARNAL RING ROAD STARTING FROM NH-44 NEAR VILLAGE SHAMGARH (DESIGN (NHAI) (N24002038)	11/2022	8/2025 (N.A.) {8/2025}	1,691.45 (1,998.00) {1,998.00}	590.77	42

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		504	CONSTRUCTION OF 6-LANE GREENFIELD AMBALA RING ROAD STARTING FROM JUNCTION WITH SHAMLI-AMBALA SECTION (NHAI) (N24002039)	2/2023	10/2025 (N.A.) {10/2025}	1,088.64 (1,178.00) {1,178.00}	316.25	27.23
		505	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM RANIPUR BARS (SAHARANPUR DISTRICT) TO ADHOYA (NHAI) (N24002040)	4/2022	5/2025 (N.A.) {5/2028}	1,554.21 (N.A.) {1,554.21}	409.06	36.1
		506	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM ADHOYA MUSALMANA (AMBALA DISTRICT) TO SADOPUR (NHAI) (N24002041)	4/2022	5/2025 (N.A.) {5/2025}	1,491.71 (N.A.) {1,491.71}	606.10	35.22
		507	CONSTRUCTION OF 4-LANING OF BHIWANI HANSI ROAD SECTION OF NH 148B (DESIGN LENGTH 42.934 KM) UNDER BH (NHAI) (N24002042)	11/2022	12/2025 (N.A.) {12/2025}	1,322.13 (N.A.) {1,322.13}	156.12	43.18
		508	CONSTRUCTION OF 4-LANE GREENFIELD JALBEHRA - SHAHBAD SECTION OF NH 152G FROM KM 0+000 TO KM 22+850 (NHAI) (N24002043)	3/2022	6/2025 (N.A.) {6/2025}	927.22 (N.A.) {927.22}	354.10	52.11
		509	4L AMBALA - KALAAMB FROM KM. -0.800 TO KM. 33.015 OF OLD NH-72 (NHAI) (N24002044)	6/2023	6/2025 (N.A.) {6/2025}	629.16 (N.A.) {629.16}	121.00	69
		510	6L ACCESS CONTROLLED HIGHWAY FROM JN WITH JAIPUR PUSHTA ROAD TO JN WITH SECTOR 62/65 DIVIDING ROAD (NHAI) (N24002047)	5/2020	8/2023 (N.A.) {10/2024}	1,328.07 (2,346.00) {2,346.00}	1,087.16	97.12

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		511	CONSTRUCTION OF GREENFIELD CONNECTIVITY TO JEWAR INTERNATIONAL AIRPORT FROM DND FARIDABAD BALLABHGAR (NHAI) (N24002048)	7/2022	6/2025 (N.A.) {6/2025}	2,414.67 (2,898.00) {2,898.00}	1,028.68	25.6
HIMACHAL PRADESH	DEPARTMEN T OF HIGHER EDUCATION	512	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR (CPWD EDUCATION) (N42000008)	9/2018	6/2022 (Dec-24) {1/2025}	392.51 (N.A.) {446.43}	295.98	88
		513	CONSTRUCTION OF PERMANENT CAMPUSES OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND DHARAMSHAL (CPWD) (N42000011)	3/2021	8/2022 (Jul-25) {7/2025}	512.37 (512.37) {512.37}	109.56	52
	HEALTH AND FAMILY WELFARE	514	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH (CPWD FOR HEALTH) (N28000127)	12/2018	6/2021 (Aug-26) {8/2026}	260.00 (371.78) {371.78}	46.24	7
	POWER	515	PARBATI HEP (4X200 MW) (NHPC) II (NHPC) (180100210)	9/2002	9/2009 (N.A.) {12/2024}	3,919.59 (N.A.) {12,160.00}	11,879.05	97.91
		516	LUHRI HYDROELECTRIC PROJECT (STAGE1) (SJVN) (N18000279)	11/2020	1/2026 (N.A.) {6/2027}	1,810.56 (N.A.) {3,060.71}	1,506.13	50.99
		517	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) (SJVN) (N18000291)	10/2020	11/2025 (N.A.) {5/2026}	687.97 (N.A.) {1,426.00}	696.74	59.38
		518	SUNNI DAM HYDRO ELECTRIC PROJECT (SJVN) (N18000344)	1/2023	4/2028 (N.A.) {4/2028}	2,614.51 (N.A.) {2,614.51}	771.43	25.67
	RAILWAYS	519	BHANUPALI-BILASPUR BERI NL (RVNL) (N22000273)	4/2008	12/2026 (N.A.) {3/2025}	2,966.99 (N.A.) {6,753.42}	5,190.99	49

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	520	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH (NHAI) (N24000613)	9/2016	7/2020 (N.A.) {8/2024}	1,273.71 (N.A.) {1,478.61}	1,383.76	92.46
		521	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M (NHAI) (N24000852)	3/2018	5/2021 (Dec-24) {12/2024}	478.74 (N.A.) {1,514.46}	1,349.59	83
		522	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA (MoRTH) (N24001381)	8/2020	4/2021 (N.A.) {4/2021}	272.98 (N.A.) {272.98}	132.82	97
		523	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA- ASHYARI SECTION (KM 25.000 TO KM 50. (MoRTH) (N24001382)	8/2020	3/2021 (N.A.) {7/2024}	242.80 (N.A.) {242.80}	81.08	83
		524	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 (MoRTH) (N24001383)	8/2020	4/2021 (N.A.) {4/2021}	349.20 (N.A.) {349.20}	239.34	100
		525	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF ASHYARI- SHRI KYARI SECTION (KM 50.000 TO K (MoRTH) (N24001422)	2/2021	9/2021 (N.A.) {7/2024}	345.89 (N.A.) {345.89}	147.63	80
		526	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HAMIRPUR- KARNOHAL SECTION (KM 141.000 TO K (MoRTH) (N24001447)	8/2020	12/2024 (N.A.) {12/2024}	371.93 (N.A.) {371.93}	187.96	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		527	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF KALWAHAN-MANDI SECTION (KM 208.950 TO KM 2 (MoRTH) (N24001470)	8/2020	4/2025 (N.A.) {4/2025}	314.32 (N.A.) {314.32}	68.39	0
		528	REHABILITATION AND UPGRADING FROM 2 L TO 4 L FROM BHANGBAR(NEAR RANITAL) TO KANGRA BYPASS SECTION OF (NHAI) (N24001808)	3/2021	12/2024 (Dec-24) {12/2024}	1,322.95 (1,442.47) {1,442.47}	762.01	77.73
		529	CONVERSION OF PARTIALLY EXCAVATED ESCAPE TUNNEL TO UNIDIRECTIONAL TWO LANE TUNNEL (INCLUDING CONSTRU (NHAI) (N24001809)	5/2022	3/2024 (Dec-24) {12/2024}	469.95 (N.A.) {280.00}	289.24	95.68
		530	4L SUNDER NAGAR BYPASS FROM KM173.900 TO KM 179.600 OF NH-21 IN THE STATE OF HP (NHAI) (N24001810)	2/2022	6/2024 (N.A.) {6/2024}	190.60 (N.A.) {163.00}	103.48	100
		531	4L OF MO - SIHUNI FROM KM. 42.00 TO KM. 51.00 OF OLD NH-20 (NEW NH-154) (PACKAGE-IB) (NHAI) (N24001811)	4/2021	6/2024 (N.A.) {9/2024}	583.93 (704.30) {704.30}	170.71	98.13
		532	4L OF HP/PUNJAB BO4L OF HP/PUNJAB BORDER - MO FROM KM. 11.00 TO KM. 42.00 OF OLD NH-20 (NEW NH-154) (NHAI) (N24001812)	3/2021	5/2024 (N.A.) {12/2025}	1,002.11 (1,361.79) {1,361.79}	188.77	40.97
		533	4L OF END OF PINJORE BYPASS - BADDI - NALAGARH SECTION (KM. 4.200 TO KM. 35.370) OF NH21A (NHAI) (N24001813)	7/2021	9/2024 (N.A.) {9/2024}	1,692.05 (N.A.) {1,692.05}	942.14	21.6

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		534	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS-5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001915)	3/2021	6/2026 (N.A.) {6/2026}	230.54 (N.A.) {230.54}	0.00	20
		535	IMPROVEMENT/CONSTRUCTION OF EXISTING CLASS 5 ROAD TO NH INTERMEDIATE LANE SPECIFICATION WITH HARD SH (BRO) (N24001916)	3/2021	5/2026 (N.A.) {5/2026}	314.67 (N.A.) {314.67}	0.00	29
		536	PKG NAME: 4L OF KATHLIGHAT TO SHAKRAL VILLAGE FROM KM 128.835 TO KM 146.300 OF NH- 5 (SHIMLA BYPASS (NHAI) (N24002049)	3/2022	4/2026 (N.A.) {4/2026}	1,703.48 (2,278.00) {2,278.00}	651.98	14.5
		537	REHABILITATION AND UPGRADATION TO 4L CONFIGURATION and STRENGTHENING OF SIHUNI TO RAJOL FROM KM 51.0 (NHAI) (N24002050)	2/2022	9/2025 (N.A.) {9/2025}	696.65 (698.46) {698.46}	326.95	40.25
		538	CONSTRUCTION OF NEW 2 LANE WITH PAVED SHOULDER OF HAMIRPUR BYPASS (PACKAGE IVA) OF NH-88 (NEW NH-103 (NHAI) (N24002051)	7/2022	10/2025 (N.A.) {10/2025}	739.39 (N.A.) {739.39}	268.70	43.26
		539	REHABILITATION AND UP-GRADATION OF EXISTING ROAD TO 2L PS FROM END OF HAMIRPUR BYPASS (NEAR CHILBAHA (NHAI) (N24002052)	2/2022	4/2025 (N.A.) {4/2025}	1,146.19 (N.A.) {1,146.19}	867.07	47.37
	URBAN DEVELOPMENT	540	CONSTRUCTION OF PERMANENT CAMPUS OF CENTRAL UNIVERSITY OF HIMACHAL PRADESH AT DEHRA AND JADRANGAL (D (CPWD) (N28000154)	4/2022	11/2024 (N.A.) {11/2024}	512.34 (N.A.) {512.34}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
JAMMU AND KASHMIR	CIVIL AVIATION	541	JAMMU - CONSTRUCTION OF NEW CIVIL ENCLAVE (AAI) (N04000107)	7/2022	6/2026 (N.A.) {6/2026}	861.37 (N.A.) {861.37}	56.09	11
	DEPARTMEN T OF HIGHER EDUCATION	542	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) (CPWD EDUCATION) (N28000130)	3/2019	7/2022 (Aug-24) {8/2024}	424.93 (500.91) {500.91}	467.62	98
		543	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) (CPWD EDUCATION) (N28000131)	1/2018	4/2023 (Sep-24) {9/2024}	676.00 (1,148.68) {1,144.68}	64.75	96
	HEALTH AND FAMILY WELFARE	544	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR (CPWD FOR HEALTH) (N21000029)	3/2019	9/2023 (Oct-24) {10/2024}	1,404.00 (1,642.00) {1,642.00}	1,415.98	99.5
		545	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR (CPWD FOR HEALTH) (N28000150)	3/2019	9/2025 (Jan-25) {11/2025}	1,828.00 (1,577.00) {1,577.00}	1,099.94	57
	PETROLEUM	546	SETTING UP A COMMON USER PETROLEUM TERMINAL AT JAMMU FOR RE-SITEMENT OF EXISTING DEPOTS OF PSU OMCS (BPCL) (N16000500)	4/2021	3/2025 (N.A.) {3/2025}	676.89 (N.A.) {676.89}	439.01	46.5
		547	CGD PROJECT AT JAMMU DISTRICTS (IOCL) (N16000527)	3/2022	3/2032 (Sep-34) {9/2034}	538.00 (N.A.) {538.00}	4.16	0.4
	POWER	548	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) (CVPPPL) (N18000172)	10/2014	4/2020 (Jul-25) {9/2026}	8,112.12 (N.A.) {8,112.12}	4,943.12	59
		549	KIRU HYDRO ELECTRIC PROJECT (CVPPPL) (N18000278)	3/2019	8/2024 (N.A.) {9/2026}	4,287.59 (N.A.) {4,287.59}	1,844.78	42.63
		550	RATLE HE PROJECT (NHPC) (N18000324)	2/2021	2/2026 (N.A.) {12/2026}	5,281.94 (N.A.) {5,281.94}	784.25	16.08
		551	KWAR HE PROJECT (CVPPPL) (N18000363)	5/2022	11/2026 (N.A.) {12/2027}	4,526.12 (N.A.) {4,526.12}	738.69	12.13

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>RAILWAYS</u>	552	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR (NR) (220100133)	3/1995	11/2002 (Dec-24) {12/2024}	2,500.00 (37,012.26) {42,500.00}	40,742.04	99
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	553	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A (NHAI) (N24000488)	12/2015	12/2018 (Nov-24) {11/2024}	2,136.97 (2,644.00) {2,644.00}	2,377.88	99.5
		554	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE (NHAI) (N24000717)	12/2017	7/2021 (Sep-24) {9/2024}	1,471.75 (1,471.75) {1,903.98}	1,605.21	97.08
		555	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA (NHIDCL) (N24000868)	3/2018	7/2021 (Aug-23) {12/2024}	253.44 (N.A.) {253.44}	179.18	77.58
		556	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA (NHIDCL) (N24001253)	12/2019	12/2023 (N.A.) {7/2024}	2,680.42 (N.A.) {2,680.42}	0.00	95.05
		557	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D (NHIDCL) (N24001256)	8/2020	9/2026 (N.A.) {9/2026}	6,808.69 (N.A.) {6,808.69}	3,013.84	49.92
		558	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA- KHEL (NHIDCL) (N24001264)	7/2020	4/2022 (Oct-24) {12/2024}	228.39 (N.A.) {228.39}	63.12	84.91
		559	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K (NHIDCL) (N24001266)	7/2020	4/2022 (Nov-23) {12/2024}	210.79 (N.A.) {210.79}	64.28	86.38

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		560	KHELLANI-KHANABAL PKG-1 (NHIDCL) (N24001323)	3/2021	9/2022 (Oct-24) {12/2024}	486.45 (N.A.) {486.45}	120.08	94.36
		561	KHELLANI-KHANABAL PKG-3 (NHIDCL) (N24001341)	3/2021	12/2022 (Jul-24) {10/2024}	398.51 (N.A.) {398.51}	75.26	90.07
		562	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 (NHIDCL) (N24001342)	3/2021	12/2022 (N.A.) {7/2024}	260.40 (N.A.) {260.40}	191.88	93.8
		563	KHELLANI-KHANABAL PKG-2 (NHIDCL) (N24001394)	7/2021	2/2023 (Jun-25) {12/2025}	512.43 (N.A.) {512.43}	65.31	48.21
		564	KHELLANI-KHANABAL PKG-4 (NHIDCL) (N24001395)	7/2021	8/2023 (Jul-24) {12/2025}	859.67 (N.A.) {859.67}	163.52	37.93
		565	KHELLANI-KHANABAL PKG-5 (NHIDCL) (N24001396)	7/2021	2/2023 (Jul-24) {3/2025}	497.09 (N.A.) {497.09}	142.12	70.58
		566	GOHA-KHELLANI PKG-3 (NHIDCL) (N24001397)	2/2021	3/2023 (Oct-24) {12/2024}	431.28 (N.A.) {431.28}	296.98	87.9
		567	BALANCE WORKS OF FOUR LANING FROM RAMBAN KM 151.00 TO BANIHAL KM 187.00 OF NH-1A (NOW NH-44) WITH VA (NHAI) (N24001472)	9/2021	12/2023 (Oct-24) {10/2024}	811.19 (N.A.) {811.19}	799.00	99
		568	CONSTRUCTION OF FOUR LANE RINGROAD BYPASS SRINAGAR CITY (NHAI) (N24001511)	3/2021	2/2024 (Aug-24) {6/2025}	2,919.96 (N.A.) {2,919.96}	2,147.28	58.8
		569	FOUR LANING OF JAMMU-AKHNOOR PKG-1 (NHIDCL) (N24001543)	7/2022	1/2025 (N.A.) {1/2025}	245.34 (N.A.) {245.34}	46.49	31.02
		570	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XVI) EXISTING JAKH (VIJAYPUR)-KUNJWANI SECTION OF NH- 4 (NHAI) (N24001550)	9/2021	9/2024 (Sep-25) {9/2025}	1,821.72 (1,917.32) {1,917.32}	791.93	61.53

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		571	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XIV) FROM JUNCTION WITH PATHANKOT-GURDASPUR ROAD (NH-5 (NHA/) (N24001551)	10/2021	9/2024 (Jul-25) {7/2025}	3,044.02 (3,044.02) {3,044.02}	1,232.00	48.53
		572	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-II PKG-XV) [JUNCTION WITH HIRANAGAR ROAD NEAR VILLAGE GURHA B (NHA/) (N24001552)	10/2021	9/2024 (Jul-25) {7/2025}	2,714.95 (2,714.95) {2,714.95}	1,468.77	64.6
		573	CORRIDOR EFFICIENCY IMPROVEMENT INCLUDING REMOVAL OF BLACK SPOTS IN LAKHANPUR - SAMBA SECTION OF NH- (NHA/) (N24001619)	8/2022	6/2024 (Jun-25) {6/2025}	200.05 (200.05) {208.92}	93.73	38.5
		574	CONSTRUCTION OF TUNNELS/VIADUCTS AT IDENTIFIED SLIDING/SLIP ZONES AT KM.130.550 TO KM.130.750; KM. (NHA/) (N24001620)	9/2021	10/2023 (May-25) {5/2025}	442.14 (N.A.) {442.14}	245.08	19.88
		575	4L OF KM.165.092 TO KM.171.855 (NORTH BOUND) AND FROM KM.166.895 TO KM.173.638 (SOUTH BOUND), EXCL. (NHA/) (N24001621)	7/2021	8/2024 (Jun-25) {6/2025}	614.48 (N.A.) {614.48}	151.85	7
		576	4L TWIN TUBE TUNNEL INCLUDING APPROACHES FROM DIGDOL TO KHUNI NALLAH (NORTH BOUND CONNECTING WITH EX (NHA/) (N24001622)	7/2021	6/2024 (Jun-25) {6/2025}	1,401.87 (N.A.) {1,401.87}	516.78	0
		577	BANIHAL BYPASS (DELINKED FROM SRINAGAR - BANIHAL) FROM KM. 187.00 TO KM. 189.350 (NHA/) (N24001623)	1/2020	1/2024 (Dec-24) {12/2024}	336.01 (N.A.) {336.01}	175.08	34

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		578	CONSTRUCTION OF EMERGENCY LANDING FACILITY FROM KM. 246.60 TO KM. 249.70 ON SRINAGAR - BANIHAL SECTI (NHAI) (N24001624)	7/2019	10/2020 (Apr-23) {9/2024}	157.05 (N.A.) {157.05}	134.60	100
		579	4L OF TWIN TUBE TUNNEL CONFIGURATION INCLUDING APPROACHES FROM MAROG TO DIGDOL (FROM KM.154.210 TO K (NHAI) (N24001627)	7/2021	2/2025 (Feb-25) {2/2025}	1,912.17 (N.A.) {1,912.17}	37.21	0
		580	JAMMU - AKHNOOR SECTION OF NH 144A PKG-3B (NHIDCL) (N24001833)	7/2022	3/2025 (N.A.) {3/2025}	198.28 (N.A.) {198.28}	65.99	49.01
		581	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 102 TO KM 13 (BRO) (N24001897)	3/2021	7/2024 (N.A.) {12/2024}	642.24 (N.A.) {642.24}	469.60	92
		582	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 30.000 TO K (BRO) (N24001898)	7/2020	11/2024 (N.A.) {11/2024}	272.49 (N.A.) {272.49}	169.15	82.02
		583	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 134.95 TO KM (BRO) (N24001899)	2/2021	7/2024 (N.A.) {3/2025}	395.25 (N.A.) {395.25}	198.77	60
		584	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 49.150 TO KM (BRO) (N24001900)	3/2020	8/2024 (N.A.) {3/2025}	796.97 (N.A.) {796.97}	453.08	75

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		585	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHAINAGE KM 64.535 TO K (BRO) (N24001901)	3/2020	9/2023 (N.A.) {3/2025}	152.93 (N.A.) {152.93}	101.68	77
		586	CONSTRUCTION OF TWIN TUBE TUNNELS ON JAMMU KASHMIR RING ROAD (NH-244A) BETWEEN DESIGN CH. 50+600 TO (NHAI) (N24001926)	3/2023	6/2025 (N.A.) {6/2025}	939.86 (N.A.) {939.86}	235.63	36.46
		587	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDER FROM (DESIGN CH. 14+200 TO 24+400), (DESIGN CH. 35+300 TO (BRO) (N24001998)	6/2022	8/2025 (N.A.) {8/2025}	832.46 (N.A.) {823.46}	301.83	24.01
		588	2L NH-1 FROM KM 8.660 TO KM 33.775 (SUMBAL TO WAYUL) TO 4L DUAL CARRIAGEWAY NH STANDARD AS PART OF S (NHAI) (N24002059)	9/2022	6/2026 (N.A.) {6/2026}	1,183.60 (N.A.) {1,183.60}	121.14	2
		589	DELHI AMRITSAR KATRA EXPRESSWAY (PHASE-II PKG XVIII) DEVELOPMENT AND UPGRADATION OF FOUR LANE ACCESS (NHAI) (N24002060)	3/2023	11/2025 (N.A.) {11/2025}	1,107.00 (N.A.) {1,107.00}	77.75	13.83
		590	4/6L ACCESS CONTROL EXPRESSWAY FROM DESIGN CHAINAGE KM 515.000 TO 528.300 (KUNJWANI TO SIDHRA SECTIO (NHAI) (N24002061)	8/2022	6/2025 (N.A.) {6/2025}	2,474.47 (N.A.) {2,675.93}	715.57	17.5
		591	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM 162.800 TO KM (BRO) (N24002119)	10/2022	1/2026 (N.A.) {1/2026}	562.45 (N.A.) {562.45}	25.62	4
JHARKHAND	COAL	592	CHURI BENTI UG (0.81 MTY) (CCL) (N06000083)	8/2007	3/2011 (N.A.) {11/2024}	163.51 (N.A.) {163.51}	133.35	84.4

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		593	RAJRAPPA RCE OCP (3.0 MTY) (CCL) (N06000087)	12/2009	3/2016 (N.A.) {3/2025}	510.85 (N.A.) {510.85}	488.31	74.5
		594	MURAI DIH UG TURN-KEY PROJECT (BCCL) (N06000096)	2/2011	4/2014 (N.A.) {1/2026}	339.88 (N.A.) {339.88}	151.61	70
		595	MOONIDIH XV SEAM UG (BCCL) (N06000098)	8/2011	3/2019 (N.A.) {2/2026}	1,230.27 (N.A.) {1,230.27}	592.64	80
		596	MADHUBAND NLW WASHERY (BCCL) (N06000126)	8/2010	5/2014 (N.A.) {11/2023}	289.45 (N.A.) {302.00}	299.73	100
		597	CHITRA EAST (RCE) OCP (ECL) (N06000169)	8/2018	3/2024 (Mar-26) {3/2026}	513.98 (N.A.) {513.98}	182.90	51
		598	TETARIAKHAR EXPANSION OCP (CCL) (N06000186)	11/2019	3/2023 (N.A.) {3/2025}	243.52 (N.A.) {243.52}	44.35	46.6
		599	PACHWARA SOUTH COAL BLOCK (NLC) (N06000193)	7/2013	9/2028 (N.A.) {9/2028}	2,242.92 (2,242.90) {2,242.90}	223.28	43
		600	PATHERDIH 2.5 NLW COAL WASHERY (BCCL) (N06000194)	10/2015	4/2018 (N.A.) {6/2025}	334.27 (N.A.) {334.27}	121.65	40
		601	REVISED PROJECT REPORT MAGADH EXPANSION OCP (CCL) (N06000216)	8/2020	3/2028 (N.A.) {3/2028}	7,254.37 (N.A.) {7,254.37}	1,245.76	19
		602	EXPANSION PROJECT AMRAPALI OCP (CCL) (N06000217)	8/2020	3/2028 (N.A.) {3/2028}	5,136.15 (N.A.) {5,136.15}	686.05	19
		603	UCE OF EPR OF NORTH URIMARI OCP (CCL) (N06000218)	7/2021	3/2026 (N.A.) {3/2026}	778.80 (N.A.) {778.80}	683.05	75
		604	KOTRE BASANTPUR PACHMO OCP (CCL) (N06000237)	8/2020	3/2032 (N.A.) {3/2032}	625.40 (625.40) {625.40}	394.31	38
		605	CHANDRAGUPT OCP (CCL) (N06000238)	8/2020	3/2032 (N.A.) {3/2032}	973.50 (N.A.) {973.50}	7.95	12.4

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		606	SIRKA OCP (CCL) (N06000239)	5/2020	3/2025 (N.A.) {3/2025}	222.82 (N.A.) {222.82}	139.31	60
		607	JHARKHAND LAIYO OCP (CCL) (N06000240)	8/2020	3/2031 (N.A.) {3/2031}	764.57 (N.A.) {764.57}	145.80	20
		608	EPR TAPIN SOUTH OCP (CCL) (N06000241)	11/2020	3/2025 (N.A.) {3/2025}	230.41 (N.A.) {230.41}	18.14	18.3
		609	EPR PUNDI OCP (CCL) (N06000242)	11/2020	3/2027 (N.A.) {3/2027}	713.35 (N.A.) {713.35}	236.57	39
		610	EPR ROHINI KARKATA OCP (CCL) (N06000243)	1/2021	3/2028 (N.A.) {3/2028}	1,020.42 (N.A.) {1,020.42}	82.92	11.7
		611	EXPANSION OF KONAR OCP (CCL) (N06000245)	1/2022	3/2032 (N.A.) {3/2032}	799.34 (N.A.) {799.34}	384.03	32
		612	EXPANSION OF KARO OCP (CCL) (N06000246)	1/2022	3/2026 (N.A.) {3/2026}	908.47 (N.A.) {908.47}	145.14	17.2
		613	EXPANSION OF ASHOK OCP (CCL) (N06000247)	5/2021	3/2028 (N.A.) {3/2028}	2,898.28 (N.A.) {2,898.28}	175.01	12.1
		614	AMALGAMATED NTST KUJAMA OCP 8.5 MTY (BCCL) (N06000273)	1/2023	3/2030 (N.A.) {3/2030}	4,011.85 (N.A.) {4,011.85}	389.65	24.1
		615	HURA C OC (ECL) (N06000275)	8/2022	3/2029 (N.A.) {3/2029}	859.41 (N.A.) {859.41}	33.33	62
	DEPARTMEN T OF HIGHER EDUCATION	616	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD (CPWD EDUCATION) (N28000067)	9/2012	3/2016 (N.A.) {3/2016}	171.86 (N.A.) {171.86}	175.21	0
	PETROLEUM	617	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK (ONGC) (N16000239)	12/2015	3/2023 (Mar-24) {3/2025}	823.27 (1,137.79) {1,137.79}	1,046.44	83.1
		618	DEVELOPMENT OF JHARIA CBM BLOCK (PHASE-1) (ONGC) (N16000445)	11/2019	1/2024 (Mar-24) {12/2024}	431.00 (N.A.) {431.00}	162.34	56.4

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		619	LAYING OF NATURAL GAS PIPELINE FROM HAZARIBAGH TO RANCHI (IOCL) (N16000480)	3/2023	2/2026 (N.A.) {2/2026}	202.07 (N.A.) {202.07}	45.05	33.42
		620	CGD PROJECT IN BIHAR JHARKHAND (HPCL) (N16000497)	6/2022	6/2030 (N.A.) {6/2030}	1,377.00 (N.A.) {1,377.00}	178.29	17.7
	POWER	621	NORTH KARANPURA STPP (3X660 MW) (NTPC) (N18000177)	2/2014	6/2019 (Oct-22) {12/2024}	16,242.90 (N.A.) {17,007.00}	15,361.62	85
		622	PATRATU STPP-I (3X800MW) (NTPC) (N18000275)	11/2017	3/2023 (N.A.) {11/2025}	17,112.00 (N.A.) {17,112.00}	13,151.45	68
		623	BADAM COAL MINING PROJECT (NTPC) (N18000367)	2/2019	10/2024 (N.A.) {10/2024}	501.79 (N.A.) {501.79}	40.35	0
		624	KERANDARI COAL MINING PROJECT (NTPC) (N18000370)	9/2015	11/2019 (N.A.) {11/2019}	1,553.00 (N.A.) {2,804.00}	0.00	0
	RAILWAYS	625	KODERMA-TILAIYA (NL), ECR (ECR) (220100305)	4/2002	(N.A.) {3/2025}	459.91 (1,625.87) {1,700.00}	1,757.62	70
		626	BONDAMUNDA RANCHI DOUBLING (SER) (N22000396)	3/2016	3/2021 (N.A.) {6/2026}	1,724.20 (3,029.04) {3,029.04}	2,162.68	80
		627	LODHMA TO PISKA LINK LINE BY PASSING HATIA/RANCHI WITH Y CONNECTION (17.2 KM) (SER) (N22000508)	4/2018	6/2022 (N.A.) {6/2026}	428.65 (N.A.) {472.50}	272.44	2
		628	DOUBLING OF PRADHANKHUNTA JN - PATHERDIH BAZAR-BHOJUDIH (ECR) (N22000529)	11/2022	11/2027 (N.A.) {11/2027}	202.00 (349.22) {349.22}	6.62	0
		629	KHARAGPUR-ADITYAPUR - 3RD LINE (132 KM) (RVNL) (N22000595)	12/2015	3/2025 (N.A.) {3/2025}	1,116.00 (N.A.) {3,270.07}	2,875.04	98
		630	3RD LINE BETWEEN DHANBAD SONNAGAR (RVNL) (N22000599)	11/2016	3/2026 (N.A.) {3/2026}	8,975.00 (N.A.) {7,906.38}	4,630.47	90

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		631	GARHWA ROAD - RAIL OVER RAIL (ECR) (N22000610)	3/2017	3/2024 (N.A.) {3/2025}	262.71 (N.A.) {262.71}	196.01	73
		632	GOMOH - FLYOVER FOR DOWN TRAINS (ECR) (N22000611)	1/2018	12/2025 (N.A.) {12/2025}	487.73 (N.A.) {487.73}	303.35	16
	ROAD TRANSPORT AND HIGHWAYS	633	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 (NHAI) (N24000725)	1/2018	11/2021 (Sep-24) {9/2024}	273.46 (N.A.) {276.17}	255.63	97
		634	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION (NHAI) (N24000726)	1/2018	11/2021 (Jun-25) {6/2025}	1,155.16 (N.A.) {950.49}	629.74	69
		635	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K (NHAI) (N24000854)	3/2018	3/2021 (Dec-24) {12/2024}	1,005.08 (1,073.10) {1,073.10}	699.05	81
		636	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I (MoRTH) (N24001216)	12/2016	9/2021 (Dec-24) {12/2024}	196.00 (N.A.) {196.00}	164.21	90
		637	HARIHARGANJ TO PARWA MODE SECTION FROM KM 23.284 TO KM 57.049 OF NH-98 (NHAI) (N24001589)	9/2020	3/2024 (Dec-24) {12/2024}	755.26 (N.A.) {1,039.00}	546.41	82.5
		638	4L FROM KM 196.87 (SANKHA) TO KM 219.6 (KAJURI) ON NH-75 [REHLA / GARHWA BYPASS] (NHAI) (N24001590)	9/2020	10/2023 (Dec-24) {12/2024}	748.99 (N.A.) {903.00}	808.09	99.98
		639	ELEVATED CORRIDOR IN RANCHI CITY FROM KM 0.00 TO KM 3.260 OF NH-75 INCLUDING DOWN RAMP ON NH-23 FROM (NHAI) (N24001594)	2/2022	1/2025 (N.A.) {1/2025}	534.73 (N.A.) {534.73}	14.87	70

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		640	4L OF PALMA TO GUMLA SECTION OF NH23 FROM KM. 26.00 TO KM. 89.170 ON HAM MODE IN THE STATE OF JHARKH (NHA) (N24001595)	8/2020	3/2024 (N.A.) {10/2024}	1,034.00 (1,785.18) {1,785.18}	41.50	81.72
		641	4L OF MIRZA CHAUKI TO FARKKA SECTION OF NH80 FROM KM 215.00 TO KM 260.00 ON HAM MODE IN THE STATE OF (NHA) (N24001596)	11/2021	7/2023 (Jun-25) {6/2025}	1,302.72 (1,504.80) {1,504.80}	798.61	54.47
		642	BALANCE WORK OF RANCHI-MAHULIA SECTION OF NH-33 FROM KM 113.730 (VIKAS) TO KM 140.000 (RAMPUR) (PKG- (NHA) (N24001597)	1/2019	12/2020 (Jul-24) {7/2024}	466.55 (518.00) {466.55}	0.00	99.25
		643	FOUR LANING WITH PAVED SHOULDER OF SECTION FROM KM 53.600 (GOLA ON NH-320) TO KM 81.446 (ORMANJHI ON (NHA) (N24001854)	6/2023	6/2025 (N.A.) {6/2025}	1,214.93 (1,324.95) {1,324.95}	650.50	42
		644	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM 0.00 TO 44.00 (KURU-GHAGHRA SECTION) OF NH-143A INCLU (MoRTH) (N24001922)	2/2020	8/2023 (Dec-24) {12/2024}	153.01 (N.A.) {153.01}	83.63	84
		645	WIDENING AND STRENGTHENING OF EXISTING PAVEEMNT TO TWO LANE WITH PAVED SHOULDERS FROM KM 116.00 TO K (MoRTH) (N24001923)	1/2022	7/2024 (Dec-24) {12/2024}	315.21 (N.A.) {315.21}	75.24	75
		646	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDER/TWO LANE+ PAVED SHOULDER WITH SERVICE ROA (MoRTH) (N24001924)	3/2022	8/2025 (N.A.) {8/2025}	514.22 (N.A.) {514.22}	10.49	6

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		647	WIDENING AND STRENGTHENING/RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDER/ TWO LANE WITH PAVED SHOUL (MoRTH) (N24001925)	3/2022	8/2025 (N.A.) {8/2025}	423.18 (N.A.) {423.18}	0.11	0
		648	FOUR LANING OF KHAJURI TO WYNDHAMGANJ FROM KM 219.600 TO KM 260.483 ON NH-75 PKG SEC-V ON HAM (NHAI) (N24002053)	4/2022	9/2025 (N.A.) {9/2025}	1,232.00 (1,343.00) {1,400.00}	343.03	47.18
		649	FOUR LANING OF BHOGU TO SANKHA FROM KM 147.450 TO KM 196.870 ON NH- 75 PKG SEC-III (NHAI) (N24002054)	10/2022	11/2025 (N.A.) {11/2025}	1,390.77 (1,391.00) {1,600.00}	196.32	52.05
		650	FOUR LANING OF BASUKINATH- DEOGHAR SECTION OF NH-114A FROM KM 85.081 TO KM 130.240 UNDER NHDP PHASE-I (NHAI) (N24002055)	3/2023	12/2025 (N.A.) {12/2025}	1,444.94 (N.A.) {1,444.94}	0.00	0
		651	BHARATMALA PARIYOJANA OF BOKARO JAINA MORE - GOLA SECTION OF NH-320 FROM KM. 21.110 TO KM. 53.600 IN (NHAI) (N24002056)	6/2020	6/2025 (N.A.) {6/2025}	964.64 (N.A.) {964.64}	362.33	25.7
		652	FOUR LANING OF MEHGAMA HANSDIHA SECTION OF NH-33 FROM EXISTING KM 41.900 TO 93.000 IN THE STATE OF J (NHAI) (N24002057)	12/2022	5/2025 (N.A.) {5/2025}	1,443.77 (N.A.) {1,443.77}	0.00	0
	STEEL	653	NEW SINTER PLANT AT BOKARO STEEL PLANT (SAIL) (N12000095)	3/2015	10/2017 (Dec-21) {11/2026}	1,034.01 (N.A.) {1,034.01}	871.85	51.74
		654	REVAMPING OF OLD SUB SYSTEM OF BLAST FURNACE 3 AT BOKARO STEEL PLANT (SAIL) (N12000129)	9/2023	7/2025 (N.A.) {7/2025}	513.82 (N.A.) {513.82}	74.46	40

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
KARNATAKA		655	REBUILDING OF COKE OVEN BATTERY NO.6 OF BOKARO STEEL PLANT (SAIL) (N12000133)	11/2023	11/2026 (N.A.) {11/2026}	627.31 (N.A.) {627.31}	50.84	18
		656	REPLACEMENT OF REMAINING 04 NOS. OF BATTERY CYCLONES WITH 04 NOS. OF ESPS IN SINTER PLANT-1 AT BSL (SAIL) (N12000135)	3/2024	6/2026 (N.A.) {6/2026}	260.37 (N.A.) {260.37}	0.00	1.5
	CIVIL AVIATION	657	BELAGAVI AIRPORT- EXPANSION OF TERMINAL BUILDING AND ASSOCIATED WORKS (AAI) (N04000105)	6/2023	2/2026 (N.A.) {2/2026}	322.45 (N.A.) {322.45}	40.61	16
		658	HUBBALI AIRPORT - CONSTRUCTION OF NEW DOMESTIC TERMINAL BUILDING AND MISCELLANEOUS WORKS (AAI) (N04000108)	6/2023	2/2026 (N.A.) {1/2026}	320.47 (N.A.) {320.47}	14.07	13
	DEPARTMEN T OF HIGHER EDUCATION	659	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) (CPWD EDUCATION) (N42000006)	7/2019	3/2022 (Oct-22) {3/2023}	851.00 (851.00) {851.00}	886.26	100
		660	ADDITIONAL INFRASTRUCTURE AT IISC BANGALORE SH RCC MONOLITHIC FOR MEN WOMEN HOSTEL (CPWD) (N42000010)	8/2021	2/2024 (Nov-24) {11/2024}	316.25 (N.A.) {316.25}	333.42	94
	PETROLEUM	661	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE (HPCL) (N16000369)	12/2018	12/2022 (Mar-25) {3/2025}	854.00 (854.00) {854.00}	618.55	90
		662	REVAMPING, AUGMENTATION OF FACILITIES AT EXISTING PORT TERMINAL AT MANGALORE (IOCL) (N16000437)	1/2022	7/2025 (Dec-25) {12/2025}	463.00 (500.62) {500.62}	170.51	56.2

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		663	POWER SYSTEM UPGRADATION PROJECT (MANGALORE REFIN) (N16000509)	10/2023	2/2026 (N.A.) {2/2026}	385.00 (N.A.) {385.00}	57.52	28.87
		664	DEMO PLANT FOR PRODUCTION OF BIO- ATF (MANGALORE REFIN) (N16000536)	3/2024	3/2027 (N.A.) {3/2027}	364.00 (N.A.) {364.00}	5.25	0
	POWER	665	TS FOR INTRGRATION OF RE ZONE (PHASE II) IN KOPPAL II (PHASE A&B) AND GADAG II (PHASE A) IN KARNATAK (PGCIL) (N18000385)	12/2023	12/2025 (N.A.) {12/2025}	2,889.00 (N.A.) {2,889.00}	0.00	0
		666	TS FOR SOLAR ENERGY ZONE IN BIDAR (2500MW), KARNATAKA [BIDAR TRANSMISSION LTD] (PGCIL) (N18000388)	2/2024	2/2026 (N.A.) {2/2026}	2,148.00 (N.A.) {2,148.00}	0.00	3
	RAILWAYS	667	TUMKUR-CHITRADURGA-DAVENGERE NL (SWR) (N22000256)	4/2011	(N.A.) {12/2027}	1,801.01 (N.A.) {1,801.01}	324.85	12
		668	BAGALKOT-KUDACHI NL (SWR) (N22000258)	4/2010	3/2016 (N.A.) {12/2026}	986.30 (1,378.00) {1,378.00}	537.70	34
		669	HOSPET-HUBLI-LONDA-VASCODAGAMA DL (RVNL) (N22000297)	4/2010	3/2023 (N.A.) {12/2026}	2,127.00 (N.A.) {3,692.60}	3,481.82	86
		670	GADAG-WADI NL (SWR) (N22000299)	4/2013	12/2018 (N.A.) {12/2027}	2,841.84 (N.A.) {2,841.84}	1,203.98	28
		671	MARIKUPPAM - KUPPAM (SWR) (N22000308)	4/2012	3/2016 (N.A.) {12/2026}	279.54 (296.72) {296.72}	99.49	14
		672	KADUR CHIKMAGALUR SAKLSEHPUR NEW LINE (93 KM) (SWR) (N22000486)	3/1996	3/2017 (N.A.) {12/2025}	644.78 (825.31) {825.31}	605.47	66
		673	BAIYYAPPANAHALLI-HOSUR (48 KM) (NCRTC) (N22000542)	4/2019	3/2026 (N.A.) {3/2026}	375.67 (N.A.) {375.67}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		674	YESHVANTHPUR-CHANNASANDRA (21.7 KM) (<i>NCRTC</i>) (N22000543)	4/2019	3/2026 (N.A.) {3/2026}	169.65 (N.A.) {169.65}	71.75	0
		675	BELGAUM-DHARWAD VIA KITTUR (73.10 KM) (UMBRELLA WORK PB#22/2019-20/NR) (<i>SWR</i>) (N22000557)	9/2020	3/2026 (N.A.) {12/2027}	1,590.80 (927.42) {927.42}	0.36	0
		676	HASSAN (ALUR) - BELUR (32 KM) (UMBRELLA WORK PB#23/2018-19/NR) (<i>SWR</i>) (N22000558)	6/2019	4/2028 (N.A.) {12/2027}	663.03 (748.85) {748.85}	0.34	1
		677	SHIMOGA-SHIKARIPURA-RANEBENNUR (UMBRELLA WORK PB#23/2018-19/NR) (<i>SWR</i>) (N22000559)	9/2019	12/2027 (N.A.) {12/2027}	1,453.73 (994.47) {994.47}	66.02	7
		678	BANGALORE-WHITEFIELD-BANGALORE CITY-KRISHNARAJAPURAM QUADRUPLING (<i>SWR</i>) (N22000621)	3/2018	3/2025 (N.A.) {6/2025}	492.87 (N.A.) {492.87}	169.03	46
	ROAD TRANSPORT AND HIGHWAYS	679	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP (<i>MoRTH</i>) (N24000334)	3/2015	11/2015 (Aug-24) {8/2024}	165.67 (N.A.) {165.67}	126.47	99
		680	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION (<i>NHAI</i>) (N24000462)	5/2014	8/2016 (Dec-24) {12/2024}	1,655.01 (2,639.00) {2,639.00}	1,803.36	97.8
		681	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY (<i>NHAI</i>) (N24000552)	3/2016	3/2019 (Dec-23) {3/2025}	701.40 (591.86) {701.40}	460.17	79
		682	HOSPET-BELLARY-KARNATAKA AP BORDER (<i>NHAI</i>) (N24000603)	8/2016	3/2019 (May-25) {5/2025}	1,167.42 (N.A.) {1,224.01}	795.47	77.9

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		683	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM (NHAI) (N24000622)	9/2016	8/2019 (Jun-24) {12/2024}	950.69 (1,487.46) {2,525.02}	1,911.26	99.12
		684	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS PA (MoRTH) (N24001156)	1/2017	9/2017 (May-23) {5/2023}	166.67 (N.A.) {264.34}	192.08	100
		685	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH (MoRTH) (N24001157)	8/2016	2/2017 (Jul-24) {7/2024}	175.50 (N.A.) {241.60}	189.72	90.1
		686	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 (MoRTH) (N24001158)	3/2018	6/2019 (Dec-23) {12/2023}	159.97 (N.A.) {242.61}	113.15	100
		687	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION (MoRTH) (N24001159)	1/2018	7/2018 (N.A.) {3/2022}	159.70 (N.A.) {159.70}	142.88	100
		688	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR (MoRTH) (N24001160)	9/2017	10/2018 (Apr-22) {4/2022}	191.60 (N.A.) {191.60}	112.03	100
		689	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- (MoRTH) (N24001161)	12/2017	1/2019 (Apr-22) {4/2022}	297.30 (N.A.) {318.28}	280.25	100

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		690	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN (MoRTH) (N24001162)	3/2018	10/2018 (Nov-22) {11/2022}	325.86 (N.A.) {386.41}	356.78	100
		691	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN (MoRTH) (N24001164)	10/2016	3/2017 (Jul-22) {7/2022}	396.96 (N.A.) {396.96}	329.58	100
		692	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT (MoRTH) (N24001165)	11/2016	3/2017 (Oct-21) {10/2021}	314.90 (N.A.) {314.90}	233.95	100
		693	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) (MoRTH) (N24001166)	3/2015	1/2016 (N.A.) {7/2024}	159.12 (N.A.) {159.12}	127.72	98
		694	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT (MoRTH) (N24001168)	5/2018	5/2018 (Dec-23) {12/2023}	171.60 (N.A.) {171.60}	134.81	100
		695	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U (MoRTH) (N24001172)	1/2017	8/2017 (N.A.) {6/2022}	291.49 (N.A.) {291.49}	238.77	100
		696	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI JADERCELA SECTION (MoRTH) (N24001173)	2/2017	5/2019 (N.A.) {10/2025}	157.32 (188.00) {187.61}	62.31	60

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		697	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT (MoRTH) (N24001387)	1/2017	9/2017 (May-23) {5/2023}	264.34 (N.A.) {264.34}	201.07	100
		698	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA (MoRTH) (N24001388)	3/2019	12/2019 (Nov-24) {11/2024}	423.15 (N.A.) {423.15}	284.58	82
		699	4L OF ADDAHOLE TO BANTWAL CROSS SECTION INCLUDING FLYOVER AT KALLADKA TOWN (NHAI) (N24001425)	3/2021	11/2021 (Mar-25) {3/2025}	1,100.88 (1,713.98) {1,713.98}	908.41	63.5
		700	4L OF ADDAHOLE TO BANTWAL CROSS SECTION (NHAI) (N24001426)	3/2021	10/2021 (Mar-25) {3/2025}	317.90 (576.32) {576.32}	339.70	94.7
		701	6L FROM SANKESHWAR BYPASS TO MH KNT BORDER FROM KM. 555.017 TO KM. 592.853 OF NH-48 (PKG II) (NHAI) (N24001598)	1/2022	4/2025 (Apr-25) {4/2025}	1,388.70 (1,388.70) {1,388.70}	299.54	48.4
		702	BELAKERI PORT TO KUMTA - SIRSI ROAD FROM KM 0.00 - KM 4.265 OF BELEKERI PORT ROAD LINK RD. AND KM 4. (NHAI) (N24001599)	3/2018	12/2022 (Apr-25) {4/2025}	440.16 (N.A.) {440.16}	301.22	58.84
		703	BANGALORE/TN BORDER TO HOSKOTE (NHAI) (N24001674)	2/2023	2/2025 (N.A.) {2/2025}	1,240.60 (N.A.) {1,240.60}	618.05	58.13
		704	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 162.5 TO KM. 203.100 (NHAI) (N24001675)	11/2022	5/2025 (N.A.) {5/2025}	1,732.73 (N.A.) {1,732.73}	540.35	95.56

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		705	6L OF MH/KN BORDER (NIMBAL VILLAGE) TO KN/TS BORDER (SINGNODI VILLAGE) FROM KM. 26.000 TO KM. 97.000 (NHAI) (N24001676)	12/2022	6/2025 (N.A.) {6/2025}	2,718.46 (N.A.) {2,718.46}	312.90	32.24
		706	BALANCE WORK OF 2L PS FROM KM 30.800 TO 70.800 AND 2L WITH RIGID CARRIAGEWAY FROM 70.800 TO KM 84.12 (NHAI) (N24001677)	11/2022	5/2024 (May-24) {5/2024}	226.76 (226.76) {226.76}	70.45	51.51
		707	6L FROM BELGAUM TO SANKESHWAR BYPASS FROM KM 515.000 TO KM 555.017 OF NH 48 (NHAI) (N24001679)	10/2022	4/2025 (Apr-25) {4/2025}	1,479.30 (1,479.30) {1,479.30}	395.27	83.88
		708	4L OF SANNUR TO BIKARNAKATTE SECTION FROM KARKALA TO MANGALORE (NHAI) (N24001680)	3/2021	10/2024 (Jun-25) {6/2025}	1,409.68 (1,633.91) {1,633.91}	800.63	41.91
		709	TUMKUR - NELAMANGALA(6L) (NHAI) (N24001681)	8/2022	8/2025 (Aug-25) {12/2025}	2,032.15 (2,032.15) {2,032.15}	162.33	43.53
		710	UPGRADATION 2/4 LANE NH CONNECTIVITY UNDER SAGARMALA SCHEME SH 2 HAVERI YEKAMBI SH 69 YEKAMBI KUMTA (NHAI) (N24001682)	3/2022	3/2024 (Sep-25) {9/2025}	294.62 (N.A.) {294.62}	32.02	13.09
		711	AURAD - BIDAR KM 0.00 TO KM 45.878 (NHAI) (N24001683)	9/2021	4/2023 (Dec-24) {12/2024}	912.37 (N.A.) {424.16}	327.34	98.04
		712	4L OF CHANNARAYAPATNA BYPASS AND HASSAN BYPASS WITH STRUCTURES IN DEVIHALLI -HASSAN SECTION (NHAI) (N24001684)	9/2020	1/2023 (Sep-20) {5/2025}	688.00 (602.09) {688.00}	473.79	75.53

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		713	CONSTRUCTION OF 4 LANE BANGALORE -CHENNAI EXPRESSWAY FROM KM 53.500 TO KM 71.000 SECTION OF NE-7 (BA (NHAI) (N24001685)	1/2021	1/2024 (May-24) {10/2024}	1,069.00 (N.A.) {1,609.42}	840.40	99.99
		714	FOUR LANING OF BANAVARA TO BETTADAHALLI SECTION FROM KM. 119+790 (DESIGN KM. 121+900) TO KM. 166+100 (NHAI) (N24001686)	3/2021	3/2023 (Oct-24) {10/2024}	1,065.06 (1,444.50) {1,444.50}	158.15	88.94
		715	FOUR LANING OF BETTADAHALLI TO SRIRAMPURA SECTION FROM KM. 166+100 (DESIGN KM. 170+415) TO KM. 217+0 (NHAI) (N24001687)	10/2021	10/2023 (Oct-24) {3/2025}	1,331.77 (2,082.98) {2,082.98}	330.13	68.61
		716	CONSTRUCTION OF 4 LANE BANGALORE- CHENNAI EXPRESSWAY FROM KM 0.000 TO KM 26.400 NE-7(ALONG WITH 0.700 (NHAI) (N24001688)	10/2020	9/2023 (Mar-24) {12/2024}	3,184.00 (N.A.) {2,867.98}	1,165.00	98.55
		717	CONSTRUCTION OF 4 LANE BANGALORE - CHENNAI EXPRESSWAY FROM KM 26.400 TO KM 53.500 SECTION OF NE-7 (M (NHAI) (N24001689)	12/2020	9/2023 (Mar-24) {11/2024}	1,745.00 (N.A.) {1,609.42}	1,252.90	98.53
		718	FOUR LANING OF KARADI TO BANAVARA SECTION FROM KM. 66+540 (DESIGN KM. 65+195) TO KM. 119+790 (DESIGN (NHAI) (N24001691)	10/2019	10/2021 (Oct-24) {10/2024}	1,225.24 (1,505.85) {1,505.85}	77.62	93.63
		719	BALANCE WORK OF CONTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM. 54.370 TO KM. 101.400 (BI (MoRTH) (N24001936)	3/2021	3/2023 (Jul-24) {7/2024}	344.79 (N.A.) {344.79}	10.00	90

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		720	BALANCE WORK OF REHABILITATION AND UPGRADING TO 2LANE/2LANE WITH PAVED SHOULDER CONFIGURATION AND ST (MoRTH) (N24001937)	2/2023	2/2024 (Feb-25) {2/2025}	398.48 (N.A.) {398.48}	5.00	50
		721	CONSTRUCTION OF ELEVATED CORRIDOR FROM KM. 135.650 TO 136.300 ON 63, FROM KM. 249 TO KM. 250.050 ON (MoRTH) (N24001938)	6/2021	6/2024 (Jun-25) {6/2025}	298.00 (N.A.) {298.00}	10.70	52
		722	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM DESIGN KM 103.200 (EXISTING KM 103.200) TO DESIGN KM 11 (MoRTH) (N24001940)	1/2023	1/2026 (Sep-25) {9/2025}	166.58 (N.A.) {166.58}	3.54	0
		723	WIDENING TO 4 LANE FROM KM. 133.00 TO 158.04 (DESIGN CHAINAGE KM. 130.88 TO 155.145) (SHIRUR CROSS T (MoRTH) (N24001941)	1/2023	1/2025 (Jan-25) {1/2025}	350.69 (N.A.) {350.69}	10.00	56
		724	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM. 33.13 TO KM. 40.23 AND KM. 52.00 TO KM. 71.00 (EX (MoRTH) (N24001943)	9/2022	3/2024 (Jan-25) {1/2025}	172.98 (N.A.) {172.98}	6.48	65
		725	WIDENING TO INTERMEDIATE/TWO LANE TO 2 LANE WITH PAVED SHOULDER FROM EXISTING CHANGES KM 112.750 TO (MoRTH) (N24001944)	1/2023	6/2024 (Jul-24) {7/2024}	255.88 (N.A.) {255.88}	60.99	78
		726	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 116.800 TO 149.070(DESIGN CHANGES) ON HOSADURGA HOL (MoRTH) (N24001945)	8/2022	2/2024 (Dec-24) {12/2024}	170.34 (N.A.) {170.34}	4.25	72

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		727	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM 24.400 TO 27.270, 40.500 TO 41.900, 84.300 TO 88.20 (MoRTH) (N24001946)	11/2022	11/2024 (Nov-24) {11/2024}	218.93 (N.A.) {218.93}	10.00	95
		728	WIDENING TO EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FROM DESIGN KM 153.00 (MoRTH) (N24001947)	2/2023	2/2025 (Feb-25) {2/2025}	177.94 (N.A.) {177.94}	6.66	47
		729	WIDENING TO 4 LANE FROM KM 51.60 TO 76.20 (HEBRI TO PARKALA) AND FROM KM 85.20 TO 88.90 (KARAVALI JU (MoRTH) (N24001948)	10/2022	10/2024 (Dec-24) {12/2024}	355.72 (N.A.) {355.72}	11.32	60
		730	FOUR LANING OF LEFT OVER WORKS OF HOSPET BELLARY KARNATAKA/ AP BORDER FROM KM.280.080 TO KM. 375.450 (NHAI) (N24001989)	3/2023	5/2025 (N.A.) {5/2025}	830.28 (N.A.) {830.28}	401.84	49.3
		731	DEVELOPMENT OF 6 LANE ACCESS CONTROLLED GREENFIELD HIGHWAY FROM KM. 97.000 TO KM. 162.500 MARADGI S (NHAI) (N24001993)	12/2022	10/2025 (N.A.) {10/2025}	1,589.00 (N.A.) {1,589.00}	400.00	43.25
		732	4/6L OF BANGALORE - PUNE SECTION OF BYPASS CONNECTING DHARWAD - HUBLI FROM KM. 403.80 TO KM. 433.20 (NHAI) (N24001994)	5/2022	3/2023 (N.A.) {9/2025}	1,135.39 (N.A.) {1,135.39}	231.38	43.65
		733	BALANCE WORK OF CONSTRUCTION OF TWO/FOUR LANE WITH PAVED SHOULDER FROM KM 422.000 TO 523.600 (CHITR (MoRTH) (N24002011)	12/2021	6/2024 (Dec-24) {12/2024}	516.96 (N.A.) {516.96}	19.93	70

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		734	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40.00 TO KM 75.00 (EXISTING CHAINAGES) OF MANGALOR (MoRTH) (N24002012)	3/2023	3/2025 (Mar-25) {3/2025}	718.52 (N.A.) {718.52}	24.81	23
		735	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM KM.0 TO KM. 80 ON NH 548B (VIJAYAPURA-SANKESWAR SE (MoRTH) (N24002013)	3/2021	2/2022 (Oct-24) {10/2024}	766.64 (N.A.) {766.64}	13.55	75
	URBAN DEVELOPMENT	736	BANGALORE METRO RAIL PROJECT PHASE-2 (BMRCCL) (N28000058)	2/2014	2/2021 (N.A.) {3/2025}	26,405.14 (N.A.) {26,405.14}	20,936.29	89
		737	BANGALORE METRO RAIL PROJECT LIMITED. PHASE. 2A AND 2B (BMRCCL) (N28000151)	6/2021	6/2026 (N.A.) {6/2026}	14,788.10 (N.A.) {14,788.10}	2,424.04	30
KERALA	CIVIL AVIATION	738	CALICUT AIRPORT - DEVELOPMENT OF ADDITIONAL RESA ON EITHER END ON RUNWAY 10-28 AT CALICUT AIRPORT (AAI) (N04000111)	6/2023	9/2025 (N.A.) {9/2025}	323.98 (N.A.) {323.98}	0.00	2.75
	DEPARTMENT OF HIGHER EDUCATION	739	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA (CPWD EDUCATION) (N28000140)	7/2019	3/2021 (Mar-23) {11/2025}	753.63 (N.A.) {753.63}	412.37	67
	HEALTH AND FAMILY WELFARE	740	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST (CPWD FOR HEALTH) (N28000112)	9/2017	3/2020 (May-24) {9/2024}	150.29 (N.A.) {162.00}	149.49	99.5
	PETROLEUM	741	REPLACEMENT AND EXTENSION OF JETTY PIPELINES AT KOCHI REFINERY (BPCL) (N16000508)	3/2023	3/2026 (N.A.) {3/2026}	621.87 (N.A.) {621.87}	74.44	59.6

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		742	SETTING UP POLYPROPYLENE UNIT AT KOCHI REFINERY (BPCL) (N16000530)	12/2023	10/2027 (N.A.) {10/2027}	4,460.00 (N.A.) {4,460.00}	62.16	4.1
	<u>RAILWAYS</u>	743	TRIVANDRUM-KANYAKUMARI DOUBLING (SR) (N22000399)	2/2015	(Dec-26) {12/2026}	1,431.90 (3,785.45) {3,785.45}	3,097.41	30
		744	TURAVUR-AMBALAPUZHA DOUBLING (SR) (N22000400)	2/2015	(N.A.) {3/2025}	1,000.00 (N.A.) {1,416.49}	1.63	0
		745	ERNAKULAM-KUMBALAM - PATCH DOUBLING (7.71 KM) (SR) (N22000619)	12/2010	3/2028 (Jul-26) {7/2026}	600.82 (595.39) {595.39}	270.57	0.5
		746	KUMBALAM-THURAVUR - PATCH DOUBLING (15.59 KM) (SR) (N22000620)	12/2011	8/2023 (Sep-26) {9/2026}	812.85 (802.80) {802.80}	258.69	0.5
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	747	4-LANNING OF THALSERRY -MAHE BYPASS (NHAI) (N24000704)	9/2017	5/2020 (Nov-23) {2/2024}	1,124.11 (1,573.18) {1,573.18}	1,522.32	100
		748	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH (NHAI) (N24000784)	2/2018	2/2023 (Dec-24) {3/2025}	1,424.77 (1,862.77) {1,862.77}	671.63	76.23
		749	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK (MoRTH) (N24001369)	2/2017	8/2017 (Mar-22) {8/2024}	294.28 (296.53) {296.53}	285.30	98
		750	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) (MoRTH) (N24001370)	2/2017	9/2017 (Jan-23) {8/2024}	380.76 (372.87) {372.87}	337.83	100

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		751	CONSTRUCTION OF 6 LANE ELEVATED CORRIDOR ALONG WITH DEVELOPMENT OF EXISTING 4 LANE ROAD AT GROUND LE (NHAI) (N24001648)	8/2022	1/2026 (N.A.) {1/2026}	2,429.52 (N.A.) {2,429.52}	538.62	35.83
		752	SIX LANING OF PARAVOOR(DESIGN KM. 417+000) TO KOTTUKULANGARA(DESIGN KM. 454+500) SECTION OF NEW NH-6 (NHAI) (N24001649)	12/2021	2/2025 (Feb-25) {2/2025}	3,273.61 (N.A.) {3,273.61}	464.60	44.5
		753	SIX LANING OF KADAMBATTUKONAM TO KAZHAKKOOTTAM SECTION OF NH- 66(OLD NH-47) FROM KM. 517+250 TO KM.54 (NHAI) (N24001650)	12/2021	1/2025 (Aug-25) {8/2025}	3,635.64 (N.A.) {3,635.64}	280.32	36.28
		754	SIX LANING OF THURAVOOR (DESIGN KM. 378+612) TO PARAVOOR (DESIGN KM.417+000) SECTION OF NEW NH-66 (O (NHAI) (N24001651)	9/2021	9/2024 (Mar-26) {9/2024}	2,878.97 (N.A.) {2,878.97}	336.60	26.35
		755	6L MINOR BRIDGE (PALOLI PALAM) AT KM. 203.160 and MAJOR BRIDGE (MORAD) AT KM. 204.895 AND ALLIED WOR (NHAI) (N24001652)	3/2020	6/2022 (Feb-24) {6/2024}	210.37 (216.94) {216.94}	198.10	100
		756	SIX LANING FROM KODUNGALLUR TO EDAPALLY SECTION OF NH 66 (OLD NH- 17) FROM DESIGN CHAINAGE 397+750 () (NHAI) (N24001653)	11/2021	4/2025 (N.A.) {4/2025}	3,565.82 (N.A.) {3,064.11}	1,909.75	42.88
		757	SIX LANING OF START OF KOLLAM BYPASS (KM.486+000) KADAMBATTUKONAM (KM.517+250) SECTION OF NEW NH-66 (NHAI) (N24001654)	6/2021	3/2025 (Feb-25) {2/2025}	2,641.37 (N.A.) {2,641.37}	385.44	52.47

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		758	SIX LANING FROM KAPPIRIKKAD TO THALIKULAM SECTION OF NH 66 (OLD NH-17) FROM DESIGN CH. 335+850 (EX (NHA)) (N24001655)	6/2021	2/2025 (N.A.) {11/2025}	3,606.00 (3,946.56) {3,946.56}	2,982.18	51.33
		759	SIX LANING FROM THALIKULAM TO KODUNGALLUR SECTION OF NH 66 (OLD NH-17) FROM DESIGN CH.369+015 (EX. (NHA)) (N24001656)	6/2021	3/2025 (N.A.) {12/2025}	2,595.00 (N.A.) {4,009.57}	2,916.74	43.3
		760	SIX LANING OF KOTTUKULANGARA (DESIGN KM. 454+500) TO START OF KOLLAM BYPASS (DESIGN KM. 486+000) SEC (NHA)) (N24001657)	6/2021	10/2024 (Dec-25) {12/2025}	2,842.14 (N.A.) {2,842.14}	455.59	57
		761	SIX LANING OF RAMANATTUKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66 (OLD NH-17) FROM (NHA)) (N24001658)	1/2021	7/2024 (Mar-25) {3/2025}	4,265.42 (N.A.) {4,728.40}	3,353.90	83.6
		762	SIX LANING FROM START OF VALANCHERY BYPASS TO KAPPIRIKKAD- SECTION OF NH-66(OLD NH-17) FROM DESIGN CH (NHA)) (N24001659)	2/2021	7/2024 (Mar-25) {3/2025}	3,375.31 (3,824.07) {3,824.07}	2,240.28	84
		763	SIX LANING OF THALIPARAMBHA- MUZHAPILANGAD SECTION FROM KM 137.900 TO KM. 170.600 OF NH-17 (NEW NH (NHA)) (N24001660)	8/2020	2/2024 (Nov-21) {12/2025}	2,714.60 (3,319.41) {2,714.60}	1,691.38	60.1
		764	6L OF AZHIYUR-VENGALAM FROM KM. 189.200 TO KM. 230.400 OF NH-66 (NHA)) (N24001661)	10/2020	4/2024 (May-25) {12/2025}	3,219.47 (3,713.14) {3,713.14}	2,079.48	47.83

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		765	SIX LANING OF KT/KL BORDER (THALAPPDY) TO CHENGALA SECTION OF NH17 (NEW NH-66) FROM CH. 17.200 TO CH (NHAI) (N24001662)	5/2020	5/2024 (Nov-21) {3/2025}	1,981.07 (2,467.68) {1,981.07}	1,368.63	77.02
		766	SIX LANING OF NEELESHWARAM TO THALIPARAMBHA SECTION FROM CH. 94+540 (EXISTING KM 96+450) TO CH. 134+ (NHAI) (N24001663)	6/2020	4/2024 (Oct-21) {12/2025}	3,041.65 (3,799.76) {3,041.65}	2,156.43	52.5
		767	SIX LANING OF CHENGALA TO NEELESHWARAM SECTION OF NH-17 (NEW NH-66) FROM CH. 56+200 (EXISTING KM 57+ (NHAI) (N24001664)	6/2020	4/2024 (Oct-21) {11/2025}	1,746.45 (2,377.88) {1,746.45}	1,125.92	59.79
		768	WIDENING/DEVELOPMENT OF EXISTING NH-85 FROM KM 0.000 TO KM 124.636 SECTION TO 2L@L+PS SECTION IN TH (NHAI) (N24002074)	8/2022	6/2025 (N.A.) {6/2025}	1,231.74 (N.A.) {1,231.74}	103.06	18
	URBAN DEVELOPME NT	769	KOCHI METRO RAIL PROJECT (KMRCL) (N28000081)	7/2012	7/2017 (Sep-20) {9/2020}	5,181.79 (N.A.) {6,218.14}	6,059.17	100
		770	KOCHI METRO RAIL PROJECT PHASE II FROM JLN STADIUM TO INFOPARK VIA KAKKANAD (KMRCL) (N28000158)	7/2018	11/2026 (N.A.) {11/2026}	1,957.05 (N.A.) {1,957.05}	2.81	0
		771	KOCHI METRO RAIL PROJECT PHASE IB SECTION FROM S N JUNCTION TO THRIPUNITHURA (KMRCL) (N28000159)	6/2019	9/2023 (N.A.) {9/2023}	355.70 (448.00) {448.33}	1.64	0
	LADAKH	772	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT (AAI) (N04000078)	7/2018	9/2021 (Oct-24) {10/2025}	480.33 (N.A.) {640.00}	357.99	60.09
		773	KARGIL-ZANSKR PACKAGE-1 (NHIDCL) (N24001343)	3/2021	1/2023 (Dec-24) {10/2025}	384.23 (N.A.) {384.23}	115.95	58.5
	ROAD TRANSPORT AND HIGHWAYS							

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>HIGHWAYS</u>	774	KARGIL-ZANSKR PACKAGE-2 (NHIDCL) (N24001344)	3/2021	1/2023 (Nov-23) {10/2025}	404.89 (N.A.) {404.89}	153.90	52.48
		775	KARGIL-ZANSKR PACKAGE-3 (NHIDCL) (N24001345)	8/2020	1/2023 (Jun-24) {11/2024}	381.01 (N.A.) {381.01}	179.01	67.17
		776	KARGIL-ZANSKR PACKAGE-8 (NHIDCL) (N24001348)	3/2021	1/2023 (Aug-24) {11/2024}	398.37 (N.A.) {398.37}	186.05	79.01
		777	CONSTRUCTION OF REALIGNMENT BETWEEN PANDRASS- PASHKYUN (TOTAL LENGTH 27.10 KM) ON ROAD ZOZILA-KARGIL (BRO) (N24001999)	11/2021	6/2025 (N.A.) {6/2025}	426.14 (N.A.) {426.14}	46.38	23
<u>MADHYA PRADESH</u>	<u>CIVIL AVIATION</u>	778	UPGRADATION OF JABALPUR AIRPORT (AAI) (N04000087)	6/2016	6/2021 (N.A.) {7/2024}	412.24 (N.A.) {412.24}	401.11	100
		779	DEVELOPMENT OF GWALIOR AIRPORT PHASE 01 (AAI) (N04000098)	10/2021	8/2023 (Jun-24) {8/2024}	446.12 (N.A.) {446.12}	430.55	100
	<u>COAL</u>	780	KANCHAN OC EXPANSION (SECL) (N06000125)	12/2014	3/2021 (Mar-26) {3/2026}	371.04 (N.A.) {371.04}	134.01	47
		781	AMADAND OPENCAST EXPANSION PROJECT (SECL) (N06000148)	3/2016	3/2021 (Mar-27) {3/2027}	869.44 (N.A.) {869.44}	250.19	64
		782	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) (NCL) (N06000162)	11/2017	3/2022 (N.A.) {3/2025}	1,255.17 (N.A.) {1,255.17}	1,236.61	96.89
		783	GANDHIGRAM UG MINE (WCL) (N06000183)	8/2019	3/2026 (N.A.) {3/2026}	414.16 (N.A.) {414.16}	24.98	28
		784	BLOCK-B EXPANSION OPENCAST PROJECT (NCL) (N06000184)	7/2019	3/2023 (N.A.) {3/2025}	998.71 (N.A.) {998.71}	360.14	26.29

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		785	NIGAH I EXPANSION OCP (15 TO 25 MTPA) (NCL) (N06000196)	11/2020	3/2025 (N.A.) {3/2025}	1,729.68 (N.A.) {1,729.68}	647.51	40.74
		786	RAMPUR BATURA OC (4.0 MTY) (SECL) (N06000233)	7/2019	3/2026 (N.A.) {3/2026}	1,248.93 (N.A.) {1,248.93}	468.43	44
		787	TAWA III UG MINE (WCL) (N06000250)	12/2021	3/2027 (N.A.) {3/2027}	324.25 (N.A.) {324.25}	12.32	9
		788	AMALGAMATED DHANKASA JAMUNIA UG (1.84 MTY) (WCL) (N06000257)	9/2022	3/2027 (N.A.) {3/2027}	497.01 (N.A.) {497.01}	160.98	42
		789	VISHNUPURI UG TO OC (WCL) (N06000260)	11/2022	3/2029 (N.A.) {3/2029}	227.65 (N.A.) {227.65}	7.02	7
		790	URDHAN OC (WCL) (N06000265)	7/2022	3/2031 (N.A.) {3/2031}	228.42 (N.A.) {228.42}	27.67	9
		791	SHARDA UG (WCL) (N06000266)	7/2022	3/2028 (N.A.) {3/2028}	200.16 (N.A.) {200.16}	34.40	11
	PETROLEUM	792	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF (BPCL) (N16000518)	5/2023	5/2028 (N.A.) {5/2028}	43,367.00 (N.A.) {43,367.00}	805.00	6.3
	POWER	793	OMKARESHWAR FLOATING SOLAR POWER PROJECT (90 MW) (SJVN) (N18000342)	11/2022	4/2024 (N.A.) {8/2024}	646.17 (N.A.) {646.17}	600.77	100
		794	SHAJAPUR 325MW SOLAR PV PROJECT (NTPC) (N18000348)	6/2022	3/2024 (N.A.) {3/2024}	1,530.49 (N.A.) {1,530.49}	590.76	0
		795	TS FOR EVACUATION POWER RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX): PART-C (PGCIL) (N18000392)	8/2024	8/2026 (N.A.) {8/2026}	2,708.00 (N.A.) {2,708.00}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
RAILWAYS		796	RAMGANJMUNDI-BHOPAL (NL),WCR (WCR) (220100314)	4/2001	3/2021 (Dec-25) {12/2025}	424.60 (3,032.46) {5,125.16}	2,947.26	68
		797	RATLAM-MHOW-KHANDWA-AKOLA (GC) (WR) (N22000120)	4/2008	3/2022 (Feb-27) {2/2027}	3,503.69 (5,677.80) {6,203.51}	3,898.71	80
		798	KATNI - SINGRAULI DOUBLING PROJECT (WCR) (N22000351)	12/2015	3/2020 (N.A.) {10/2024}	1,763.93 (N.A.) {2,445.30}	2,857.25	100
		799	KATNI-BINA 3RD LINE (263 KM) (WCR) (N22000415)	6/2016	3/2022 (N.A.) {6/2024}	2,478.23 (N.A.) {2,938.00}	1,279.35	0
		800	KATNI GRADE SEPARATOR/BYE PASS (WCR) (N22000416)	8/2016	3/2022 (N.A.) {9/2024}	582.13 (N.A.) {1,247.64}	1,096.23	80
		801	ANUPPUR-KATNI (SECR) (N22000485)	4/2015	12/2021 (Dec-23) {12/2024}	1,370.00 (1,680.00) {2,311.02}	1,618.93	74
		802	NIMACH BADI SADRI NEW LINE PROJECT (WR) (N22000503)	4/2017	3/2022 (N.A.) {3/2026}	495.18 (N.A.) {495.18}	165.27	10
		803	NIMACH-RATLAM (133 KM) (WR) (N22000536)	10/2021	10/2027 (Mar-25) {3/2025}	910.00 (1,095.88) {1,095.88}	765.20	87
		804	POWARKHEDA - JUJHARPUR - SINGLE LINE FLYOVER IN UP DIRECTION (15.89 KM) (WCR) (N22000552)	12/2016	3/2024 (N.A.) {3/2024}	199.63 (N.A.) {199.63}	0.00	0
		805	SATNA - REWA (50 KM) (WCR) (N22000554)	11/2015	3/2026 (N.A.) {3/2026}	500.00 (40.00) {500.00}	1.41	80
		806	INDORE BUDNI (INDORE JABALPUR) (RVNL) (N22000601)	9/2018	9/2030 (N.A.) {9/2030}	4,340.00 (N.A.) {7,393.75}	1,004.86	12
	ROAD TRANSPORT AND HIGHWAYS	807	UMARIYA TO SHAHDOL SECTION OF NH- 78 IN MADYA PRADESH KM 68/4 TO 142/200 (MoRTH) (N24000513)	3/2015	8/2017 (Dec-23) {12/2024}	511.83 (N.A.) {511.83}	485.18	93.06

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		808	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN (NHAI) (N24000709)	12/2017	2/2020 (Sep-24) {9/2024}	950.27 (N.A.) {786.43}	627.09	98.44
		809	2L+PS OF THIKRI ANJAD SECTION OF NH- 347B (MoRTH) (N24000892)	11/2017	7/2018 (N.A.) {9/2023}	249.05 (N.A.) {249.05}	221.19	100
		810	4LBERKHEDI TO GODPEHRA NH-44 (NHAI) (N24001614)	2/2022	11/2024 (N.A.) {11/2024}	524.84 (N.A.) {524.84}	2,138.61	35
		811	4L OF SAGAR - MOHARI FROM KM.8 TO KM.50 (PKG-I) (NHAI) (N24001615)	3/2021	4/2024 (May-24) {8/2024}	790.78 (N.A.) {790.78}	1,383.43	46
		812	2L PS OF SATNA - MAIHAR SECTION OF NH-135BG FROM KM 80.800 TO KM 120.125 (NHAI) (N24001616)	1/2021	10/2023 (N.A.) {12/2024}	428.04 (N.A.) {428.04}	350.95	98.89
		813	KATNI BYPASS FROM KM. 359.50 TO KM. 378.50 (NHAI) (N24001618)	9/2019	9/2022 (N.A.) {12/2024}	194.40 (N.A.) {194.40}	170.92	86.5
		814	4L OF UJJAIN TO BADNAWAR FROM KM 26.900 TO KM 96.00 OF NH-752D (NHAI) (N24001756)	10/2020	10/2024 (N.A.) {10/2024}	1,352.56 (N.A.) {1,480.94}	832.71	90.01
		815	4L OF SUHAGADI TO BARDIYA AMRA FROM KM. 89.200 TO KM. 135.351 OF NH- 752D (PKG-III) (NHAI) (N24001758)	1/2020	10/2024 (N.A.) {10/2024}	823.05 (N.A.) {823.05}	368.50	98.92
		816	4L OF CHANDESARA TO KHEDAKHAJURIYA FROM KM. 0.000 TO (-) 750 AND KM 0.000 TO KM 41.400 OF NH- 752D (NHAI) (N24001759)	1/2020	6/2024 (Dec-24) {12/2024}	909.84 (N.A.) {909.84}	421.21	72.3

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		817	4L OF HARDA - BETUL (PKG-II) FROM KM. 30.00 TO KM.81.00 [TEMAGAON TO CHICHOLI] (NHAI) (N24001761)	2/2023	2/2025 (Feb-25) {2/2025}	520.28 (N.A.) {520.28}	351.15	86.91
		818	INDORE - HARDA (PKG-III) [NANASA TO PIDGAON SECTION FROM KM 95.000 TO KM 142.445] (NHAI) (N24001762)	10/2021	1/2024 (Dec-24) {12/2024}	1,146.22 (N.A.) {1,146.22}	550.78	78.88
		819	ADDITIONAL WORKS (2VUPS, MR-10 JUNCTION FLYOVER AND UNDERPASS) IN SIX LANE INDORE-DEWAS SECTION OF N (NHAI) (N24001765)	8/2022	7/2024 (N.A.) {5/2025}	207.77 (N.A.) {207.77}	41.36	32.19
		820	INDORE - HARDA (PKG-I) [INDORE TO RAGHAV GARH FROM KM. 0.25 TO KM. 26.903] (NHAI) (N24001766)	1/2022	10/2024 (N.A.) {10/2024}	1,011.29 (N.A.) {1,011.29}	150.94	31.06
		821	4L OF INDORE - BOREGAON (PKG-III) [BALWARA TO DHANGAON] FROM KM. 42.260 TO KM. 82.660 OF NH347BG AND (NHAI) (N24001767)	1/2021	4/2024 (N.A.) {4/2024}	1,001.69 (N.A.) {1,001.69}	467.18	77.1
		822	BALANCE WORK OF 4L OF INDORE- GUJARAT/MP BORDER FROM KM 106.210 TO KM 115.250 (START AND END POINT OF (NHAI) (N24001768)	8/2019	4/2023 (N.A.) {11/2023}	323.51 (N.A.) {323.51}	48.20	100
		823	DHANGAON - BORGGAON SECTION (KM 81.000 TO KM 139.000) [INDORE - EDLABAD PKG IV] (NHAI) (N24001769)	11/2018	8/2023 (Nov-24) {11/2024}	831.00 (N.A.) {831.00}	840.30	99.8
		824	4L OF OBEDULLGANJ - BUDNI SECTION FROM KM. 8.400 TO KM. 20.700 IN RATANPANI WILDLIFE AREA OF NH - 69 (NHAI) (N24001770)	2/2022	3/2024 (Dec-24) {12/2024}	417.51 (N.A.) {417.51}	223.58	73.5

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		825	2- LANE WITH PAVED SHOULDERS OF HINOTIYA TO MEHULWA FROM DESIGN KM 27+000 9OF EXISTING SH-19 KM 26+5 (NHAI) (N24001921)	8/2021	9/2025 (N.A.) {9/2025}	581.65 (592.03) {581.65}	124.59	22.05
		826	CONSTRUCTION OF MIHONA BYPASS, LAHAR BYPASS, DABOH BYPASS and BHANDER BYPASS (TOTAL LENGTH 20.60 KM) (MoRTH) (N24001962)	3/2022	12/2024 (N.A.) {12/2024}	179.19 (N.A.) {179.19}	75.91	60
		827	UPGRADATION OF NASRULLAGANI- REHTI-BUDHNI SCCTION TO 2-LANE WITH PAVED SHOULDER FROM KM 0+150 TO KM (MoRTH) (N24001963)	12/2021	10/2024 (N.A.) {3/2025}	305.12 (N.A.) {305.12}	73.80	17.25
		828	UPGRADATION and WIDENING OF JHARKHEDA- BERASIA - DHOLKHEDI FROM DESIGN KM 0+000 TO KM 87+900 (DESIGN (MoRTH) (N24001964)	3/2022	5/2025 (N.A.) {5/2025}	365.21 (N.A.) {365.21}	151.39	64
		829	REHABILITATION AND UPGRADATION OF KURWAIMUNGAOLICHANDERI ROAD SECTION OF NH-346, FROM DESIGN CHAIN (MoRTH) (N24001965)	3/2022	2/2025 (N.A.) {2/2025}	386.49 (N.A.) {386.49}	103.75	32
		830	BALANCE WORK FOR REHABILITATION AND UP-GRADATION OF SIDHI- SINGRAULI FROM KM 82.400 TO KM 187.993 SEC (MoRTH) (N24001966)	12/2020	4/2023 (May-23) {12/2024}	529.44 (N.A.) {529.44}	165.60	45.69
		831	4L GREENFIELD RUDHI TO DESHGAON (PKG V OF BETUL- KHANDWA/DESHGAON) - N/04015/06003/MP (NHAI) (N24001967)	11/2018	10/2025 (N.A.) {10/2025}	521.21 (N.A.) {521.21}	58.23	14.25

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		832	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF JIRAPUR-SUSNER-MP-RJ B (MoRTH) (N24002018)	1/2022	3/2025 (N.A.) {3/2025}	239.72 (232.22) {232.22}	129.45	80.71
		833	UPGRADATION OF DINDORI-SAGARTOLA-KABICHABUTRA (MP-CG BORDER) SECTION OF NH -45 FROM KM 0+00(DESIGN) (MoRTH) (N24002019)	1/2022	9/2025 (N.A.) {9/2025}	329.14 (319.09) {319.09}	111.42	23.5
		834	CONSTRUCTION OF KAITHI-PADARIA KALA BYPASS, PATNA-TAMOLI BYPASS, JASO BYPASS , NAGOD BYPASS (TOTAL L (MoRTH) (N24002020)	3/2022	10/2025 (N.A.) {10/2025}	158.36 (158.00) {158.36}	37.78	17
		835	BALANCE WORK OF 4L OF NAURADEHI SANCTUARY DE-SCOPED STRETCH OF HIRAN RIVER TO SINDOOR RIVER FROM KM. (NHAI) (N24002067)	1/2021	7/2023 (N.A.) {12/2024}	178.18 (N.A.) {178.18}	161.64	84.39
		836	CONSTRUCTION OF 4-LANE FROM BARELA TO MANEGAON SECTION OF NH-30 FROM DESIGN CH. 2.900 TO DESIGN CH. (NHAI) (N24002068)	12/2022	3/2025 (N.A.) {3/2025}	652.33 (N.A.) {652.33}	235.49	48.59
		837	CONSTRUCTION OF ADDITIONAL 3 LANE WITH PAVED SHOULDER (DESIGN LENGTH 8.87 KM) AS REALIGNMENT OF BAKA (NHAI) (N24002069)	7/2022	12/2024 (N.A.) {12/2024}	209.29 (N.A.) {209.29}	124.20	93.21
		838	INDORE - EDLABAD (PKG-II) [TEJAJINAGAR TO BALWARA] (NHAI) (N24002070)	1/2022	1/2025 (N.A.) {1/2025}	1,162.80 (N.A.) {1,162.80}	470.63	72.5

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MAHARASHTRA	SOCIAL JUSTICE URBAN DEVELOPMENT	839	CONSTRUCTION OF (I) 4-LANE HIGHWAY FROM VIDISHA TO HINOTIYA FROM KM. 0.000 TO KM. 27.000 (LENGTH=27 (NHA) (N24002077)	9/2022	12/2025 (N.A.) {12/2025}	1,000.63 (N.A.) {1,000.63}	134.50	17.05
		840	CENTRE FOR DISABILITY SPORTS (CPWD) (N38000001)	2/2019	3/2024 (N.A.) {3/2024}	170.99 (N.A.) {170.99}	73.80	74
		841	BHOPAL METRO RAIL (MPMRCL) (N28000124)	11/2018	2/2023 (Dec-27) {12/2027}	6,941.40 (N.A.) {6,941.40}	2,405.61	31.36
		842	INDORE METRO RAIL (MPMRCL) (N28000125)	11/2018	2/2023 (Dec-27) {12/2027}	7,500.80 (N.A.) {7,500.80}	3,127.60	47.25
	CIVIL AVIATION	843	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT (AAI) (N04000079)	3/2017	4/2021 (N.A.) {12/2023}	475.39 (N.A.) {520.00}	505.77	100
		844	EXTENSION OF RUNWAY WITH BLAST PAD, RESA, TAXIWAY, APRON, GSE AREA, ISOLATION BAY, NEW DOMESTIC TERM (AAI) (N04000096)	6/2017	12/2020 (N.A.) {4/2024}	255.68 (N.A.) {270.00}	267.38	100
	COAL	845	AMALGAMATED YEKONA-I YEKONA-II (WCL) (N06000132)	8/2015	3/2025 (N.A.) {3/2025}	727.28 (N.A.) {727.28}	534.87	86
		846	UKNI DEEP OC (WCL) (N06000179)	11/2018	3/2021 (Mar-25) {3/2025}	318.14 (N.A.) {318.14}	253.27	91
		847	BELLORA-NAIGAON DEEP OC (WCL) (N06000180)	11/2018	3/2021 (Mar-25) {3/2025}	252.71 (N.A.) {252.71}	122.94	56
		848	GHONSA EXPANSION DEEP OC (WCL) (N06000205)	3/2021	3/2028 (N.A.) {3/2028}	241.72 (N.A.) {241.72}	59.30	6
		849	SASTI EXPANSION OC (WCL) (N06000206)	8/2020	3/2026 (N.A.) {3/2026}	371.59 (N.A.) {371.59}	105.64	24

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		850	DHUPTALA OC(SASTI UG TO OC) (WCL) (N06000209)	2/2019	3/2028 (N.A.) {3/2028}	720.87 (N.A.) {720.87}	179.54	33
		851	ADASA UG TO OC (1.50 MTY) (WCL) (N06000219)	11/2018	3/2024 (Mar-25) {3/2025}	333.43 (N.A.) {333.43}	223.17	78
		852	DINESH (MAKARDHOKDA-III) OC (8.0 MTY) (WCL) (N06000222)	2/2020	3/2027 (N.A.) {3/2027}	1,184.33 (N.A.) {1,184.33}	849.44	48
		853	AMALGAMATED INDER-KAMPTEE DEEP OC (3.20 MTY) (WCL) (N06000226)	9/2018	3/2024 (Mar-25) {3/2025}	313.34 (N.A.) {313.34}	205.45	87
		854	MUNGOLI NIRGUDA EXTENSION (DEEP) OC (WCL) (N06000231)	11/2020	3/2026 (N.A.) {3/2026}	826.80 (N.A.) {826.80}	518.85	52
		855	SAONER UG MINE I EXPANSION (WCL) (N06000251)	1/2022	3/2028 (N.A.) {3/2028}	253.51 (N.A.) {253.51}	111.68	27
		856	SINGHORI DEEP OC (WCL) (N06000252)	5/2022	3/2029 (N.A.) {3/2029}	421.84 (N.A.) {421.84}	115.89	16
		857	MAKARDHOKDA I EXPANSION OC (WCL) (N06000253)	6/2022	3/2026 (N.A.) {3/2026}	497.06 (N.A.) {497.06}	144.88	12
		858	BHATADI EXPANSION OC (WCL) (N06000254)	2/2020	3/2028 (N.A.) {3/2028}	729.86 (N.A.) {729.86}	159.12	17
		859	NEW MAJARI UG TO OC (3.0 MTY) (WCL) (N06000255)	5/2019	3/2027 (N.A.) {3/2027}	496.38 (N.A.) {496.38}	143.72	27
		860	BHANEGAON OC (1.15MTY) (WCL) (N06000256)	9/2022	3/2028 (N.A.) {3/2028}	494.60 (N.A.) {494.60}	99.87	7
		861	GOKUL EXPANSION OC (WCL) (N06000264)	4/2021	3/2026 (N.A.) {3/2026}	456.95 (N.A.) {456.95}	148.57	7
		862	KOLGAON EXPANSION (DEEP) OC (WCL) (N06000267)	1/2023	3/2027 (N.A.) {3/2027}	206.19 (N.A.) {206.19}	7.75	5

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		863	AMALGAMATED GAURI PAUNI EXPANSION OC (WCL) (N06000271)	3/2024	3/2030 (N.A.) {3/2030}	1,428.25 (N.A.) {1,428.25}	203.03	17
	DEPARTMENT OF HIGHER EDUCATION	864	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI (CPWD EDUCATION) (N28000117)	1/2018	7/2020 (Nov-23) {2/2024}	223.37 (275.00) {230.00}	141.16	100
	HEALTH AND FAMILY WELFARE	865	500 BEDDED HOSPITAL INCLUDING 50 SUPERSPECIALITY BEDS FOR ESIC AT PUNE (CPWD) (N21000033)	7/2022	9/2025 (N.A.) {9/2025}	429.25 (N.A.) {429.25}	27.16	0
	PETROLEUM	866	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS (ONGC) (N16000213)	12/2015	4/2018 (Dec-23) {5/2026}	3,190.69 (3,375.90) {3,375.90}	2,961.86	87.6
		867	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV (ONGC) (N16000358)	4/2019	3/2022 (Jun-24) {2/2025}	3,228.80 (3,976.67) {3,976.67}	3,940.46	98.8
		868	SETTING UP 500KTPA PROPANE DEHYDROGENATION INTEGRATED WITH POLYPROPYLENE UNIT ALONG WITH OFFSITE AND (GAIL) (N16000430)	5/2019	4/2025 (Oct-25) {10/2025}	8,797.00 (11,256.00) {11,256.00}	5,065.86	73.6
		869	PIPELINE REPLACEMENT PROJECT - VII (ONGC) (N16000436)	1/2022	5/2024 (Jan-25) {1/2025}	3,183.58 (N.A.) {3,645.23}	3,417.00	99.1
		870	DEBOTTLENECKING AND AUGMENTATION OF CRYOGENIC FACILITIES AT URAN LPG IMPORT TERMINAL (BPCL) (N16000442)	4/2021	6/2024 (N.A.) {4/2025}	1,164.69 (N.A.) {1,164.69}	578.28	56.5
		871	EXPANSION OF CRYOGENICS GROUP BY SETTING UP NEW MANUFACTURING FACILITY (IOCL) (N16000446)	9/2021	10/2023 (May-24) {5/2024}	378.00 (N.A.) {378.00}	120.07	39.08

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		872	CONSTRUCTION OF LUBE OIL BLENDING AND FILLING PLANT AT RASAYANI (BPCL) (N16000452)	5/2022	3/2024 (N.A.) {9/2024}	423.39 (N.A.) {423.39}	181.29	65
		873	ATF PIPELINE FROM JAWAHARLAL NEHRU PORT TRUST (JNPT) TO NAVI MUMBAI INTERNATIONAL AIRPORT (NMIA) (IOCL) (N16000456)	9/2022	8/2025 (N.A.) {8/2025}	165.00 (N.A.) {165.00}	45.25	50.88
		874	DAMAN UPSIDE DEVELOPMENT PROJECT (DUDP) IN TAPTI DAMAN BLOCK (ONGC) (N16000470)	6/2022	10/2025 (N.A.) {2/2026}	4,144.41 (6,406.90) {6,406.90}	243.43	11
		875	CGD PROJECT AT BEED, JALGAON AND JALNA DISTRICTS (IOCL) (N16000487)	3/2022	3/2030 (N.A.) {9/2031}	865.00 (N.A.) {865.00}	42.76	1.5
		876	ANDHERI RESIDENTIAL TOWERS MUMBAI (IOCL) (N16000503)	6/2017	5/2025 (N.A.) {5/2025}	281.35 (N.A.) {281.35}	83.70	41.1
		877	CONSTRUCTION OF ADDITIONAL TANKAGES AND ALLIED FACILITIES AT JNPT TERMINAL (IOCL) (N16000504)	4/2022	10/2024 (Aug-26) {8/2026}	341.43 (N.A.) {341.43}	194.49	26
		878	INSTALLATION OF INDEPENDENT DE- AROMATIZED SOLVENTS PRODUCTION FACILITIES AT MUMBAI REFINERY (BPCL) (N16000507)	3/2023	7/2025 (N.A.) {7/2025}	405.00 (N.A.) {405.00}	60.50	54.5
		879	PART REPLACEMENT PIPELINE PROJECT (PRPP) (ONGC) (N16000515)	11/2022	5/2024 (Dec-24) {12/2024}	1,219.48 (N.A.) {1,145.10}	29.82	43.5
		880	POL AND LOBS INSTALLATIONS WITH RECEIPT PIPELINES AT RASAYANI (BPCL) (N16000519)	5/2023	5/2026 (N.A.) {5/2026}	2,585.00 (N.A.) {2,585.00}	105.39	27.9

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		881	MHN TCPP PGC BGC PROJECT (MTPBP) (ONGC) (N16000526)	2/2024	5/2026 (N.A.) {5/2026}	2,329.45 (N.A.) {2,354.23}	94.42	15.3
		882	PRP-VIII GROUP B (NH AND BS ASSET) (ONGC) (N16000533)	6/2024	5/2026 (N.A.) {2/2026}	2,379.84 (N.A.) {2,379.84}	0.00	0
		883	HP TDAE UNIT IN MUMBAI REFINERY (HPCL) (N16000534)	6/2024	4/2026 (N.A.) {4/2026}	240.00 (N.A.) {240.00}	5.36	6.7
		884	INTEGRATED DEVELOPMENT OF 4 CONTRACT AREAS UNDER DSF2 (ONGC) (N16000537)	5/2023	4/2027 (N.A.) {4/2027}	6,183.79 (N.A.) {6,183.79}	0.00	0
	POWER	885	BIKANER SOLAR POWER PROJECT (SJVN) (N18000335)	4/2022	5/2024 (N.A.) {7/2025}	5,491.89 (532.00) {5,491.89}	2,701.37	62
		886	TS FOR EVACUATION OF 7GW RE INJECTION AT KHAVDA PS UNDER PHASE-IV PART E4 (PGCIL) (N18000377)	11/2023	7/2025 (N.A.) {7/2025}	224.00 (N.A.) {224.00}	0.00	0
	RAILWAYS	887	AHMEDNAGAR-PARLI VAIJNATH(NL) CR (CR) (220100181)	2/1997	3/2021 (N.A.) {12/2025}	2,271.50 (N.A.) {4,944.99}	4,342.69	89
		888	MUMBAI URBAN TRANSPORT PROJECT PHASE-II (MRTP) (N22000092)	4/2008	3/2014 (N.A.) {3/2014}	5,300.00 (N.A.) {918.53}	7,135.77	21
		889	WARDHA-NANDED MAHARASHTRA (CR) (N22000231)	4/2008	3/2023 (N.A.) {12/2026}	3,168.29 (N.A.) {3,445.48}	2,673.74	0
		890	KALYAN-KASARA 3RD LINE (CR) (N22000233)	4/2011	3/2021 (N.A.) {12/2025}	792.89 (N.A.) {1,432.61}	773.05	50
		891	WARDHA-SEWAGRAM NGP 3RD LINE (CR) (N22000250)	4/2012	3/2022 (N.A.) {5/2025}	540.02 (N.A.) {540.02}	618.24	72

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		892	WARDHA-BALHARSHAH - 3RD LINE (132 KM) (CR) (N22000356)	2/2015	3/2022 (N.A.) {8/2025}	1,272.19 (N.A.) {1,384.72}	1,170.15	67
		893	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) (CR) (N22000358)	2/2015	3/2023 (N.A.) {3/2027}	2,449.91 (N.A.) {2,449.91}	1,422.71	42
		894	PUNE-MIRAJ-LONDA (467 KM) (CR) (N22000359)	2/2015	3/2024 (N.A.) {1/2025}	3,627.47 (3,627.00) {6,463.49}	4,054.95	84
		895	DAUND - MANMAD (236 KM) (CR) (N22000360)	2/2016	3/2023 (N.A.) {12/2024}	1,876.00 (N.A.) {2,081.27}	2,272.22	87
		896	MANMAD - JALGAON - 3RD LINE (160 KM) (CR) (N22000361)	2/2016	3/2022 (N.A.) {3/2025}	1,035.16 (N.A.) {1,552.24}	1,362.15	75
		897	WARDHA - NAGPUR - 4TH LINE (76 KM) (CR) (N22000362)	2/2016	3/2023 (N.A.) {5/2025}	637.95 (N.A.) {637.95}	793.21	70
		898	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) (SECR) (N22000420)	9/2016	3/2023 (Dec-23) {12/2025}	1,908.51 (2,753.05) {3,544.25}	2,747.21	80
		899	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (WR) (N22000434)	3/2010	(N.A.) {3/2024}	265.88 (N.A.) {311.36}	0.00	0
		900	WADSA-GADHCHIROLI NEW LINE (52.36 KM) (SECR) (N22000480)	6/2018	12/2021 (N.A.) {12/2026}	229.00 (N.A.) {1,886.05}	474.93	22
		901	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (N22000511)	8/2022	8/2027 (N.A.) {3/2027}	955.00 (N.A.) {955.39}	56.34	0
		902	SOLAPUR-TULJAPUR-OSMANABAD (UMBRELLA WORK) (CR) (N22000513)	1/2019	3/2028 (N.A.) {10/2027}	904.92 (N.A.) {3,295.74}	1,026.25	5

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		903	DHULE (BORVIHIR)-NARDANA (UMBRELLA WORK) (CR) (N22000514)	1/2019	3/2026 (N.A.) {9/2027}	492.76 (N.A.) {1,102.50}	151.37	5
		904	KALYAN-MURBAD VIA ULHASNAGAR (UMBRELLA WORK) (CR) (N22000515)	2/2023	3/2027 (N.A.) {3/2027}	836.12 (N.A.) {836.12}	7.52	0
		905	BARAMATI - LONAND (CR) (N22000615)	2/1999	3/2027 (N.A.) {2/2026}	736.44 (N.A.) {1,843.90}	540.33	50
		906	MUMBAI URBAN TRANSPORT PROJECT IIIA (MRVC) (N22000627)	4/2019	3/2025 (N.A.) {12/2027}	33,690.00 (N.A.) {33,690.00}	846.83	0
		907	NAGPUR- NAGBHIR RAILWAY LINE GAUGE CONVERSION PROJECT (MRIDC) (N22000629)	10/2019	6/2024 (N.A.) {6/2024}	1,400.00 (N.A.) {1,400.00}	0.00	77
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	908	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM (MoRTH) (N24000332)	1/2015	(N.A.) {}	225.81 (N.A.) {225.81}	167.96	0
		909	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN (NHAI) (N24000442)	12/2015	3/2019 (Nov-23) {12/2024}	649.50 (N.A.) {649.50}	585.49	88.04
		910	NAGPUR RING ROAD PACKAGE-1 (NHAI) (N24000558)	3/2016	7/2019 (Jul-23) {9/2024}	546.00 (N.A.) {546.00}	526.26	100
		911	NAGPUR RING ROAD PACKAGE-2 (NHAI) (N24000560)	3/2016	7/2019 (Mar-24) {12/2024}	591.66 (N.A.) {591.66}	617.70	90.72
		912	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000584)	3/2016	(N.A.) {12/2023}	1,142.62 (1,907.03) {1,142.62}	1,056.08	95.17

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		913	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE (MoRTH) (N24000585)	3/2016	(N.A.) {}	1,101.58 (N.A.) {1,101.58}	608.53	65.22
		914	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST (NHAI) (N24000655)	3/2017	3/2020 (Dec-24) {12/2024}	247.02 (N.A.) {157.49}	91.81	98.69
		915	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) (NHAI) (N24000656)	3/2017	3/2020 (Jul-22) {7/2024}	744.64 (N.A.) {1,007.00}	380.66	74.89
		916	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) (NHAI) (N24000659)	3/2017	3/2017 (May-21) {10/2024}	1,059.73 (1,071.00) {1,071.00}	878.19	82.04
		917	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF (NHAI) (N24000851)	3/2018	7/2021 (N.A.) {9/2024}	1,162.92 (1,182.87) {1,182.87}	371.48	52.46
		918	SARSAM TO KOTHARI (MoRTH) (N24001002)	2/2016	7/2019 (N.A.) {12/2023}	545.64 (N.A.) {545.64}	232.64	93.68
		919	AKOLA TO AKOT (MoRTH) (N24001003)	1/2017	6/2019 (N.A.) {12/2023}	313.95 (N.A.) {313.95}	270.26	99
		920	DIGRAS DARWAH KARANJA (MoRTH) (N24001013)	1/2017	6/2019 (N.A.) {12/2023}	391.06 (391.00) {391.06}	287.60	92.76
		921	DAHEGAON TO KUHI (MoRTH) (N24001017)	1/2017	6/2019 (N.A.) {12/2023}	228.89 (229.00) {228.89}	154.82	99
		922	BHANDARA TO GHOTITOK (MoRTH) (N24001018)	1/2017	6/2019 (N.A.) {6/2019}	392.83 (393.00) {392.83}	274.75	100
		923	AMDIT TO SAONER (MoRTH) (N24001021)	1/2017	6/2019 (N.A.) {12/2023}	396.91 (397.00) {396.91}	289.79	98.69

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		924	WADI TO ASOLA (MoRTH) (N24001022)	1/2017	9/2019 (N.A.) {12/2023}	363.82 (364.00) {363.82}	154.65	93.15
		925	WAKAN PALI KHOPOLI (MoRTH) (N24001026)	1/2017	5/2019 (N.A.) {10/2023}	376.19 (N.A.) {376.19}	118.74	99.15
		926	SHAHPUR PATGAON SECTION I (MoRTH) (N24001027)	1/2018	12/2019 (N.A.) {3/2024}	150.79 (N.A.) {150.79}	81.14	70.66
		927	AHMADPUR TO PIMPLA (MoRTH) (N24001029)	1/2017	8/2019 (N.A.) {12/2023}	422.38 (N.A.) {422.38}	269.59	83
		928	PIMPLA TO MANJARUMBHA (MoRTH) (N24001030)	1/2017	8/2019 (N.A.) {12/2023}	595.77 (N.A.) {595.77}	357.73	89.6
		929	MANSAR TO SALAIKHURD (MoRTH) (N24001035)	1/2018	12/2019 (N.A.) {11/2023}	418.36 (N.A.) {418.36}	263.13	99
		930	JINTUR TO PARBHANI (MoRTH) (N24001039)	1/2017	(N.A.) {12/2023}	356.66 (N.A.) {356.66}	209.48	80.48
		931	JAHIRABAD TO LATUR (MoRTH) (N24001040)	1/2017	11/2019 (N.A.) {11/2023}	461.96 (N.A.) {461.96}	329.59	0
		932	SHIROD SHAHPURER TO NANDED (MoRTH) (N24001041)	1/2017	7/2019 (N.A.) {12/2023}	211.34 (N.A.) {211.34}	136.33	99.9
		933	SALAIKHURD TO TIRORA (MoRTH) (N24001042)	1/2018	12/2019 (N.A.) {12/2023}	415.25 (415.25) {415.25}	274.02	98
		934	NILAJPHATA TO BHANDARA (MoRTH) (N24001043)	1/2018	5/2020 (N.A.) {12/2023}	420.63 (421.00) {420.63}	219.40	71.25
		935	RALEGAON TO RAMTIRTH (MoRTH) (N24001046)	1/2017	7/2019 (N.A.) {8/2023}	210.81 (N.A.) {210.81}	210.81	96.5
		936	MEHKAR TO AJISPUR (MoRTH) (N24001048)	1/2017	7/2019 (N.A.) {8/2023}	232.77 (N.A.) {232.77}	151.60	100
		937	VITA TO NAGAJ (MoRTH) (N24001050)	3/2018	12/2019 (N.A.) {12/2023}	304.58 (305.00) {304.58}	154.68	68.39
		938	KARAD PATAN CHIPLUN GUHAGAR (MoRTH) (N24001057)	2/2017	6/2019 (N.A.) {10/2023}	407.19 (407.00) {407.19}	323.02	89.97

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		939	KARWANDI TO RAJURI (MoRTH) (N24001058)	3/2018	12/2019 (N.A.) {3/2024}	276.95 (277.00) {276.95}	160.94	92.06
		940	PALPHATA TO PHULAMBARI (MoRTH) (N24001060)	3/2018	12/2019 (N.A.) {12/2023}	227.19 (227.00) {227.19}	141.92	95
		941	CHIKALI TO DHAD (MoRTH) (N24001061)	3/2018	12/2019 (N.A.) {3/2024}	189.46 (189.00) {189.46}	133.07	97.76
		942	DHAD BHOKARDAN TO BHOKARDHAN SILLOD (MoRTH) (N24001062)	3/2018	12/2019 (N.A.) {3/2024}	336.21 (336.00) {336.21}	236.11	99.82
		943	PARBHANI TO GANGKHED (MoRTH) (N24001065)	3/2018	12/2019 (N.A.) {10/2023}	238.19 (238.00) {238.19}	194.54	99
		944	NANDED TO JALKOT (MoRTH) (N24001069)	12/2017	9/2019 (N.A.) {9/2019}	456.93 (457.00) {456.93}	278.22	0
		945	KOTHARI TO DHANORA (MoRTH) (N24001073)	9/2018	8/2020 (N.A.) {8/2020}	301.38 (301.00) {301.38}	240.32	0
		946	OSMANNAGAR TO KUNDRAL (MoRTH) (N24001075)	9/2017	8/2020 (N.A.) {12/2023}	344.25 (344.00) {344.25}	194.72	95.63
		947	PUNE TO MALE VILLAGE (MoRTH) (N24001078)	3/2018	12/2019 (N.A.) {12/2023}	228.31 (N.A.) {228.31}	100.97	93.83
		948	ARDHAPUR TO HIMAYATNAGAR (MoRTH) (N24001079)	12/2017	6/2020 (N.A.) {12/2023}	426.06 (426.00) {426.06}	271.40	96.25
		949	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER (MoRTH) (N24001080)	3/2018	12/2019 (N.A.) {10/2023}	256.15 (N.A.) {256.15}	126.62	98
		950	HIMAYATNAGAR TO PHULSAWANGI (MoRTH) (N24001081)	3/2018	12/2019 (N.A.) {12/2023}	294.87 (295.00) {294.87}	183.17	89.99
		951	PUNE RAIGARH DISTRICT BORDER TO MANGAON (MoRTH) (N24001082)	3/2018	12/2019 (N.A.) {12/2023}	223.46 (N.A.) {223.46}	123.46	100
		952	KOLDE TO KHETIYA (MoRTH) (N24001090)	1/2017	7/2019 (N.A.) {12/2023}	509.18 (N.A.) {509.18}	283.13	94.81

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		953	SATARA TO MHASWAD (MoRTH) (N24001092)	1/2017	7/2019 (N.A.) {12/2023}	653.46 (N.A.) {653.46}	369.62	76.76
		954	SATARA MURVAD PILLOV PANDHARPUR (MoRTH) (N24001095)	1/2017	(N.A.) {6/2024}	388.44 (N.A.) {388.44}	240.05	88.16
		955	SELDOH TO PANVAR (MoRTH) (N24001097)	7/2018	5/2020 (N.A.) {5/2020}	404.33 (404.00) {404.33}	140.65	0
		956	MHASWAD TO TEMBHURNI (MoRTH) (N24001099)	1/2017	7/2019 (N.A.) {12/2023}	488.60 (N.A.) {488.60}	279.42	76.5
		957	KURUDWADI TO PANDHARPUR (MoRTH) (N24001101)	1/2017	7/2019 (N.A.) {11/2023}	307.63 (N.A.) {307.63}	232.57	96.27
		958	PANDHARPUR TO SANGOLA (MoRTH) (N24001102)	7/2017	7/2019 (N.A.) {12/2023}	218.38 (N.A.) {218.38}	182.63	99.78
		959	CHIMUR TO WARORA (MoRTH) (N24001105)	11/2016	3/2019 (N.A.) {3/2019}	467.70 (N.A.) {467.70}	235.04	100
		960	PEN TO KHOPOLI (MoRTH) (N24001106)	3/2018	3/2018 (N.A.) {1/2024}	301.39 (302.00) {301.39}	170.12	82.07
		961	PANCHARAL TO MANDANGHAR (MoRTH) (N24001107)	7/2018	5/2020 (N.A.) {5/2020}	381.08 (302.00) {381.08}	45.66	0
		962	KOLHA TO NASRATPUR (MoRTH) (N24001111)	4/2016	4/2019 (N.A.) {8/2024}	281.78 (282.00) {281.78}	77.83	0
		963	NASRATPUR TO BARASGAON (MoRTH) (N24001112)	7/2016	9/2019 (N.A.) {3/2024}	406.54 (407.00) {406.54}	274.30	80.7
		964	BARASGAON TO RAHATEE (MoRTH) (N24001113)	7/2016	9/2018 (N.A.) {12/2023}	289.11 (290.00) {289.11}	232.56	99
		965	INDAPUR TO VADPALE (MoRTH) (N24001114)	1/2017	12/2019 (N.A.) {3/2024}	1,202.52 (1,656.94) {1,202.52}	1,450.82	61.42
		966	PAITHAN TO SHIRUR (MoRTH) (N24001122)	3/2017	6/2019 (N.A.) {3/2024}	341.80 (N.A.) {341.80}	226.19	78.6

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		967	SHIRUR TO KHARDA (MoRTH) (N24001123)	2/2017	6/2019 (N.A.) {12/2023}	381.77 (N.A.) {381.77}	199.48	83.93
		968	AURANGABAD TO SILLOD (MoRTH) (N24001124)	2/2017	6/2019 (N.A.) {12/2023}	456.32 (541.93) {456.32}	355.54	94.07
		969	SILLOD TO FARDAPUR (MoRTH) (N24001125)	2/2017	6/2019 (N.A.) {12/2023}	337.46 (432.98) {337.46}	335.30	91.56
		970	FARDAPUR TO JALGAON (MoRTH) (N24001126)	2/2017	6/2019 (N.A.) {6/2019}	456.45 (N.A.) {456.45}	427.43	0
		971	KUMBHARI PHTA TO DEULGAON RAJA (MoRTH) (N24001127)	2/2017	6/2019 (N.A.) {2/2024}	406.51 (N.A.) {406.51}	340.26	0
		972	BHOGAN KHURD TO KASHEDI (MoRTH) (N24001132)	9/2017	6/2021 (N.A.) {12/2023}	743.21 (743.00) {743.21}	911.64	88.69
		973	KANTE TO WAKED (MoRTH) (N24001134)	3/2016	11/2019 (N.A.) {12/2024}	1,230.02 (1,230.00) {1,230.02}	791.80	0
		974	PARLI PIMPLA DAHIGUDA (MoRTH) (N24001138)	2/2017	6/2019 (N.A.) {8/2023}	205.72 (206.00) {205.72}	85.71	100
		975	WARDHA TO ARVI (MoRTH) (N24001150)	2/2018	4/2020 (N.A.) {12/2023}	313.58 (N.A.) {313.58}	230.41	0
		976	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001377)	2/2019	1/2022 (Aug-23) {8/2023}	731.89 (731.99) {731.99}	689.19	0.2
		977	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001378)	2/2019	1/2022 (Jun-23) {6/2023}	362.46 (372.46) {372.46}	347.31	0.7
		978	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 (NHAI) (N24001379)	2/2019	1/2022 (Aug-23) {8/2023}	594.75 (594.75) {613.75}	585.20	0.5

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		979	UPGRADATION OF ADHALGAON- JAMKHEDE SECTION OF NH-548 D FROM KM 132/600 TO KM 195/375 TO TWO LANE WITH (MoRTH) (N24001448)	11/2021	2/2022 (N.A.) {2/2022}	223.35 (N.A.) {223.35}	209.36	0
		980	REPANPALLI TO SIRONCHA (MoRTH) (N24001468)	3/2022	6/2022 (N.A.) {6/2024}	282.07 (N.A.) {282.07}	34.65	0
		981	TUNNEL AT KHAMBATKI GHAT SECTION AND ITS APPROACHES FROM EXISTING KM. 771.730 TO EXISTING KM. 782.0 (NHAI) (N24001486)	2/2019	2/2022 (Dec-24) {12/2024}	493.00 (N.A.) {493.00}	374.15	72.34
		982	DHARAMPURI-LONAND FROM KM. 117.00 TO 166.40 (PKG-IV) ON MOHOL-ALANDI SECTION (NHAI) (N24001488)	9/2021	9/2023 (Dec-24) {12/2024}	618.45 (N.A.) {618.45}	586.95	90
		983	6L OF KAGAL-SATARA SECTION FROM KM 658.000 TO KM 725.000 OF NH-48 (PKG-II) (NHAI) (N24001493)	12/2022	12/2024 (N.A.) {12/2024}	1,749.86 (N.A.) {1,749.86}	1,311.00	57.96
		984	4L OF RATNAGIRI - KOLHAPUR SECTION OF NH-166 FROM KM 0.000 TO KM 19.769 AND KM 31.000 TO KM 67.140 () (NHAI) (N24001495)	11/2022	11/2024 (N.A.) {11/2024}	930.00 (N.A.) {930.00}	557.53	59.95
		985	PATAS-VASUNDE PHATA - BARAMATI BYPASS (NHAI) (N24001501)	9/2021	9/2023 (Jul-23) {7/2023}	531.86 (532.41) {532.41}	520.71	0.5
		986	4L OF BARAMATI TO INDAPUR (PKG-II) FROM KM. 41.400 TO KM. 84.550 OF NH- 965G (SAINT TUKARAM MARG) (NHAI) (N24001502)	9/2021	9/2023 (Mar-24) {12/2024}	624.45 (580.15) {580.15}	398.06	2

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		987	4L OF INDAPUR TO TONDLE (PKG-III) FROM KM.84.550 TO KM. 131.00 OF NH- 965G (SAINT TUKARAM MARG) (NHAI) (N24001503)	9/2021	9/2023 (Mar-24) {12/2024}	667.66 (666.21) {666.21}	579.71	13
		988	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XI) [KM. 77.000 TO KM. 103.400] (GANJAD - TALSARI) (NHAI) (N24001504)	5/2022	5/2024 (Jan-25) {1/2025}	1,260.00 (N.A.) {1,260.00}	488.05	90.58
		989	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XII) [KM. 50.700 TO KM. 77.000] (MASVAN - GANJAD) (NHAI) (N24001505)	3/2022	3/2024 (Oct-24) {10/2024}	1,549.02 (N.A.) {1,549.02}	537.10	51.8
		990	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIII) [KM. 26.582 TO KM. 50.700] (SHIRSAD - MASVAN) (NHAI) (N24001506)	2/2022	2/2024 (Jun-25) {6/2025}	2,747.00 (N.A.) {2,747.00}	929.38	63.7
		991	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XIV) [KM. 3.000 TO KM. 20.200 OF SPUR] (SHIRSAD - AKLOLI) (NHAI) (N24001507)	11/2022	5/2024 (Aug-25) {8/2025}	1,124.00 (N.A.) {1,124.00}	299.43	44
		992	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVI) [KM. 43.000 TO KM. 69.800 OF SPUR] (AMNE - BHOJ) (NHAI) (N24001508)	11/2022	10/2024 (N.A.) {10/2024}	1,450.00 (N.A.) {1,450.00}	545.51	63.27
		993	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XV) [KM. 20.200 TO KM. 43.000 OF SPUR] (AKLOLI - AMNE) (NHAI) (N24001521)	11/2022	10/2024 (Apr-25) {4/2025}	990.00 (N.A.) {990.00}	296.63	50.5
		994	6L OF KAGAL-SATARA SECTION FROM KM 592.240 TO KM 658.000 OF NH-48 (PKG-I) (NHAI) (N24001546)	1/2023	1/2025 (N.A.) {1/2025}	1,025.20 (N.A.) {1,025.20}	758.28	39.1

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		995	BALANCE WORKS OF 4L PANVEL- INDAPUR SECTION OF NH-66 (OLD NH- 17) FROM KM 42.300 (KASU) TO KM 84.600 ((NHAI) (N24001607)	10/2022	5/2024 (N.A.) {5/2024}	332.00 (N.A.) {332.00}	185.61	42.44
		996	VADODARA MUMBAI EXPRESSWAY (PHASE II - PKG XVII) [KM. 69.800 TO KM. 79.783 OF SPUR] (BHOJ - MORBE) (NHAI) (N24001608)	9/2021	7/2025 (N.A.) {7/2025}	2,208.68 (N.A.) {2,208.68}	411.34	50.36
		997	BALANCE WORK OF 4 LANING OF PANVEL TO INDAPUR SECTION OF NH- 66(OLD NH- 17) FROM KM 0.000 (PANVEL) TO (NHAI) (N24001609)	1/2023	12/2023 (Dec-24) {12/2024}	151.26 (N.A.) {151.26}	103.54	67.03
		998	4L OF EXISTING 2/4L STRETCH FROM LONAND TO DIVE GHAT (KM 166.400 TO KM 220.900) OF MOHOL ALANDI S (NHAI) (N24001610)	1/2022	5/2024 (Mar-25) {3/2025}	1,833.73 (N.A.) {1,833.73}	391.72	79.02
		999	FOUR LANING OF AURANGABAD- PAITHAN SECTION OF NH-752E ON EPC MODE IN THE STATE OF MAHARASHTRA (NHAI) (N24001795)	10/2022	7/2024 (N.A.) {9/2024}	490.40 (N.A.) {289.00}	241.93	77
		1000	4L OF RAJURA-KORPANA-ADILABAD ROAD UPTO M.S. BORDER FROM KM 32.910 TO KM 89.090 OF NH-353B (NHAI) (N24001796)	3/2022	10/2024 (Apr-25) {4/2025}	1,013.33 (1,013.33) {1,111.33}	355.07	62.01
		1001	6L OF WAINGANGA BRIDGE - BHANDARA (INCLUDING BHANDARA BYPASS) SECTION FROM KM 485.000 TO KM 499.800 (NHAI) (N24001797)	10/2021	1/2024 (N.A.) {3/2025}	815.77 (N.A.) {815.77}	619.93	91.54

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1002	4L MITIGATION MEASURE STRUCTURES ON CH/MH BORDER TO WAINGANGA BRIDGE SECTION OF NH-53 (NHAI) (N24001798)	2/2021	11/2023 (N.A.) {11/2024}	540.21 (N.A.) {540.21}	415.87	94.44
		1003	4L OF NAGPUR-KATOL SECTION FROM KM. 13.00 TO KM. 62.900 OF NH-353J (NHAI) (N24001799)	2/2021	10/2023 (N.A.) {12/2024}	1,166.96 (N.A.) {1,251.00}	1,035.36	80
		1004	BAL. WORKS OF FAGNE (KM. 510.000) TO MAHARASHTRA/GUJARAT BORDER (KM. 650.794) (NHAI) (N24001804)	12/2019	9/2022 (Jun-24) {6/2024}	1,654.07 (N.A.) {980.00}	835.19	91.76
		1005	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 67.140 TO KM 112.340 OF NH- 166 (PKG II) (NHAI) (N24001834)	5/2023	5/2025 (N.A.) {5/2025}	839.00 (N.A.) {839.00}	412.49	37.72
		1006	4L OF RATNAGIRI - KOLHAPUR SECTION FROM KM 112.340 TO KM 145.300 OF NH- 166 (PKGIII) (NHAI) (N24001835)	5/2023	5/2025 (N.A.) {5/2025}	986.00 (N.A.) {986.00}	315.88	37.45
		1007	REHABILITATION AND UP-GRADATION TO 4 LANE ROAD WITH PAVED SHOULDER CONFIGURATION OF SECTION FROM UND (MoRTH) (N24001880)	3/2022	7/2025 (N.A.) {7/2025}	778.18 (N.A.) {778.18}	135.78	27.35
		1008	REHABILITATION AND UPGRADATION OF AMBOLI JUNCTION (DESIGN CH. 71+530) TO AJARA (DESIGN CH.100+835) SE (MoRTH) (N24001881)	6/2021	11/2024 (N.A.) {11/2024}	574.00 (N.A.) {574.00}	574.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1009	CONSTRUCTION OF NEW FOUR LANE BYPASS TO PARBHANI CITY (PARWA TO ASOLA) KM 463/265 TO KM 481/180 (DES (MoRTH) (N24001882)	3/2022	10/2024 (N.A.) {10/2024}	496.64 (N.A.) {496.64}	0.00	8
		1010	CONSTRUCTION OF 4 LANE FLYOVER AT NAGPUR RTO CHOWK TO NAGPUR UNIVERSITY CAMPUS FROM CH 2/250 TO 5/10 (MoRTH) (N24001883)	3/2021	3/2024 (N.A.) {4/2024}	478.83 (N.A.) {478.83}	233.48	65
		1011	REHABILITATION AND UPGRADATION OF SATANA TO MANGRUL (CHANDWAD) SECTION OF NH752 G DESIGN CH: KM 64.0 (MoRTH) (N24001884)	3/2023	5/2025 (N.A.) {5/2025}	428.80 (N.A.) {428.80}	54.11	30.69
		1012	REHABILITATION AND UP-GRADATION OF JINTUR- SHIRAD SHAHAPUR SECTION KM 258.300 TO KM 306.300 [DESIGN (MoRTH) (N24001885)	2/2023	12/2024 (N.A.) {12/2024}	414.81 (N.A.) {414.81}	0.00	0
		1013	DEVELOPMENT/WIDENING OF TALEGAON CHAKAN SHIKRAPUR NHAVARA SECTION OF NH 548DG (NHAVARA TO CHOU (MoRTH) (N24001886)	10/2022	8/2024 (N.A.) {8/2024}	304.68 (N.A.) {304.68}	97.09	58.78
		1014	REHABILITATION AND UPGRADATION OF BHOKARDAN TO KUMBHARI FATA DESIGN CH. (KM 13+500 TO 17+00) AND RAJ (MoRTH) (N24001887)	8/2022	6/2024 (N.A.) {6/2024}	291.37 (N.A.) {291.37}	102.94	0
		1015	UP-GRADATION OF TIRORA-GONDIA, STATE HIGHWAY FROM EXISTING KM 163+213 (ON SH-335, TIRORA) TO KM 191+ (MoRTH) (N24001888)	8/2021	4/2023 (N.A.) {5/2024}	288.14 (N.A.) {288.14}	63.01	46.31

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1016	2 LANE + PS PIMPLNER TO SATANA - [DESIGN CHAINAGE KM 21.427 TO 64.00] OF NH-752G] (MoRTH) (N24001889)	9/2019	7/2021 (N.A.) {12/2023}	277.81 (N.A.) {277.81}	148.68	0
		1017	REHABILITATION AND UPGRADATION OF PARLI TO SIRSALA SECTION OF NH-361F (KM 136+700 TO 115+000) (LENGT (MoRTH) (N24001890)	2/2023	12/2024 (N.A.) {12/2024}	261.82 (N.A.) {261.82}	70.59	46
		1018	BALANCE WORK OF REHABILITATION AND UP-GRADATION TO NH-166F FROM MAHAD JUNCTION (AT KM 123/400 ON NH- (MoRTH) (N24001891)	7/2021	11/2023 (N.A.) {3/2024}	256.54 (N.A.) {256.54}	80.10	59.66
		1019	REHABILITATION AND UPGRADATION OF SHIRAPUR JUNCTION TO SHIVAJI CHOWK (DESIGN CHAINAGE KM. 130+00 TO (MoRTH) (N24001892)	2/2023	12/2024 (N.A.) {12/2024}	245.61 (N.A.) {245.61}	43.39	32.5
		1020	SHEWALI (SAKRI) - NANDURBAR (MoRTH) (N24001893)	9/2022	4/2024 (N.A.) {7/2024}	232.59 (N.A.) {232.59}	97.70	77.64
		1021	2 LANE + PS ASTHAMODE - TIVATYAL [DESIGN CH. KM 24.300 - 62.00] [KM 134.98-172.95 OF NH-63] (MoRTH) (N24001894)	9/2019	7/2021 (N.A.) {12/2023}	228.82 (N.A.) {228.82}	144.54	95.44
		1022	REHABILITATION AND UPGRADATION TO TWO LANES WITH PAVED SHOULDER CONFIGURATION FROM WATUR TO CHARTHANA (MoRTH) (N24001895)	11/2021	9/2023 (N.A.) {12/2023}	228.01 (N.A.) {228.01}	103.01	99
		1023	UPGRADATIOBN AND REHABILITATION OF SECTION OF NH 361 F FROM PARLI (00/000) TO GANGAKHED (30/400) TO (MoRTH) (N24001896)	11/2021	9/2023 (N.A.) {4/2024}	224.44 (N.A.) {224.44}	75.34	45.63

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1024	REHABILITATION AND UP-GRADATION OF SABALKHED TO ASHTI SECTION FROM KM 37+900 TO KM 55+100 AND CHINCH (MoRTH) (N24001902)	12/2022	9/2024 (N.A.) {9/2024}	213.32 (N.A.) {213.32}	20.00	34
		1025	REHABILITATION AND UP-GRADATION OF MUDKHED TO NANDED SECTION FROM KM. 372+000 TO KM 388+400 OF NH 16 (MoRTH) (N24001903)	8/2022	4/2025 (N.A.) {4/2025}	206.54 (N.A.) {206.54}	21.36	0
		1026	KOPARGAON TO SAVALI VIHIR SECTION (MoRTH) (N24001904)	9/2022	7/2024 (N.A.) {7/2024}	195.38 (N.A.) {195.38}	29.59	19.76
		1027	CONSTRUCTION OF MAJOR BRIDGE ACROSS MANJRA RIVER NEAR YESGI VILLAGE @ KM, 166/500 ON NH 63 TQ BILOLI (MoRTH) (N24001905)	10/2021	8/2023 (N.A.) {12/2023}	188.69 (N.A.) {188.69}	111.26	95.8
		1028	UP-GRADATION TO 4 LANING OF DAULTABAD T-POINT TO MALIWADA [FROM DESIGN KM.0.000 TO KM 4.000] AND UPG (MoRTH) (N24001906)	8/2022	3/2024 (N.A.) {3/2024}	185.59 (N.A.) {185.59}	63.56	48
		1029	CONSTRUCTION OF SIX LANE FLYOVER AT KATRAJ JUNCTION AT KM, 3/880 OF NH 548-DD (VADGAON - KATRAJ - KO (MoRTH) (N24001907)	6/2021	2/2024 (N.A.) {3/2024}	169.15 (N.A.) {169.15}	36.94	35.96
		1030	UPGRADATION OF EXHISTING 2 LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDERS RIGID PAVEMENT FROM DESI (MoRTH) (N24001908)	12/2021	5/2024 (N.A.) {5/2024}	167.97 (N.A.) {167.97}	35.28	36.76

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1031	STRENGTHING AND WIDINING OF EXISTING CARRIAGEWAY TO 10 M IN KM, 156/160 TO 229/160 (TEMBHURNI - KUSL (MoRTH) (N24001909)	11/2021	6/2024 (N.A.) {6/2024}	157.72 (N.A.) {157.72}	55.38	90.41
		1032	REHABILITATION AND UPGRADATION OF JAMKHEDE TO SAUTADA SECTION OF NH548 D (FROM KM 195.375 TO KM 208.7 (MoRTH) (N24001910)	9/2022	7/2024 (N.A.) {7/2024}	157.62 (N.A.) {157.62}	13.86	17.03
		1033	PANGAON TO DHARMAPURI AND PARALI TO INJEGAON 2L+PS (MoRTH) (N24001911)	3/2018	7/2024 (N.A.) {12/2023}	152.03 (N.A.) {152.03}	81.35	97.57
		1034	4L OF INDORA CHOWK TO PACHPAOLI AND AGRASEN CHOWK - ASHOKA CHOWK (NHAI) (N24002071)	3/2023	6/2026 (N.A.) {6/2026}	998.27 (N.A.) {998.27}	127.21	16.75
		1035	IMPROVEMENT OF EXISTING ALIGNMENT OF PANDHARPUR TOWN PART BYPASSED SECTION FROM WAKHARI TO LORD VITT (NHAI) (N24002072)	7/2022	10/2025 (N.A.) {10/2025}	150.21 (150.21) {150.21}	12.74	15.86
		1036	STRENGTHENING OF 6-LANE PIMPALGAON-NASHIK-GONDE (KM. 380 - KM. 440) SECTION OF NH-3 IN MAHARASHTRA U (NHAI) (N24002137)	2/2024	3/2025 (N.A.) {3/2025}	175.00 (N.A.) {175.00}	66.62	27.1
	URBAN DEVELOPME NT	1037	MUMBAI METRO LINE 3 (COLABA- BANDRA-SEEPZ) (MMRCL) (N28000086)	7/2013	3/2020 (N.A.) {12/2023}	23,136.00 (N.A.) {37,276.00}	23,687.33	87.2
		1038	PUNE METRO RAIL PROJECT (PHASE 1) (MMRC) (N28000121)	12/2016	11/2021 (Sep-24) {9/2024}	11,420.00 (13,656.22) {13,656.22}	12,485.83	100
		1039	NAGPUR METRO RAIL PROJECT PHASE II (NMRCL) (N28000155)	12/2022	12/2027 (N.A.) {12/2027}	6,708.00 (N.A.) {6,708.00}	293.46	12.7

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1040	PCMC NIGDI PROJECT EXTENSION OF CORRIDOR 1 OF PUNE METRO PHASE 1 (MMRC) (N28000157)	10/2023	1/2027 (N.A.) {1/2027}	910.18 (N.A.) {910.18}	0.00	6
	<u>WATER RESOURCES</u>	1041	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA (BPB) (N30000001)	3/2017	12/2019 (Aug-24) {12/2023}	233.57 (N.A.) {233.57}	217.42	
<u>MANIPUR</u>	<u>CIVIL AVIATION</u>	1042	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, CONTROL TOWER CUM TECHNICAL BLOCK, APRON, LINK TAX (AAI) (N04000100)	11/2021	7/2024 (Dec-25) {12/2025}	499.00 (N.A.) {499.00}	106.39	36.88
	<u>RAILWAYS</u>	1043	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) (NFR) (220100288)	4/2003	3/2011 (Mar-28) {12/2028}	4,454.17 (12,274.06) {19,517.70}	14,774.02	79.8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1044	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) (NHIDCL) (N24001270)	3/2020	6/2022 (Dec-23) {12/2024}	292.24 (N.A.) {292.24}	127.86	85.33
		1045	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) (NHIDCL) (N24001271)	6/2020	8/2022 (N.A.) {12/2024}	365.53 (N.A.) {365.53}	156.31	77.36
		1046	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) (NHIDCL) (N24001272)	3/2020	6/2022 (N.A.) {12/2024}	167.95 (204.12) {167.95}	88.05	69.89
		1047	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) (NHIDCL) (N24001273)	7/2020	8/2022 (N.A.) {12/2024}	177.76 (N.A.) {177.76}	89.67	80.53

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1048	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI (NHIDCL) (N24001274)	8/2020	4/2022 (Jun-25) {8/2025}	379.39 (N.A.) {379.39}	189.86	45.88
		1049	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO (NHIDCL) (N24001275)	8/2020	4/2022 (N.A.) {12/2025}	268.98 (N.A.) {268.98}	22.08	0
		1050	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI (NHIDCL) (N24001276)	8/2020	4/2022 (N.A.) {12/2025}	228.97 (N.A.) {228.97}	0.00	0
		1051	MARIAM - PEREN PKG-1A (NHIDCL) (N24001349)	2/2021	12/2022 (N.A.) {4/2025}	226.32 (N.A.) {226.32}	86.41	63.75
		1052	MARIAM - PEREN (PKG 1B) (NHIDCL) (N24001350)	2/2021	12/2022 (Oct-24) {10/2024}	188.36 (N.A.) {188.36}	126.71	95.37
		1053	IMPHAL MOREH PACKAGE- 3 (NHIDCL) (N24001352)	3/2021	12/2022 (N.A.) {6/2024}	259.31 (N.A.) {259.31}	144.94	100
		1054	IMPHAL - KHONGSANG PKG-2 (NHIDCL) (N24001353)	3/2021	12/2022 (Nov-23) {6/2025}	195.14 (N.A.) {195.14}	59.99	50.75
		1055	TAMENGLONG - MAHUR PKG-3 (NHIDCL) (N24001354)	3/2021	12/2022 (Jan-25) {1/2025}	234.08 (N.A.) {234.08}	139.45	90.34
		1056	IMPHAL MOREH (PACKAGE 4) (NHIDCL) (N24001399)	3/2021	1/2023 (N.A.) {4/2024}	277.99 (N.A.) {277.99}	146.35	100
		1057	SENAPATI- IMPHAL PKG-5B (NHIDCL) (N24001400)	3/2021	1/2023 (N.A.) {5/2025}	211.70 (N.A.) {211.70}	35.16	34.86
		1058	IMPHAL - KHONGSANG PKG-3 (NHIDCL) (N24001401)	7/2021	3/2023 (Feb-24) {3/2025}	467.00 (N.A.) {467.00}	183.55	75.23
		1059	TAMENGLONG - MAHUR PKG-1 (NHIDCL) (N24001402)	7/2021	3/2023 (Jan-25) {1/2025}	185.80 (N.A.) {185.80}	112.31	92.65

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1060	TAMENGLONG - MAHUR PKG-2 (NHIDCL) (N24001403)	7/2021	3/2023 (May-24) {2/2025}	483.87 (N.A.) {483.87}	278.89	91.03
		1061	TAMENGLONG - MAHUR PKG-4 (NHIDCL) (N24001404)	7/2021	3/2023 (Feb-25) {2/2025}	198.77 (N.A.) {198.77}	110.09	85.12
		1062	CHURACHANPUR TUIVAI PKG-3 (NHIDCL) (N24001405)	7/2021	10/2023 (Feb-24) {6/2025}	673.27 (N.A.) {673.27}	357.47	72.74
		1063	TAMENGLONG - MAHUR PKG-5 (NHIDCL) (N24001436)	8/2021	5/2023 (Jan-25) {2/2025}	477.86 (N.A.) {477.86}	235.67	80.3
		1064	TAMENGLONG - MAHUR PKG-6 (NHIDCL) (N24001437)	9/2021	5/2023 (Oct-23) {4/2025}	311.18 (N.A.) {311.18}	171.57	72.7
		1065	MARAM - PEREN PKG-3 (NHIDCL) (N24001439)	8/2021	5/2023 (N.A.) {10/2024}	467.41 (N.A.) {467.41}	243.19	92.18
		1066	IMPHAL - KHONGSANG PKG-4 (NHIDCL) (N24001453)	8/2021	12/2023 (N.A.) {12/2025}	579.63 (N.A.) {579.63}	131.58	52.55
		1067	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001473)	9/2021	2/2024 (N.A.) {4/2025}	310.76 (N.A.) {310.76}	116.81	76.8
		1068	IMPHAL - KHONGSANG PKG-5 (NHIDCL) (N24001538)	12/2021	5/2024 (N.A.) {10/2025}	410.68 (N.A.) {410.68}	105.71	50.81
		1069	IMPHAL - KHONGSANG PKG-6 (NHIDCL) (N24001539)	12/2021	2/2025 (N.A.) {11/2025}	504.76 (N.A.) {504.76}	101.94	44.33
		1070	AKASH BRIDGE - JESSAMI SECTION PKG- 2 (NHIDCL) (N24001540)	3/2022	2/2025 (N.A.) {2/2025}	152.11 (N.A.) {152.11}	53.26	72.82
		1071	CONSTRUCTION OF 2-LANING WITH HARD SHOULDER ROAD OF UKHRUL - TOLOI - TADUBI SECTION OF NH-102A FROM (NHIDCL) (N24001974)	9/2021	1/2025 (N.A.) {1/2025}	315.56 (N.A.) {315.56}	60.70	49.44

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MEGHALAYA		1072	LMPHAL TO JIRIBAM PKG-7 (NHIDCL) (N24002028)	1/2023	12/2025 (N.A.) {3/2026}	760.16 (N.A.) {760.16}	63.80	27.83
		1073	UKHRUL TOLOI TADUBI PKG-2 (NHIDCL) (N24002131)	3/2023	2/2026 (N.A.) {3/2026}	578.98 (N.A.) {578.98}	56.22	31.54
	DEPARTMEN T OF HIGHER EDUCATION	1074	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA (RITES OF HIGHER) (N42000001)	9/2013	9/2014 (Jul-24) {7/2024}	484.32 (429.70) {429.70}	274.05	72.5
	DONER	1075	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR (HSCL FOR DONER) (N12000103)	4/2014	9/2017 (N.A.) {9/2017}	151.33 (N.A.) {151.33}	148.33	98.5
	RAILWAYS	1076	NEW BG LINE FROM BYRNIHAT TO SHILLONG (NFR) (N22000205)	4/2010	3/2021 (N.A.) {3/2021}	906.46 (1,202.33) {8,324.28}	269.80	2
	ROAD TRANSPORT AND HIGHWAYS	1077	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T (NHIDCL) (N24000771)	4/2017	9/2021 (Jul-23) {3/2025}	553.51 (610.09) {553.51}	343.73	67.31
		1078	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM (NHIDCL) (N24000903)	3/2019	3/2022 (Dec-23) {12/2023}	306.28 (N.A.) {306.28}	233.49	100
		1079	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM () (NHIDCL) (N24001313)	11/2020	12/2023 (Oct-25) {10/2025}	351.12 (N.A.) {351.12}	223.73	24.2

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1080	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL (NHIDCL) (N24001314)	11/2020	12/2023 (N.A.) {8/2026}	525.68 (N.A.) {525.68}	384.55	13.5
		1081	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL (NHIDCL) (N24001334)	11/2020	12/2023 (N.A.) {4/2026}	445.51 (N.A.) {445.51}	191.35	6.2
		1082	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B (NHIDCL) (N24001335)	11/2020	12/2023 (N.A.) {11/2026}	284.21 (N.A.) {284.21}	45.46	1.5
		1083	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) (NHIDCL) (N24001339)	10/2020	4/2022 (Jun-24) {12/2024}	157.86 (146.92) {157.86}	146.19	97.49
		1084	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 (NHIDCL) (N24001360)	3/2021	12/2022 (Jun-24) {11/2024}	260.21 (N.A.) {260.21}	202.19	89.14
		1085	REHABILITATION AND UPGRADATION OF NONGSTOIN TO WAHKAJI SECTION OF PROJECT ROAD KM 0.000 TO KM 43.06 (MoRTH) (N24001441)	8/2020	2/2022 (Oct-24) {10/2024}	302.88 (N.A.) {302.88}	209.63	93
		1086	REHABILITATION AND UP GRADATION OF NONGSTOIN-RAMBRAI-KYRSHAI ROAD UP TO MEGHALAYA-ASSAM BORDER FROM (NHIDCL) (N24001474)	9/2021	5/2024 (N.A.) {1/2025}	359.86 (N.A.) {359.86}	219.87	78.5
		1087	RANIKOR- MAHESHKHOLA- BAGHMARA PKG-2 (NHIDCL) (N24001541)	11/2021	6/2024 (N.A.) {12/2024}	283.50 (N.A.) {283.50}	201.77	70.68

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
MIZORAM		1088	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADUM (NHIDCL) (N24002156)	3/2023	9/2026 (N.A.) {9/2026}	620.30 (N.A.) {620.30}	168.64	0
		1089	SHILLONG WESTERN BYPASS PACKAGE-2 (NHIDCL) (N24002157)	3/2023	9/2026 (N.A.) {9/2026}	686.00 (N.A.) {686.00}	241.74	0
		1090	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDERS OF SHILLONG WESTERN BYPASS STARTING FROM NH-06 NEAR LADU (NHIDCL) (N24002158)	3/2023	9/2026 (N.A.) {9/2026}	562.48 (N.A.) {562.48}	263.14	0
	RAILWAYS	1091	BHAIRABI SAIRONG, NL, NEFR (NFR) (N22000100)	4/2008	3/2014 (N.A.) {7/2025}	2,393.47 (5,021.45) {8,213.72}	7,520.14	93
	ROAD TRANSPORT AND HIGHWAYS	1092	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000857)	4/2017	4/2023 (Mar-24) {1/2025}	519.09 (785.65) {785.65}	649.83	90
		1093	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000858)	4/2017	7/2023 (May-24) {7/2024}	640.07 (990.88) {1,286.35}	1,217.65	99
		1094	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000859)	4/2017	6/2023 (Mar-24) {3/2024}	642.96 (988.23) {988.23}	729.79	99.5
		1095	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000861)	4/2017	4/2023 (Nov-23) {2/2025}	473.18 (688.25) {688.25}	520.26	83.66

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1096	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000862)	4/2017	4/2023 (Oct-23) {2/2025}	537.82 (789.05) {789.05}	746.61	91.6
		1097	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000863)	4/2017	6/2023 (Feb-24) {3/2025}	518.53 (906.76) {906.76}	784.80	88.5
		1098	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000864)	4/2017	4/2024 (Jul-24) {3/2025}	404.29 (750.32) {750.32}	589.53	83.2
		1099	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO (NHIDCL) (N24000865)	4/2017	9/2023 (May-24) {3/2025}	428.11 (746.39) {746.39}	579.70	87.17
		1100	CONSTRUCTION OF CHHIATHLANG - SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 (NHIDCL) (N24001277)	9/2020	10/2022 (Apr-24) {3/2024}	275.02 (247.25) {247.25}	231.19	99.73
		1101	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) (NHIDCL) (N24001278)	3/2020	7/2022 (Jan-24) {6/2024}	206.88 (219.33) {219.33}	206.55	97.01
		1102	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) (NHIDCL) (N24001281)	3/2020	7/2022 (Mar-24) {7/2025}	292.24 (331.17) {331.17}	287.95	91.42

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1103	DULTE- KWALKULH - CHAMPAI PKG.1 (NHIDCL) (N24001355)	3/2021	12/2022 (Mar-24) {3/2024}	374.39 (374.39) {374.39}	292.27	100
		1104	DULTE- KWALKULH - CHAMPAI PKG.2 (NHIDCL) (N24001356)	3/2021	12/2022 (Apr-24) {4/2024}	233.25 (233.25) {233.25}	178.37	100
		1105	DULTE- KWALKULH - CHAMPAI PKG.3 (NHIDCL) (N24001357)	3/2021	6/2023 (Jan-24) {1/2024}	674.71 (674.71) {674.71}	589.25	100
		1106	TLABUNG - LUNGLEI PKG-A (NHIDCL) (N24001358)	3/2021	12/2022 (Dec-24) {12/2025}	698.44 (698.45) {698.45}	383.62	42.2
		1107	TLABUNG - LUNGLEI PKG-B (NHIDCL) (N24001359)	3/2021	1/2023 (Dec-24) {12/2025}	740.58 (740.58) {740.58}	276.77	41.5
		1108	KEIFANG - TUVAI PKG-1 (NHIDCL) (N24001440)	9/2021	5/2023 (Jun-24) {12/2024}	492.94 (492.94) {492.94}	355.00	84.7
		1109	UP-GRADATION TO 2-LANE WITH PAVED SHOULDERS OF NGOPA - PAWLRRANG SECTION OF NH 102B OF AIZAWL - IMPHA (NHIDCL) (N24001975)	9/2021	2/2025 (N.A.) {2/2026}	523.78 (N.A.) {523.78}	236.92	40
		1110	KEIFANG - TUVAI PKG-3 (NHIDCL) (N24002027)	12/2021	2/2025 (N.A.) {12/2025}	500.88 (N.A.) {500.88}	137.25	36.31
MULTI STATE	COAL	1111	NILJAI EXPANSION (DEEP) OC (3.5 MTY) (WCL) (N06000154)	8/2016	3/2022 (Mar-25) {3/2025}	319.76 (319.76) {319.76}	281.40	98
		1112	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) (WCL) (N06000157)	2/2017	3/2021 (Mar-25) {3/2025}	328.00 (N.A.) {328.00}	321.43	96
		1113	BINA KAKRI AMALGAMATION OCP 14 MTPA (NCL) (N06000192)	8/2020	3/2024 (N.A.) {3/2025}	836.42 (N.A.) {836.42}	670.84	54.77

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DPIIT</u>	1114	NATIONAL INDUSTRIAL CORRIDOR PROJECT (DMIC FOR DPIIT) (N40000001)	9/2011	3/2027 (Mar-27) {3/2027}	20,084.00 (20,084.00) {20,084.00}	9,718.22	50.99
	<u>PETROLEUM</u>	1115	KOCHI-KOOTTANAD-BANGALORE- MANGALORE PIPELINE PHASE-II (GAIL) (N16000285)	6/2009	12/2012 (Feb-25) {3/2025}	2,915.00 (5,909.00) {5,909.00}	4,073.20	91.8
		1116	SRIKAKULAM ANGUL PIPELINE PROJECT (GAIL) (N16000388)	9/2019	7/2022 (Jun-25) {6/2025}	2,658.34 (N.A.) {2,658.34}	1,985.10	91.8
		1117	DHAMRA HALDIA PIPELINE PROJECT (GAIL) (N16000391)	3/2020	11/2022 (Mar-25) {3/2025}	1,030.65 (N.A.) {1,030.65}	774.20	84.4
		1118	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT (GAIL) (N16000398)	6/2020	5/2023 (Jun-25) {6/2025}	7,844.25 (N.A.) {7,844.25}	5,782.10	89.8
		1119	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS (IOCL) (N16000426)	6/2019	12/2029 (Mar-30) {3/2030}	169.00 (N.A.) {169.00}	70.56	17.9
		1120	NORTH EAST GAS GRID (IGGL) (N16000439)	11/2020	3/2024 (Mar-25) {3/2027}	9,265.00 (9,265.00) {9,265.00}	5,420.48	83.24
		1121	GURDASPUR JAMMU PIPELINE (GAIL) (N16000531)	7/2023	7/2026 (Jul-26) {7/2026}	521.92 (521.92) {521.92}	6.70	14.4
	<u>POWER</u>	1122	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO (PGCIL) (N18000184)	3/2015	3/2018 (N.A.) {12/2024}	197.40 (N.A.) {197.40}	161.89	96
		1123	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P (PGCIL) (N18000249)	12/2014	12/2018 (Mar-25) {3/2025}	4,754.42 (9,129.32) {9,129.32}	6,724.24	77.14

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1124	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES (PGCIL) (N18000250)	12/2014	12/2018 (Mar-25) {3/2025}	5,111.33 (6,700.00) {6,700.00}	4,942.92	95.1
		1125	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN (PGCIL) (N18000264)	8/2017	2/2020 (Apr-23) {9/2025}	1,931.39 (2,635.55) {2,635.55}	1,964.44	99
		1126	NORTH EASTERN REGION STRENGTHENING SCHEME-XII (PGCIL) (N18000316)	5/2021	3/2023 (N.A.) {8/2024}	576.42 (576.42) {576.42}	418.96	100
		1127	TS FOR EVACUATION OF POWER FROM PAKALDUL HEP IN CHENAB VALLEY HEPS - LTA SYSTEM (PGCIL) (N18000328)	2/2022	4/2025 (N.A.) {4/2025}	318.12 (N.A.) {318.12}	142.75	83
		1128	TRANSMISSION SYSTEM STRENGTHENING FOR SRINAGAR-LEH TRANSMISSION SYSTEM (PGCIL) (N18000330)	3/2022	12/2024 (N.A.) {12/2024}	288.71 (N.A.) {288.71}	112.79	39
		1129	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000331)	2/2022	9/2023 (N.A.) {12/2024}	359.47 (N.A.) {359.47}	200.97	63
		1130	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000332)	5/2022	11/2023 (N.A.) {12/2024}	1,666.00 (N.A.) {1,666.00}	1,318.62	81
		1131	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART B (PGCIL) (N18000337)	7/2022	6/2023 (N.A.) {12/2024}	4,546.26 (N.A.) {4,546.26}	2,180.35	64

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1132	TRANSMISSION NETWORK EXPANSION IN GUJARAT TO INCREASE ATC FROM ISTS: PART C (PGCIL) (N18000338)	7/2022	3/2025 (N.A.) {3/2025}	186.19 (N.A.) {186.19}	61.53	65
		1133	SYSTEM STRENGTHENING SCHEME FOR EASTERN AND NORTH EASTERN REGION (PGCIL) (N18000343)	10/2022	10/2025 (N.A.) {10/2025}	307.87 (N.A.) {307.87}	83.31	52
		1134	TRANSMISSION SYSTEM FOR KURNOOL WIND ENERGY ZONE SOLAR ENERGY ZONE (AP) PART-A PART B (PGCIL) (N18000352)	3/2023	11/2024 (N.A.) {3/2025}	3,546.94 (N.A.) {3,546.94}	1,222.14	50
		1135	ER WR TRANSMISSION LIMITED (PGCIL) (N18000353)	3/2023	3/2025 (N.A.) {3/2025}	281.16 (N.A.) {281.16}	27.14	27
	RAILWAYS	1136	NANGALDAM-TALWARA(NL),NR (NR) (220100188)	3/1981	7/2012 (N.A.) {11/2024}	450.00 (N.A.) {2,017.96}	1,190.75	43
		1137	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) (WCR) (220100232)	9/1998	5/2008 (N.A.) {3/2025}	247.66 (63.57) {8,248.50}	2,520.04	43
		1138	CHHAPRA-BALLIA UP (NER) (N22000134)	3/2013	1/2019 (N.A.) {2/2025}	295.00 (954.00) {995.82}	987.32	95
		1139	CHOTTAUDEPUR-DHAR(NL) (WR) (N22000138)	4/2007	3/2022 (Dec-27) {12/2027}	1,347.26 (1,793.63) {1,793.63}	1,464.86	58
		1140	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) (WR) (N22000139)	4/2007	3/2022 (Feb-27) {2/2027}	1,640.04 (1,873.10) {2,873.11}	2,030.41	58
		1141	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) (NCR) (N22000148)	4/2011	3/2022 (N.A.) {12/2024}	2,912.96 (N.A.) {3,845.60}	1,024.32	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1142	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI- TANTPUR AND TANPUR-BANSI PAHARPUR (NCR) (N22000158)	4/2010	(Dec-26) {12/2026}	2,030.50 (746.83) {746.83}	81.25	19
		1143	NEW BONGAIGAON-RANGIA- KAMAKGHYA DOUBLING (NFR) (N22000183)	4/2013	3/2019 (N.A.) {9/2024}	1,798.00 (N.A.) {2,832.35}	3,148.37	95
		1144	NEW BG LINE FROM BALURGHAT TO HILLY NFR (NFR) (N22000206)	4/2010	3/2020 (N.A.) {3/2027}	242.22 (N.A.) {1,195.95}	387.08	5
		1145	NEW BG LINE FROM JAGBANI TO BIRATNAGAR (NFR) (N22000207)	4/2010	(N.A.) {3/2023}	241.52 (N.A.) {401.65}	343.30	85.42
		1146	MURKONGSELEK-PASIGHAT NL (NFR) (N22000208)	4/2011	3/2020 (N.A.) {5/2025}	414.84 (N.A.) {1,265.16}	580.91	33
		1147	MADURAI-TUTICORIN VIA ARUPPUKOTTAI (SR) (N22000215)	4/2011	3/2019 (Dec-27) {12/2027}	120.70 (N.A.) {2,053.39}	342.13	14
		1148	PIRPAINTI-JASIDIH (ER) (N22000219)	4/2013	3/2022 (Mar-28) {3/2028}	915.98 (N.A.) {2,610.84}	809.34	45
		1149	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION (SCR) (N22000261)	4/2012	3/2023 (N.A.) {3/2025}	1,856.95 (N.A.) {1,952.68}	1,354.36	0
		1150	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL (NR) (N22000274)	4/2007	(N.A.) {2/2024}	336.91 (N.A.) {791.39}	572.99	40
		1151	RAYADURGA-TUMKUR NL (SWR) (N22000279)	4/2007	(N.A.) {2/2027}	2,062.30 (2,495.59) {2,495.59}	1,413.42	60
		1152	PHULERA - DIGANA DOUBLING (NWR) (N22000326)	5/2015	3/2020 (Apr-24) {4/2024}	600.00 (N.A.) {701.81}	765.54	100
		1153	HOTGI-KUDGI-GADAG (SWR) (N22000333)	3/2015	3/2019 (N.A.) {6/2025}	1,614.59 (1,877.81) {2,458.87}	2,408.17	89

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1154	KAZIPET-BALHRSHA (SCR) (N22000367)	4/2015	3/2021 (N.A.) {1/2025}	2,063.03 (N.A.) {2,909.00}	2,578.41	0
		1155	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT (NHSRCL) (N22000463)	12/2015	12/2023 (N.A.) {8/2027}	108,000.00 (N.A.) {108,000.00}	66,326.00	46.64
		1156	WESTERN DEDICATED FREIGHT CORRIDOR (DFCC) (N22000464)	11/2007	3/2020 (N.A.) {3/2020}	16,592.00 (51,101.00) {51,101.00}	47,476.00	83
		1157	CHANDIGARH-BADDI (NR) (N22000467)	4/2007	3/2023 (N.A.) {6/2025}	328.14 (N.A.) {1,540.14}	482.67	10
		1158	NARAYANGARH TO BHADRAK 3RD LINE (155 KM) (SER) (N22000506)	3/2019	5/2023 (N.A.) {12/2025}	1,866.31 (N.A.) {1,866.31}	1,627.16	55
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1159	VARANASI-AURANGABAD KM.786 TO KM.978.40 (NHAI) (N24000182)	9/2011	3/2014 (N.A.) {9/2024}	2,848.00 (N.A.) {3,241.56}	3,901.66	85.61
		1160	4/6L OF SPUR TO HARIDWAR (GREENFIELD) FROM KM. 0.000 TO KM. 49.000 (NHAI) (N24001628)	11/2021	2/2025 (N.A.) {2/2025}	2,155.95 (N.A.) {2,155.95}	1,026.00	42.13
		1161	6L WITH ACCESS CONTROL PROVISION SAHARANPUR BYPASS TO GANESHPUR SECTION FROM 13.89 KM TO 41.820 KM O (NHAI) (N24001629)	4/2022	11/2024 (N.A.) {11/2024}	796.65 (N.A.) {796.65}	268.84	52.85
	<u>SHIPPING AND PORTS</u>	1162	JAL MARG VIKAS PROJECT (IWAI) (N25000072)	1/2018	3/2023 (Dec-25) {12/2025}	5,369.18 (4,633.81) {5,061.15}	3,078.56	61.04
	<u>TELECOMMU NICATIONS</u>	1163	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB- P3 DATA CENTERS WITH STATE OF THE ART (BSNL) (N26000114)	3/2020	6/2021 (Nov-21) {12/2024}	461.42 (461.42) {461.42}	159.98	81

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1164	SUPER EDGE ROUTERS FOR BSNL INTERNET PROTOCOL - MULTI PROTOCOL LABEL SWITCHING (IPMPLS) NETWORK and (BSNL) (N26000115)	3/2023	3/2024 (Jul-24) {9/2024}	239.60 (N.A.) {239.60}	165.31	100
		1165	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK (MAAN) IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (N26000116)	5/2023	8/2024 (Nov-24) {11/2024}	645.13 (N.A.) {645.13}	258.87	75.33
		1166	PLANNING ENGINEERING SUPPLY INSTALLATION TESTING COMMISSIONING INTEGRATION and ANNUAL MAINTENANCE OF (BSNL) (N26000117)	6/2023	6/2025 (N.A.) {6/2025}	24,556.35 (24,544.55) {24,544.55}	3,417.37	40.6
		1167	OPTICAL TRANSPORT NETWORK (OTN) PH-4 IN BSNL (BSNL) (N26000118)	2/2024	8/2025 (N.A.) {8/2025}	810.99 (N.A.) {810.99}	250.00	17.74
	URBAN DEVELOPME NT	1168	DELHI GHAZIABAD MEERUT RRTS CORRIDOR (NCRTC) (N28000134)	3/2019	6/2025 (N.A.) {6/2025}	30,274.00 (N.A.) {30,274.00}	22,615.28	80.3
NAGALAND	PETROLEUM	1169	AUGMENTATION OF DIMAPUR DEPOT, DIMAPUR (IOCL) (N16000529)	8/2023	11/2027 (N.A.) {11/2027}	227.62 (N.A.) {227.62}	0.20	7.5
	RAILWAYS	1170	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) (NFR) (N22000124)	4/2006	3/2015 (N.A.) {12/2029}	2,326.52 (6,663.20) {6,663.20}	3,770.54	58
	ROAD TRANSPORT AND HIGHWAYS	1171	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 (NHIDCL) (N24000686)	3/2016	9/2019 (Nov-22) {12/2024}	373.07 (534.41) {534.41}	382.50	99.81

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1172	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 (NHIDCL) (N24000688)	3/2016	8/2022 (Sep-25) {9/2025}	429.52 (794.74) {794.74}	287.46	83.4
		1173	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. (NHIDCL) (N24000752)	2/2017	9/2020 (Feb-23) {12/2024}	387.00 (688.12) {688.12}	387.50	99.32
		1174	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING (NHIDCL) (N24000753)	3/2018	11/2022 (Aug-24) {12/2024}	500.09 (698.81) {698.81}	373.62	94.81
		1175	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA- ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO (NHIDCL) (N24000756)	3/2018	9/2022 (Jan-23) {7/2024}	285.68 (N.A.) {285.68}	174.28	99.9
		1176	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG- TAMLU-MON ROAD FROM EXISTING KM 20.456 TO (NHIDCL) (N24000763)	3/2018	12/2021 (Aug-22) {8/2025}	215.79 (N.A.) {215.79}	107.40	27.45
		1177	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG- TAMLU-MON ROAD FROM EXISTING KM 60.345 TO (NHIDCL) (N24000765)	3/2018	9/2018 (Jun-23) {9/2025}	323.98 (N.A.) {323.98}	81.60	16.04
		1178	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN (MoRTH) (N24001179)	3/2017	11/2020 (Feb-23) {2/2023}	217.35 (N.A.) {217.35}	214.18	100

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1179	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- (MoRTH) (N24001180)	3/2019	12/2022 (Jan-23) {1/2023}	237.51 (N.A.) {237.51}	201.20	100
		1180	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D (NHIDCL) (N24001255)	9/2020	10/2022 (Apr-24) {9/2024}	277.44 (N.A.) {277.44}	160.86	62.27
		1181	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG (NHIDCL) (N24001257)	8/2020	10/2022 (Jun-25) {6/2025}	159.85 (342.29) {159.85}	76.99	15.94
		1182	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES (NHIDCL) (N24001258)	8/2020	4/2022 (Apr-23) {2/2025}	202.36 (N.A.) {202.36}	71.92	26.96
		1183	UPGRADATION OF EXISTING ROAD TO 2- LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM (NHIDCL) (N24001259)	9/2020	4/2022 (May-24) {2/2025}	315.63 (N.A.) {315.63}	95.84	74.23
		1184	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) (NHIDCL) (N24001280)	3/2020	6/2022 (Mar-23) {9/2023}	320.97 (N.A.) {320.97}	182.21	100
		1185	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) (NHIDCL) (N24001282)	3/2020	6/2022 (N.A.) {1/2026}	355.79 (N.A.) {355.79}	109.24	60.93
		1186	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) (NHIDCL) (N24001284)	3/2020	6/2022 (Jun-23) {6/2024}	361.53 (365.42) {365.42}	200.22	97.42

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1187	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) (NHIDCL) (N24001286)	3/2020	6/2022 (Oct-22) {6/2023}	278.95 (N.A.) {278.95}	166.29	100
		1188	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) (NHIDCL) (N24001287)	4/2020	12/2021 (Nov-25) {11/2025}	330.80 (N.A.) {330.80}	110.22	58.59
		1189	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D (NHIDCL) (N24001288)	8/2020	4/2022 (Nov-26) {11/2026}	232.29 (350.88) {232.29}	39.59	1.62
		1190	CHANGTONGYA TO LONGLENG ROAD PKG-2 (NHIDCL) (N24001389)	3/2020	6/2022 (Sep-22) {1/2025}	206.53 (N.A.) {206.53}	119.25	99.4
		1191	PEREN-DIMAPUR SECTION PKG-2 (NHIDCL) (N24001406)	7/2021	3/2023 (Sep-25) {9/2025}	258.52 (N.A.) {258.52}	62.78	57.55
		1192	PEREN-DIMAPUR PKG-5 (NHIDCL) (N24001407)	2/2021	3/2023 (N.A.) {3/2023}	207.33 (N.A.) {207.33}	0.00	0
		1193	MERANGKONG-TAMLU-MON (MTM) PKG- 5 (NHIDCL) (N24001438)	7/2021	12/2023 (N.A.) {9/2025}	161.73 (N.A.) {161.73}	43.05	23.71
		1194	WIDENING OF EXISTING SINGLE LANE / INTERMEDIATE LANE ROAD TO 2 LANE FROM KM 101 TO KM 125 OF NH 61 I (MoRTH) (N24001465)	6/2020	9/2024 (Jun-26) {6/2026}	252.19 (N.A.) {252.19}	0.28	0
		1195	WIDENING TO EXISTING SINGLE LANE /INTERMEDIATE LANE TO 2 LANE FROM KM185.00 TO KM 220.00 OF NH-61 (N (MoRTH) (N24001466)	3/2021	7/2024 (Mar-25) {3/2025}	297.24 (N.A.) {297.24}	109.40	55.07

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1196	WIDENING TO EXISTING SINGRE/INTERMEDIATE RANE TO 2 LANE FROM KM 135 TO KM 147 AND FROM KM 156.00 TO (MoRTH) (N24001467)	3/2021	2/2024 (Feb-25) {2/2025}	226.44 (N.A.) {226.44}	109.16	76.78
		1197	CONSTRUCTION OF 2 LANE WITH HARD SHOULDER FROM DESIGN CHAINAGE KM 283.000 TO KM 325.440 (5- LEGGED J (NHIDCL) (N24001475)	3/2022	12/2024 (N.A.) {12/2024}	605.36 (N.A.) {605.36}	214.50	84.14
		1198	WIDENING OF EXISTING SINGLE LANE ROAD TO INTERMEDIATE LANE ROAD FROM MOKOKCHUNG TO CHARE VIA DIKHU I (MoRTH) (N24001855)	2/2021	6/2025 (Jun-25) {6/2025}	192.93 (N.A.) {192.93}	55.72	53.23
		1199	PEREN-DIMAPUR PKG-3 (NHIDCL) (N24001912)	2/2021	6/2025 (N.A.) {6/2025}	177.77 (199.02) {199.02}	17.31	26.64
		1200	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-I (DESIGN CH (NHIDCL) (N24001976)	12/2022	2/2026 (N.A.) {2/2026}	430.24 (N.A.) {430.24}	35.44	20.02
		1201	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-II (DESIGN C (NHIDCL) (N24001977)	12/2022	2/2026 (N.A.) {2/2026}	442.54 (N.A.) {442.54}	17.58	11.32
		1202	WIDENING TO 2 LANE WITH HARD SHOULDER OF AKEGWO-AVANGKHU SECTION OF NH-202K FOR PACKAGE-III (DESIGN (NHIDCL) (N24001978)	12/2022	2/2026 (N.A.) {2/2026}	497.18 (N.A.) {497.18}	68.58	29.41
ODISHA	COAL	1203	BASUNDHARA (WEST) OC EXTN(7.00 MTY) (MCL) (N06000112)	5/2014	3/2019 (N.A.) {3/2027}	479.15 (N.A.) {479.15}	266.56	62

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1204	SIARMAL OCP (40.00MTY) (MCL) (N06000113)	2/2021	3/2029 (N.A.) {3/2029}	5,194.96 (N.A.) {5,194.96}	3,392.69	42.5
		1205	GARJANBAHAL OCP (MCL) (N06000117)	11/2014	3/2021 (N.A.) {3/2026}	1,375.38 (N.A.) {1,375.38}	828.22	58
		1206	INTEGRATED LAKHANPUR-BELPAHAR- LILARI OCP (MCL) (N06000167)	5/2018	3/2027 (N.A.) {3/2027}	2,434.75 (N.A.) {2,434.75}	1,815.42	51
		1207	REORGANISATION OF BHARATPUR OCP EXPANSION (MCL) (N06000171)	11/2018	3/2029 (N.A.) {3/2029}	2,838.87 (N.A.) {2,838.87}	1,668.41	44
		1208	TALABIRA II AND III OCP (NLC) (N06000189)	7/2017	1/2027 (N.A.) {1/2027}	2,401.07 (N.A.) {2,401.07}	1,370.54	52.8
		1209	NAINI COAL MINE (SCCL) (N06000203)	3/2020	3/2024 (N.A.) {3/2026}	494.30 (N.A.) {494.30}	491.33	35
		1210	BHUBANESWARI EXPANSION OCP (MCL) (N06000227)	3/2024	3/2031 (N.A.) {3/2031}	6,321.73 (N.A.) {6,321.73}	1,130.44	18
		1211	GOPALJI-KANIHA OCP (MCL) (N06000229)	4/2022	3/2028 (N.A.) {3/2028}	6,107.87 (N.A.) {6,107.87}	1,620.58	16.5
		1212	BALARAM EXPANSION OCP (MCL) (N06000230)	8/2020	3/2029 (N.A.) {3/2029}	3,504.21 (N.A.) {3,504.21}	905.09	49
		1213	KULDA EXPANSION OCP- 15 MTY (MCL) (N06000248)	6/2014	3/2018 (N.A.) {3/2026}	348.16 (N.A.) {348.16}	199.85	60
		1214	SUBHADRA OCP (MCL) (N06000249)	5/2021	3/2029 (Mar-29) {3/2029}	1,693.81 (N.A.) {1,693.81}	1,135.45	39
		1215	RPR OF HINGULA -II EXPANSION PH-III (MCL) (N06000261)	12/2022	3/2029 (N.A.) {3/2029}	2,264.68 (N.A.) {2,264.68}	1,002.42	39
		1216	NLC TALABIRA THERMAL POWER PROJECT (PHASE-1: 3 X 800 MW) (NLC) (N06000270)	1/2024	5/2029 (N.A.) {5/2029}	27,213.00 (N.A.) {27,213.00}	970.41	1.51

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>DEPARTMENT OF HIGHER EDUCATION</u>	1217	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR (CPWD EDUCATION) (N28000126)	1/2019	3/2022 (N.A.) {11/2024}	790.79 (N.A.) {790.79}	665.30	94
	<u>MINES</u>	1218	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT (NALCO) (N10000010)	12/2014	4/2021 (Sep-25) {9/2025}	4,103.00 (5,677.40) {5,677.40}	3,201.37	67.87
		1219	UTKAL D AND E COAL BLOCK (NALCO) (N10000011)	5/2016	1/2020 (Nov-23) {3/2024}	534.00 (N.A.) {1,021.97}	752.42	80.2
		1220	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (NALCO) (N10000012)	12/2015	11/2020 (Sep-25) {11/2026}	355.00 (581.00) {581.00}	109.88	12.6
		1221	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN (NALCO) (N10000013)	11/2017	4/2021 (May-25) {5/2025}	483.00 (483.00) {483.00}	344.11	85.22
		1222	POTTANGI BAUXITE MINES (NALCO) (N10000016)	5/2018	12/2024 (N.A.) {5/2025}	1,437.00 (N.A.) {1,381.00}	649.96	50.1
		1223	CONSTRUCTION OF RED MUD POND - II AT NALCO DAMANJODI ODISHA (NALCO) (N10000017)	9/2019	3/2023 (May-24) {5/2024}	225.79 (N.A.) {270.66}	5.00	100
	<u>PETROLEUM</u>	1224	ADDITIONAL STORAGE TANKS AT PARADIP (IOCL) (N16000361)	11/2018	9/2021 (Dec-24) {12/2024}	462.30 (552.44) {552.44}	469.43	94.87
		1225	Fuel Quality Upgradation Project at Paradip Refinery (IOCL) (N16000362)	5/2019	8/2021 (Dec-24) {12/2024}	3,361.00 (N.A.) {3,361.00}	2,709.09	98.1

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1226	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY (IOCL) (N16000368)	6/2019	9/2022 (Dec-24) {12/2024}	427.10 (427.10) {427.10}	298.98	94.32
		1227	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY (IOCL) (N16000396)	7/2020	1/2024 (Apr-25) {4/2025}	13,805.00 (N.A.) {13,805.00}	6,713.48	85.28
	POWER	1228	EASTERN REGION EXPANSION SCHEME XXIX (PGCIL) (N18000351)	3/2023	11/2025 (N.A.) {11/2025}	524.04 (N.A.) {524.04}	311.97	56
		1229	TALCHER THERMAL POWER PROJECT STAGE III(2X660 MW) (NTPC) (N18000364)	8/2022	5/2027 (N.A.) {5/2027}	11,844.00 (N.A.) {11,844.00}	1,405.09	8.4
	RAILWAYS	1230	KHURDA ROAD-BOLANGIR(NL)ECOR (ECOR) (220100284)	4/1994	3/2009 (Dec-26) {12/2026}	2,923.13 (3,791.66) {5,089.37}	4,091.11	78
		1231	TALCHER-BIMALAGARH(NL)(ECOR) (ECOR) (220100328)	4/2005	6/2021 (N.A.) {3/2026}	810.78 (N.A.) {1,928.07}	1,463.13	40
		1232	BHADRAK - NERGUNDI 3RD LINE (ECOR) (N22000316)	3/2013	10/2020 (N.A.) {10/2025}	843.04 (1,284.39) {1,284.39}	1,106.54	70
		1233	JAGADALPUR-KORAPUT DOUBLING (ECOR) (N22000376)	4/2015	3/2022 (N.A.) {3/2022}	1,547.38 (N.A.) {1,547.38}	1,202.08	88.5
		1234	KORAPUT - SINGAPUR ROAD DOUBLING (ECOR) (N22000379)	4/2015	3/2022 (Mar-26) {3/2026}	2,361.74 (2,361.74) {2,361.74}	1,540.64	68
		1235	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE (ECOR) (N22000380)	4/2015	11/2018 (Aug-26) {8/2026}	701.61 (N.A.) {810.02}	545.71	75

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1236	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. (ECOR) (N22000381)	4/2015	12/2018 (N.A.) {7/2025}	1,172.92 (2,087.43) {2,087.43}	1,584.75	70
		1237	VIZIANAGARAM -SAMABALPUR 3RD LINE (RVNL) (N22000409)	1/1991	12/2024 (N.A.) {12/2026}	2,335.67 (73.00) {4,803.16}	4,620.71	73
		1238	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL (IRCON) (N22000418)	4/2016	3/2020 (N.A.) {12/2025}	5,200.00 (N.A.) {5,200.00}	0.00	17.4
		1239	JEYPORE MALKANGIRI NEW LINE (ECOR) (N22000516)	2/2018	7/2033 (N.A.) {7/2033}	642.69 (N.A.) {642.69}	163.46	0.1
		1240	JEYPORE NABARANGPUR NEWLINE (ECOR) (N22000517)	7/2017	7/2028 (N.A.) {7/2028}	499.99 (N.A.) {747.91}	0.00	0
		1241	TALCHER - ANGUL NEW LINE WITH Y CONNECTION AT TALCHER (ECOR) (N22000518)	7/2018	12/2026 (N.A.) {12/2026}	278.96 (495.00) {494.62}	29.50	0
		1242	KODINGMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (ECOR) (N22000519)	8/2022	8/2027 (N.A.) {8/2027}	190.90 (N.A.) {190.90}	10.00	0
		1243	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION (ECOR) (N22000520)	9/2022	9/2027 (N.A.) {9/2027}	189.93 (N.A.) {189.93}	5.14	0
		1244	BRUNDAMAL-JHARSUGUDA- FLYOVER CONNECTION FOR JOINING DN LINE (ECOR) (N22000521)	12/2009	12/2026 (N.A.) {12/2026}	48.44 (297.00) {297.00}	0.00	0
		1245	BAGHUAPAL FLY OVER (20 KM) (ECOR) (N22000522)	8/2019	8/2027 (N.A.) {8/2027}	183.00 (N.A.) {183.00}	0.06	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1246	ROURKELA-BONDAMUNDA A-CABIN 5TH LINE (10 KM) (UMBRELLA WORK PB#57/2019-20/NR) (SER) (N22000571)	9/2022	9/2026 (N.A.) {3/2026}	209.75 (N.A.) {244.99}	40.04	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1247	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S (NHAI) (N24000619)	9/2016	8/2019 (N.A.) {10/2024}	2,510.04 (N.A.) {2,510.04}	1,104.98	98
		1248	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO (NHAI) (N24000715)	12/2017	7/2020 (N.A.) {12/2024}	686.65 (565.00) {686.65}	574.26	86.5
		1249	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE () (NHAI) (N24000733)	1/2018	8/2022 (N.A.) {2/2025}	633.68 (492.83) {633.68}	560.38	80
		1250	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG (NHAI) (N24000734)	1/2018	8/2021 (N.A.) {10/2024}	614.48 (503.30) {757.12}	664.48	99
		1251	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON (NHAI) (N24000736)	1/2018	9/2020 (N.A.) {12/2024}	686.65 (504.09) {1,015.16}	435.85	80
		1252	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 (NHAI) (N24000738)	1/2018	9/2021 (N.A.) {3/2025}	999.00 (1,152.70) {1,152.70}	387.08	77.49

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1253	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) ((NHA)) (N24000739)	1/2018	6/2021 (Dec-24) {12/2024}	503.88 (609.03) {609.03}	536.89	95
		1254	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. (MoRTH) (N24000912)	8/2016	2/2017 (N.A.) {9/2024}	287.70 (N.A.) {293.66}	272.95	98.66
		1255	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA (MoRTH) (N24000914)	12/2016	8/2018 (N.A.) {9/2024}	223.50 (N.A.) {223.50}	220.50	92
		1256	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA (MoRTH) (N24000917)	3/2018	8/2018 (N.A.) {11/2024}	199.16 (N.A.) {199.16}	155.44	98
		1257	BALANCE WORK OF PANIKOILI RIMULI SECTION OF NEW NH-20 FROM KM 0.00 TO KM. 163.000 (NHA)) (N24001647)	8/2020	3/2022 (N.A.) {10/2024}	200.00 (154.73) {154.73}	137.04	100
		1258	6L GREENFIELD KANDILI - ALURU SECTION OF NH-130-CD ROAD FROM KM 342+500 TO KM 365+033 (PACKAGE-OD-8 (NHA)) (N24001665)	12/2021	10/2024 (N.A.) {8/2025}	1,592.00 (1,592.00) {1,592.00}	810.84	56.08
		1259	6L GREENFIELD BARAJA - KANDILI SECTION OF NH- 130-CD ROAD FROM KM 338+500 TO KM 342+500 (PACKAGE- OD (NHA)) (N24001666)	12/2021	9/2024 (N.A.) {8/2025}	714.00 (714.00) {714.00}	448.24	72.52
		1260	6L GREENFIELD KALIAGURA BAUNSAGUAR SECTION OF NH-130-CD ROAD FROM KM 249+000 TO KM 293+000 (PACKAG (NHA)) (N24001667)	9/2021	5/2024 (N.A.) {10/2025}	1,734.00 (1,734.00) {1,734.00}	1,040.60	72.01

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1261	6L OF BADA KUMARI - KARKI SECTION FROM KM 179.000 TO KM 226.500 OF NH- 130-CD (PACKAGE OD-3) (NHAI) (N24001668)	3/2021	4/2024 (N.A.) {3/2025}	1,249.00 (N.A.) {1,249.00}	405.98	70.6
		1262	6L OF DHANARA - HATIBENA SECTION FROM KM 124.611 TO KM 146.50 OF NH- 130-CD (PACKAGE OD-1) (NHAI) (N24001669)	2/2021	3/2024 (N.A.) {3/2025}	586.00 (N.A.) {586.00}	186.65	63.37
		1263	6L OF KARKI KALIAGURA SECTION FROM KM 226.500 TO KM 249.000 OF NH- 130-CD (PACKAGE OD-4) (NHAI) (N24001670)	2/2021	3/2024 (N.A.) {12/2024}	593.00 (N.A.) {593.00}	251.76	87.34
		1264	6L OF HATIBENA - BADA KUMARI SECTION FROM KM 146.50 TO KM 179.00 OF NH-130-CD (PACKAGE OD-2) (NHAI) (N24001671)	2/2021	3/2024 (N.A.) {12/2024}	925.00 (N.A.) {925.00}	397.54	94.91
		1265	6L GREENFIELD BAUNSAGUAR - BARAJA SECTION OF NH-130-CD ROAD FROM KM 293+000 TO KM 338+500 (PACKAGE (NHAI) (N24001678)	8/2021	6/2024 (N.A.) {6/2025}	1,460.00 (1,460.00) {1,460.00}	812.50	74.63
		1266	CONSTRUCTION OF ROAD FROM KM 0/0 TO 72/0 OF NH-26 SUCH AS 4 LANE FROM KM 0/0 TO 21/0 (BARGARH TO BAR (MoRTH) (N24001857)	6/2020	12/2023 (N.A.) {12/2024}	414.24 (N.A.) {414.24}	264.66	60
		1267	WIDENING AND STRENGTHENING TO 2L+PS INCLUDING LA OF KANDARPUR- BALIKUDA FROM KM 277/500 TO 318/970 OF (MoRTH) (N24001858)	3/2022	6/2025 (N.A.) {6/2025}	499.79 (N.A.) {499.79}	232.34	7.25

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1268	CONSTRUCTION OF BYPASS ON NH-59 FROM KM 336/350 TO 349/910 (13.56 KM) NEAR BERHAMPUR TOWN INCLUDING (MoRTH) (N24001859)	3/2021	3/2024 (N.A.) {3/2025}	196.94 (N.A.) {196.94}	66.09	10.58
		1269	CONSTRUCTION OF BYPASS TO NAYAGARH TOWN FROM KM 235.469 TO 252.482 OF NH-57 INCLUDING LAND ACQUISITI (MoRTH) (N24001860)	1/2022	4/2025 (N.A.) {4/2025}	300.33 (N.A.) {300.33}	161.93	9
		1270	CONSTRUCTION OF BYPASS TO KHORDHA TOWN FROM KM 294/000 TO 300/300 ON NH-57 INCLUDING LA IN THE STATE (MoRTH) (N24001861)	2/2022	11/2024 (Mar-25) {3/2025}	157.49 (N.A.) {157.49}	62.04	15.75
		1271	CONSTRUCTION OF BYPASS ROAD TO BALANGIR TOWN FROM KM 72/400 (DESING KM 0/0) TO KM 79/800 (DESIGN KM (MoRTH) (N24001862)	2/2022	10/2025 (Nov-25) {11/2025}	238.78 (N.A.) {238.78}	17.26	0
		1272	CONSTRUCTION OF 5 HL BRIDGES AT KM 379/000 (PANGAM), KM 439/400 (POTTERU), KM 444/237 (KONGURUKONDA) (MoRTH) (N24001863)	3/2021	6/2024 (N.A.) {6/2025}	154.05 (N.A.) {154.05}	47.47	0
		1273	CONSTRUCTION OF FOUR LANE ROB AND ITS APPROACHES IN LIEU OF EXISTING LEVEL CROSSING NO. RV-71 AT KM (MoRTH) (N24001864)	11/2021	6/2025 (N.A.) {6/2025}	154.49 (N.A.) {154.49}	48.40	0
		1274	CONSTRUCTION OF 4 LANE ROB WITH APPROACHES IN LIEU OF LC NO. RV-172 AT KM 176.00 OF NH-201 (PRESENT (MoRTH) (N24001865)	12/2021	5/2025 (N.A.) {5/2025}	324.09 (N.A.) {324.09}	74.04	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1275	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM. (NHAI) (N24002078)	12/2023	12/2025 (N.A.) {12/2025}	711.00 (N.A.) {711.00}	96.90	20.02
		1276	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002079)	12/2023	12/2025 (N.A.) {12/2025}	742.25 (N.A.) {742.25}	146.86	22.65
		1277	REHABILITATION AND UP GRADATION FROM 4 TO 8 LANING OF CHANDIKHOLE PARADIP SECTION OF NH 53 FROM KM (NHAI) (N24002080)	12/2023	12/2025 (N.A.) {12/2025}	762.75 (N.A.) {762.75}	161.57	22.12
		1278	3L MAJOR BRIDGE OVER RIVER BRAHMANI AT KM. 401.250 (DUBURI CHANDIKHOLE SECTION) OF NH 200 (NEW NH 5 (NHAI) (N24002081)	8/2022	1/2025 (N.A.) {6/2025}	153.61 (N.A.) {153.61}	14.22	15.6
		1279	WIDENING AND STRENGTHENING TO 2L+PS FROM KM 0.000 TO 40.000 (DHAUGAON- PODAMARI SECTION) OF NH 326 I (MoRTH) (N24002135)	3/2022	2/2026 (N.A.) {2/2026}	186.52 (N.A.) {186.52}	22.06	0
		1280	WIDENING AND STRENGTHENING TO 4L+PS/2L+PS FROM KM 0.000 TO 35.800 (KUAKHIA - MANGALPUR SECTION) OF N (MoRTH) (N24002136)	3/2022	2/2026 (N.A.) {2/2026}	636.10 (N.A.) {636.10}	181.98	0
	STEEL	1281	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY (SAIL) (N12000122)	11/2020	5/2023 (N.A.) {10/2024}	377.18 (N.A.) {377.18}	402.45	89.47

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1282	INSTALLATION OF 4TH SLAB CASTER ALONG WITH ITS AUXILIARIES AND A NEW LADLE FURNACE IN SMS-II AT RSP (SAIL) (N12000125)	1/2022	5/2025 (N.A.) {5/2025}	970.18 (N.A.) {970.18}	455.12	62.99
PUNJAB	DEPARTMENT OF HIGHER EDUCATION	1283	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. (CPWD EDUCATION) (N28000142)	10/2019	5/2022 (N.A.) {12/2024}	348.24 (N.A.) {348.24}	274.08	87
	PETROLEUM	1284	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB (HPCL) (N16000402)	5/2020	2/2023 (Sep-24) {9/2024}	1,421.46 (N.A.) {1,421.46}	1,034.00	94.8
		1285	BHATINDA SANGRUR PIPELINE (HPCL) (N16000440)	11/2021	5/2024 (N.A.) {2/2025}	367.00 (N.A.) {367.00}	280.29	83.2
		1286	CGD PROJECT AT PATHANKOT DISTRICT (IOCL) (N16000488)	3/2022	3/2030 (N.A.) {9/2033}	151.00 (N.A.) {151.00}	7.91	1.5
	RAILWAYS	1287	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI (NR) (N22000502)	6/2009	8/2016 (N.A.) {8/2025}	404.00 (N.A.) {404.00}	190.00	60
		1288	LUDHIANA MULLANPUR DOUBLING (NR) (N22000589)	9/2020	3/2025 (N.A.) {3/2025}	82.99 (N.A.) {235.00}	0.00	0
		1289	RAJPURA-BHATINDA (172.64 KM) (MEGA) (N22000597)	6/2017	3/2024 (N.A.) {3/2024}	1,775.73 (N.A.) {1,775.73}	0.00	0
		1290	FEROZPUR - PATTI (25.72 KM) (NR) (N22000614)	4/2017	3/2027 (N.A.) {3/2027}	299.74 (N.A.) {299.74}	0.00	0
	ROAD TRANSPORT AND HIGHWAYS	1291	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA (MoRTH) (N24000907)	3/2018	8/2020 (N.A.) {7/2024}	293.10 (N.A.) {315.00}	306.60	100

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1292	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 (MoRTH) (N24000909)	10/2017	10/2019 (N.A.) {12/2025}	1,069.59 (N.A.) {1,069.59}	739.08	62
		1293	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 (MoRTH) (N24000910)	3/2018	11/2020 (N.A.) {6/2024}	170.57 (192.48) {150.00}	104.98	79
		1294	REHABILITATION AND UPGADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES (MoRTH) (N24000941)	3/2018	8/2020 (N.A.) {8/2020}	293.64 (N.A.) {293.64}	295.46	100
		1295	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-VI) FROM JUNCTION WITH PATIALA-SAMANA-PATRAN ROAD (SH-1 (NHAI) (N24001414)	12/2020	1/2024 (May-24) {7/2024}	733.00 (908.28) {908.28}	868.44	95.33
		1296	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH PATIALA- BATHINDA ROAD (NH-7) NEAR BHAWANIGARH TO (NHAI) (N24001415)	12/2020	4/2024 (Jul-24) {7/2024}	881.00 (N.A.) {881.00}	865.46	88.54
		1297	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA- MALERKOTLA ROAD (SH-11) NEAR BHOGIWAL VI (NHAI) (N24001416)	12/2020	1/2024 (Mar-25) {3/2025}	989.66 (N.A.) {989.66}	319.95	31.08
		1298	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM JUNCTION WITH LUDHIANA-MOGA ROAD (NH-5) NEAR MULLANPUR DAKHA TO (NHAI) (N24001417)	12/2020	4/2024 (Jul-24) {7/2024}	1,234.40 (N.A.) {1,234.40}	744.28	57.09

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1299	DELHI-AMRITSAR-KATRA EXPRESSWAY FROM CH.KM 303+900 TO KM 319+400 OF MAIN EXPRESSWAY) AND AMRITSAR CO (NHAI) (N24001418)	12/2020	4/2024 (Jul-24) {7/2024}	1,094.46 (N.A.) {1,094.46}	757.42	60.36
		1300	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XI) FROM JUNCTION WITH JALANDHAR - KAPURTHALA ROAD (NH- (NHAI) (N24001419)	2/2021	4/2024 (Nov-24) {11/2024}	1,269.96 (N.A.) {1,269.96}	584.69	43.45
		1301	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I PKG-XII) FROM JUNCTION WITH AMRITSAR-MEHTA-SRIHARGOBINDPUR- (NHAI) (N24001420)	2/2021	4/2024 (N.A.) {4/2024}	853.66 (N.A.) {853.66}	112.33	12.64
		1302	FOUR LANING OF EXISTING 2 LANE SECTION FROM MALOUT (DESIGN KM 44.500, EXISTING KM 80.200 OF NH-07) V (NHAI) (N24001514)	1/2021	1/2024 (Nov-24) {11/2024}	1,060.29 (N.A.) {1,060.29}	975.55	99
		1303	4/6L GREENFIELD LUDHIANA RUPNAGAR HIGHWAY FROM JUNCTION WITH NE 05 VILLAGR NEAR TO MANEWAL (LUDHIANA (NHAI) (N24001630)	7/2021	2/2025 (N.A.) {2/2025}	1,501.02 (N.A.) {1,501.02}	280.00	63
		1304	6L OF IT CITY CHOWK TO KURALI CHANDIGARH ROAD (NHAI) (N24001631)	3/2021	10/2024 (N.A.) {10/2024}	1,525.31 (N.A.) {1,525.31}	278.00	68
		1305	CONSTRUCTION OF FOUR LANE GREENFIELD PROJECT OF DELHI- AMRITSAR-KATRA EXPRESSWAY (PHASE- I PKG-V) FROM (NHAI) (N24001632)	1/2021	5/2024 (N.A.) {4/2025}	1,741.86 (N.A.) {1,741.86}	1,123.64	85.5

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1306	CONSTRUCTION OF FOUR/SIX LANE GREENFIELD LUDHIANA RUPNAGAR NATIONAL HIGHWAY NO. NH-205K UNDER BHAR (NHAI) (N24001636)	5/2021	12/2024 (Dec-24) {12/2024}	1,368.91 (1,368.91) {1,368.91}	163.58	15.31
		1307	DEVELOPMENT OF 6 LANE JALANDHAR BYPASS FROM KAHLWAN NATIONAL HIGHWAY 03 DESIGN KM 0.00 ENDING AT K (NHAI) (N24001637)	3/2021	1/2025 (N.A.) {1/2025}	1,754.84 (N.A.) {1,754.84}	924.11	28.2
		1308	4L GREENFIELD A. MALOUT BYPASS FROM CH. KM 44.500 TO CH. KM 35.500 ON NH-07 AND CH. KM 0.000 TO KM 6 (NHAI) (N24001638)	11/2021	7/2024 (Dec-24) {12/2024}	646.42 (646.42) {646.42}	481.67	90
		1309	FOUR LANING OF MOGA TO BAJAKHANA LAMBWALI SECTION OF 105B GREENFIELD ALIGNMENT FROM DESIGN CHAINAGE (NHAI) (N24001639)	5/2020	12/2024 (Aug-25) {8/2025}	864.23 (864.23) {864.23}	434.88	37
		1310	6L AMRITSAR BATHINDA GREENFIELD SECTION FROM VILLAGE TIBA ON NE 5A TO JN. WITH MOGA JALANDHAR ROAD N (NHAI) (N24001640)	3/2021	11/2024 (N.A.) {11/2024}	1,229.38 (N.A.) {1,229.38}	635.45	29.15
		1311	DELHI AMRITSAR KATRA EXPRESSWAY PHASE I SPUR III FROM JUNCTION WITH AMRITSAR JALANDHAR ROAD NH3 NEAR (NHAI) (N24001641)	3/2021	10/2024 (Sep-25) {9/2025}	1,641.75 (N.A.) {1,641.75}	164.43	22.51
		1312	FOUR LANING OF AMRITSAR BYPASS FROM NEW TARN TARAN ROAD TO AJNALA ROAD FROM DESIGN KM. 0.750 TO DESI (NHAI) (N24001642)	2/2021	8/2024 (Mar-25) {3/2025}	1,474.77 (N.A.) {1,474.77}	384.91	62.28

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1313	4L OF AMRITSAR GHOMAN TANDA UNA SECTION FROM KM 8.270 TO KM 54.000 OF NH 503A PACKAGE I (NHAI) (N24001643)	12/2020	6/2024 (Jun-25) {6/2025}	857.91 (N.A.) {857.91}	127.71	34.53
		1314	AMRITSAR AIRPORT JUNCTION RAMDAS FROM KM. 100.835 TO KM. 139.813 PKG IV (NHAI) (N24001644)	12/2020	9/2023 (Mar-25) {3/2025}	524.88 (416.58) {416.58}	157.14	69
		1315	4L OF MALOUT-MANDI DABWALI SECTION PKG-01 DANEWALA AT KM 7.000 TO MANDI DABWALI AT KM 29.500 OF NH-0 (NHAI) (N24001645)	12/2020	6/2023 (Feb-24) {2/2024}	366.85 (366.85) {366.85}	519.77	100
		1316	UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION OF NH-354 SECTION ARIFKES-FEROZEPUR- MUKTS (MoRTH) (N24001960)	3/2021	10/2023 (N.A.) {4/2025}	263.19 (N.A.) {220.00}	30.00	21
		1317	WORK OF WIDENING/UPGRADATION OF 2-LANE WITH PAVED SHOULDER OF SRI MUKTSAR SAHIB TO MALOUT ROAD FROM (MoRTH) (N24001961)	3/2022	10/2023 (N.A.) {4/2025}	152.58 (N.A.) {152.58}	33.45	20
		1318	6L OF JODHPUR ROMANA (BATHINDA) - MANDI DABWALI (PUNJAB HARYANA BORDER) SECTION OF NH-54 FROM KM. 0. (NHAI) (N24002075)	12/2020	8/2025 (Aug-25) {8/2025}	757.13 (757.00) {757.00}	246.51	87
		1319	6L AMRITSAR-BATHINDA GREENFIELD SECTION FROM JN. WITH BHAGTA BHAI KA-BHADAUR ROAD NEAR DYALPURA BHAI (NHAI) (N24002076)	3/2021	10/2025 (Oct-25) {10/2025}	2,029.17 (2,029.00) {2,029.00}	84.23	23

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1320	6L ACCESS CONTROLLED LUDHIANA-BATHINDA GREENFIELD HIGHWAY FROM JN. WITH AMRITSAR-BATHANDA GREENFIELD (NHAI) (N24002091)	6/2021	9/2025 (Sep-25) {9/2025}	906.51 (906.51) {906.51}	134.05	29.27
		1321	6-LANE AMRITSAR-BATHINDA GREENFIELD SECTION OF NH-754A FROM JUNCTION WITH MOGA JALANDHAR ROAD (NH-70) (NHAI) (N24002092)	3/2021	10/2025 (N.A.) {10/2025}	1,801.37 (N.A.) {1,801.37}	796.47	16.8
		1322	6L OF AMBALA-CHANDIGARH GREENFIELD SECTION FROM KM. 0.000 TO KM. 25.000 WITH 4L SPUR TO LALRU FROM K (NHAI) (N24002098)	3/2022	10/2025 (N.A.) {10/2025}	1,641.66 (N.A.) {1,641.66}	81.00	31
		1323	4L OF EXISTING BEAS BABA BAKALA - DERA BABA NANAK SECTION FROM START OF BATALA BYPASS TILL INTERSE (NHAI) (N24002100)	10/2021	6/2025 (N.A.) {6/2025}	1,003.38 (N.A.) {1,003.38}	219.90	59.6
		1324	4L OF BEAS-MEHTA-BATALA-DERA BABA NANAK FROM INTERSECTION WITH JALANDHAR-AMRITSAR HIGHWAY (NH-3) NEA (NHAI) (N24002101)	8/2021	6/2025 (N.A.) {6/2025}	809.51 (N.A.) {809.51}	125.89	34.8
		1325	DELHI-AMRITSAR-KATRA EXPRESSWAY (PHASE-I SPUR-I) FROM JN. WITH KAPURTHALA - SULTANPUR LODHI ROAD (NH (NHAI) (N24002102)	1/2020	4/2026 (N.A.) {4/2026}	2,165.23 (N.A.) {2,165.23}	120.50	14.08
RAJASTHAN	ATOMIC ENERGY	1326	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) (NPCIL) (N02000027)	10/2009	12/2016 (N.A.) {12/2026}	12,320.00 (22,924.00) {22,924.00}	19,056.00	93.54
	CIVIL AVIATION	1327	CONSTRUCTION OF NEW TERMINAL BUILDING AT JODHPUR AIRPORT (AAI) (N04000101)	5/2022	11/2024 (N.A.) {6/2025}	480.00 (N.A.) {480.00}	119.07	50

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1328	UDAIPUR AIRPORT- CONSTRUCTION OF NEW INTEGRATED PASSENGER TERMINAL BUILDING (AAI) (N04000104)	6/2023	3/2026 (Sep-26) {9/2026}	887.00 (N.A.) {887.00}	132.96	28.88
	<u>COAL</u>	1329	NLCIL 300 MW SOLAR POWER PROJECT (PART OF 510 MW CPSU SCHEME) (NLC) (N06000269)	3/2023	9/2024 (N.A.) {3/2025}	1,813.00 (N.A.) {1,813.00}	402.73	27.05
	<u>PETROLEUM</u>	1330	NEW MUNDRA-PANIPAT CRUDE OIL PIPELINE (IOCL) (N16000435)	12/2021	10/2024 (Dec-24) {12/2024}	9,028.00 (N.A.) {9,028.00}	5,650.96	64.28
		1331	CGD PROJECT AT JHUNJHUNU, SIKAR AND NAGAUH DISTRICTS (IOCL) (N16000489)	3/2022	3/2030 (N.A.) {3/2031}	575.00 (N.A.) {575.00}	110.71	7.4
		1332	CGD PROJECT IN TONK, SAWAI MADHOPUR, DAUSA, KARAUH (HPCL) (N16000496)	3/2022	3/2030 (N.A.) {3/2030}	1,751.00 (N.A.) {1,751.00}	182.72	19.2
		1333	SETTING UP OF PETROCHEMICAL EVACUATION MARKETING TERMINAL (PEMT) AT BARMER (HPCL) (N16000512)	12/2023	12/2026 (N.A.) {12/2026}	461.05 (N.A.) {461.05}	22.85	18.7
		1334	RAJASTHAN REFINERY PROJECT (HPCLRRL(JV)) (N16000513)	10/2017	10/2022 (Mar-25) {3/2025}	43,129.00 (72,937.00) {72,937.00}	49,508.70	82.1
		1335	CGD PROJECTS AT FAZILKA (EXCEPT AREA ALREADY AUTHORIZED) GANGANAGAR AND HANUMANGARH DISTRICTS (BPCL) (N16000520)	12/2022	6/2030 (N.A.) {6/2030}	3,207.00 (N.A.) {3,207.00}	188.64	16.2
	<u>POWER</u>	1336	SAMBHU KI BHURJ-II SOLAR 300MW (NTPC) (N18000286)	3/2020	9/2021 (N.A.) {9/2024}	1,782.00 (N.A.) {1,782.00}	1,279.42	0
		1337	ANTA SOLAR 90 MW (NTPC) (N18000292)	1/2021	3/2022 (N.A.) {3/2022}	382.22 (N.A.) {382.22}	497.17	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1338	BHENSARA 320 MW (NTPC) (N18000293)	1/2021	7/2022 (N.A.) {7/2022}	1,221.73 (N.A.) {1,221.73}	719.49	0
		1339	CHHATTARGARH 150 MW (NTPC) (N18000294)	2/2021	7/2022 (Mar-24) {3/2024}	599.99 (N.A.) {599.99}	243.12	0
		1340	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000306)	6/2021	12/2022 (N.A.) {12/2024}	1,562.00 (N.A.) {1,562.00}	1,199.25	94
		1341	TRANSMISSION SYSTEM STRENGTHENING SCHEME FOR EVACUATION OF POWER FROM SOLAR ENERGY ZONES IN RAJASTHA (PGCIL) (N18000307)	6/2021	12/2022 (N.A.) {10/2024}	1,006.00 (N.A.) {1,006.00}	880.11	98
		1342	NOKH PLOT-1 SOLAR PV PROJECT 245MW (NTPC) (N18000320)	3/2022	8/2023 (N.A.) {9/2024}	1,352.71 (N.A.) {1,352.71}	359.51	0
		1343	NOKH PLOT-2 SOLAR PV PROJECT 245MW (NTPC) (N18000321)	3/2022	8/2023 (N.A.) {9/2024}	1,409.52 (N.A.) {1,409.52}	632.99	0
		1344	NOKH PLOT-3 SOLAR PV PROJECT 245MW (NTPC) (N18000322)	3/2022	8/2023 (N.A.) {9/2024}	1,426.94 (N.A.) {1,426.94}	362.86	0
		1345	BHADLA-II 500MW SOLAR PV PROJECT (NTPC) (N18000347)	6/2022	3/2024 (N.A.) {12/2024}	2,598.92 (N.A.) {2,598.92}	468.43	0
		1346	TRANSMISSION SYSTEM SCHEME FOR EVACUATION OF POWER FROM REZ RAJASTHAN (8.1 GW) UNDER PHASE-II PART (PGCIL) (N18000356)	3/2023	9/2024 (N.A.) {12/2024}	1,433.28 (N.A.) {1,433.28}	540.47	40

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1347	300 MW SOLAR POWER PROJECT UNDER CPSU SCHEME (NHPC) (N18000368)	5/2022	11/2023 (N.A.) {3/2025}	1,677.12 (N.A.) {1,677.12}	724.79	62
		1348	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PHASE-IV PART-I (BIKANER COMPLEX) PAR (PGCIL) (N18000372)	6/2023	1/2025 (N.A.) {12/2024}	202.39 (N.A.) {202.39}	20.04	53
		1349	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III, PART E1 (PGCIL) (N18000373)	8/2023	2/2025 (N.A.) {2/2025}	688.74 (N.A.) {688.74}	121.10	18
		1350	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART H (PGCIL) (N18000374)	10/2023	4/2025 (N.A.) {4/2025}	2,211.00 (N.A.) {2,211.00}	206.83	17
		1351	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART C1 (PGCIL) (N18000375)	10/2023	4/2025 (N.A.) {4/2025}	1,796.00 (N.A.) {1,796.00}	405.48	13
		1352	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART B1 (PGCIL) (N18000376)	9/2023	4/2025 (N.A.) {4/2025}	2,191.00 (N.A.) {2,191.00}	457.26	17
		1353	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART J (PGCIL) (N18000378)	12/2022	3/2025 (N.A.) {8/2025}	331.00 (N.A.) {331.00}	7.66	26
		1354	TS FOR EVACUATION POWER FROM REZ IN RAJASTHAN (20GW) UNDER PHASE-III PART E2 (PGCIL) (N18000379)	11/2023	6/2025 (N.A.) {6/2025}	428.00 (N.A.) {428.00}	0.00	1

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1355	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART A [BIKANER III N (PGCIL) (N18000386)	12/2023	12/2025 (N.A.) {12/2025}	2,998.00 (N.A.) {2,998.00}	126.98	3
		1356	TS FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV (PART-1) [BIKANER COMPLEX] PART D [NEEMRANA II B (PGCIL) (N18000387)	12/2023	12/2025 (N.A.) {12/2025}	2,056.00 (N.A.) {2,056.00}	144.00	8
		1357	TS FOR EVACUATION OF POWER FROM REZ IN RAJASTHAN (20GW) UNDER PH-III PART D [SIKAR KHETRI TRANSMISSI (PGCIL) (N18000389)	2/2024	8/2025 (N.A.) {8/2025}	2,000.00 (N.A.) {2,000.00}	0.00	0
		1358	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) PART-B (JAISALMER/BARMER COMPLEX) (PGCIL) (N18000391)	8/2024	8/2026 (N.A.) {8/2026}	3,279.00 (N.A.) {3,279.00}	0.00	0
		1359	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-C (PGCIL) (N18000393)	8/2024	8/2026 (N.A.) {8/2026}	2,227.00 (N.A.) {2,227.00}	0.00	0
		1360	TS FOR EVACUATION POWER FROM RAJASTHAN REZ PH-IV (PART-2:5.5GW) (JAISALMER/BARMER COMPLEX) PART-E (PGCIL) (N18000394)	8/2024	8/2026 (N.A.) {8/2026}	3,251.00 (N.A.) {3,251.00}	0.00	0
	RAILWAYS	1361	DAUSA-GANGAPUR CITY(NL),NWR (NWR) (220100184)	2/1997	2/2019 (N.A.) {3/2024}	410.08 (N.A.) {1,020.00}	1,060.42	100
		1362	AGRA FORT-BANDIKUI (NCR) (N22000553)	6/2022	6/2027 (N.A.) {5/2026}	1,389.81 (N.A.) {987.83}	0.24	11

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1363	GUDHA THATHANA MITHRI TEST TRACK FOR RDSO (NWR) (N22000593)	4/2019	3/2025 (N.A.) {3/2025}	528.48 (N.A.) {528.48}	326.97	70
		1364	DEDICATED TEST TRACK FOR RDSO (PHASE II) (NWR) (N22000594)	11/2021	11/2026 (N.A.) {12/2024}	466.42 (N.A.) {466.42}	545.21	72
		1365	DOUBLING BETWEEN CHURU- RATANGARH (42.81 KM) (NWR) (N22000605)	2/2023	2/2028 (N.A.) {1/2026}	422.60 (N.A.) {422.60}	109.40	38
		1366	SAWAIMADHOPUR - BYPASS LINE (6.98 KM) (UMBRELLA WORK PB#57/2019- 20/NR) (NWR) (N22000607)	12/2022	6/2026 (N.A.) {12/2025}	304.00 (239.54) {239.54}	78.23	20
		1367	GC OF NATHDWARA - DEVGARH MADARIYA (82.5KM) (NWR) (N22000608)	1/2023	6/2028 (N.A.) {1/2027}	968.92 (N.A.) {968.92}	202.02	18
	ROAD TRANSPORT AND HIGHWAYS	1368	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT- RAMGARH BHADASAR-JA (NHAI) (N24000795)	2/2018	4/2021 (Oct-24) {10/2024}	741.86 (649.00) {649.00}	672.53	96
		1369	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO (MoRTH) (N24001241)	3/2020	10/2022 (Dec-24) {12/2024}	255.23 (N.A.) {255.23}	256.00	96
		1370	4L+PS OF NH -58 FROM BEAWAR-GOMTI (OLD CH KM 58.245 TO KM. 108.600) PKG- I. (MoRTH) (N24001411)	12/2020	10/2023 (N.A.) {12/2025}	379.23 (N.A.) {379.23}	232.62	92
		1371	2L+PS FOR WORK OF NH-325 (BALOTRA TO SANDERAO VIA JALORE) BY CONSTRUCTION OF BYPASSES:(1) ASOTRA- BR (MoRTH) (N24001527)	12/2021	5/2024 (N.A.) {12/2024}	411.40 (N.A.) {411.40}	162.61	55

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1372	WIDENING OF PACHPADRA-BAGUNDI SECTION TO 4 LANE FROM KM 73/60 TO 95/70 OF NH-25 ON EPC MODE IN THE (MoRTH) (N24001528)	1/2022	12/2024 (N.A.) {12/2024}	194.88 (N.A.) {194.88}	104.69	68
		1373	44 LANE DIVIDED CARRIAGEWAY OF BARMER BYPASS OF NH-15 (NEW NH-68) IN THE STATE OF RAJASTHAN ON EPC M (MoRTH) (N24001529)	12/2021	8/2024 (N.A.) {12/2024}	451.66 (N.A.) {451.66}	401.78	97
		1374	UPGRADATION TO TWO LANE PAVED SHOULDER OF KOTHUN-LALSOT-KAROLI-DHOLPUR ROAD NH-23 (OLD NH-11B) IN TH (MoRTH) (N24001530)	12/2021	9/2024 (N.A.) {3/2025}	150.11 (N.A.) {150.11}	57.33	63
		1375	4L GREENFIELD SPUR FROM DELHI-VADODARA GREENFIELD EXPRESSWAY NEAR BANDIKUI TO JAIPUR (NHAI) (N24001557)	3/2022	11/2024 (Dec-24) {12/2024}	1,636.15 (N.A.) {1,636.15}	717.59	78.98
		1376	4L OF KARWAR (KM. 281.980 OF NH-62 NAGPUR ROAD) TO DANGIYAVAS OF JODHPUR RING ROAD (PKG-II) (NHAI) (N24001558)	11/2021	8/2024 (Dec-24) {12/2024}	736.75 (N.A.) {736.75}	216.39	73.1
		1377	2L PS SRIGANGANAGAR TO RAISINGHNAGAR (DESIGN CHAINAGE - 0.500 KM TO DESIGN CHAINAGE 101.000 KM) (PACK (NHAI) (N24001559)	9/2021	6/2024 (Jan-25) {1/2025}	672.35 (N.A.) {672.35}	389.01	93.5
		1378	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE-I) (AJ/DRGB-PACKAGE-8) (NHAI) (N24001561)	10/2019	10/2023 (Oct-24) {10/2024}	839.63 (N.A.) {839.63}	213.85	100

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1379	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE- I) (AJ/DRGB-PACKAGE-6) (NHAI) (N24001563)	10/2019	8/2023 (Oct-24) {10/2024}	846.59 (N.A.) {846.59}	145.98	97.8
		1380	DEOGARH (NEAR DHANDHANIYA)- RAJASTHAN/GUJARAT BORDER (PHASE- I) (AJ/DRGB-PACKAGE-7) (NHAI) (N24001564)	10/2019	7/2023 (Oct-24) {10/2024}	662.08 (N.A.) {662.08}	110.81	96.5
		1381	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-11) (CH. 319.400 TO CH. 331.030) [HARDEOGANJ VILL (NHAI) (N24001566)	11/2019	5/2023 (Oct-24) {10/2023}	1,640.10 (N.A.) {1,640.10}	1,159.13	100
		1382	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-10) (CH. 292.950 TO CH. 319.400) [END OF INTERCHA (NHAI) (N24001567)	11/2019	10/2022 (Nov-24) {11/2024}	1,272.97 (N.A.) {1,272.97}	595.43	82.72
		1383	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-14) (CH. 388.420 TO CH. 419.000) [JUNCTION WITH N (NHAI) (N24001568)	11/2019	5/2023 (Oct-24) {10/2024}	1,119.35 (N.A.) {1,119.35}	1,433.58	99.8
		1384	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-12) (CH. 331.030 TO CH. 359.170) [MAJOR BRIDGE ON (NHAI) (N24001569)	11/2019	3/2023 (Jun-24) {6/2024}	1,425.02 (N.A.) {1,425.02}	1,373.31	100
		1385	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-13) (CH. 359.170 TO CH. 388.420) [JUNCTION WITH S (NHAI) (N24001571)	11/2019	12/2023 (Oct-24) {10/2024}	1,341.36 (N.A.) {1,341.36}	1,085.34	99.55

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1386	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-09) (CH. 247.310 TO CH. 292.950) [JUNCTION WITH M (NHAI) (N24001573)	11/2019	12/2022 (Oct-24) {10/2024}	1,658.06 (N.A.) {1,658.06}	180.39	99.9
		1387	DELHI-VADODARA GREENFIELD ALIGNMENT (NH-148N) (PKG-15) (CH. 419.000 TO CH.427.300) [JUNCTION WITH NH (NHAI) (N24001612)	7/2020	1/2024 (Sep-25) {9/2025}	1,788.69 (N.A.) {1,788.69}	823.67	68
		1388	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FOR FATEHPUR BYPASS, MANDAWA BYPASS AND JHUNJHUNU BYPAS (MoRTH) (N24001866)	3/2022	8/2024 (N.A.) {6/2025}	186.29 (N.A.) {186.29}	142.69	67
		1389	UPGRADATION OF TWO LANE PAVED SHOULDER FROM SHAHPURA TO THANAGAZI OF NH-248A ON EPC MODE IN THE STAT (MoRTH) (N24001867)	3/2022	7/2024 (N.A.) {6/2025}	174.34 (N.A.) {174.34}	104.08	62
		1390	Sagwara Bypass and Garhi- Partapur Bypass of NH- 927A in the State of Rajasthan. (MoRTH) (N24001868)	3/2022	8/2025 (N.A.) {2/2025}	187.65 (N.A.) {187.65}	66.57	44
		1391	UPGRADATION AND REHABILITATION TO TWO LANE WITH PAVED SHOULDER OF GHAGARIYA- MUNABAO SECTION FROM KM (MoRTH) (N24001869)	12/2022	8/2025 (N.A.) {8/2025}	235.15 (N.A.) {235.15}	92.29	65
		1392	UP-GRADATION TO 2 LANE WITH PAVED SHOULDER FROM CHARBHUJA AT DESIGN KM 0.00 (EXISTING KM 150.00) TO (MoRTH) (N24001927)	2/2022	9/2025 (N.A.) {9/2025}	838.43 (N.A.) {838.43}	237.87	42

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1393	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER NORTHERN BYPASS PHASE-II OF KOTA CITY FROM DESIGN CHAINAG (MoRTH) (N24001928)	3/2022	4/2025 (N.A.) {4/2025}	317.74 (N.A.) {317.74}	136.23	5
		1394	ADDITIONAL STRUCTURES ON 6LGURGAON-JAIPUR SECTION OF NH-48 BETWEEN KM 42.700 TO KM 273.00 (NHAI) (N24002058)	8/2022	6/2024 (N.A.) {6/2025}	409.64 (N.A.) {409.64}	187.81	44.8
SIKKIM	CIVIL AVIATION	1395	PAKYONG AIRPORT- WIDENING OF BASIC STRIP AT WESTERN SIDE OF RUNWAY CHAINAGE 80M TO 920M I/C SLOPE ST (AAI) (N04000110)	11/2023	6/2026 (N.A.) {6/2026}	323.26 (N.A.) {323.26}	6.01	3
	DEPARTMEN T OF HIGHER EDUCATION	1396	CONSTRUCTION OF SIKKIM UNIVERSITY CAMPUS PHASE-I, PACKAGE -II AT YANGANG SOUTH SIKKIM (Sikkim Universi) (N44000002)	8/2020	1/2025 (N.A.) {12/2024}	314.06 (N.A.) {303.55}	157.24	54
	POWER	1397	TEESTA VI HE PROJECT (NHPC) (N18000325)	3/2019	3/2024 (N.A.) {12/2027}	5,748.04 (N.A.) {5,748.04}	3,731.76	63.39
		1398	RANGIT IV HE PROJECT (NHPC) (N18000326)	3/2021	5/2024 (N.A.) {5/2025}	938.29 (N.A.) {1,871.23}	1,240.93	79.41
	RAILWAYS	1399	SEVOK RANGPO, NEFR (NFR) (N22000102)	4/2008	12/2015 (N.A.) {12/2023}	1,339.48 (N.A.) {7,876.92}	3,290.96	39.8
	ROAD TRANSPORT AND HIGHWAYS	1400	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 (NHIDCL) (N24000767)	3/2017	4/2022 (May-22) {12/2023}	375.80 (N.A.) {375.80}	287.54	95.26
		1401	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 (NHIDCL) (N24000768)	11/2017	10/2020 (Aug-23) {4/2024}	290.05 (N.A.) {290.05}	218.36	96.98

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1402	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N (NHIDCL) (N24001251)	3/2019	4/2022 (N.A.) {1/2025}	402.94 (N.A.) {402.94}	236.53	73.11
		1403	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 (NHIDCL) (N24001252)	8/2020	4/2023 (Nov-24) {3/2025}	295.97 (N.A.) {295.97}	243.68	93.39
		1404	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 (NHIDCL) (N24001254)	3/2020	6/2022 (N.A.) {1/2024}	242.97 (N.A.) {244.45}	246.91	100
		1405	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001261)	8/2020	4/2023 (N.A.) {10/2024}	311.00 (N.A.) {273.78}	240.56	93.88
		1406	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV (NHIDCL) (N24001262)	7/2020	4/2023 (Aug-24) {3/2025}	345.38 (395.59) {395.59}	355.08	89.04
		1407	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L (NHIDCL) (N24001322)	9/2020	5/2022 (Oct-23) {3/2025}	183.31 (439.56) {439.56}	351.16	46.26
		1408	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) (NHIDCL) (N24001325)	9/2020	5/2023 (Aug-24) {3/2025}	262.84 (414.20) {414.20}	220.26	46.17

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1409	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM (NHIDCL) (N24001327)	8/2020	5/2022 (Oct-23) {3/2025}	292.80 (N.A.) {292.80}	179.62	49.25
		1410	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO (NHIDCL) (N24001336)	8/2020	4/2023 (Oct-24) {6/2025}	230.45 (244.91) {244.91}	200.82	77.2
		1411	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT (NHIDCL) (N24001337)	10/2020	11/2023 (Jul-25) {7/2025}	493.42 (478.79) {478.79}	269.79	40.05
		1412	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 (NHIDCL) (N24001338)	10/2020	12/2023 (Jun-25) {12/2025}	816.79 (786.60) {786.60}	278.65	35.5
		1413	RISHI BORDER- ROLEP- MENLA PKG- 2A (NHIDCL) (N24001361)	1/2021	9/2023 (Apr-25) {12/2025}	332.20 (N.A.) {332.20}	148.86	40.97
		1414	RISHI BORDER- ROLEP- MENLA PKG- 3B (NHIDCL) (N24001362)	12/2020	2/2024 (Apr-25) {6/2025}	410.60 (379.30) {379.30}	188.53	43.19
		1415	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER GANGTOK BYPASS ROAD FROM RANIPOOL TO BURTUK (L=23.316KM) (MoRTH) (N24001442)	10/2021	5/2024 (Jan-25) {1/2025}	385.15 (N.A.) {385.15}	167.49	75
		1416	SPECIAL PROTECTION WORK ON REHABILITATION AND RESTORATION OF SLIDING AND SINKING ZONE FROM RANGPO TO (NHIDCL) (N24001913)	3/2017	6/2022 (N.A.) {6/2022}	165.56 (N.A.) {165.56}	0.00	71.74

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
TAMIL NADU	ATOMIC ENERGY	1417	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) (BHAVNI) (020100044)	9/2003	9/2010 (N.A.) {3/2025}	3,492.00 (N.A.) {7,670.00}	6,921.72	98
		1418	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 (NPCIL) (N02000028)	3/2013	11/2020 (N.A.) {11/2026}	39,849.00 (68,893.00) {68,893.00}	45,718.00	73.8
		1419	KUDANKULAM NUCLEAR POWER PROJECT 5 AND 6 (NPCIL) (N02000029)	6/2017	9/2027 (N.A.) {9/2027}	49,621.00 (N.A.) {49,621.00}	18,135.00	30.45
	CIVIL AVIATION	1420	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI (AAI) (N04000074)	6/2018	2/2022 (N.A.) {12/2025}	2,467.00 (N.A.) {2,467.00}	1,502.24	58.5
		1421	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI (AAI) (N04000075)	8/2018	10/2021 (N.A.) {12/2023}	951.28 (N.A.) {1,112.49}	1,112.49	100
		1422	DEVELOPMENT OF TUTICORIN AIRPORT (AAI) (N04000090)	6/2019	3/2022 (Dec-24) {12/2024}	380.87 (452.93) {452.93}	313.98	92
	COAL	1423	JAWAHAR KHANI OPENCAST (JK OC) MINE (SCCL) (N06000259)	12/2021	3/2025 (N.A.) {3/2025}	297.88 (N.A.) {297.88}	45.15	20
	FINANCE	1424	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI (CPWD FOR FINANC) (N28000109)	11/2017	11/2021 (N.A.) {11/2022}	348.77 (N.A.) {348.77}	223.39	100
	MINES	1425	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (NALCO) (N10000014)	9/2017	6/2019 (Mar-24) {12/2024}	166.62 (163.17) {163.17}	135.63	65
	PETROLEUM	1426	IRUGUR-DEVANGONTHI POL PIPELINE (BPCL) (N16000234)	11/2012	2/2017 (Oct-25) {10/2025}	678.00 (1,732.00) {1,732.00}	532.05	41

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1427	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE (IOCL) (N16000253)	5/2016	12/2018 (Mar-25) {3/2025}	4,497.00 (6,025.00) {6,025.00}	5,516.39	93.06
		1428	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI (IOCL) (N16000403)	10/2020	9/2023 (Dec-24) {12/2024}	921.00 (N.A.) {921.00}	727.09	92.4
		1429	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI (IOCL) (N16000405)	10/2020	12/2023 (Dec-24) {12/2024}	1,398.00 (1,587.00) {1,587.00}	1,202.00	93
		1430	CBR 9 MMTPA PROJECT (CPCL) (N16000434)	1/2021	6/2025 (N.A.) {6/2025}	31,580.00 (31,580.00) {36,354.00}	1,228.65	10.1
		1431	GRASS ROOT POL TERMINAL AT VALLUR, CHENNAI (IOCL) (N16000438)	1/2022	7/2024 (Dec-24) {6/2025}	827.00 (887.71) {887.71}	477.48	74
		1432	CBR ASANUR PIPELINE AND ITS HOOK UP WITH EXISTING CHENNAI TRICHY MADURAI PRODUCT PIPELINE (IOCL) (N16000451)	3/2022	11/2024 (N.A.) {11/2024}	564.00 (N.A.) {564.00}	144.55	35.67
		1433	LAYING OF POL PIPELINES IN COMMON CORRIDOR FOR PROPOSED GRASS ROOT TERMINAL AT VALLUR (CHENNAI) (IOCL) (N16000455)	1/2022	7/2024 (May-26) {5/2026}	829.00 (N.A.) {829.00}	209.56	50.79
		1434	EXTENSION OF ASANUR-SANKARI SECTION OF CHENNAI-TRICHY-MADURAI PIPELINE UPTO COIMBATORE (IRUGUR) (IOCL) (N16000479)	1/2023	1/2025 (N.A.) {1/2025}	346.70 (N.A.) {346.70}	0.72	17.25

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1435	CGD PROJECT AT DHARMAPURI AND KRISHNAGIRI DISTRICTS (IOCL) (N16000486)	3/2022	3/2030 (N.A.) {12/2030}	501.00 (N.A.) {501.00}	79.31	3.8
		1436	CGD PROJECT AT MADURAI, THENI AND VIRUDHNAGAR DISTRICTS (IOCL) (N16000490)	3/2022	3/2030 (N.A.) {12/2030}	1,328.00 (N.A.) {1,328.00}	140.66	4.1
		1437	CGD PROJECT AT KANYAKUMARI, TUTICORIN, TIRUNVELI KATTABO AND TENKASI DISTRICTS (IOCL) (N16000492)	3/2022	3/2030 (N.A.) {12/2030}	1,295.00 (N.A.) {1,295.00}	131.80	4.4
		1438	CGD PROJECTS AT THE NILGIRIS AND ERODE DISTRICTS (BPCL) (N16000521)	12/2022	3/2030 (N.A.) {3/2030}	3,685.00 (N.A.) {3,685.00}	83.87	4.6
	RAILWAYS	1439	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP (MRTTP) (N22000028)	4/2006	6/2013 (Oct-24) {12/2024}	495.74 (N.A.) {734.01}	628.07	98
		1440	MAYLADUTHURAI-THIRUVARUR- KARAIKUDI-THIRU 'PONDIL'- AGASTIYAMPALLI (SR) (N22000079)	9/2007	2/2019 (N.A.) {3/2027}	724.69 (N.A.) {3,118.34}	1,928.79	78
		1441	TIDIVANAM-NAGARI (NL) (SR) (N22000085)	9/2006	(Dec-26) {3/2027}	582.83 (3,631.34) {3,631.34}	774.31	10
		1442	Chinnasalem-Kallakurichi New Line (MM of cuddalore- Salem 191 KM) (SR) (N22000567)	1/2006	3/2025 (Dec-24) {12/2025}	417.50 (N.A.) {419.44}	199.70	75
		1443	CHENNAI BEACH-CHENNAI EGMORE (4.3 KM) (UMBRELLA WORK PB#57/2019- 20/NR) (SR) (N22000568)	3/2022	3/2026 (Dec-24) {12/2024}	359.60 (274.20) {274.20}	215.88	70
		1444	MORAPPUR-DHARMAPURI (SR) (N22000618)	2/2019	3/2028 (Mar-27) {3/2027}	358.95 (N.A.) {358.95}	37.70	1

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1445	KARAIKAL - PERALAM NEW LINE (MM OF TIRUCHCHIRAPPALLI-NAGORE-KARAIKAL) (SR) (N22000625)	1/2019	3/2026 (Dec-24) {12/2024}	304.22 (N.A.) {373.42}	302.47	72
		1446	NAGAPATTINAM- THIRUTURAI PUNDI VIA THIRUKUVALAI NEW LINE (MM OF TIRUCHCHIRAPPALLI-NAGORE-KARAIKAL) (SR) (N22000626)	7/2008	3/2026 (Mar-27) {3/2027}	677.12 (N.A.) {788.05}	167.05	17
	ROAD TRANSPORT AND HIGHWAYS	1447	FOUR LANNING OF VIKRAVANDI- SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. (NHAI) (N24000652)	3/2017	3/2020 (May-24) {5/2024}	848.45 (N.A.) {848.45}	303.04	48.26
		1448	FOUR LANNING OF CHOLOPURAM- THANJAVUR (NHAI) (N24000697)	8/2017	9/2020 (Sep-24) {9/2024}	1,176.37 (N.A.) {1,176.37}	1,325.06	96.3
		1449	4-LANNING OF STHIYATHOPU- CHOLOPURAM (NHAI) (N24000708)	9/2017	8/2020 (Nov-24) {11/2024}	1,227.87 (N.A.) {1,227.87}	1,319.28	90.05
		1450	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 (NHAI) (N24000826)	3/2018	10/2022 (Jan-24) {1/2024}	505.35 (N.A.) {837.69}	376.61	99.75
		1451	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300) (NHAI) (N24000827)	3/2018	11/2020 (Apr-23) {4/2023}	628.71 (N.A.) {756.13}	583.02	100
		1452	FOUR LANING OF VILUPPURAM TO PUDHUCHERRY (DESIGN CH. KM. 00/000 TO KM. 29/000) SECTION OF NH-45A ON (NHAI) (N24001428)	3/2018	11/2021 (Dec-24) {12/2024}	998.70 (1,358.32) {1,358.32}	872.60	96.88

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1453	FOUR LANING OF PUDUCHERRY (KM.29/000) TO POONDIYANKUPPAM (KM.67/000) SECTION OF NH-45A ON HAM UNDER (NHAI) (N24001429)	3/2018	11/2021 (Dec-24) {12/2024}	1,294.47 (1,588.40) {1,588.40}	854.58	95.3
		1454	FOUR LANING OF POONDIYANKUPPAM (KM.67/000) TO SATTANATHAPOURAM (KM.123/800) SECTION OF NH-45A ON HAM (NHAI) (N24001430)	3/2018	1/2022 (Dec-24) {12/2024}	2,120.40 (2,565.63) {2,565.63}	1,432.64	99.6
		1455	FOUR LANING OF SATTANATHAPURAM (KM.123/800) TO NAGAPATTINAM (KM.179/555) SECTION OF NH-45A ON HAM UN (NHAI) (N24001431)	3/2018	10/2020 (Aug-25) {8/2025}	1,872.68 (2,661.51) {2,756.09}	1,098.02	51.17
		1456	CONSTRUCTION OF 4 LANE WITH PAVED SHOULDERS THIRUVAYARU BYPASS IN BETWEEN EXISTING KM.55/926 TO 62/6 (MoRTH) (N24001455)	2/2022	8/2022 (N.A.) {10/2024}	191.33 (N.A.) {191.33}	160.10	88
		1457	BALANCE WORK 2-LANE WITH PAVED SHOULDERS OF NAGAPATTINAM - THANJAVUR SECTION OF NH-67 (NEW NH-83) (NHAI) (N24001600)	10/2020	5/2023 (Dec-24) {12/2024}	434.12 (N.A.) {434.12}	258.89	99
		1458	4-LANING OF KAMALAPURAM - ODDANCHATRAM SECTION OF NH-209 (NHAI) (N24001601)	1/2019	1/2023 (Jun-25) {6/2025}	1,051.69 (N.A.) {1,051.69}	545.11	75.11
		1459	4-LANING OF MADATHUKULAM - POLLACHI SECTION OF NH-209 (NEW NH- 83) (NHAI) (N24001602)	1/2019	12/2022 (Nov-25) {11/2025}	1,409.38 (N.A.) {1,409.38}	619.74	85.6

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1460	4-LANING OF ODDANCHATRAM - MADATHUKULAM SECTION OF NH-209 (NEW NH-83) (NHA) (N24001603)	1/2019	10/2022 (Dec-23) {12/2023}	1,518.53 (N.A.) {1,607.54}	915.40	100
		1461	REMAINING WORK OF 2L+PS OF TRICHY - KARAIKUDI SECTION OF NH-210, INCLUDING TRICHY BYPASS (NHA) (N24001604)	2/2019	3/2021 (N.A.) {10/2023}	166.90 (N.A.) {166.90}	121.94	100
		1462	4-LANING OF MELUR - PILLAYARPATTI - KARAIKUDI SECTION OF NH-338, NH-36, NH-383 (NHA) (N24001605)	6/2018	3/2022 (N.A.) {1/2025}	1,103.86 (N.A.) {1,103.86}	461.32	69
		1463	4-LANING OF VADIPPATTI - THAMARAIPATTI SECTION OF NH-744A (MADURAI RING ROAD) (NHA) (N24001606)	12/2018	3/2022 (Mar-25) {3/2025}	854.94 (N.A.) {854.94}	334.05	65.85
		1464	BALANCE WORKS OF FOUR LANE FROM KM 43+950 (THIRUVALLUR BYPASS) TO KM 61+470 (VEPPAMPATTU BYPASS) PAS (NHA) (N24001692)	1/2022	9/2024 (N.A.) {9/2024}	467.99 (N.A.) {468.00}	18.83	12.2
		1465	FOUR LANING OF NERALURU TO THORAPALLI AGRAHARAM SECTION OF NH-844 (PKG-I) FROM KM.0+000 TO KM.23+350 (NHA) (N24001693)	9/2021	10/2024 (N.A.) {10/2024}	1,751.18 (N.A.) {1,757.27}	49.69	0
		1466	FOUR LANING OF THORAPALLI AGRAHARAM TO JITTANDAHALLI SECTION OF NH-844 (PKG-II) FROM KM.23+350 TO KM (NHA) (N24001694)	2/2019	12/2023 (Dec-24) {12/2024}	1,243.57 (N.A.) {1,243.57}	171.63	0
		1467	FOUR LANING OF JITTANDAHALLI TO DHARMAPURI SECTION OF NH-844 (PKG- III) FROM KM.60+100 TO KM.94+460 (NHA) (N24001696)	2/2019	8/2023 (Dec-24) {12/2024}	1,291.37 (N.A.) {1,291.37}	215.02	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1468	THOPPUR METTUR BHAVANI ERODE SECTION OF NH 544H FOR A LENGTH OF 85 KM (NHAI) (N24001716)	7/2022	8/2023 (Dec-24) {12/2024}	186.50 (210.81) {210.81}	12.92	85
		1469	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE III (ARAKKONAM TO KANCHEEPURAM) FROM KM 204.500 TO K (NHAI) (N24001717)	11/2020	8/2024 (N.A.) {3/2025}	1,155.49 (1,458.45) {1,458.45}	444.56	52.39
		1470	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE II (WALAJAHPET TO ARAKKONAM) FROM KM 180.000 TO KM 2 (NHAI) (N24001718)	12/2020	7/2024 (N.A.) {11/2024}	843.48 (1,051.36) {1,051.36}	389.23	84.02
		1471	4L BANGALORE-CHENNAI EXPRESSWAY FROM KM. 230.000 TO KM. 261.705 OF KANCHEPURAM TO SRIPERUMBUDUR SECT (NHAI) (N24001719)	2/2021	7/2024 (N.A.) {2/2025}	2,948.31 (3,516.83) {3,516.83}	728.20	64.18
		1472	BANGALORE CHENNAI EXPRESSWAY PHASE-III PACKAGE I (GUDIPALA TO WALAJAHPET) FROM KM 156.000 TO KM 1 (NHAI) (N24001720)	10/2020	5/2024 (N.A.) {12/2024}	1,023.91 (1,341.51) {1,341.51}	513.56	70.35
		1473	FOUR LANING OF MAMALLAPURAM TO MUGAIYUR SECTION OF NH332A FROM KM 0.000 TO KM 31.000 (NHAI) (N24001721)	2/2019	5/2024 (Aug-25) {8/2025}	1,008.99 (1,360.53) {1,360.53}	167.11	38.24
		1474	6L OF MADURAVOYAL TO SRIPERUMBUDUR SECTION FROM KM. 13.800 TO KM. 37.000 OF NH-4 THROUGH STATE HIGH (NHAI) (N24001722)	11/2021	2/2023 (N.A.) {10/2024}	463.44 (463.07) {463.44}	331.01	98.5

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1475	KARAIPETTAI TO WALAJAPET FROM KM 71.015 TO 107.091 (NHAI) (N24001723)	10/2018	2/2021 (N.A.) {3/2025}	707.90 (766.51) {766.51}	401.98	80.37
		1476	6L OF SRIPERUMBUDUR TO KARAIPETTAI FROM KM 37.000 TO KM 71.015 OF NH 48 (NHAI) (N24001725)	1/2019	5/2021 (N.A.) {3/2026}	819.89 (1,314.82) {922.85}	384.20	57.32
		1477	CONSTRUCTION OF BYPASS TO GUDIYATHAM TOWN IN KM 23/100 29/250 INCLUDING LA AND SHIFTING OF NH-234 (MoRTH) (N24001828)	1/2022	11/2024 (N.A.) {11/2024}	221.03 (243.95) {243.95}	131.16	70
		1478	FOUR LANING OF OTTANCHATRAM TO PALANI SECTION FROM KM 30/700 TO KM 55/000 OF NH 209(NEW NH-83) INCLU (MoRTH) (N24001829)	10/2022	11/2024 (N.A.) {11/2024}	172.15 (N.A.) {172.15}	90.80	78.5
		1479	CONSTRUCTION OF STRR (WEST SIDE)- NH948A-BALAGONDAPALLI (TAMIL NADU) TO KARNATAKA/TAMIL NADU BORDER F (NHAI) (N24001968)	4/2022	5/2025 (N.A.) {5/2025}	1,260.74 (N.A.) {1,260.74}	413.87	43.46
		1480	4L OF THIRUMANGALAM TO VADUGAPATTI SECTION FROM KM 0.000 TO KM 36.000 OF NH-744 (NHAI) (N24002084)	3/2022	2/2025 (N.A.) {3/2025}	1,076.97 (N.A.) {1,076.97}	325.73	63.42
		1481	CONSTRUCTION OF NEW DOUBLE TIER 4 LANE ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI (NHAI) (N24002107)	3/2023	5/2026 (N.A.) {5/2026}	1,382.00 (N.A.) {1,382.00}	0.00	0
		1482	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002108)	3/2023	5/2026 (N.A.) {5/2026}	1,618.96 (N.A.) {1,618.96}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1483	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002109)	3/2023	5/2026 (N.A.) {5/2026}	1,301.37 (N.A.) {1,301.37}	0.00	0
		1484	CONSTRUCTION OF NEW DOUBLE TIER 4L ELEVATED CORRIDOR FROM CHENNAI PORT TO MADURAVOYAL IN CHENNAI DIS (NHAI) (N24002110)	3/2023	5/2026 (N.A.) {5/2026}	1,207.40 (N.A.) {1,207.40}	0.00	0
		1485	FOUR LANING OF MUGAIYUR TO MARAKKANAM SECTION OF NH-332A FROM KM 31.000 TO KM 62.000 (NHAI) (N24002111)	2/2019	12/2025 (Dec-25) {12/2025}	825.94 (1,116.13) {1,116.13}	147.70	23.66
		1486	SIX LANING OF TUTICORIN PORT ROAD SECTION OF NH-7A (NEW NH-138) FROM KM 0.000 TO KM 6.140 [EFFECTIVE (NHAI) (N24002112)	3/2023	7/2024 (N.A.) {1/2025}	200.30 (N.A.) {200.30}	57.34	65.95
		1487	4L OF LEFT-OVER WORKS INCLUDING ADDITIONAL STRUCTURES FROM KERALA/TAMIL NADU BORDER TO KANYAKUMARI S (NHAI) (N24002113)	3/2023	8/2025 (N.A.) {8/2025}	1,141.78 (N.A.) {1,141.78}	197.80	20.53
		1488	4L OF VADUGAPATTI TO THERKUVENGANALLUR (RAJAPALYAM) SECTION FROM KM 36.000 TO KM 71.600 OF NH744 UND (NHAI) (N24002114)	2/2022	4/2025 (N.A.) {4/2025}	1,097.59 (N.A.) {1,317.06}	507.85	70.33
		1489	WIDENING TO 4L/4L+PS AND STRENGTHENING IN SELECTED STRETCHES FROM KM 0/8 TO 50/570 OF NH 532 INCLUD (MoRTH) (N24002151)	3/2022	1/2024 (N.A.) {7/2025}	257.14 (294.70) {295.00}	78.32	30

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1490	WIDENING FROM 2L+PS TO 4L/4L+PS AND IMPROVEMENTS THE SELECTED STRETHCES FROM KM 26/5 - 81/2 INCLU (MoRTH) (N24002152)	3/2023	11/2023 (N.A.) {11/2025}	274.84 (N.A.) {274.84}	155.97	58
		1491	STRENGTHENING OF 2L+PS FROM KM 17/8 18/2, CONSTRUCTION OF 2L+PS FROM KM 18/2 TO KM 20/0 AND CONSTR (MoRTH) (N24002153)	3/2023	2/2024 (N.A.) {8/2025}	169.68 (N.A.) {169.68}	43.21	35
		1492	CONSTRUCTION OF BYPASS TO MADURAI - ACHAMBATHU - VIRATIPATHU IN KM 6/850 - 10/382 OF NH 49 EXTN. (NE (MoRTH) (N24002165)	3/2022	8/2026 (N.A.) {8/2026}	238.97 (N.A.) {238.97}	0.00	0
	URBAN DEVELOPEMENT	1493	CHENNAI METRO RAIL LTD (PHASE 1) (CMRL) (N28000084)	2/2009	12/2015 (N.A.) {12/2015}	14,600.00 (N.A.) {18,380.00}	17,619.68	100
		1494	CHENNAI METRO RAIL LTD (PHASE 1 EXT) (CMRL) (N28000097)	6/2016	3/2018 (N.A.) {2/2021}	3,770.00 (N.A.) {3,770.00}	2,527.73	100
TELANGANA	CIVIL AVIATION	1495	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD (AAI) (N04000086)	5/2020	5/2022 (Jun-23) {6/2023}	353.61 (N.A.) {353.61}	303.22	100
	COAL	1496	KAKATIYAKHANI OPENCASE III PROJECT PHASE-1 (SCCL) (N06000161)	3/2017	3/2022 (N.A.) {3/2025}	413.84 (N.A.) {413.84}	379.13	60
		1497	GODAVARIKHANI COAL MINE (SCCL) (N06000202)	7/2019	3/2023 (N.A.) {3/2025}	438.98 (N.A.) {438.98}	152.32	68
		1498	VENKATESH KHANI COAL MINE (SCCL) (N06000204)	10/2020	3/2023 (N.A.) {3/2026}	484.51 (N.A.) {484.51}	150.64	30
		1499	RCE OF RAMAGUNDAM OPENCASE II EXTENSION PROJECT (SCCL) (N06000210)	11/2015	3/2023 (N.A.) {3/2025}	489.62 (N.A.) {489.62}	405.54	70

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1500	RCE OF INDARAM OPENCASST PROJECT (SCCL) (N06000211)	8/2017	3/2021 (N.A.) {3/2025}	349.28 (N.A.) {424.81}	335.24	80
		1501	RCE OF KALYANIKHANI OPENCASST PROJECT (SCCL) (N06000213)	3/2016	3/2020 (N.A.) {3/2025}	384.32 (N.A.) {384.32}	241.21	75
		1502	RCE OF KAKATHIYAKHANI OC - 2 PROJECT (SCCL) (N06000214)	8/2017	3/2020 (N.A.) {3/2025}	442.42 (N.A.) {442.42}	174.29	63
		1503	GOLETI OPENCASST MINE (SCCL) (N06000258)	7/2021	3/2026 (N.A.) {3/2026}	345.60 (N.A.) {345.60}	50.25	18
	HEALTH AND FAMILY WELFARE	1504	COMPREHENSIVE PLANNING, DESIGNING, EXECUTION OF ALL INDIA INSTITUTE OF MEDICAL SCIENCES AT BIBINAGAR (HITES) (N21000031)	12/2018	7/2024 (Feb-25) {2/2025}	1,110.55 (1,110.55) {1,110.55}	576.80	73
		1505	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD (CPWD FOR HEALTH) (N28000098)	10/2016	3/2020 (Sep-24) {9/2024}	209.84 (281.05) {281.05}	248.47	97.5
	POWER	1506	TELANGANA SUPER THERMAL POWER PROJECT PHASE I (NTPC) (N18000212)	1/2016	11/2020 (Jul-22) {2/2024}	10,598.98 (N.A.) {10,998.00}	10,437.71	100
	RAILWAYS	1507	MANOHARABAD-KOTHPALL NEW LINE(SCR) (SCR) (N22000032)	4/2006	3/2010 (N.A.) {3/2025}	1,160.48 (N.A.) {3,014.00}	1,286.11	0
		1508	MANMAD-PARBHANI-NANDED- SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K (SCR) (N22000432)	4/2017	3/2022 (N.A.) {3/2022}	119.73 (185.00) {242.28}	54.15	50

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>ROAD TRANSPORT AND HIGHWAYS</u>	1509	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT (MoRTH) (N24000245)	1/2014	3/2016 (Sep-19) {9/2019}	270.00 (N.A.) {270.00}	0.00	72.15
		1510	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR (MoRTH) (N24000247)	10/2014	2/2017 (Dec-22) {3/2025}	295.47 (N.A.) {295.47}	224.42	80.07
		1511	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM (MoRTH) (N24000248)	3/2015	1/2017 (N.A.) {12/2023}	153.21 (N.A.) {153.21}	101.15	93.11
		1512	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON (MoRTH) (N24000980)	10/2016	2/2019 (Jun-22) {8/2024}	298.32 (N.A.) {298.32}	178.47	98
		1513	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ (MoRTH) (N24000981)	10/2016	3/2019 (Apr-23) {8/2024}	248.83 (N.A.) {248.83}	173.82	100
		1514	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE (MoRTH) (N24000982)	1/2017	5/2019 (Aug-19) {8/2019}	244.54 (N.A.) {244.54}	176.32	99.9
		1515	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH (MoRTH) (N24000983)	1/2017	10/2019 (Oct-19) {2/2024}	196.52 (N.A.) {196.52}	125.53	95.7

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1516	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI (MoRTH) (N24000984)	1/2017	12/2019 (Dec-19) {12/2019}	283.00 (N.A.) {283.00}	259.15	99.3
		1517	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION (MoRTH) (N24000986)	1/2017	5/2019 (Jul-21) {1/2024}	300.00 (N.A.) {300.00}	242.86	96.05
		1518	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH (MoRTH) (N24000987)	1/2018	5/2020 (Dec-22) {8/2024}	283.15 (N.A.) {283.15}	278.69	92.59
		1519	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 (MoRTH) (N24000988)	1/2018	12/2019 (Nov-20) {11/2020}	230.03 (N.A.) {230.03}	231.34	99.9
		1520	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 (MoRTH) (N24000989)	2/2018	6/2020 (Jan-21) {1/2021}	206.13 (N.A.) {206.13}	190.94	98.36
		1521	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT (MoRTH) (N24000990)	2/2018	11/2019 (Mar-22) {1/2024}	294.13 (N.A.) {294.13}	200.10	86.92
		1522	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC (MoRTH) (N24000993)	3/2018	9/2020 (Jun-22) {6/2023}	322.81 (N.A.) {322.81}	317.05	98.09

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1523	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES (MoRTH) (N24000994)	3/2018	7/2020 (Jun-24) {2/2026}	626.76 (N.A.) {626.76}	274.58	44.21
		1524	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR (MoRTH) (N24000996)	1/2017	10/2019 (Oct-19) {6/2021}	605.08 (N.A.) {605.08}	416.32	99.84
		1525	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL MALLAMPALLY SECTION OF NH-365 (MoRTH) (N24000997)	3/2018	7/2019 (Jun-22) {8/2024}	192.67 (N.A.) {192.67}	176.37	92
		1526	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR (MoRTH) (N24000998)	1/2019	(Jan-23) {8/2024}	193.19 (249.72) {249.72}	224.10	95
		1527	KHAMMAM-DEVARAPALLE PKG I [4L ACCESS CONTROLLED (GREENFIELD) FROM THALLAMPADU VILLAGE TO SOMAVARAM (NHAI) (N24001482)	8/2022	10/2024 (N.A.) {10/2024}	772.11 (N.A.) {772.11}	452.54	54.24
		1528	KHAMMAM DEVARAPALLE PKG II 4L ACCESS CONTROLLED (GREENFIELD) FROM SOMAVARAM VILLAGE TO CHINTAGUDEM V (NHAI) (N24001483)	2/2022	9/2024 (N.A.) {9/2024}	637.11 (N.A.) {637.11}	324.52	53.5
		1529	KHAMMAM-DEVARAPALLE PKG III [4L ACCESS CONTROLLED (GREENFIELD) FROM CHINTAGUDEM VILLAGE TO RECHERLA (NHAI) (N24001484)	9/2022	2/2024 (Dec-24) {12/2024}	804.69 (N.A.) {804.69}	410.82	61.76

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1530	4L OF KODAD (DESIGN KM 0.00/EXISTING KM 185.00 OF NH-65) TO KHAMMAM (DESIGN KM 31.800/EXISTING KM 29 (NHAI) (N24001522)	1/2021	1/2024 (Dec-24) {12/2024}	1,307.95 (N.A.) {1,307.95}	586.49	95.59
		1531	6 LANING OF EXISTING 4-LANE STRETCH FROM KALKALLU AT KM.454+000 TO GUNDLA POCHAMPALLY AT KM.471+000, (NHAI) (N24001555)	3/2022	1/2025 (N.A.) {1/2025}	955.49 (N.A.) {955.49}	172.69	28.09
		1532	6L OF EXISTING 4L FROM GUNDLAPOCHAMPALLY TO BOWENPALLY FROM KM 471.300 TO KM 481.331 OF NH-44 (NHAI) (N24001556)	12/2021	7/2024 (N.A.) {7/2024}	521.53 (N.A.) {521.53}	214.84	40.45
		1533	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JULEKAL VILLAGE TO DINNEDEVARAPADU VILLAGE FROM KM 242.20 (NHAI) (N24001625)	1/2022	1/2025 (N.A.) {1/2025}	1,227.57 (N.A.) {1,227.57}	4.98	0.95
		1534	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF NANDINNE VILLAGE TO JULEKAL VILLAGE FROM KM 202.900 TO KM (NHAI) (N24001626)	2/2022	1/2025 (N.A.) {1/2025}	972.06 (N.A.) {972.06}	8.38	2.14
		1535	WIDENING AND STRENGTHENING OF EXISTING 2 LANE WITH PAVED SHOULDER TO 4 LANE WITH PAVED SHOULDER FRO (MoRTH) (N24002000)	3/2021	7/2024 (N.A.) {8/2024}	317.19 (N.A.) {317.19}	164.72	67
		1536	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF MEDAK - SIDDIPET SECTION FROM KM 0/0 TO KM 69/978 OF NH- (MoRTH) (N24002001)	1/2022	1/2025 (N.A.) {6/2025}	882.18 (N.A.) {882.18}	245.95	56.17

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1537	WIDENING AND IMPROVEMENT OF EXISTING CARRIAGE WAY TO 2 LANE WITH PAVED SHOULDERS FROM KM. 86/160 TO (MoRTH) (N24002002)	1/2022	12/2024 (N.A.) {12/2024}	423.48 (N.A.) {423.48}	198.05	63.6
		1538	REHABILITATION AND UP-GRADATION OF VALIGONDA TO THORRUR SECTION TO TWO LANE WITH PAVED SHOULDERS FRO (MoRTH) (N24002003)	1/2022	12/2024 (N.A.) {3/2025}	549.28 (N.A.) {549.28}	156.95	54.92
		1539	REHABILITATION AND UPGADATION OF LB-NAGAR TO MALKAPUR SECTION TO 6- LANE MAIN CARRIAGEWAY WITH SERVI (MoRTH) (N24002004)	3/2021	7/2024 (N.A.) {6/2025}	545.11 (N.A.) {545.11}	264.25	64.11
		1540	WIDENING TO TWO LANE WITH PAVED SHOULDERS OF 'BODHAN BASAR BHAINSA ' SECTION FROM KM 38/900 TO 95/3 (MoRTH) (N24002005)	3/2022	3/2025 (N.A.) {6/2025}	644.45 (N.A.) {644.45}	205.53	58
		1541	ONSTRUCTION OF 4-LANE FLYOVER AT AMBERPET-X ROAD, HYDERABAD ON NH- 202 IN THE STATE OF TELANGANA (MoRTH) (N24002006)	10/2017	6/2023 (N.A.) {12/2024}	186.71 (N.A.) {186.71}	174.93	84.1
		1542	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/000 TO KM 79/300 OF KALWAKURTHY - KOLLAPUR SECTI (MoRTH) (N24002007)	3/2022	7/2025 (N.A.) {7/2025}	886.69 (N.A.) {886.69}	127.12	41.53
		1543	WIDENING TO 2 LANE WITH PAVED SHOULDERS OF SIDDIPET- ELKATHURTHY SECTION FROM KM 69/978 TO KM 133/6 (MoRTH) (N24002008)	1/2022	12/2024 (N.A.) {12/2024}	578.85 (N.A.) {578.85}	172.76	70

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1544	WIDENING AND STRENGTHENING TO 2/4 LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR CHINCHOLI SECTION FROM (MoRTH) (N24002009)	1/2022	1/2025 (N.A.) {7/2025}	703.68 (N.A.) {703.68}	249.04	44.95
		1545	WIDENING AND STRENGTHENING TO 4 LANE / 2-LANE WITH PAVED SHOULDERS OF MAHABUBNAGAR-CHINCHOLI SECTION (MoRTH) (N24002010)	3/2022	3/2024 (N.A.) {10/2025}	631.49 (N.A.) {631.49}	45.12	16
		1546	IMPROVEMENT OF GEOMETRICS OF THONDUPALLY TO KOTHUR FROM KM 22.300 TO KM 34.14 OF NH-44-RCW (NHAI) (N24002082)	2/2022	9/2024 (N.A.) {9/2024}	541.58 (N.A.) {541.58}	20.82	0
		1547	FOUR LANING OF KARIMNAGAR-WARANGAL SECTION OF NH-563 FROM DESIGN CH.48.860 KM NEAR SH-1 CH.170.400 K (NHAI) (N24002083)	3/2022	7/2025 (N.A.) {7/2025}	2,146.86 (2,413.00) {2,413.00}	740.96	44.78
TRIPURA	PETROLEUM	1548	GRASS ROOT RAIL FED DEPOT AT SEKERKOTE, AGARTALA AS RESITEMENT OF EXISTING DHARMANAGAR DEPOT (IOCL) (N16000495)	6/2022	8/2025 (Sep-25) {9/2025}	656.00 (N.A.) {656.00}	301.82	64
	RAILWAYS	1549	AGARTALA-AKHAURA NL (NFR) (N22000195)	4/2012	3/2020 (Jun-22) {9/2022}	569.63 (N.A.) {708.73}	380.92	84
	ROAD TRANSPORT AND HIGHWAYS	1550	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION (NHIDCL) (N24001263)	6/2020	1/2022 (Feb-24) {10/2024}	277.50 (302.02) {302.02}	253.50	99.12
		1551	KAILASHAHAR TO KHOWAI PKG-4 (NHIDCL) (N24001309)	11/2020	6/2022 (Oct-23) {10/2024}	159.13 (171.50) {171.50}	79.43	98.36

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1552	2-LANING FROM JOLAIBARI - BELONIA (NHIDCL) (N24001317)	6/2020	1/2022 (Jul-24) {11/2024}	201.99 (287.47) {287.47}	144.07	95.4
		1553	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 (NHIDCL) (N24001318)	9/2020	4/2022 (Oct-22) {10/2023}	173.17 (N.A.) {173.17}	93.35	100
		1554	MANU-SIMLUNG (PKG 4) (NHIDCL) (N24001363)	3/2021	12/2022 (Jun-23) {1/2025}	354.79 (N.A.) {354.79}	34.08	17.2
		1555	2 LANING FROM MANU-SIMLUNG PKG-2 (NHIDCL) (N24001542)	2/2022	1/2025 (N.A.) {1/2025}	456.88 (N.A.) {456.88}	95.50	39.4
		1556	IMPROVEMENT AND WIDENING TO 2- LANE WITH EARTHEN PAVED SHOULDER FROM UDAIPUR TO SRIMANTAPUR (NHIDCL) (N24001914)	5/2023	11/2024 (N.A.) {2/2025}	195.95 (N.A.) {195.95}	15.22	17.4
		1557	4 LANE WITH PAVED SHOULDER AGARTALA BYPASS (WESTERN SIDE) CONNECTING NH-8 (NHIDCL) (N24002132)	3/2023	3/2027 (N.A.) {3/2027}	2,026.05 (N.A.) {2,026.05}	0.00	0.48
		1558	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 25.250 TO KM 36.460 (TOTAL LENGTH: 11.210 KM) (NHIDCL) (N24002159)	2/2020	3/2026 (N.A.) {3/2026}	174.43 (N.A.) {174.43}	0.00	0
		1559	IMPROVEMENT AND WIDENING TO 2- LANE WITH PAVED SHOULDER OF ROAD FROM KM 101.300 TO KM 127.319 (TOTAL (NHIDCL) (N24002160)	1/2024	7/2026 (N.A.) {7/2026}	431.78 (N.A.) {431.78}	0.00	0
		1560	KHOWAI TELIAMURA-AMARPUR-HARINA- SABROOM PACKAGE-2 (NHIDCL) (N24002161)	1/2024	9/2026 (N.A.) {9/2026}	657.21 (N.A.) {657.21}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1561	KHOWAI TELIAMURA-AMARPUR-HARINA-SABROOM PACKAGE-3 (NHIDCL) (N24002162)	1/2024	9/2026 (N.A.) {9/2026}	670.90 (N.A.) {670.90}	0.00	0
UTTAR PRADESH	CIVIL AVIATION	1562	CCS INTERNATIONAL AIRPORT , LUCKNOW (AAI) (N04000077)	6/2018	9/2021 (Oct-26) {10/2026}	1,383.00 (1,938.00) {3,291.81}	2,117.08	76.05
		1563	DEVELOPMENT OF AYODHYA AIRPORT PHASE-01 (AAI) (N04000094)	3/2021	12/2022 (Oct-24) {10/2024}	242.14 (328.00) {358.00}	338.50	99.9
		1564	PRAYAGRAJ AIRPORT - CONSTRUCTION OF NEW TERMINAL BUILDING, SECOND LINK TAXI TRACK, APRON EXPANSION, (AAI) (N04000102)	5/2023	11/2024 (N.A.) {12/2024}	185.75 (232.52) {232.52}	80.95	43
		1565	AGRA: DEVELOPMENT OF NEW CIVIL ENCLAVE AT AGRA AIRPORT. (AAI) (N04000113)	6/2024	7/2026 (N.A.) {7/2026}	579.00 (N.A.) {579.00}	0.00	0
		1566	VARANASI: DEVELOPMENT OF LAL BAHADUR SHASTRI INTERNATIONAL AIRPORT, VARANASI. (AAI) (N04000114)	7/2024	7/2027 (N.A.) {7/2027}	2,869.65 (N.A.) {2,869.65}	0.00	0
	COAL	1567	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW (NLC) (N06000152)	7/2016	11/2021 (Mar-25) {3/2025}	17,237.00 (19,406.12) {19,406.12}	18,281.63	85.46
		1568	KHADIA EXPANSION OCP (NCL) (N06000208)	6/2021	3/2025 (N.A.) {3/2026}	491.67 (N.A.) {491.67}	36.25	5.93
	HOME AFFAIRS	1569	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI (CPWD FOR MHA) (N45000003)	5/2019	1/2022 (Mar-23) {3/2023}	199.31 (N.A.) {199.31}	86.49	85
	PETROLEUM	1570	60 KTA POLYPROPYLENE PROJECT (GAIL) (N16000429)	3/2019	4/2024 (Apr-24) {3/2025}	910.56 (1,299.02) {1,299.02}	809.40	90.7

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1571	AUGMENTATION OF FACILITIES AT MATHURA BITUMEN PLANT (IOCL) (N16000505)	4/2022	4/2025 (Dec-26) {12/2026}	260.12 (N.A.) {260.12}	0.97	18.4
		1572	GRASS-ROOT TERMINAL AT MIRZAPUR UTTAR PRADESH (IOCL) (N16000506)	9/2022	6/2026 (N.A.) {11/2026}	980.45 (N.A.) {980.45}	130.21	34.1
		1573	CITY GAS DISTRIBUTION PROJECTS AT LAKHIMPUR KHERI , SITAPUR, BAHRAICH, SHRAVASTI,BALRAMPUR, (BPCL) (N16000525)	12/2022	6/2030 (N.A.) {6/2030}	16,654.00 (N.A.) {16,654.00}	270.09	4.5
	POWER	1574	KHURJA SUPER THERMAL POWER PROJECT (THDCIL) (N18000272)	3/2019	9/2023 (N.A.) {3/2025}	11,089.42 (N.A.) {13,129.25}	11,108.48	92.6
		1575	KALPI SOLAR POWER PROJECT (NHPC) (N18000323)	7/2020	3/2022 (Mar-24) {3/2024}	314.64 (N.A.) {350.46}	316.03	92
		1576	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III (2X800 MW) (BHEL) (N18000382)	3/2024	2/2030 (N.A.) {2/2030}	17,195.31 (N.A.) {17,195.31}	531.00	0
	RAILWAYS	1577	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING (RVNL) (N22000401)	4/2015	3/2022 (N.A.) {12/2024}	943.60 (N.A.) {2,018.23}	1,779.61	98
		1578	RAMNA - SINGRAULI DOUBLING (ECR) (N22000417)	8/2015	3/2020 (N.A.) {9/2024}	2,436.21 (2,880.40) {2,880.40}	2,921.85	90
		1579	KARAILA ROAD - SHAKTINAGAR DOUBLING (ECR) (N22000419)	8/2015	3/2019 (N.A.) {8/2024}	528.57 (762.97) {762.97}	774.05	90
		1580	BURHWAL - GONDA - 3RD RUNNING LINE. (NER) (N22000468)	4/2016	(N.A.) {9/2025}	602.50 (N.A.) {1,015.59}	860.92	52

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1581	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. (NER) (N22000470)	4/2016	12/2019 (N.A.) {12/2024}	1,177.96 (N.A.) {1,777.39}	1,733.32	76
		1582	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING (NCR) (N22000495)	3/2018	3/2023 (N.A.) {3/2026}	4,329.53 (N.A.) {4,329.53}	60.37	3
		1583	JHANSI BINA DOUBLING (NCR) (N22000496)	9/2016	3/2021 (N.A.) {12/2023}	2,001.00 (2,001.00) {2,001.00}	1,118.80	85
		1584	MATHURA-JHANSI-3RD LINE (273.80 KM) (RVNL) (N22000501)	6/2016	12/2023 (N.A.) {12/2024}	3,677.76 (N.A.) {5,190.26}	4,969.16	80
		1585	SURFACE TRIANGLE LINE BETWEEN BHADURA STATION AND NEW CROSSING STN KARMA DOUBLING (ECR) (N22000525)	10/2022	10/2027 (N.A.) {10/2027}	199.96 (N.A.) {199.96}	55.09	0
		1586	MUGHALSARAI - ALLAHABAD - 3RD LINE (NCR) (N22000544)	8/2019	12/2026 (N.A.) {12/2026}	2,390.00 (N.A.) {2,390.00}	0.00	0
		1587	ALIGARH-HARDUAGANJ FLYOVER (22 KM) (NCR) (N22000545)	4/2020	6/2026 (Jun-26) {6/2026}	1,456.89 (N.A.) {1,456.89}	0.00	5
		1588	LALITPUR - BIRARI WITH FLYOVER AT LALITPUR (NCR) (N22000546)	3/2017	12/2024 (N.A.) {12/2024}	260.00 (N.A.) {260.00}	0.00	0
		1589	ALIGARH-DAUD KHAN - 3RD LINE (6.9 KM) & CONSTRUCTION OF FLYOVER AT DAUD KHAN (NCR) (N22000562)	4/2019	12/2025 (N.A.) {12/2025}	451.99 (N.A.) {451.99}	0.00	0
		1590	ALLAHABAD-BAMHRAULI - 4TH LINE (10 KM) WITH FLY-OVER AT SUBEDARGANJ (NCR) (N22000563)	4/2019	3/2026 (N.A.) {3/2026}	494.11 (N.A.) {494.11}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1591	BHANDAI - FLYOVER FOR ETAWAH BOUND DOWN TRAINS (<i>NER</i>) (N22000564)	4/2019	12/2025 (N.A.) {3/2026}	187.21 (N.A.) {250.17}	1.75	8
		1592	SAHJANWA - DOHRIGHAT (<i>NER</i>) (N22000565)	8/2019	3/2029 (N.A.) {12/2027}	371.77 (N.A.) {1,319.75}	391.33	1
		1593	BAHRAICH - NANPARA -NEPALGANJ (56.15 KM) (<i>NER</i>) (N22000566)	7/2020	12/2024 (N.A.) {6/2025}	950.00 (N.A.) {341.66}	88.28	19
		1594	BAHRAICH SRAVASTI BALRAMPUR (TULSIPUR) (<i>NER</i>) (N22000569)	10/2018	10/2030 (N.A.) {12/2026}	1,600.00 (N.A.) {4,939.78}	824.28	5
		1595	BARABANKI AKBARPUR DOUBLING (<i>NR</i>) (N22000578)	9/2017	3/2025 (N.A.) {3/2025}	1,200.00 (N.A.) {1,700.00}	0.00	0
		1596	JAUNPUR AKBARPUR (TANDA) DOUBLING (<i>NR</i>) (N22000582)	8/2017	3/2025 (N.A.) {3/2025}	515.50 (N.A.) {676.00}	0.00	0
		1597	JANGHAI PRATAPGARH AMETHI DOUBLING (<i>NR</i>) (N22000583)	11/2017	3/2025 (N.A.) {3/2025}	701.98 (N.A.) {1,100.00}	0.00	0
		1598	BARABANKI-MALHAUR - 3RD & 4TH LINE (32.84 KM) (<i>NR</i>) (N22000590)	1/2019	3/2025 (N.A.) {3/2025}	323.85 (N.A.) {323.85}	0.00	0
		1599	DOUBLING BETWEEN JAUNPUR JN- ZAFFARABAD (6.28 KM) (<i>NR</i>) (N22000591)	3/2023	12/2026 (N.A.) {12/2026}	177.33 (N.A.) {177.33}	0.00	0
		1600	JANGHAI-PHAPHAMAU - DOUBLING WITH ELECTRIFICATION (46.79 KM) (<i>RVNL</i>) (N22000596)	11/2018	3/2025 (N.A.) {3/2025}	357.48 (N.A.) {409.38}	312.07	48
		1601	BHATNI - AUNRIHAR WITH ELECTRIFICATION (125 KM) (EXCL INDARA - MAU (116.95 KM)) (<i>RVNL</i>) (N22000598)	5/2018	3/2024 (N.A.) {2/2025}	1,177.96 (N.A.) {2,529.46}	1,574.90	76

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1602	MATHURA - VRINDAVAN (11 KM) (NCR) (N22000612)	8/2022	6/2025 (N.A.) {6/2025}	402.88 (N.A.) {402.88}	0.00	0
		1603	DOMINGARH - GORAKHPUR - GORAKHPUR CANTT - KUSUMHI - 3RD RUNNING LINE (21.15 KM) (NER) (N22000613)	11/2016	6/2024 (N.A.) {5/2025}	186.85 (N.A.) {457.68}	430.43	84
	<u>ROAD</u> <u>TRANSPORT</u> <u>AND</u> <u>HIGHWAYS</u>	1604	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B (MoRTH) (N24000331)	12/2019	4/2022 (N.A.) {12/2024}	282.41 (N.A.) {319.96}	270.96	83
		1605	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] (NHAI) (N24000551)	3/2016	4/2019 (Dec-24) {12/2024}	1,587.49 (3,473.59) {3,500.00}	3,356.10	95.68
		1606	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 (NHAI) (N24000556)	3/2016	4/2019 (Oct-24) {10/2024}	899.00 (1,623.88) {1,623.88}	1,106.35	92.15
		1607	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH 74 FROM (KM 204.300 OF NH 58) TO KM 73.00 (NHAI) (N24000564)	3/2016	7/2020 (Mar-25) {3/2025}	1,408.00 (1,659.12) {1,659.12}	1,199.58	80.09
		1608	CONSTRUCTION OF NH-24 EXTENSION 4- LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO (NHAI) (N24000796)	3/2018	12/2021 (Dec-23) {7/2024}	1,117.84 (N.A.) {1,203.92}	1,198.22	99.56
		1609	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA (NHAI) (N24000798)	3/2018	11/2021 (N.A.) {12/2024}	2,140.93 (N.A.) {2,140.93}	2,062.47	97.94

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1610	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH 14 (NHA) (N24001185)	11/2017	7/2021 (Dec-24) {12/2024}	2,159.00 (2,262.00) {2,262.00}	2,249.93	97.5
		1611	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN (NHA) (N24001306)	10/2020	3/2023 (N.A.) {5/2024}	724.60 (N.A.) {724.60}	569.96	84.92
		1612	CONSTRUCTION OF 6 LANE BRIDGE ON GANGA ON NH-96 AND ITS APPROACHES IN PHAPHAMAU ALLAHABAD ON EPC MOD (MoRTH) (N24001421)	7/2018	2/2024 (N.A.) {8/2025}	1,948.25 (N.A.) {1,948.25}	951.38	68
		1613	CONSTRUCTION OF BYPASS FOR PROVIDING INTER CONNECTIVITY AMONG (NHS) AROUND THE PRATAPGARH CITY (PRAT (MoRTH) (N24001423)	4/2021	9/2023 (N.A.) {3/2026}	309.48 (N.A.) {309.48}	112.84	51
		1614	CONSTRUCTION OF FOUR-LANE ELEVATED VIADUCT FROM KM.4+634 TO KM.6+345 ON NH-24A INCLUDING RETAINING W (MoRTH) (N24001424)	3/2021	9/2023 (N.A.) {12/2024}	185.09 (269.81) {269.81}	256.11	96
		1615	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF RADHAITA TO PILIBHIT SECTION OF 46.130 KM (MoRTH) (N24001456)	4/2020	2/2024 (N.A.) {10/2024}	199.39 (212.96) {199.39}	154.00	91
		1616	REHABILITATION AND UPGRADATION TO 2 LANE WITH PS OF MIRANPUR KATRA TO RADHAITA SECTION OF NH- 730C F (MoRTH) (N24001457)	4/2020	7/2024 (N.A.) {3/2025}	172.50 (169.56) {172.50}	94.27	60

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1617	2-LANE WITH PS OF BEWAR TO NEAR KARRI VILLAGE SECTION OF NH-92 FROM KM.0.00 TO 30.00 UNDER GNHCP (MoRTH) (N24001461)	4/2020	3/2024 (N.A.) {12/2024}	236.47 (N.A.) {236.47}	129.25	79
		1618	2-LANE WITH PS OF NEAR KARRI VILLAGE TO ETAWAH SECTION OF NH-92 FROM KM.30.000 TO 57.346 UNDER GNHCP (MoRTH) (N24001462)	4/2020	7/2024 (N.A.) {12/2024}	211.09 (N.A.) {211.09}	103.12	77
		1619	ALLAHGANJ TO MIRANPUR KATRA SECTION OF NH-730C FROM KM.52.770 TO 114.00 (MoRTH) (N24001463)	4/2020	7/2024 (N.A.) {2/2024}	294.84 (309.99) {294.84}	271.61	100
		1620	PROJECTS- REHABILITATION AND UPGRADATION OF NH-731A FROM KM 0.00 TO KM.35.00 (MoRTH) (N24001464)	3/2021	8/2023 (N.A.) {1/2025}	264.86 (N.A.) {264.86}	106.25	67
		1621	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 55.00 TO (MoRTH) (N24001469)	11/2021	5/2024 (N.A.) {3/2025}	307.11 (N.A.) {307.11}	158.36	75
		1622	R/U TO 2-LANE WITH PS OF BEWAR TO ALLAHGANJ SECTION OF NH-730C FROM KM.0.00 TO 52.770 UNDER GNHCP (MoRTH) (N24001471)	4/2020	11/2024 (N.A.) {11/2024}	325.24 (340.16) {325.24}	220.97	80
		1623	WIDENING AND UPGRADATION TO FOUR LANE CONFIGURATION FROM KM.34.900 (BHADOHI) TO KM.73.134 (JAUNPUR) (MoRTH) (N24001479)	3/2021	5/2024 (N.A.) {6/2025}	395.62 (392.03) {395.62}	240.26	54

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1624	WIDENING AND STRENGTHENING FROM KM 0.00 TO KM 15.089 OF NH-334A (PURKAJI-LAKSAR-HARIDWAR ROAD) TO TW (MoRTH) (N24001480)	10/2021	4/2024 (N.A.) {12/2024}	227.06 (N.A.) {227.06}	104.84	85
		1625	6L ACCESS-CONTROLLED HIGHWAY FROM (GANESHPUR) TO(NEAR MOHAND) OF GANESHPUR DEHRADUN SECTION FROM K (NHAI) (N24001523)	3/2021	10/2023 (Nov-24) {11/2024}	836.24 (N.A.) {836.24}	773.94	97.14
		1626	6L OF ACCESS-CONTROLLED HIGHWAY FROM MOHAND TO DAAT KALI TUNNEL OF GANESHPUR DEHRADUN SECTION FROM (NHAI) (N24001524)	3/2021	10/2023 (Nov-24) {11/2024}	990.28 (N.A.) {990.28}	997.51	97.98
		1627	WIDENING AND STRENGTHENING OF SECTION FROM BHARTHANA CHOWK TO KODARKOOT (KM. 0.00 TO KM. 40.00) OF (MoRTH) (N24001587)	3/2020	9/2024 (N.A.) {12/2024}	262.37 (343.77) {343.77}	235.13	64
		1628	4L SPUR OF SHAMLI-MUZZAFARNAGAR CONNECTING NH-709AD (PANIPAT- SHAMLI-MUZAFFARNAGAR) AND NH-58 (MEERUT (NHAI) (N24001726)	1/2023	8/2024 (N.A.) {8/2024}	391.26 (N.A.) {391.26}	14.12	77.3
		1629	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 2/4L PS FROM KM 40.000 TO 88.750, START OF KHUTAR B (NHAI) (N24001727)	3/2022	2/2025 (N.A.) {2/2025}	762.62 (N.A.) {762.62}	410.93	65.47
		1630	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 175.080 TO 229.070, FROM END OF HARDO (NHAI) (N24001728)	12/2021	7/2025 (N.A.) {7/2025}	1,138.81 (N.A.) {1,138.81}	275.48	85.62

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1631	4L SPUR OF PANIPAT - SHAMLI CONNECTING NH-709AD (PANIPAT SHAMLI MUZAFFARNAGAR) AND NH- 709A (KARN (NHAI) (N24001729)	8/2022	4/2024 (N.A.) {12/2024}	326.79 (N.A.) {329.79}	93.31	79.11
		1632	4L FROM GAJU VILLAGE AT KM 32.982 TO DEVINAGAR BYPASS (END) AT KM 208.000 OF NH 530B (PKG 1C) (NHAI) (N24001730)	12/2021	1/2025 (N.A.) {1/2025}	1,384.79 (N.A.) {1,384.79}	619.92	94
		1633	6L GREENFIELD KANPUR - LUCKNOW (EXPRESSWAY) PKG II FROM KM. 28.500 TO KM. 73.744 (NHAI) (N24001731)	12/2021	5/2025 (May-25) {5/2025}	2,470.64 (N.A.) {2,335.00}	523.01	64.09
		1634	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 229.070 TO 260.800, END OF HARDOI DIS (NHAI) (N24001732)	12/2021	10/2024 (N.A.) {10/2024}	540.97 (N.A.) {540.97}	196.42	64.56
		1635	6L ACCESS CONTROLLED GREENFIELD HIGHWAY OF JUNCTION OF EPE (VILL.- MAVIKALAN) TO VILL.-LOHADDA FROM K (NHAI) (N24001733)	3/2022	8/2024 (N.A.) {12/2024}	1,602.48 (N.A.) {1,602.48}	349.48	74.56
		1636	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-LOHADDA TO VILL- KARAUNDA MAHAJAN FROM KM. 27.000 TO KM. (NHAI) (N24001734)	3/2022	8/2024 (N.A.) {12/2024}	1,335.45 (N.A.) {1,335.45}	343.63	69.65
		1637	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KHYAWARI TO VILL- LATIFPUR AT SAHARANPUR BYPASS FROM KM (NHAI) (N24001735)	3/2022	8/2024 (N.A.) {12/2024}	1,428.19 (N.A.) {1,428.19}	414.64	69.65

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1638	6L ACCESS CONTROL GREENFIELD HIGHWAY OF VILL-KARAUNDA MAHAJAN TO VILL-KHYAWARI FROM KM. 56.500 TO K (NHAI) (N24001736)	1/2022	8/2024 (N.A.) {12/2024}	1,159.96 (N.A.) {1,159.96}	503.59	98
		1639	4LPS OF MUZAFFARNAGAR TO MIRANPUR SECTION OF NH-709AD, PKG- III (NHAI) (N24001737)	11/2021	4/2024 (N.A.) {4/2024}	923.15 (N.A.) {923.15}	455.61	97.1
		1640	2LPS OF BIJNOR TO KOTAWALI SECTION OF NH-709AD, PKG-IV (NHAI) (N24001738)	9/2021	10/2023 (Dec-24) {12/2024}	300.79 (N.A.) {300.79}	122.56	66.5
		1641	REHABILITATION and UPGRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER BHARATMALA PARIYOJANA FOR U (NHAI) (N24001739)	10/2019	11/2023 (Dec-24) {12/2024}	1,779.83 (N.A.) {2,200.00}	1,028.00	96.89
		1642	4L OF SHAMLI BYPASS- SAHARANPUR FROM KM 92.2 TO KM 155.025 SECTION OF NH-709B, PKG-II (NHAI) (N24001744)	5/2019	11/2022 (N.A.) {12/2024}	779.17 (N.A.) {779.17}	54.69	93
		1643	KANPUR LUCKNOW EXPRESSWAY PKG-1 CONSTRUCTION OF 6-LANE TO EIGHT LANE OF KANPUR LUCKNOW EXPRESSWAY (N (NHAI) (N24001745)	12/2021	7/2025 (Jul-25) {7/2025}	1,972.10 (N.A.) {1,936.00}	431.50	54.56
		1644	2-LANE EXISTING RAMPUR BYPASS OF RAMPUR TO BE DEVELOPED TO 4-LANE ON EPC MODE IN THE STATE OF UTTAR (NHAI) (N24001746)	3/2021	4/2024 (Jan-25) {1/2025}	364.47 (N.A.) {364.47}	132.40	65.01
		1645	4 LANING OF NAJIBABAD BYPASS OF NH- 119 FROM KM. 105.423 TO KM. 118.373 (EXCLUDING 2.45 KM. OF NH-74 (NHAI) (N24001753)	2/2022	6/2024 (Nov-24) {11/2024}	570.98 (578.02) {578.02}	342.08	80.03

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1646	SPUR OF MEERUT-GARH-MUKTESHWAR SECTION(NH-709A) CONNECTING NH-119 AND NH-58 BYPASSING MEERUT TOWN (NHAI) (N24001754)	1/2022	10/2024 (N.A.) {10/2024}	953.79 (N.A.) {953.79}	384.66	42.74
		1647	4-LANING OF MEERUT NAJIBABAD SECTION FROM KM. 11.500 TO KM 39.250 AND KM 86.590 TO KM. 112.545.IN TH (NHAI) (N24001755)	10/2019	3/2023 (Dec-24) {12/2024}	1,936.68 (N.A.) {2,458.03}	1,380.90	98.1
		1648	4 LANE CONNECTOR FROM DELHI MEERUT EXPRESSWAY KM 50.000 TO KM 8.520 OF NH 235 IN THE STATE OF UTTAR (NHAI) (N24001772)	8/2021	3/2024 (Dec-24) {12/2024}	1,147.26 (N.A.) {1,147.26}	81.34	33
		1649	4L BYPASSES FOR JAGATPUR, B4ABUGANJ, UNCHAHAR, ALAPUR BYPASS, AND SAI RIVER BRIDGE OF RAEBARELI- PRA (NHAI) (N24001815)	12/2022	11/2024 (N.A.) {11/2024}	1,699.00 (1,078.00) {1,699.00}	64.39	51.2
		1650	VARANASI RING ROAD (PKG-II) CONNECTING SANDAHA VILLAGE (KM 11.70 / NH-29) WITH REVASA VILLAGE (KM 81 (NHAI) (N24001826)	2/2019	2/2022 (Dec-24) {12/2024}	927.77 (N.A.) {1,603.00}	1,202.77	79.45
		1651	SIX LANE ACCESS CONTROLLED OF DELHI SAHARANPUR HIGHWAY FROM DELHI UP BORDER TO EPE JUNCTION CH.14.75 (NHAI) (N24001830)	6/2020	11/2023 (Dec-24) {12/2024}	2,002.79 (N.A.) {2,002.79}	1,989.85	99
		1652	4L FROM MATHURA BYPASS (START) AT EXISTING KM. 154.20 OF NH-44 TO GAJU VILLAGE AT KM 32.982 OF NH-53 (NHAI) (N24001851)	1/2022	3/2025 (N.A.) {3/2025}	1,738.20 (N.A.) {1,738.20}	741.63	63

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1653	6L OF AGRA BYPASS (NORTHERN) CONNECTING KM. 174.500 OF NH-2 (NEW NH-19) TO KM. 141.000 OF YAMUNA EXP (NHA) (N24001852)	10/2021	2/2025 (N.A.) {2/2025}	957.62 (N.A.) {957.62}	615.00	83.36
		1654	CONSTRUCTION OF LEFT OUT PORTION OF AGRA INNER RING ROAD CONNECTING VILLAGE DEORI TO NH-44 VILLAGE B (NHA) (N24001853)	10/2021	9/2024 (N.A.) {9/2024}	772.05 (N.A.) {772.05}	545.44	66
		1655	CONSTRUCTION OF 4-LANE GREEN FIELD HIGHWAY FROM KM. 35.000 TO KM. 49.155 OF NH-731A WITH PAVED SHOUL (MoRTH) (N24001929)	1/2022	10/2025 (N.A.) {10/2025}	697.66 (N.A.) {697.66}	254.18	63
		1656	BALANCE WORKS OF 4-LANNING OF RAMPUR-KATHGODAM SECTION OF NH- 87 (NEW NH NO. 09) FROM KM. 0.000 (KM 1 (NHA) (N24001992)	8/2022	2/2024 (Oct-24) {10/2024}	199.31 (199.38) {199.38}	130.59	63.6
		1657	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER HIGHWAY FROM DESIGN CH.0.000 TO CH.49.200 OF NH- 731B ON (MoRTH) (N24001996)	3/2022	11/2025 (N.A.) {11/2025}	640.18 (602.76) {602.76}	335.67	39
		1658	CONSTRUCTION OF SHOHRATGARH BYPASS ON NH-730 UNDER EPC MODE IN THE STATE OF UTTAR PRADESH (MoRTH) (N24001997)	10/2022	5/2025 (N.A.) {5/2025}	189.31 (N.A.) {189.31}	50.67	15
		1659	IMPROVEMENT AND UPGRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM 90.00 TO (MoRTH) (N24002015)	11/2021	6/2025 (N.A.) {6/2025}	403.36 (328.49) {403.36}	63.13	18

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1660	CONSTRUCTION OF PRATAPGARH BYPASS (EXTENSION) CONNECTING NH- 31 TO NH-330 (MoRTH) (N24002016)	10/2022	6/2025 (N.A.) {6/2025}	225.17 (N.A.) {225.17}	85.93	37
		1661	WIDENING TO FOUR LANE WITH PAVED SHOULDER FROM DESIGN KM.49.200 TO KM.89.285 OF NH-731B ON EPC MODE (MoRTH) (N24002029)	3/2022	1/2026 (N.A.) {1/2026}	917.91 (956.30) {917.91}	473.25	18
		1662	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER FROM EXISTING KM.0.000 TO KM.55.610 (DESIGN KM. 0.000 T (MoRTH) (N24002031)	12/2021	2/2026 (N.A.) {2/2026}	840.93 (773.58) {840.93}	337.83	5
		1663	CONSTRUCTION OF 4-LANE HIGHWAY WITH PAVED SHOULDERS FROM KM 49.155 TO KM 74.700 OF NH-731A ON HYBRID (MoRTH) (N24002032)	1/2022	1/2026 (N.A.) {1/2026}	1,156.72 (N.A.) {1,156.72}	200.30	21
		1664	DEVELOPMENT OF SIX-LANE ACCESS CONTROLLED HIGHWAY FROM GOGWAN JALALPUR (SHAMLI DISTRICT) TO RANIPUR (NHAI) (N24002036)	4/2022	5/2025 (N.A.) {5/2025}	1,843.59 (N.A.) {1,843.59}	774.19	33
		1665	GARHMUKTESHWAR (KM. 83.200 OF NH- 24) TO MEERUT (KM. 9.860 OF NH-235) INCLUDING CONNECTOR TO NH-119 (NHAI) (N24002073)	10/2019	10/2023 (N.A.) {6/2024}	2,068.99 (2,171.00) {2,171.00}	209.60	47
		1666	WIDENING OF RAEBARELI TO PRAYAGRAJ SECTION FROM KM. 82.650 TO KM. 161.450 OF NH-30 AND LINK ROAD FRO (NHAI) (N24002085)	11/2023	3/2025 (N.A.) {3/2025}	1,470.93 (N.A.) {1,470.93}	69.56	16.37

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1667	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002086)	10/2022	7/2025 (N.A.) {7/2025}	1,706.47 (N.A.) {1,706.47}	688.34	37.28
		1668	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002087)	10/2022	10/2025 (N.A.) {10/2025}	1,493.14 (N.A.) {1,493.14}	45.30	18.26
		1669	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER (GREENFIELD) SECTION OF (NHAI) (N24002088)	10/2022	8/2025 (N.A.) {8/2025}	1,493.50 (N.A.) {1,493.50}	474.79	24.05
		1670	CONSTRUCTION OF FOUR LANE HIGHWAY FROM GHAZIPUR BALLIA UP BIHAR STATE BORDER GREENFIELD SECTION OF N (NHAI) (N24002089)	10/2022	6/2025 (N.A.) {6/2025}	617.87 (N.A.) {617.88}	95.37	39.24
		1671	CONSTRUCTION OF FOUR-LANE WESTERN SIDE SPUR OF RAMPUR- RUDRAPUR SECTION CONNECTING NH- 24 TO NH-87 BY (NHAI) (N24002090)	3/2021	11/2024 (Apr-25) {4/2025}	646.27 (N.A.) {646.27}	45.10	20.47
		1672	IMPROVEMENT , UP-GRADATION OF NH- 734 SECTION OF MORADABAD - THAKURDWARA - KASHIPUR: PACKAGE- I: MORA (NHAI) (N24002093)	10/2022	9/2025 (N.A.) {9/2025}	1,841.92 (N.A.) {1,841.92}	202.27	24.6
		1673	IMPROVEMENT AND UP-GRADATION OF EXISTING ROAD TO 4L PS FROM KM 123.650 TO 175.080, FROM START OF SHA (NHAI) (N24002094)	9/2022	11/2025 (N.A.) {11/2025}	1,212.26 (N.A.) {1,212.26}	295.07	15.55

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1674	FOUR LANING OF SONAULI GORAKHPUR SECTION OF NH 29E (NEW NH 24) FROM DESIGN CH. 0.000 TO DESIGN CH. 7 (NHAI) (N24002095)	12/2021	3/2025 (N.A.) {3/2025}	2,555.50 (N.A.) {2,555.50}	764.75	34.1
		1675	CONSTRUCTION OF 4 LANE GREEN FIELD NORTHERN EAST SIDE GORAKHPUR BYPASS (26.616 KMS) STARTING FROM NH (NHAI) (N24002096)	2/2023	1/2026 (N.A.) {1/2026}	1,973.98 (N.A.) {1,973.98}	515.30	21.53
		1676	STRENGTHENING OF EXISTING 4L AYODHYA BYPASS SECTION FROM DESIGN KM.121.600 TO KM. 144.020 OF NH 28 () (NHAI) (N24002097)	2/2023	9/2025 (N.A.) {3/2025}	526.45 (N.A.) {526.45}	121.93	53.8
		1677	CONSTRUCTION OF RING ROAD AROUND KANPUR FROM KM.000 TO KM. 23.325 (CHACHENDI SACHENDI I TO MAHARAJPU (NHAI) (N24002104)	1/2023	6/2026 (N.A.) {6/2026}	1,754.00 (N.A.) {1,754.00}	206.15	12.5
		1678	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS (PHASE-I) FROM DESIGN KM 43+200 (AT MAHUWARI VI (NHAI) (N24002105)	8/2023	6/2026 (N.A.) {6/2026}	1,378.36 (N.A.) {739.00}	74.61	15.03
		1679	CONSTRUCTION OF NEW 4 LANE PRAYAGRAJ SOUTHERN BYPASS FROM DESIGN KM 50.860 (NABABA URF NIBI KALA UPA (NHAI) (N24002106)	8/2023	3/2025 (N.A.) {3/2025}	993.77 (N.A.) {349.48}	132.46	46.7
		1680	CONSTRUCTION OF MARIAHU BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION (KM.53.540 TO KM.59.200) (MoRTH) (N24002115)	3/2023	8/2025 (N.A.) {8/2025}	438.24 (362.39) {438.24}	169.39	12

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1681	REHABILITATION AND UPGRADATION FROM KM 51.600 TO KM 75.700 OF NH-321G (NUHKHAS TO ETAH SECTION) TO T (MoRTH) (N24002116)	1/2022	8/2025 (N.A.) {8/2025}	343.54 (N.A.) {343.54}	46.36	19
		1682	CONSTRUCTION OF JASRA BYPASS WITH FOUR LANE PAVED SHOULDER CONFIGURATION FROM KM. 379.670 ON NH-76 ((MoRTH) (N24002120)	2/2023	9/2025 (N.A.) {9/2025}	274.06 (N.A.) {274.06}	66.73	36
		1683	IMPROVEMENT AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDER CONFIGURATION FROM EXISTING KM. 420.00 (MoRTH) (N24002121)	1/2022	9/2025 (N.A.) {9/2025}	509.65 (N.A.) {509.65}	130.57	12
		1684	REHABILITATION AND UP-GRADATION FROM KM. 0.000 TO KM. 40.390 OF NH-730S (MAHARAJGANJ NICHLOUL TH (MoRTH) (N24002134)	3/2023	12/2025 (N.A.) {12/2025}	809.25 (N.A.) {809.25}	152.15	0
		1685	CONSTRUCTION OF FOUR LANE HIGHWAY WITH PAVED SHOULDER FROM KM.74.700 TO KM.112.950 OF NH-731A (I/C Y (MoRTH) (N24002138)	3/2022	6/2026 (N.A.) {6/2026}	1,141.67 (N.A.) {1,141.67}	205.24	5
		1686	CONSTRUCTION OF BALRAMPUR BYPASS WITH 2L FLEXIBLE PAVEMENT CONFIGURATION FROM KM.223.000 OF NH-330 T (MoRTH) (N24002150)	12/2022	2/2026 (N.A.) {2/2026}	515.69 (N.A.) {515.69}	104.25	0
	URBAN DEVELOPMENT	1687	KANPUR METRO RAIL PROJECT (LMRCL) (N28000144)	5/2019	3/2024 (N.A.) {6/2026}	11,076.48 (N.A.) {11,076.48}	7,639.03	66.4
		1688	AGRA METRO RAIL PROJECT (LMRCL) (N28000145)	5/2019	3/2024 (N.A.) {12/2025}	8,379.62 (N.A.) {8,379.62}	3,943.50	44.2

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	<u>WATER RESOURCES</u>	1689	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA (UPJalNigam) (N30000006)	5/2017	9/2021 (N.A.) {6/2023}	767.59 (N.A.) {767.59}	276.97	100
		1690	FARRUKHABAD I AND D AND STP WORKS HAM (UPJalNigam) (N30000008)	10/2017	3/2022 (Feb-21) {11/2024}	213.62 (261.12) {261.12}	177.62	94
		1691	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS (UPJalNigam) (N30000010)	3/2018	9/2021 (N.A.) {7/2023}	967.23 (708.70) {967.23}	254.98	100
		1692	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH (UPJalNigam) (N30000013)	3/2019	8/2021 (N.A.) {7/2024}	271.39 (N.A.) {271.39}	182.26	100
		1693	MATHURA SEWERAGE SCHEME (UPJalNigam) (N30000019)	12/2017	12/2020 (Jun-18) {6/2022}	460.45 (N.A.) {460.45}	315.30	100
		1694	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH (UPJalNigam) (N30000021)	1/2019	12/2021 (Jan-20) {11/2024}	231.79 (234.03) {234.03}	141.79	96
		1695	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH (UPJalNigam) (N30000022)	1/2019	10/2021 (N.A.) {7/2023}	206.05 (N.A.) {206.05}	139.23	100
		1696	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH (UPJalNigam) (N30000024)	2/2019	6/2022 (N.A.) {12/2025}	681.78 (N.A.) {690.71}	13.34	0
		1697	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH (UPJalNigam) (N30000025)	3/2019	7/2021 (May-20) {9/2024}	298.12 (N.A.) {240.93}	94.86	96

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
UTTARAKHAND	CIVIL AVIATION	1698	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN (AAI) (N04000085)	7/2018	9/2020 (N.A.) {9/2024}	456.86 (N.A.) {500.00}	483.05	100
	POWER	1699	TEHRI PUMPED STORAGE PLANT(1000MW) (THDCIL) (N18000010)	7/2006	2/2016 (Jun-22) {1/2025}	1,657.00 (4,825.60) {7,686.32}	7,049.84	97.5
		1700	TAPOVAN-VISHNUGAD HEP (4X130MW) (NTPC) (N18000014)	11/2006	3/2013 (N.A.) {4/2029}	2,978.48 (N.A.) {7,103.00}	6,298.38	75
		1701	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT (THDCIL) (N18000042)	8/2008	6/2013 (N.A.) {6/2026}	2,491.58 (3,860.35) {6,303.00}	4,056.80	68.4
		1702	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW (NTPC) (N18000142)	7/2012	8/2017 (N.A.) {8/2017}	1,527.00 (N.A.) {1,527.00}	149.93	0
	RAILWAYS	1703	RISHIKESH - KARNAPRAYAG NEW LINE (RVNL) (N22000406)	4/2011	12/2024 (N.A.) {3/2025}	16,216.00 (N.A.) {24,659.00}	18,267.00	82.1
	ROAD TRANSPORT AND HIGHWAYS	1704	4-LANING OF KASHIPUR-SITARGANJ SECTION (MEGA) (N24000465)	11/2012	8/2016 (N.A.) {8/2016}	605.84 (N.A.) {605.84}	0.00	0
		1705	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 (NHAI) (N24000559)	3/2016	10/2019 (Oct-24) {10/2024}	720.00 (1,150.00) {1,150.00}	639.87	94.11
		1706	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 (NHIDCL) (N24000741)	3/2018	11/2020 (Dec-22) {3/2024}	274.31 (N.A.) {274.31}	251.61	99

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	Sl No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1707	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI (NHIDCL) (N24000742)	3/2018	11/2020 (Dec-22) {3/2024}	403.36 (N.A.) {403.36}	337.72	95.91
		1708	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA (NHIDCL) (N24000743)	3/2018	11/2020 (Dec-22) {3/2024}	417.24 (N.A.) {417.24}	344.20	98.72
		1709	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000772)	12/2017	12/2019 (N.A.) {12/2019}	257.34 (N.A.) {257.34}	232.69	100
		1710	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000773)	12/2017	12/2019 (N.A.) {12/2019}	200.34 (253.43) {200.34}	227.98	100
		1711	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 (MoRTH) (N24000774)	12/2017	12/2019 (N.A.) {12/2019}	248.22 (N.A.) {248.22}	236.80	100
		1712	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000775)	6/2017	6/2019 (Mar-23) {3/2023}	282.08 (N.A.) {282.08}	234.97	100
		1713	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG (MoRTH) (N24000776)	11/2017	11/2019 (N.A.) {11/2019}	232.81 (N.A.) {232.81}	201.58	100

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1714	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION (MoRTH) (N24000777)	11/2017	11/2019 (N.A.) {11/2019}	283.51 (N.A.) {283.51}	278.51	100
		1715	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S (MoRTH) (N24000778)	11/2017	11/2019 (N.A.) {11/2019}	266.52 (N.A.) {266.52}	250.34	100
		1716	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR (MoRTH) (N24000779)	2/2018	2/2020 (Mar-23) {3/2023}	418.88 (N.A.) {418.88}	339.71	94
		1717	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K (MoRTH) (N24000780)	2/2018	(Apr-23) {4/2023}	293.68 (N.A.) {293.68}	244.25	100
		1718	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN (MoRTH) (N24000781)	5/2018	5/2020 (Dec-23) {12/2023}	248.00 (N.A.) {248.00}	120.50	65.56
		1719	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 (MoRTH) (N24000782)	3/2018	(N.A.) {}	460.73 (N.A.) {461.00}	0.00	0
		1720	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) (NHIDCL) (N24000855)	3/2018	7/2022 (Jul-22) {1/2026}	1,383.78 (N.A.) {1,383.78}	591.11	61.46

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1721	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER (MoRTH) (N24001130)	8/2016	12/2017 (N.A.) {12/2017}	234.88 (273.49) {234.88}	237.19	100
		1722	6L ACCESS-CONTROLLED HIGHWAY OF DAAT KALI TUNNEL - DEHRADUN OF GANESHPUR DEHRADUN SECTION FROM KM. (NHAI) (N24001525)	3/2021	3/2024 (Nov-24) {11/2024}	169.08 (N.A.) {169.08}	94.67	98.87
		1723	UPGRADATION AND 4L OF HARIDWAR BYPASS FROM KM 0.000 (KM 188.100 OF NH-58) TO KM. 15.100 (KM 5.100 OF (NHAI) (N24001526)	8/2021	10/2024 (Oct-24) {10/2024}	1,377.79 (1,384.11) {1,377.79}	679.10	46.81
		1724	4L MEDINIPUR TO BALLUPUR FROM KM. 458.65 TO KM. 487.65 OF NH-07(PKG-2) (NHAI) (N24001553)	3/2022	2/2025 (Feb-25) {2/2025}	1,092.90 (1,092.90) {1,092.90}	461.92	54.76
		1725	4L POANTA SAHEBMEDNIPUR FROM KM. 435.65 TO KM. 458.65 OF NH-07(PKG-1) (NHAI) (N24001990)	6/2022	5/2025 (May-25) {5/2025}	524.54 (683.26) {683.26}	74.94	45.07
		1726	ACCESS ROAD/BRIDGE CONNECTIVITY FROM NH-09 AT KM.40 NEAR JAGBUDA BRIDGE (INDIA) TO BOUNDARY PILLAR (NHAI) (N24001991)	5/2022	9/2024 (May-25) {5/2025}	314.31 (N.A.) {314.31}	139.73	52.6
		1727	4L OF DUDHADHARI ELEVATED FLYOVER (MUZAFFARNAGAR HARIDWAR SECTION) FROM KM 356.450 TO KM 353.800 OF (NHAI) (N24001995)	5/2021	11/2023 (Dec-24) {12/2024}	154.52 (N.A.) {154.52}	150.26	98.43

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1728	CONSTRUCTION FOR MITIGATION MEASURES KM 368.00-UTTARAKHAND-TO KM 433.00 ON NH-07-PKG-1 (NHIDCL) (N24002163)	12/2023	12/2025 (N.A.) {12/2025}	216.88 (N.A.) {216.88}	0.00	5
		1729	CONSTRUCTION FOR MITIGATION MEASURES KM 450.00-UTTARAKHAND-TO KM 468.00 ON NH-07-PKG-3 (NHIDCL) (N24002164)	12/2023	12/2025 (N.A.) {12/2025}	250.33 (N.A.) {250.33}	0.00	5
		1730	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH (UKJalNigam) (N30000004)	3/2017	11/2019 (N.A.) {2/2022}	158.00 (N.A.) {158.00}	105.88	100
	WATER RESOURCES							
WEST BENGAL	CIVIL AVIATION	1731	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA (AAI) (N04000080)	1/2016	3/2020 (Jun-22) {12/2023}	458.00 (N.A.) {458.00}	246.68	100
		1732	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA (AAI) (N04000081)	1/2019	11/2021 (N.A.) {5/2023}	389.71 (N.A.) {395.00}	393.60	100
		1733	NSCB AIRPORT KOLKATA: RE-CONSTRUCTION OF RIGID POSITIONS OF SECONDARY RUNWAY, 'K' AND 'A' TAXIWAY (AAI) (N04000109)	4/2023	10/2025 (N.A.) {10/2025}	328.30 (N.A.) {328.30}	47.16	23
	COAL	1734	RANIGANJ MASTER PLAN (ECL) (N06000163)	8/2009	8/2019 (N.A.) {8/2024}	2,661.73 (N.A.) {5,146.48}	760.22	40.5
		1735	SIDULI MINE (OC AND UG) (ECL) (N06000165)	5/2018	3/2026 (N.A.) {3/2026}	535.18 (N.A.) {535.17}	3.95	13.2
		1736	NAKRAKONDA KUMARDIH B OCP (ECL) (N06000170)	8/2018	3/2029 (N.A.) {3/2029}	502.68 (N.A.) {502.67}	58.91	25.3
		1737	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT (ECL) (N06000191)	4/2020	3/2025 (Mar-26) {3/2026}	483.65 (N.A.) {483.65}	32.53	12

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1738	2.0 MTPA BHOJUDIH NLW WASHERY (BCCL) (N06000195)	12/2015	3/2017 (N.A.) {10/2024}	341.22 (341.22) {341.22}	317.21	94
		1739	SONEPUR BAZARI EXPANSION OC (ECL) (N06000220)	7/2021	3/2029 (N.A.) {3/2029}	5,365.88 (5,366.00) {5,365.88}	508.61	17
		1740	EXPANSION PR OF JHANJRA UG (5.00 MTY) (ECL) (N06000223)	4/2020	3/2029 (N.A.) {3/2029}	1,210.12 (N.A.) {1,210.12}	400.47	35
		1741	MOHANPUR EXPANSION OC PHASE II (ECL) (N06000236)	11/2020	3/2025 (Mar-26) {3/2026}	888.99 (N.A.) {888.99}	90.32	30
		1742	BONJEME HARI EXPANSION OCP (ECL) (N06000244)	8/2021	3/2025 (Mar-26) {3/2026}	570.12 (N.A.) {570.11}	48.80	16
		1743	ITAPARA OC (ECL) (N06000272)	12/2023	3/2030 (N.A.) {3/2030}	929.10 (N.A.) {929.10}	43.11	5
		1744	UCE OF TILABONI UG (ECL) (N06000276)	1/2023	3/2029 (N.A.) {3/2029}	749.07 (N.A.) {749.07}	1.14	0
		1745	UCE OF PARASEA BELBAID REORGANISATION UG (ECL) (N06000277)	1/2023	3/2029 (N.A.) {3/2029}	389.10 (N.A.) {389.10}	0.00	14
	DEPARTMENT OF HIGHER EDUCATION	1746	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED (CPWD EDUCATION) (N28000146)	3/2020	6/2020 (N.A.) {5/2024}	193.83 (N.A.) {193.83}	185.75	99
	HOME AFFAIRS	1747	NSG AT KOLKATA (CPWD FOR MHA) (N28000104)	10/2014	4/2018 (N.A.) {12/2024}	162.88 (210.83) {210.83}	187.06	88
	MINES	1748	CONSTRUCTION OF BASEMENTG FLOOR10 STORIES BUILDING FOR THE STATE OF THE ART, DG, GSI AT SECTOR- V, SA (CPWD) (N10000015)	4/2019	4/2022 (N.A.) {8/2026}	255.37 (N.A.) {255.37}	56.19	25.5

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	PETROLEUM	1749	DURGAPUR-HALDIA PIPELINE PROJECT (GAIL) (N16000275)	3/2017	12/2020 (Mar-25) {3/2025}	1,740.00 (2,433.15) {2,433.15}	2,022.30	86.8
		1750	CITY GAS DISTRIBUTION IN WEST BENGAL (HPCL) (N16000392)	3/2019	3/2031 (Mar-29) {3/2029}	5,830.20 (N.A.) {5,830.20}	739.95	23
		1751	HALDIA PANAGARH PIPELINE PROJECT (HPCL) (N16000478)	11/2022	11/2025 (N.A.) {11/2025}	1,010.00 (N.A.) {1,010.00}	279.02	54.62
		1752	CGD PROJECT AT EAST MEDNIPORE, WEST MEDNIPORE AND JHARGRAM DISTRICTS (IOCL) (N16000491)	3/2022	3/2030 (N.A.) {6/2031}	609.00 (N.A.) {609.00}	63.62	1.1
		1753	CGD PROJECT IN WEST BENGAL 11TH ROUND (HPCL) (N16000498)	6/2022	6/2030 (N.A.) {6/2030}	2,628.00 (N.A.) {2,628.00}	150.93	17.2
		1754	CITY GAS DISTRIBUTION PROJECTS AT ALIPURDUAR AND COOCH BEHAR (BPCL) (N16000522)	12/2022	3/2030 (N.A.) {3/2030}	1,017.00 (N.A.) {1,017.00}	73.43	20
	POWER	1755	RAMMAM-III HEPP (3X40 MW) (NTPC) (N18000178)	9/2014	9/2019 (N.A.) {3/2029}	1,381.84 (N.A.) {1,803.00}	1,042.24	45.1
		1756	DURGAPUR PP-III (2X20 MW) - NSPCL (NTPC) (N18000277)	12/2016	11/2018 (Mar-24) {3/2024}	529.68 (633.80) {679.00}	558.39	89
	RAILWAYS	1757	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER (ER) (220100272)	4/2000	3/2019 (Mar-25) {3/2025}	1,188.91 (N.A.) {2,582.49}	1,087.01	75
		1758	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA- BARASAI VIA BIMANBANDER (MTP) (KOMRCL) (N22000108)	4/2010	3/2016 (N.A.) {3/2016}	2,397.72 (N.A.) {2,397.72}	197.20	17

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1759	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) (RVNL) (N22000109)	4/2010	3/2014 (N.A.) {12/2025}	2,298.42 (N.A.) {2,733.86}	392.84	33
		1760	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) (RVNL) (N22000110)	4/2010	3/2016 (N.A.) {3/2026}	3,951.98 (N.A.) {8,964.35}	6,817.20	73
		1761	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. (RVNL) (N22000111)	4/2010	3/2016 (N.A.) {12/2026}	2,913.51 (N.A.) {4,834.54}	3,869.56	95.41
		1762	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE (MRTP) (N22000135)	3/2013	3/2016 (Dec-23) {12/2023}	4,874.58 (8,574.98) {10,442.41}	8,008.94	96.2
		1763	PURULIA TO KOTSHILA DOUBLING (39.1 KM) (SER) (N22000510)	4/2018	6/2022 (N.A.) {12/2024}	338.00 (N.A.) {393.83}	184.84	60
		1764	AZIMGANJ-MURSHIDABAD (JIYAGANJ) INCL. RLY. BRIDGE OVER RIVER BHAGIRATHI (ER) (N22000609)	10/2001	2/2024 (N.A.) {2/2024}	164.33 (N.A.) {187.05}	157.27	100
		1765	NAHATI - RANAGHAT 3RD LINE (MM OF KALINARAYANPUR - KRISHNANAGAR) (ER) (N22000624)	7/2015	3/2025 (Mar-26) {3/2026}	283.54 (N.A.) {283.54}	159.30	44
		1766	EAST WEST METRO CORRIDOR KOLKATA (KOMRCL) (N22000628)	2/2009	9/2016 (N.A.) {6/2024}	4,874.58 (8,575.00) {10,442.41}	0.00	0
	ROAD TRANSPORT AND HIGHWAYS	1767	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) (NHAI) (N24000463)	12/2015	6/2018 (May-24) {8/2023}	1,083.00 (1,414.01) {1,414.01}	1,080.05	100

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1768	SIX-LANING OF BARWA ADDA- PANAGARH (NHAI) (N24000515)	4/2014	9/2016 (N.A.) {11/2024}	1,665.00 (N.A.) {4,913.22}	4,913.22	93.1
		1769	REHABILITATION AND UP GRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER CONFIGURATION IN PURU (NHAI) (N24000788)	3/2018	9/2022 (Dec-22) {3/2025}	841.57 (708.30) {708.30}	6,433.40	92.44
		1770	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H (MoRTH) (N24000874)	3/2016	11/2018 (Dec-23) {10/2024}	271.17 (291.20) {291.20}	180.63	76.86
		1771	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. (MoRTH) (N24000880)	2/2018	9/2020 (Jan-24) {10/2024}	426.18 (426.18) {426.18}	364.92	90.08
		1772	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND (MoRTH) (N24000885)	3/2016	9/2023 (Mar-24) {7/2024}	160.27 (213.97) {213.97}	144.31	100
		1773	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N (MoRTH) (N24000887)	6/2016	9/2021 (Feb-24) {10/2024}	236.78 (263.26) {263.26}	222.11	99.68
		1774	SIX LANE OF PALSIT TO DANKUNI SECTION FROM 588.870 TO KM. 652.700 (NHAI) (N24001747)	3/2020	9/2024 (N.A.) {9/2024}	2,193.23 (2,314.00) {2,314.00}	1,905.34	74.19
		1775	SIX LANING OF NATIONAL CORRIDOR NH19 FROM PANAGARH TO PALSIT IN THE STATE OF WEST BENGAL UNDER BHARA (NHAI) (N24001748)	3/2021	9/2024 (N.A.) {6/2025}	2,200.93 (N.A.) {2,431.60}	2,431.60	89.47

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1776	FOUR LANING OF PURULIYA BYPASS SECTION OF NH 32 IN THE STATE OF WEST BENGAL ON EPC MODE (NHA) (N24001749)	8/2021	8/2023 (N.A.) {11/2024}	557.55 (N.A.) {557.55}	468.42	90.74
		1777	CONSTRUCTION OF NEW 4 LANE BRIDGE OVER RIVER GANGA AT DOWNSTREAM OF FARAKKA BARRAGE INCLUDING APPROA (NHA) (N24001750)	8/2018	12/2021 (N.A.) {2/2025}	622.04 (N.A.) {622.04}	485.74	79.37
		1778	FOUR LANING OF BAL. WORKS OF BARASAT-KRISHNAGAR FROM KM.48.553 TO KM.115.272 (NHA) (N24001752)	12/2018	2/2023 (Aug-23) {10/2024}	2,375.87 (2,843.79) {2,843.79}	2,371.78	100
		1779	DEVELOPMENT TO 4/6-LANNING OF NH- 31 (NEW NH-10) WITH BOTH SIDE SERVICE ROADS FROM KM 569.258 TO KM 5 (MoRTH) (N24001850)	3/2022	9/2025 (Sep-25) {9/2025}	995.04 (995.04) {995.04}	241.60	33.12
	STEEL	1780	REBUILDING OF COKE OVEN BATTERY NO.4 OF DURGAPUR STEEL PLANT (SAIL) (N12000132)	11/2023	12/2026 (N.A.) {12/2026}	916.78 (N.A.) {916.78}	44.31	3
	WATER RESOURCES	1781	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS (KMDA) (N30000029)	1/2019	4/2022 (Feb-19) {12/2024}	384.96 (N.A.) {384.96}	0.00	0
		1782	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR (KMDA) (N30000030)	3/2019	4/2022 (N.A.) {12/2024}	287.53 (N.A.) {287.53}	0.00	0
		1783	I AND D AND STP WORKS AT BURDWAN WEST BENGAL (KMDA) (N30000031)	12/2018	4/2022 (N.A.) {12/2024}	234.31 (N.A.) {234.31}	0.00	0

Table:-6. Project List: Ongoing Projects as of 30th September 2024

State	Sector	SI No	Project Name (Agency Name) (Project Code)	Date of Approval (MM/YYYY)	Date of Commissioning Original (Revised) {Anticipated} (MM/YYYY)	Cost Original (Revised) {Anticipated} in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
		1784	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA (KMDA) (N30000032)	5/2018	2/2022 (N.A.) {3/2025}	198.43 (224.69) {224.69}	75.82	78
		1785	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS (KMDA) (N30000033)	3/2018	6/2022 (N.A.) {3/2024}	165.16 (N.A.) {165.16}	0.00	0
		1786	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA (KMDA) (N30000034)	8/2017	9/2022 (Jan-23) {12/2026}	307.12 (N.A.) {653.67}	0.00	0
		1787	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH (KMDA) (N30000042)	5/2018	2/2022 (Sep-20) {10/2024}	160.00 (154.73) {154.73}	84.27	88
		1788	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH (KMDA) (N30000045)	8/2017	12/2021 (Feb-21) {2/2024}	185.22 (N.A.) {185.22}	49.99	100
		1789	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR (KMDA) (N30000046)	2/2014	12/2019 (N.A.) {6/2022}	274.76 (N.A.) {332.56}	276.93	100
		1790	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE (KMDA) (N30000047)	12/2014	4/2020 (N.A.) {6/2022}	272.32 (341.68) {272.32}	306.81	100
		1791	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI (KMDA) (N30000048)	1/2018	12/2021 (Feb-21) {2/2024}	172.10 (N.A.) {172.10}	47.20	100
		1792	INTERCEPTION AND DIVERSION WITH STP AT BALLY (KMDA) (N30000049)	10/2017	12/2021 (Feb-21) {2/2024}	164.93 (N.A.) {164.93}	45.45	100
			Total			2,756,378.31 (-) {3,332,647.33}	1,753,624.20	

Abbreviations used in the Report

AGENCY_NAME	AGENCY_NAME_SHORT
AIRPORT AUTHORITY OF INDIA LIMITED	AAI
ARTIFICIAL LIMBS MANUFACTURING CORPM. OF INDIA	ALIMCO
BHARAT ALUMINUM CORPORATION	BALCO
BHABHA ATOMIC RESEARCH CENTRE	BARC
BHARAT COKING COAL LIMITED	BCCL
BRAHMAPUTRA CRECKER & POLYMER LTD.	BCPL
BHAVINI LIMITED	BHAVNI
BHARAT HEAVY ELECTRICALS LIMITED	BHEL
BANGALORE METRO RAIL CORPORATION LIMITED	BMRCL
BOKARO STEEL PLANT	BOKARO STEEL PL
BRAHMAPUTRA BOARD	BPB
BHARAT PETROLEUM CORPORATION LIMITED	BPCL
BORDER ROAD ORGANISATION	BRO
BONGAIGAON REFINERY PETROLEUM LIMITED	BRPL
BHARAT SANCHAR NIGAM LIMITED	BSNL
Bihar Urban Infrastructure Development Corporation Ltd	BUIDCO
BRAHMAPUTRA VALLY FERTILISER CORPORATION	BVFC
CENTRE FOR DEVELOPMENT OF TELEMATICS, TELECOM, TECHNOLOGY	C-DOT
CENTRAL COAL FIELDS LIMITED	CCL
CONTAINER CORPORATION OF INDIA	CCOI
CHENAB VALLEY POWER CORPORATION LIMITED	CHENAB VALLEY P
CHENNAI METRO RAIL LTD	CMRL
CHENNAI PETROLEUM CORPORATION LIMITED	CPCL
CENTRAL PUBLIC WORKS DEPARTMENT	CPWD
CPWD OF HIGHER EDUCATION	CPWD EDUCATION
CPWD FOR DEFENCE	CPWD FOR DEFENC
CPWD FOR FINANCE	CPWD FOR FINANC
CPWD FOR HEALTH	CPWD FOR HEALTH
CPWD FOR MHA	CPWD FOR MHA
CPWD FOR POWER	CPWD FOR POWER
CPWD FOR RURAL	CPWD FOR RURAL
CPWD FOR TELECOM	CPWD FOR TELECO
CPWD FOR RENEWABLE ENERGY	CPWD R ENERGY
CENTRAL RAILWAYS	CR
COCHIN REFINERY LIMITED	CRL
COCHIN SHIPYARD LTD	CSL
CHENAB VELLEY POWER PROJECTS [P] LIMITED	CVPPPL
DUMMY AGENCY	DA
DEDICATED FREIGHT CORRIDOR CORPORATION OF INDIA LTD	DFCC
DIRECTORATE GENERAL OF CIVIL AVIATION	DGCA
Delhi Jal Board	DJB
Delhi Mumbai Industrial Corridor	DMIC
DMIC FOR DPIIT	DMIC FOR DPIIT
DELHI METRO RAIL CORPORATION	DMRC
DEPARTMENT OF TELECOMMUNICATION	DOT
Department for Promotion of Industry and Internal Trade	DPIIT
DAMODAR VALLEY CORPORATION	DVC
EASTERN COAL FIELDS LIMITED	ECL
EAST COAST RAILWAY	ECOR
EAST CENTRAL RAILWAYS	ECR

AGENCY_NAME	AGENCY_NAME_SHORT
EDCIL(India) Limited	EDCIL
ENNORE PORT LTD.	ENNORE PORT LTD
ENNORE TANK TERMINAL PVT.LTD.	ENNORE TANK
EASTERN RAILWAYS	ER
FERTILISER AND CHEMICAL TRIVANCORE	FACT
FREIGHT OPERATION INFORMATION SYSTEM	FOIS
SETTING UP FILM AND TELEVISION INSTITUTE	FTI
GAS AUTHORITY OF INDIA LIMITED	GAIL
GOA SHIPYARD LIMITED	GSL
HEALTH & FAMILY WELFARE	H&FW
HINDUSTAN AERONAUTICS LTD	HAL
HINDUSTAN COPPER LIMITED	HCL
HALDIA FERTILISER CORPORATION	HFC
HLL Infra Tech Services Limited	HITES
HYDERABAD METRO RAIL LTD	HMRL
HINDUSTAN PETROLEUM CORPORATION LIMITED	HPCL
HPCL Rajasthan Refinery Limited(JV)	HPCLRRL(JV)
HPOIL Gas Pvt. Ltd	HPOIL(JV)
HOSPITAL SERVICES CONSULTANCY CORPORATION LTD	HSCC
HINDUSTAN STEELWORK CONSTRUCTION LIMITED	HSCL
HINDUSTHAN STEELWORKS CONSTRUCTION LIMITED	HSCL
HSCL FOR DONER	HSCL FOR DONER
HSCL FOR RURAL	HSCL FOR RURAL
HSCL FOR WATER	HSCL FOR WATER
INDIAN FARMERS FERTILISER CORPORATION	IFFCO
INDIRA GANDHI CENTRE FOR ATOMIC RESEARCH	IGCAR
INDRADHANUSH GAS GRID LTD	IGGL
India International Convention and Expo Centre	IICC
IICC FOR DPIIT	IICC FOR DPIIT
INDIAN IRON STEEL COMPANY	IISCO
Indian Institute of Technology, Kharagpur	IITKGP
INDIAN OIL CORPORATION LIMITED	IOCL
INDIAN PETRO-CHEMICAL CORPORATION LIMITED	IPCL
Indian Railway Construction Company Limited	IRCON
INDIAN STRATEGIC PETROLEUM RESERVES LTD	ISPRL
INDIAN TELEPHONE INDUSTRY	ITI
Inland Waterways Authority of India	IWAI
INLAND WATER TRANSPORT	IWT
JAWAHAR LAL NEHRU NATIONAL URBAN RENEWAL MISSION	JNNURM
JWAAHARLAL NEHRU PORT TRUST	JNPT
Jharkhand Urban Infrastructure Development Company Ltd	JUIDCO
Kolkata Metropolitan Development Authority	KMDA
KOCHI METRO RAIL CORPORATION LTD	KMRCL
KOLKATA METRO RAIL CORPORATION LIMITED	KOMRCL
KAMARAJAR PORT LIMITED	KPL
KONKAN RAILWAY	KR
Rail Infrastructure Development Company	KRIDE
KOCHI REFINERIES LIMITED	KRL
Kochi Salem Pipeline Private Limited(JV)	KSPPL(JV)
LINE DOUBLING	LD
LUCKNOW METRO RAIL CORPORATION LIMITED	LMRCL
MANGALORE REFINERY AND PETROCHEMICALS LIMITED	MANGALORE REFIN

AGENCY_NAME	AGENCY_NAME_SHORT
MAHANADI COAL FIELDS LIMITED	MCL
MECON LIMITED	MECON LIMITED
AHMEDABAD METRO RAIL	MEGA
MADRAS FERTILISER LIMITED	MFL
Munitions India Limited	MIL
MAHARASTRA METRO RAIL CORPORATION LTD.	MMRC
MUMBAI METRO RAIL CORPORATION LTD	MMRCL
MINISTRY OF WATER RESOURCES	MOWR
Madhya Pradesh Metro Rail Co Limited	MPMRCL
Maharashtra Rail Infrastructure Development Corporation Limited	MRIDC
MANGALORE REFINARY LIMITED	MRL
METROPOLITAN RAPID TRANSPORT PROJECTS	MRTP
Mumbai Railway Vikas Corporation	MRVC
MAHANAGAR TELEPHONE NIGAM LIMITED	MTNL
MUMBAI PORT TRUST	MUMBAI PORT TRU
Armoured Vehicles Nigam Limited	MVNL
MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)	MoRTH
NATIONAL ALUMINUM COMPANY LIMITED (NALCO)	NALCO
NATRIIP IMPLEMENTATION SOCIETY	NATIS
NATIONAL BUILDING CONSTRUCTION CORPORATION LTD	NBCC
NBCC FOR COMMERCE	NBCC FOR COMMER
NBCC FOR HEALTH	NBCC FOR HEALTH
NORTHERN COAL FIELDS LIMITED	NCL
NORTH CENTRAL RAILWAY	NCR
NATIONAL CAPITAL REGION TRANSPORT CORP	NCRTC
NATIONAL CENTRE OF EXCELLENCE	NCoE
NORTH EAST ELECTRIC POWER CORPORATION	NEEPCO
NORTH EAST GAS GRID	NEGG
NORTH EASTERN RAILWAY	NER
National Film Archive of India	NFAI
NUCLEAR FUEL CORPORATION	NFC
NATIONAL FERTILISER LIMITED	NFL
NORTH EAST FRONTIER RAILWAY	NFR
NATIONAL HIGHWAYS AUTHORITY OF INDIA	NHAI
NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.	NHIDCL
NATIONAL HYDRO-ELECTRIC POWER CORPORATION	NHPC
National High Speed Rail Corporation Limited	NHSRCL
NEW LINE	NL
NEYVELI LIGNITE CORPORATION	NLC
NATIONAL MISSION FOR CLEAN GANGA	NMCG
NATIONAL MINERAL DEVELOPMENT CORPORATION (NMDC)	NMDC
NAGPUR METRO RAIL CORPORATION LTD	NMRCL
NATIONAL PROJECTS CONSTRUCTION CORPORATION LIMITED	NPCC
NUCLEAR POWER CORPORATION OF INDIA LIMITED	NPCIL
NORTHERN RAILWAY	NR
NUMALIGARH REFINERY LIMITED	NRL
SETTING UP OF NEW RAILWAY ZONES	NRZ
NATIONAL THERMAL POWER CORPORATION	NTPC
NORTH WESTERN RAILWAY	NWR
OIL INDIA LIMITED	OIL
OIL & NATURAL GAS CORPORATION LIMITED	ONGC
PATNA METRO RAIL CORPORATION	PATNA METRO RAI

AGENCY_NAME	AGENCY_NAME_SHORT
PAWAN HANS HELICOPTERTERS LTD.	PAWAN HANS HELI
POWER GRID CORPORATION OF INDIA LIMITED	PGCIL
PORT TRUST	PORT TRUST
Polavaram Project Authority	PPA
RASHTRIYA CHEMICAL & FERTILISER LIMITED	RCF
RAILWAY ELECTRIFICATION	RE
RASTRIYA ISPAT NIGAM LIMITED	RINL
RAIL INDIA TECHNICAL AND ECONOMIC SERVICE	rites
rites OF HIGHER EDUCATION	rites OF HIGHER
RAIL VIKAS NIGAM LTD.	RVNL
SIGNALLING & TELECOMMUNICATIONS	S&T
STEEL AUTHORITY OF INDIA LIMITED (SAIL)	SAIL
SINGARENI COLLIERS COMPANY LIMITED	SCCL
SOUTH CENTRAL RAILWAY	SCR
SOUTH-EASTERN COAL FIELDS LIMITED	SECL
SOUTH EAST CENTRAL RAILWAY	SECR
SOUTH EASTERN RAILWAY	SER
SER(GC) GAUGE CONVERSION	SER(GC
SHIPPING CRP. OF INDIA	SHIPP.
SATLUJ JAL VIDYUT NIGAM LIMITED	SJVN
SOUTHERN RAILWAY	SR
SOUTH WESTERN RAILWAY	SWR
Sikkim University	Sikkim Universi
THDC INDIA LIMITED	THDCIL
TUTICORIN PORT TRUST	TUTICORIN
URANIUM CORPORATION OF INDIA LIMITED	UCIL
URBAN DEVELOPMENT	UD
Uttarakhand Pey Jal Nigam	UKJalNigam
Uttar Pradesh Jal Nigam	UPJalNigam
VISAKHAPATNAM PORT TRUST	VPT
Varanasi Smart City	Varanasi Smart
WAPCOS	WAPCOS
WESTERN COAL FIELDS LIMITED	WCL
WEST CENTRAL RAILWAY	WCR
WESTERN RAILWAY	WR
WORKSHOPS & PRODUCTION UNIT	WS&PU



Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.cspm.gov.in>
