



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation

478th — Flash Report on Central Sector Infrastructure Projects —



(Rs. 150 crore
& above)

AUGUST 2025



Scan the QR code to access
the PAIMANA Portal.

www.mospi.gov.in @GoIStats /GoIStats GoIStats Ministry of Statistics & PI



CONTENTS

I. Overview*	2-4
II. North Eastern Region	5-6
III. As per Harmonized Master List (HML) 2022	7-13
IV. Major Infrastructure Central Ministries & Departments	14-19
V. Appendix : <i>List of Tables</i>	20 onwards
Table 1: Ministry-wise Ongoing Projects	
Table 2: State-wise Ongoing Projects	
Table 3: Ongoing Projects of North Eastern Region	
Table 4: All Ongoing Projects	

**Note: This report is web-generated from the PAIMANA portal (ipm.mospi.gov.in) as of August 2025, based on the projects worth Rs. 150 crores and above reported by Central Line Ministries/ Departments/ Implementing Agencies (excluding Ministry of Road Transport & Highways, may reflect from next month onwards) on the IPM portal (indiainvestmentgrid.gov.in) latest by 12th September 2025.*





Overview





Flash Report

Central Sector Infrastructure Projects Costing Rs. 150 crore & above

AUGUST 2025

800 | 14

Ongoing Projects |
Line Ministries & Departments

₹ 23,75,332

Original Cost
(crores)

₹ 29,07,548

Revised Cost
(crores)


₹ 15,37,609

(52.88% of Revised Cost)

Expenditure
(crores)


Sectoral Comparison : Major Sectors*

[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

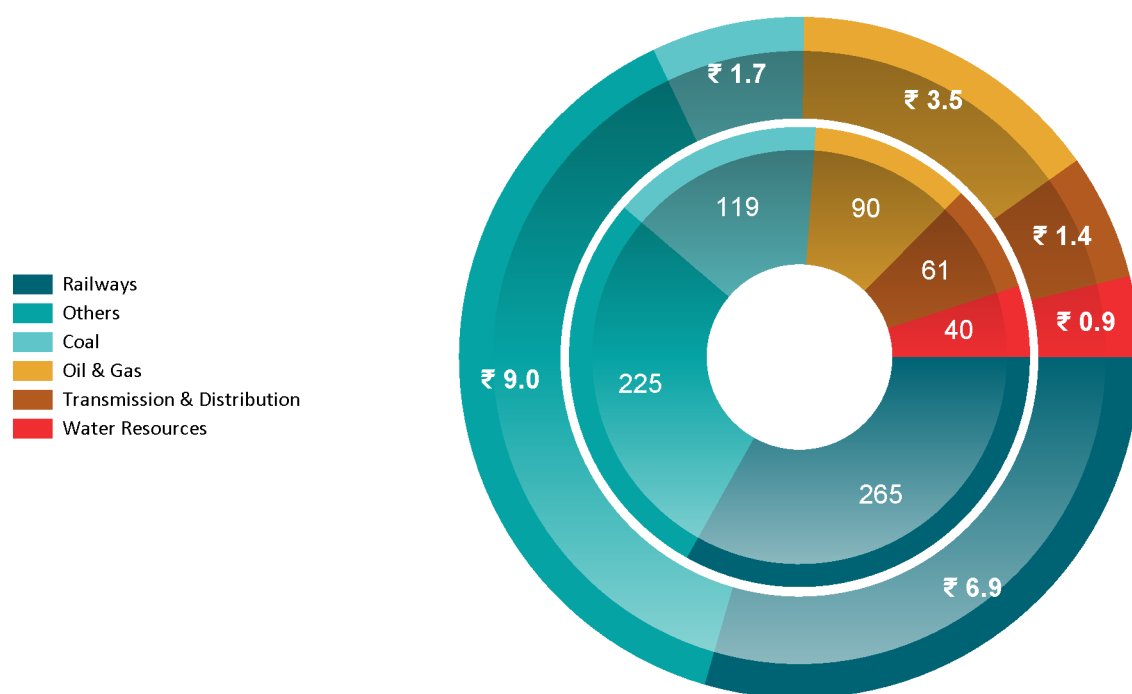


Ministry Comparison : Major Ministries*


[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

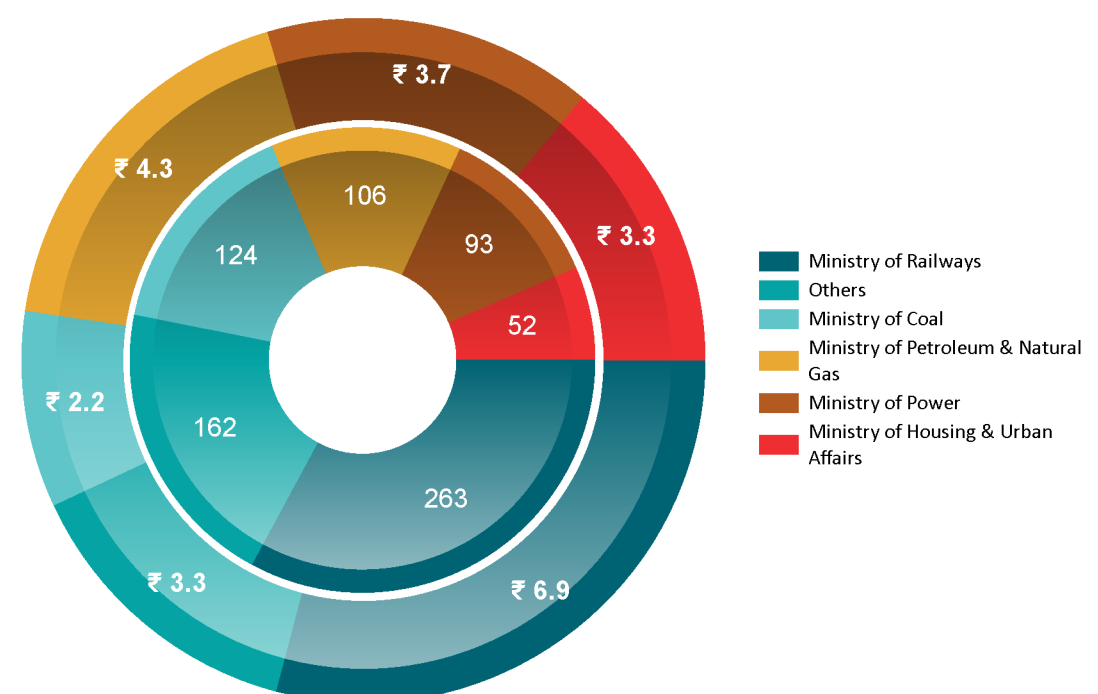

Cost Analytics : Major Sectors*

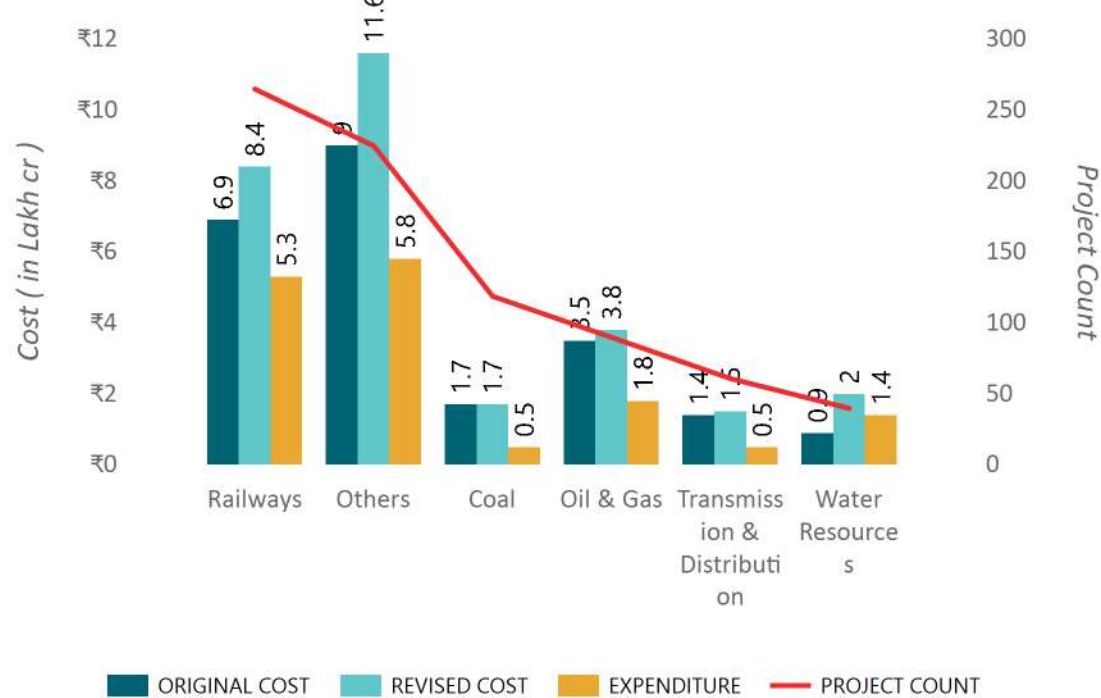


Cost Analytics : Major Ministries*

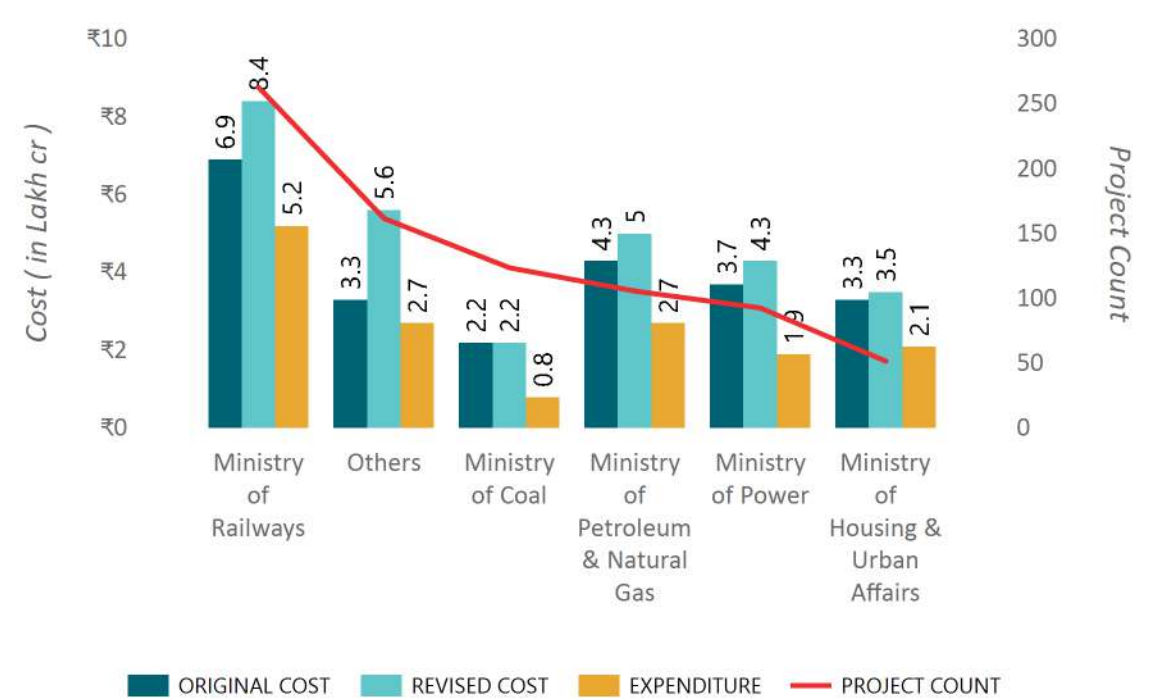


Note: * as per Project Count

Analytics: as per HML

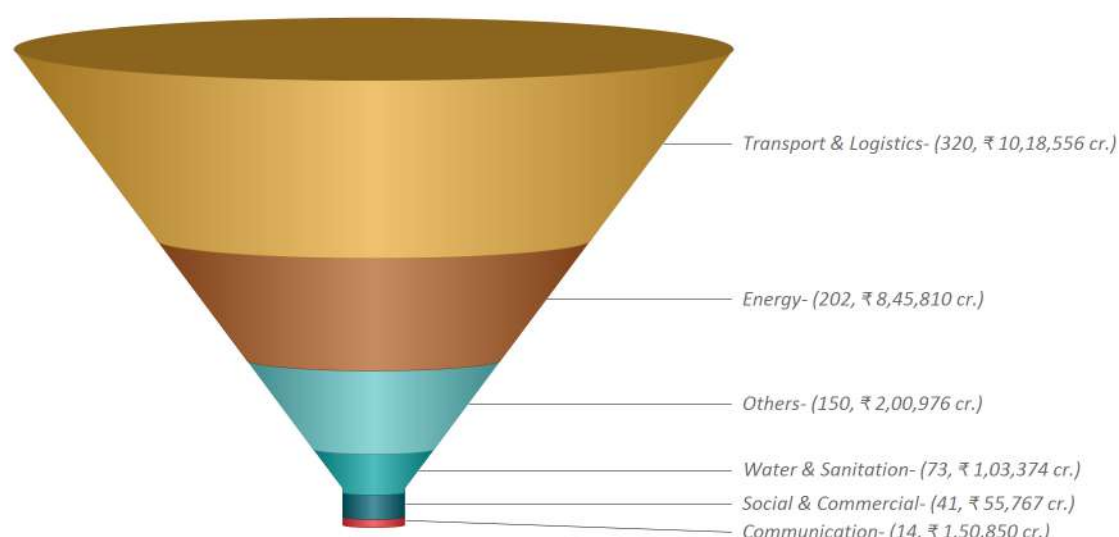


Note: all indicated legends are in format (Project count, Original Cost in crores)

Physical & Financial progress (%) : Project count

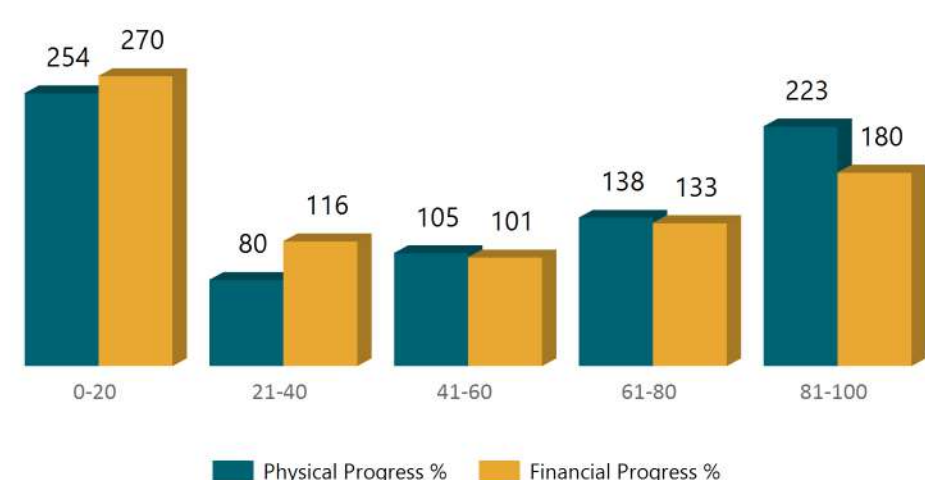




State Comparison : Major States*

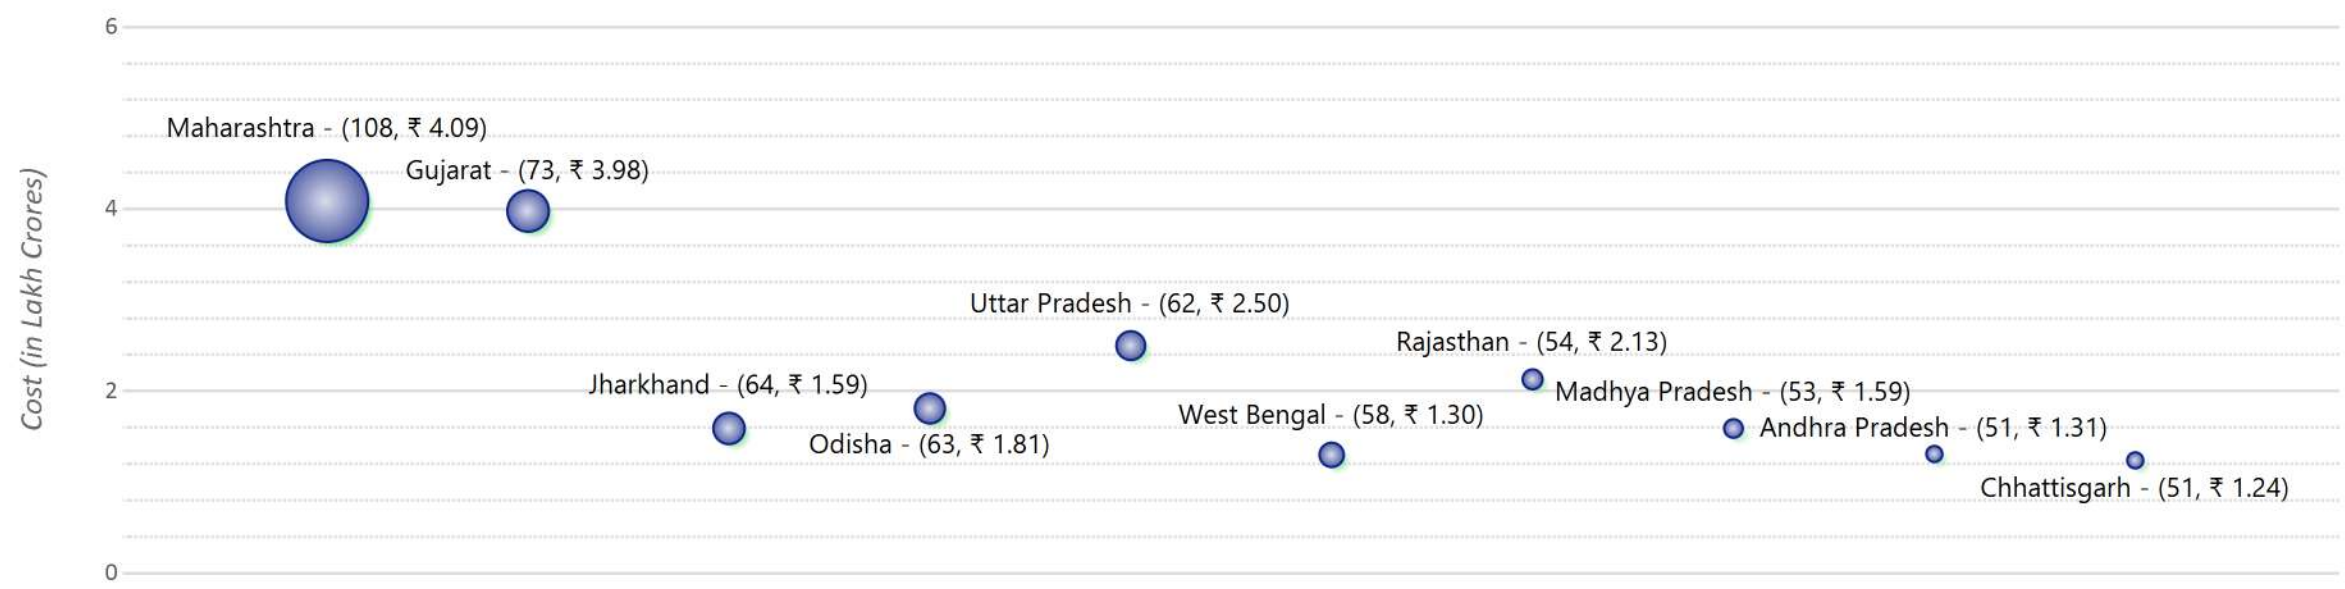


Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
* as per project count

Ministry-wise Distribution of total 223 projects with reported Physical Progress between 81-100%

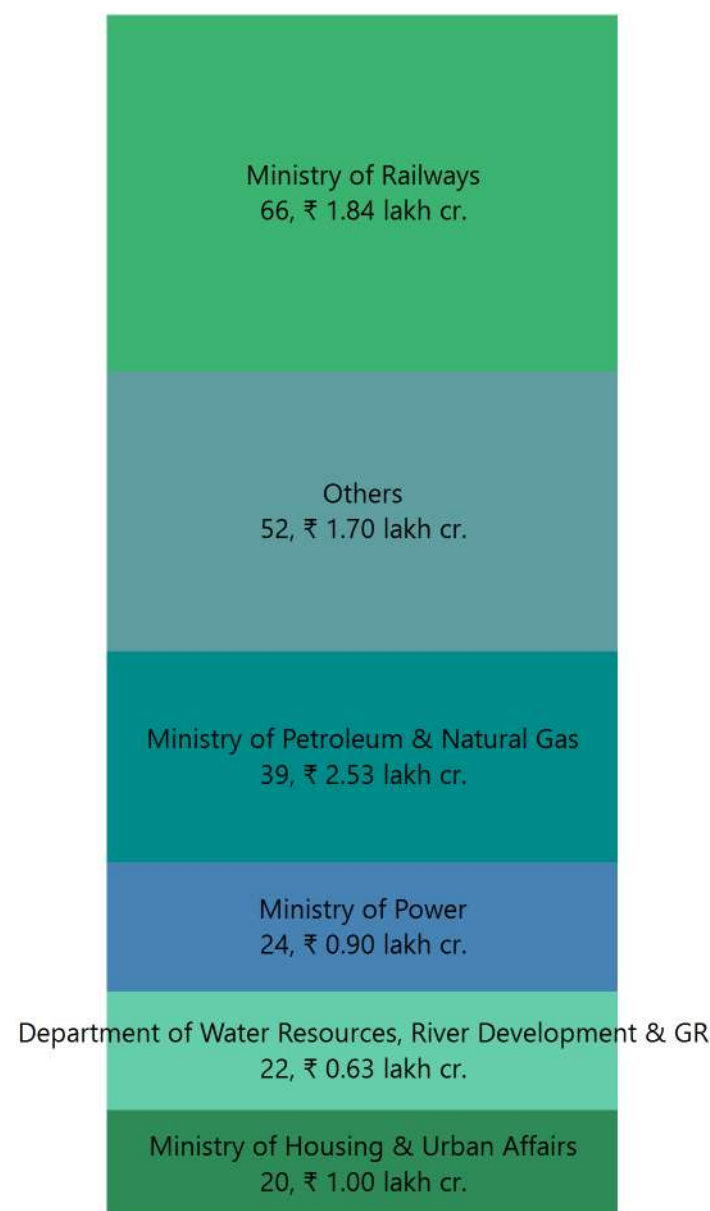

Total Ongoing Projects: Mega & Major

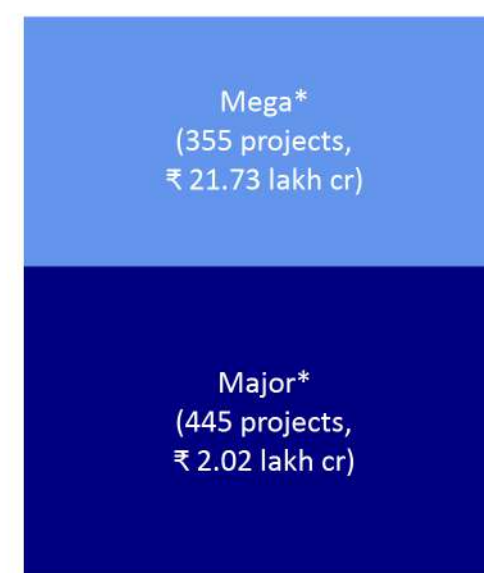


Total North East Region Ongoing Projects: Mega & Major



Note: all indicated legends are in format (Project count, Original Cost)
* Mega project if having original cost ≥ 1000 crore
* Major project if having original cost < 1000 crore

Project volume (nos.)

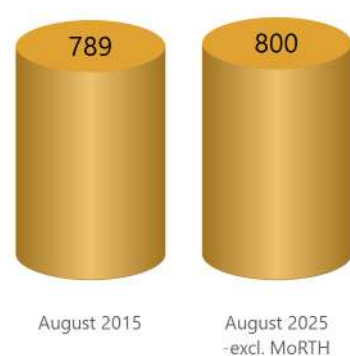

Change in Project Count : +1%

Total Project value (in lakh crore)



Change in Total Value : +120%

Cumulative Expenditure (in lakh crore)



Change in Expenditure : +204%



North Eastern Region





Special Focus : North Eastern Region

AUGUST 2025

54 | 9

Ongoing Projects |
Line Ministries & Departments

₹ 1,88,300

Original Cost
(crores)

₹ 2,79,741

Revised Cost
(crores)


₹ 1,91,944

(68.62% of Revised Cost)


Expenditure
(crores)

Ministry Comparison : Major Ministries*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

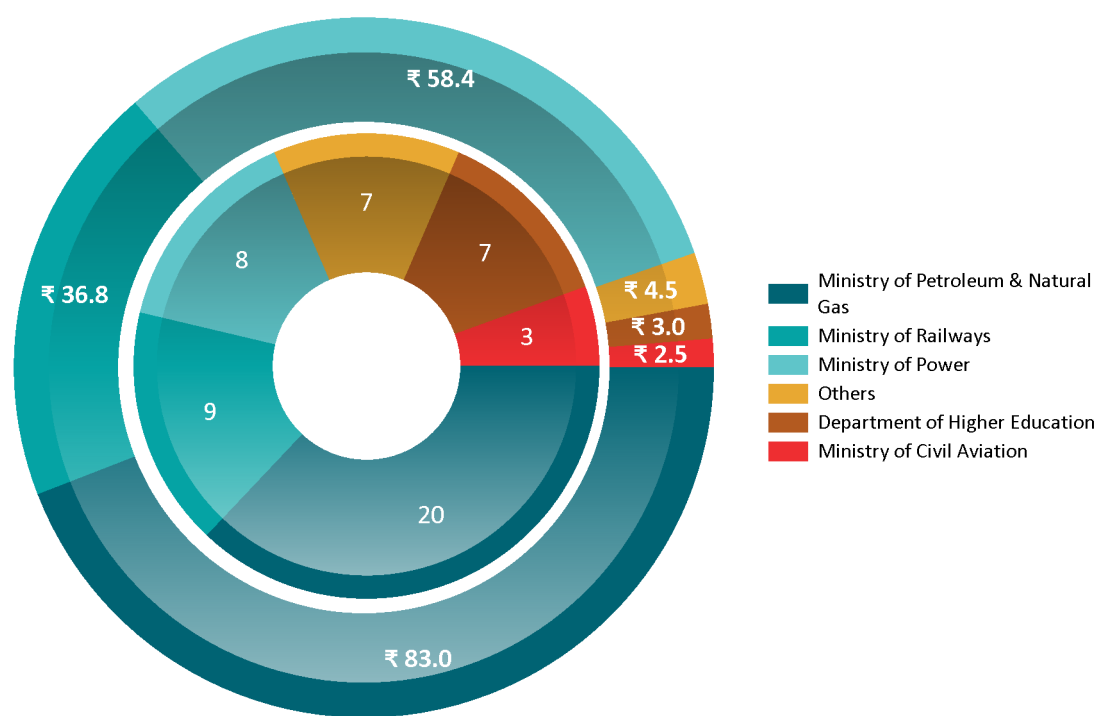


Cost Analytics : Major Ministries*

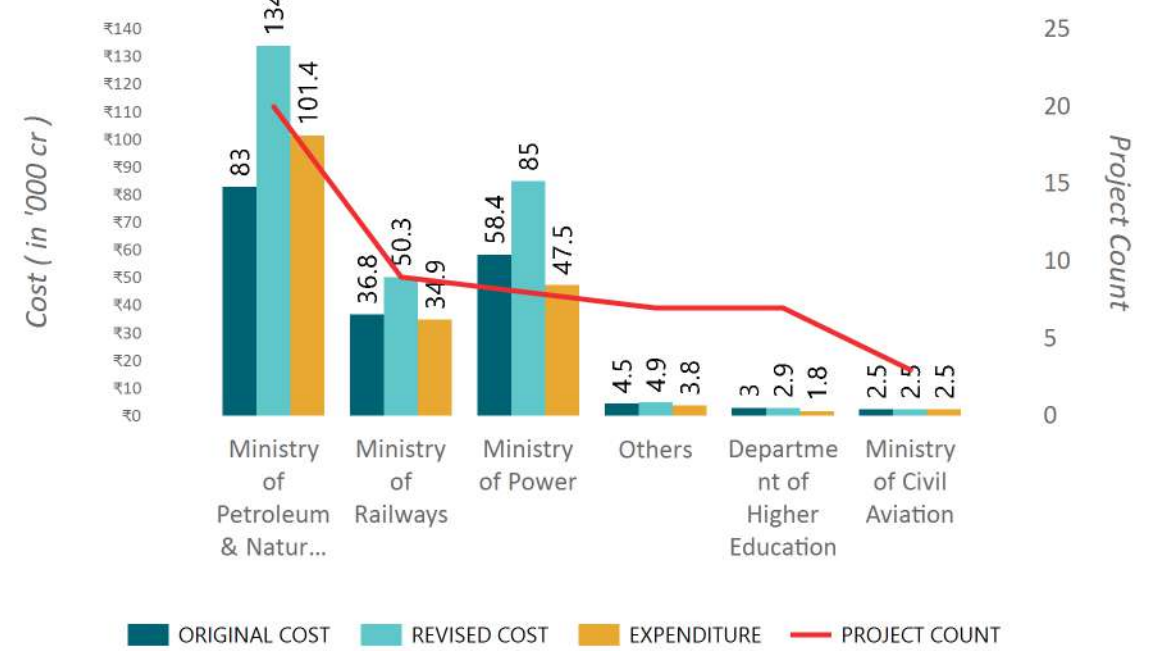


Note: * as per Project Count

Analytics: as per HML

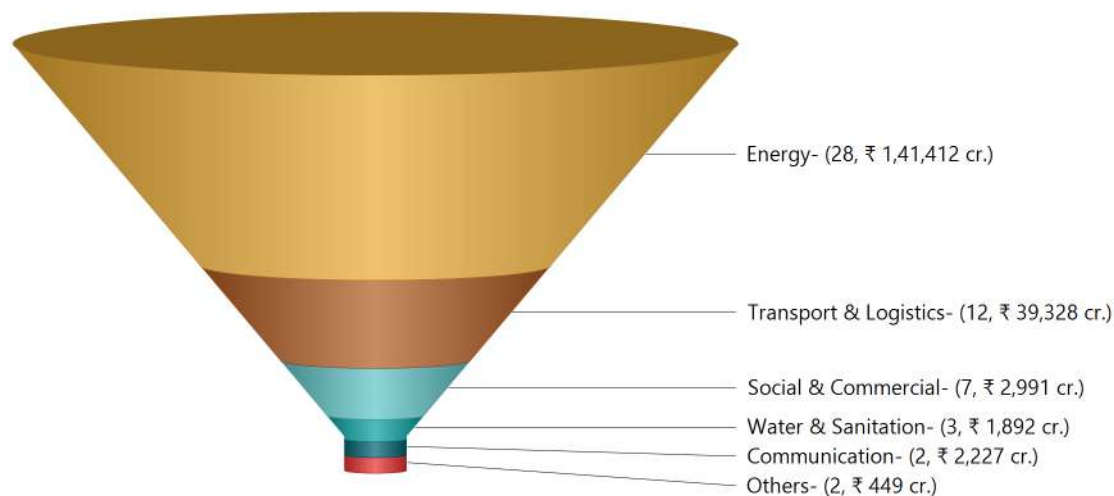


Physical & Financial progress (%) : Project count

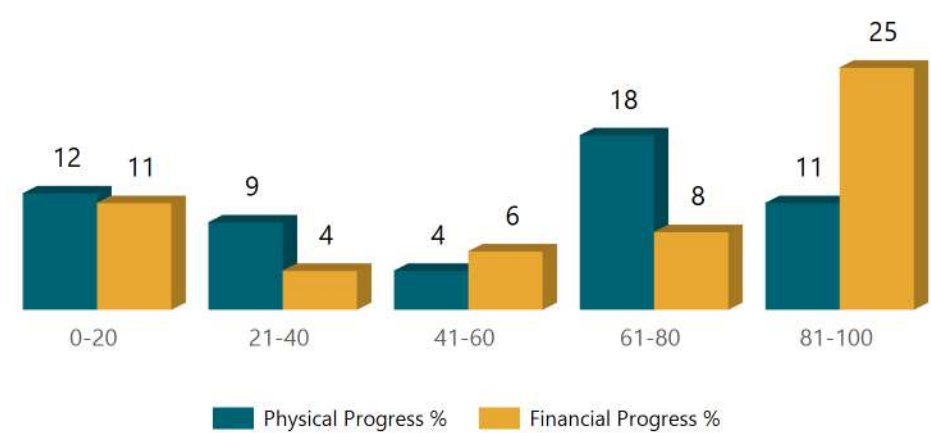

Note: all indicated legends are in format (Project count, Original Cost in crores)

State Comparison : All States

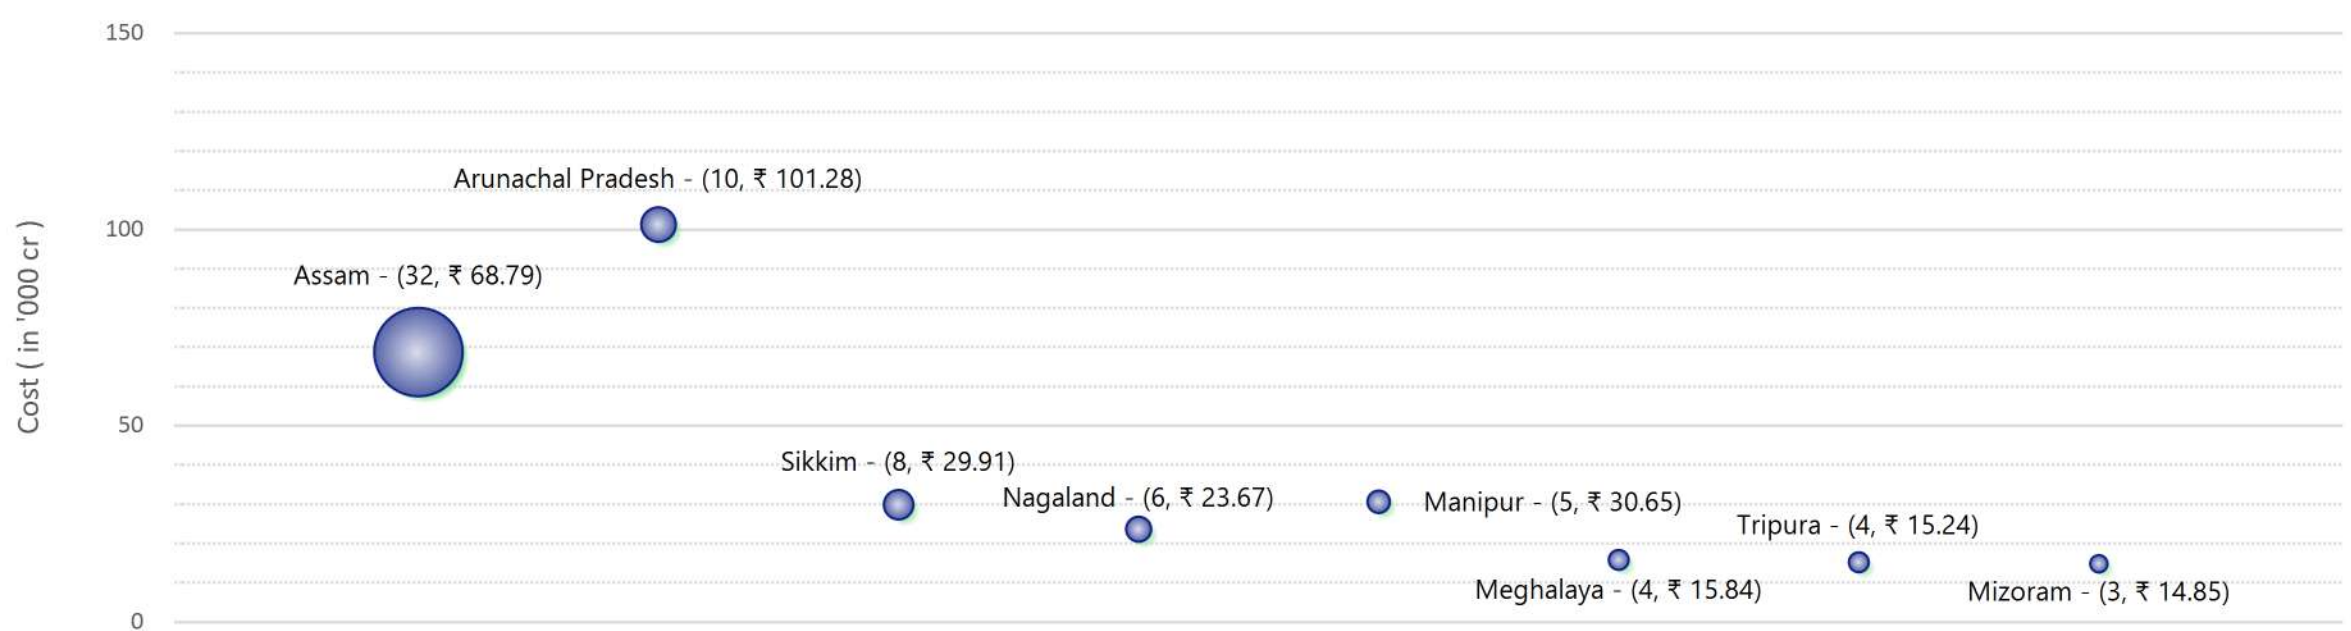

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in Thousand crores)



As per Harmonized Master List (HML)2022



HML Category 1 : Transport & Logistics



AUGUST 2025

320
Ongoing Projects

₹ 10,18,556
Original Cost
(crores)

₹ 11,85,490
Revised Cost
(crores)

₹ 7,42,655
(62.65% of Revised Cost)
Expenditure
(crores)

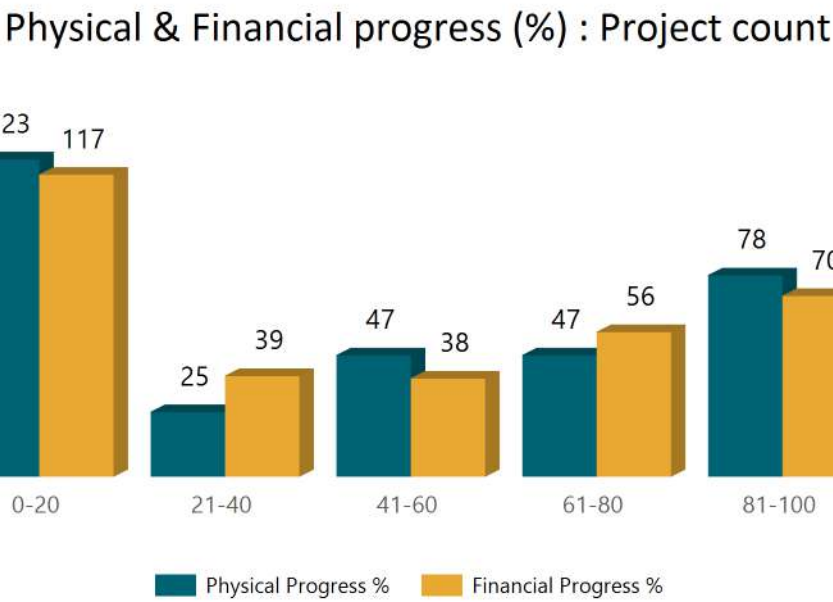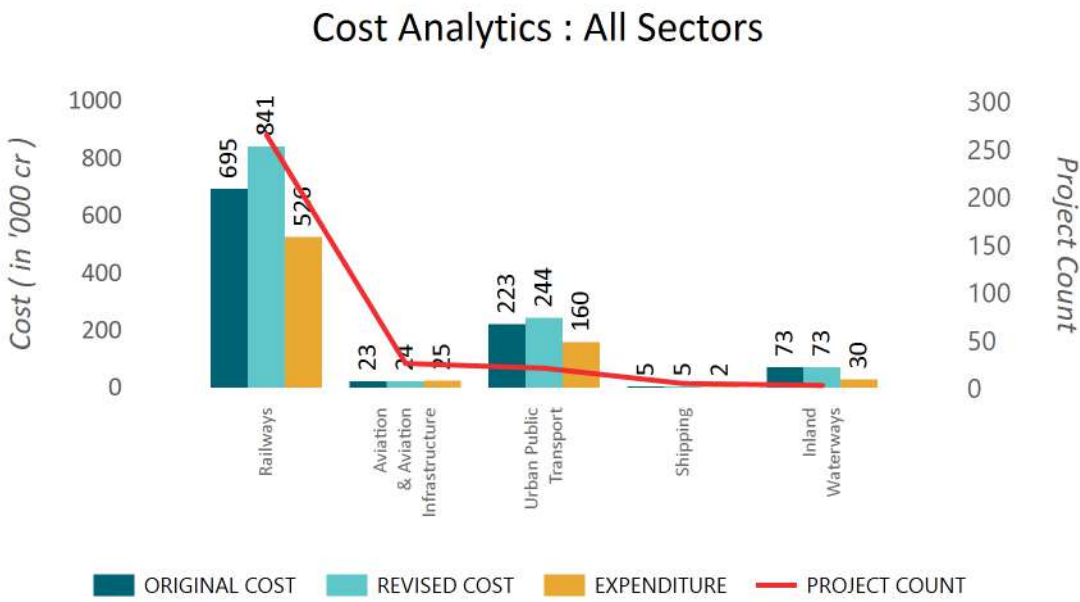

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Railways	265	694,807	841,007	525,898
2	Aviation & Aviation Infrastructure	26	23,050	23,511	24,880
3	Urban Public Transport	21	223,017	243,598	159,570
4	Shipping	5	4,823	4,823	2,021
5	Inland Waterways	3	72,859	72,551	30,287

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	79,919	53
2	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246		26,410	45
3	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
4	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	24,645	65
5	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	2,303	16

HML Category 2 : Energy



AUGUST 2025

202
Ongoing Projects

₹ 8,45,810
Original Cost
(crores)

₹ 9,82,793
Revised Cost
(crores)

₹ 4,82,645
(49.11% of Revised Cost)
Expenditure
(crores)

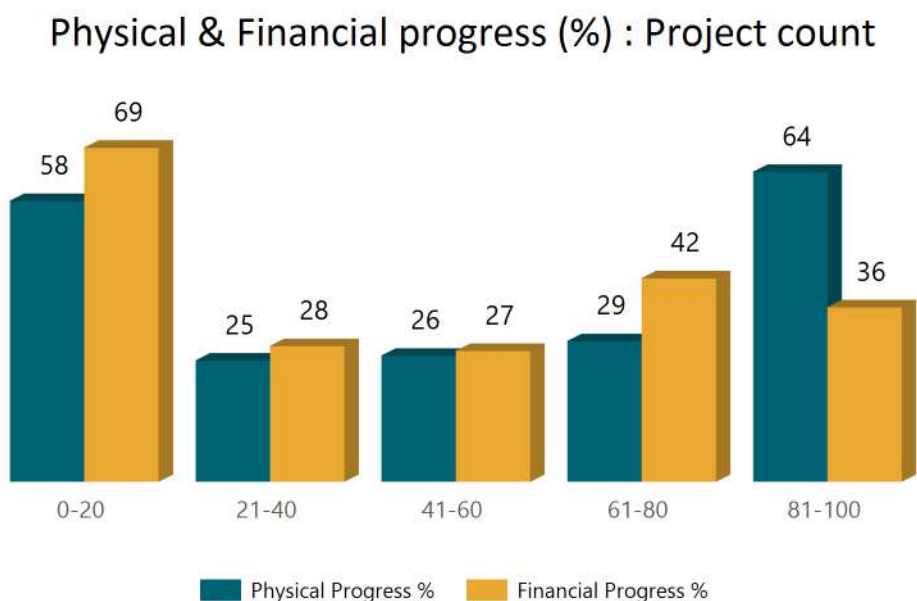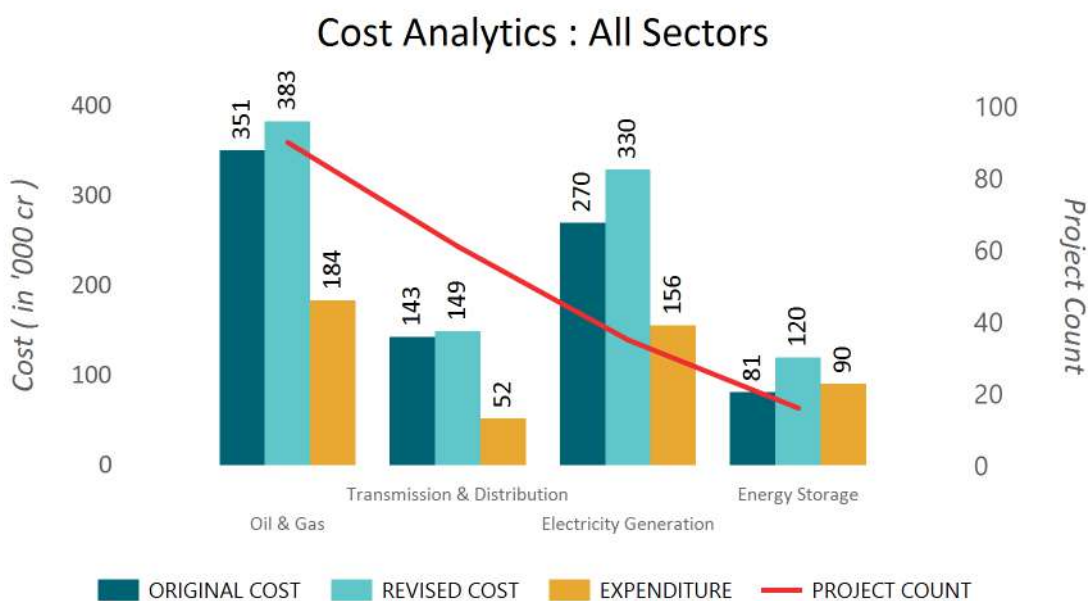

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Oil & Gas	90	351,249	383,480	184,032
2	Transmission & Distribution	61	142,977	149,491	52,183
3	Electricity Generation	35	270,284	329,637	155,932
4	Energy Storage	16	81,301	120,185	90,498

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	1,856	14
2	701263	RAJASTHAN REFINERY PROJECT	43,129	79,459	60,295	88
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	24,355	89
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	33,238	96
5	602182	DIBANG MULTIPURPOSE PROJECT	31,876		3,554	16



HML Category 3 : Water & Sanitation

AUGUST 2025

73

Ongoing Projects

₹ 1,03,374

Original Cost
(crores)


₹ 2,05,233

Revised Cost
(crores)


₹ 1,59,103

(77.52% of Revised Cost)
Expenditure
(crores)

Cost Analytics : All Sectors

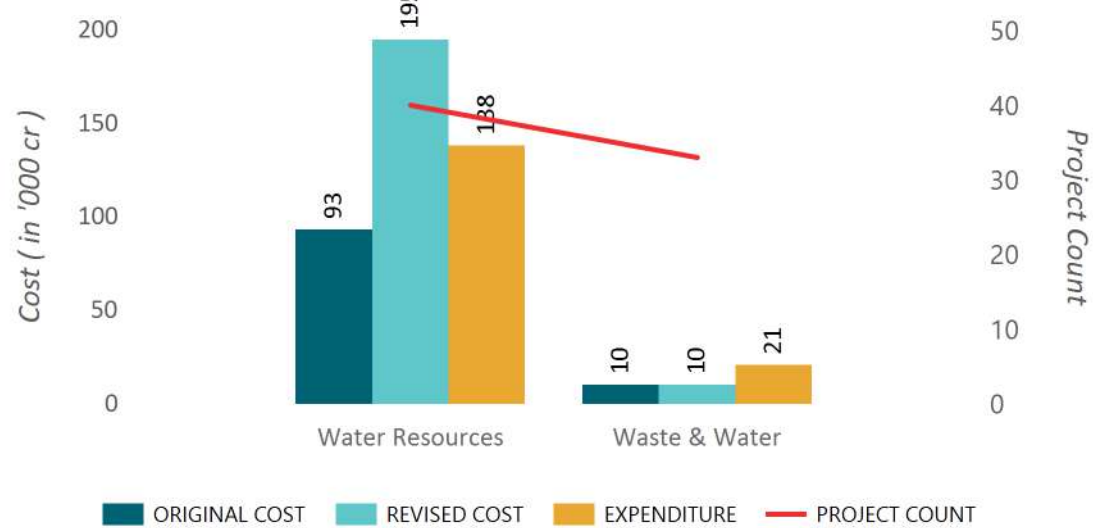

Physical & Financial progress (%) : Project count

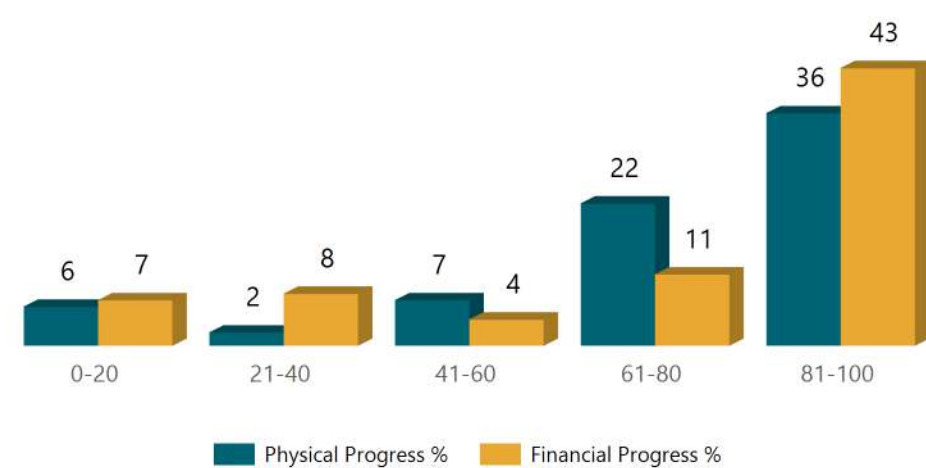

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Water Resources	40	93,249	195,108	138,397
2	Waste & Water	33	10,125	10,125	20,706

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	701372	SARDAR SAROVAR PROJECT	20,718	33,413	31,768	93
2	701415	POLAVARAM IRRIGATION PROJECT	10,151	55,549	24,348	83
3	701405	J. CHOKKA RAO DEVADULA LIFT IRRIGATION SCHEME	8,201	14,730	4,559	87
4	400112	JIGAON IRRIGATION PROJECT	7,223		8,501	90
5	701386	GOSIKHURD PROJECT	7,196	12,770	13,533	72



HML Category 4 : Communication

AUGUST 2025

14

Ongoing Projects

₹ 1,50,850

Original Cost
(crores)


₹ 2,72,942

Revised Cost
(crores)


₹ 72,123

(26.42% of Revised Cost)
Expenditure
(crores)

Cost Analytics : All Sectors

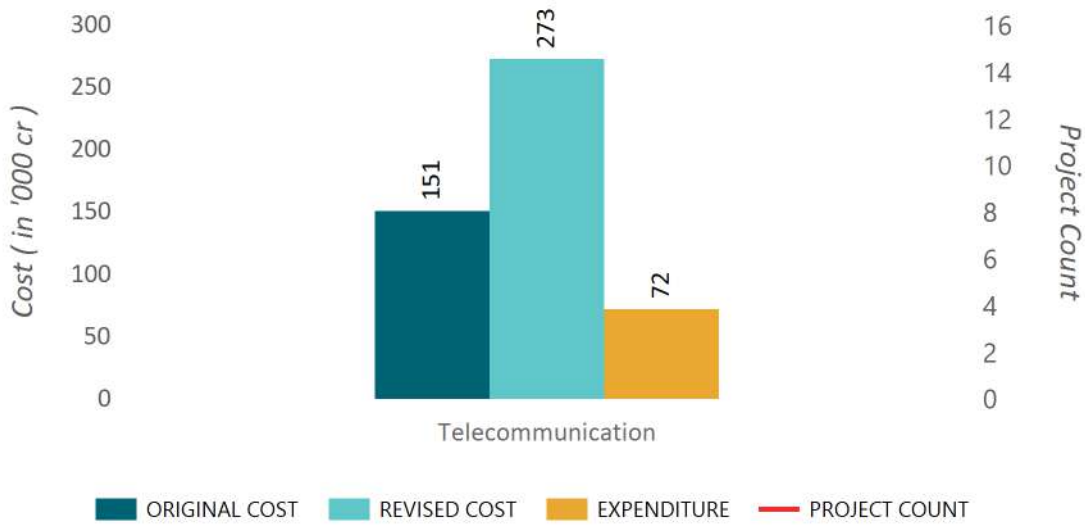

Physical & Financial progress (%) : Project count

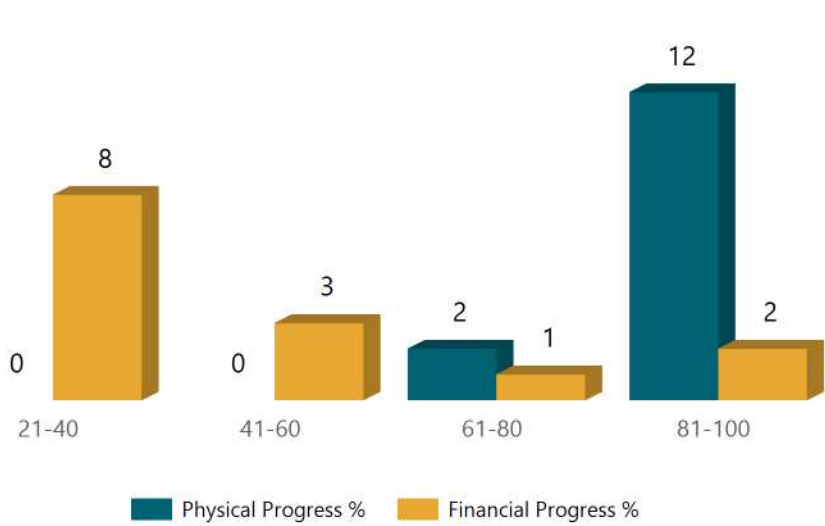

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Telecommunication	14	150,850	272,942	72,123

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	706775	BHARATNET	61,109	188,000	41,486	81
2	701593	4G SERVICES BY BSNL	28,466	19,592	8,390	96
3	400013	SATURATION 4G MOBILE COVERAGE OF UNCOVERED VILLAGES THROUGH USOF	26,316	30,620	9,792	73
4	709857	PLANNING, ENGINEERING, SUPPLY, INSTALLATION, TESTING, COMMISSIONING, INTEGRATION & ANNUAL MAINTENANCE OF 4G MOBILE NETWORK AT 1 LAKH SITES ON PAN INDIA BASIS INCLUDING MUMBAI & DELHI LSA ON TURNKEY BASIS UNDER PHASE IX.2 PROJECT.	24,545		8,391	96
5	701602	PROVISION OF 4G BASED MOBILE SERVICES IN 7,287 UNCOVERED VILLAGES OF 44 ASPIRATIONAL DISTRICT ACROSS 5 STATES OF ANDHRA PRADESH, CHHATTISGARH, JHARKHAND, MAHARASHTRA & ODISHA	3,685		1,101	79



HML Category 5 : Social & Commercial

AUGUST 2025

41

Ongoing Projects

₹ 55,767

Original Cost
(crores)


₹ 56,701

Revised Cost
(crores)


₹ 11,961

(21.1% of Revised Cost)
Expenditure
(crores)

Cost Analytics : All Sectors

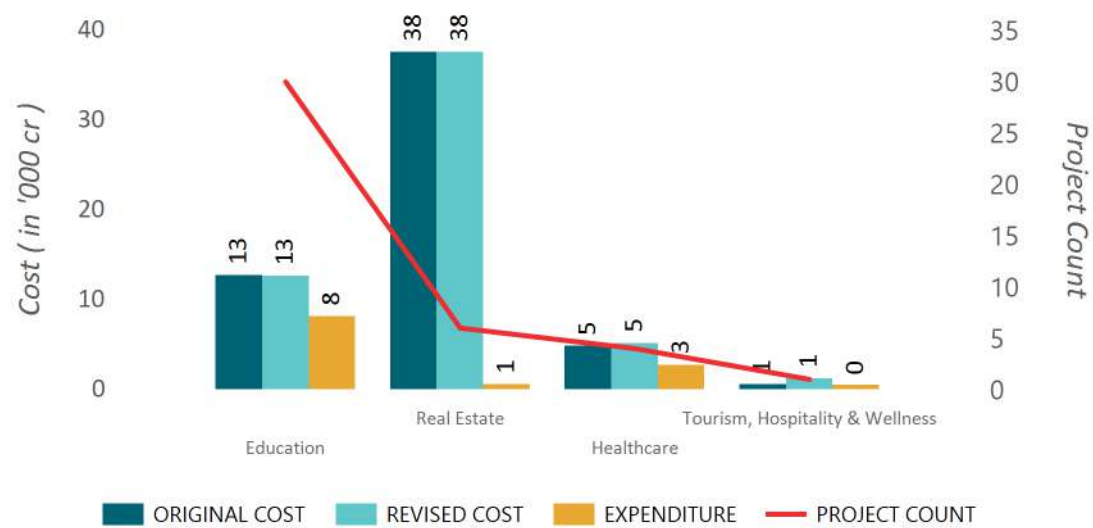

Physical & Financial progress (%) : Project count

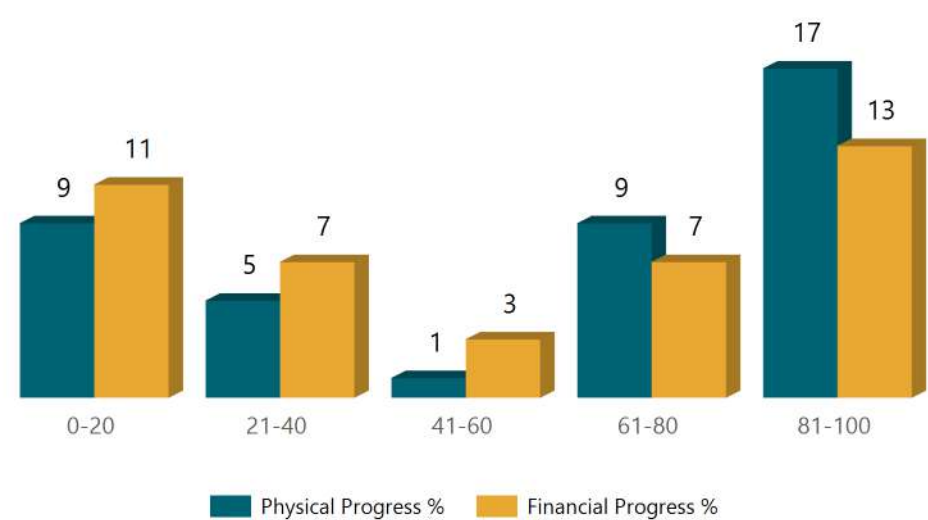

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Education	30	12,754	12,685	8,159
2	Real Estate	6	37,591	37,591	553
3	Healthcare	4	4,848	5,186	2,752
4	Tourism, Hospitality & Wellness	1	573	1,238	497

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850		0	0
2	701658	KRISHNAPATNAM NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	2,139		406	17
3	701167	AIIMS KASHMIR AT AWANTIPORA JAMMU & KASHMIR	1,828	1,828	1,532	66
4	701657	TUMAKURU NODE - PHASE 1 - ROADS AND SERVICES DEVELOPMENT	1,702		88	8
5	701173	AIIMS MAJRA REWARI HARYANA	1,299		349	28

Other Sectors

AUGUST 2025


150
Ongoing Projects

₹ 2,00,976
Original Cost
(crores)

₹ 2,04,389
Revised Cost
(crores)

₹ 69,122
(33.82% of Revised Cost)
Expenditure
(crores)

Physical & Financial progress (%) : Project count

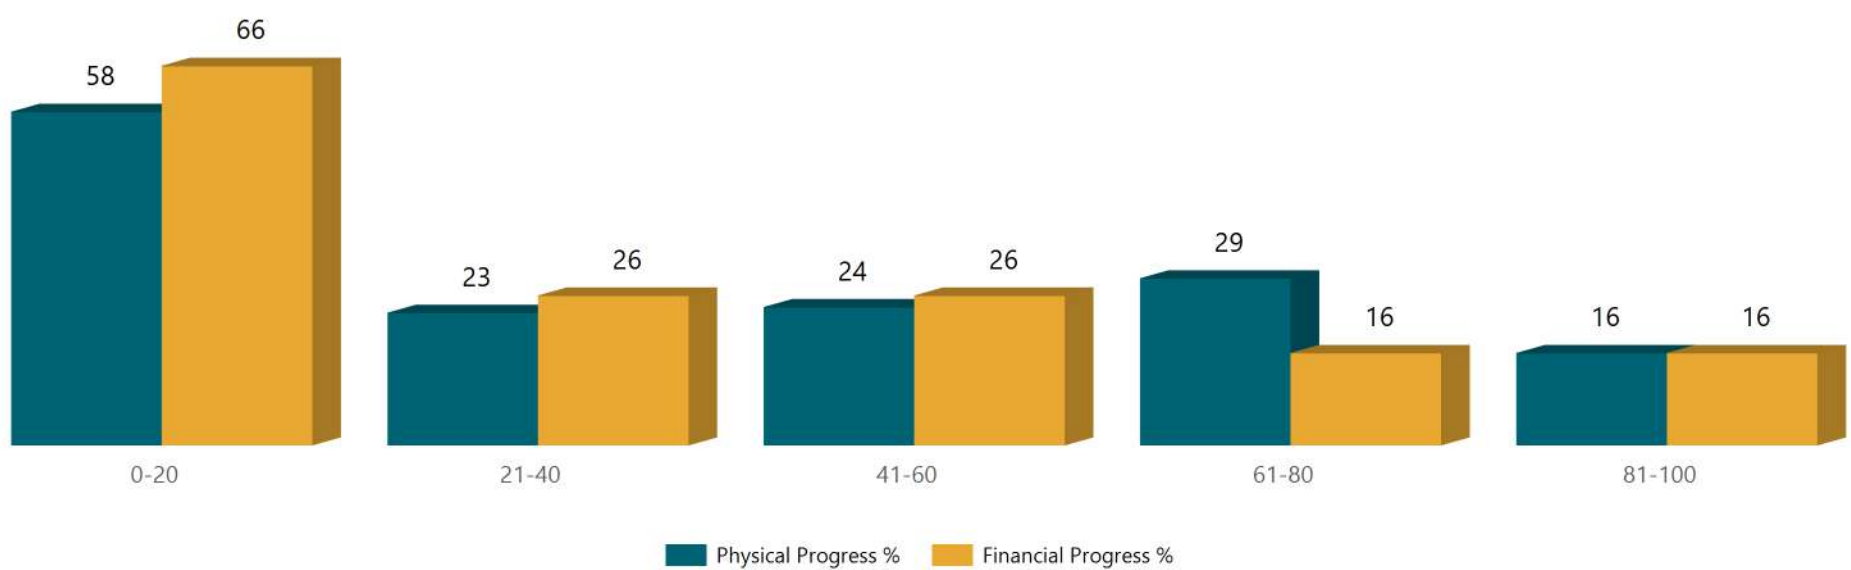

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Coal	119	168,890	166,628	54,350
2	Steel	19	16,748	19,987	7,970
3	Metals & Mining	10	14,436	16,873	6,190
4	Construction	2	902	902	612

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400424	GEVRA OC [70 MTY]	11,816		5,329	77
2	400185	GOPALJI KANIHA OCP [10 TO 30 M	8,416	6,108	1,709	17
3	400147	KUSMUNDA OC EXPANSION [15 TO 50 MTY]	7,612		4,698	81
4	612838	DIPKA OC	7,580		3,091	65
5	400150	RPR MAGADH EXP OCP	7,254		1,535	38



Major Infrastructure Central Ministries & Departments



Ministry of Railways

AUGUST 2025

263
Ongoing Projects

₹ 6,91,321
Original Cost
(crores)


₹ 8,37,521
Revised Cost
(crores)

₹ 5,24,256
(62.6% of Revised Cost)
Expenditure
(crores)

128 | ₹ 627,817
Mega Projects
Count | Original Cost (crores)

135 | ₹ 63,504
Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

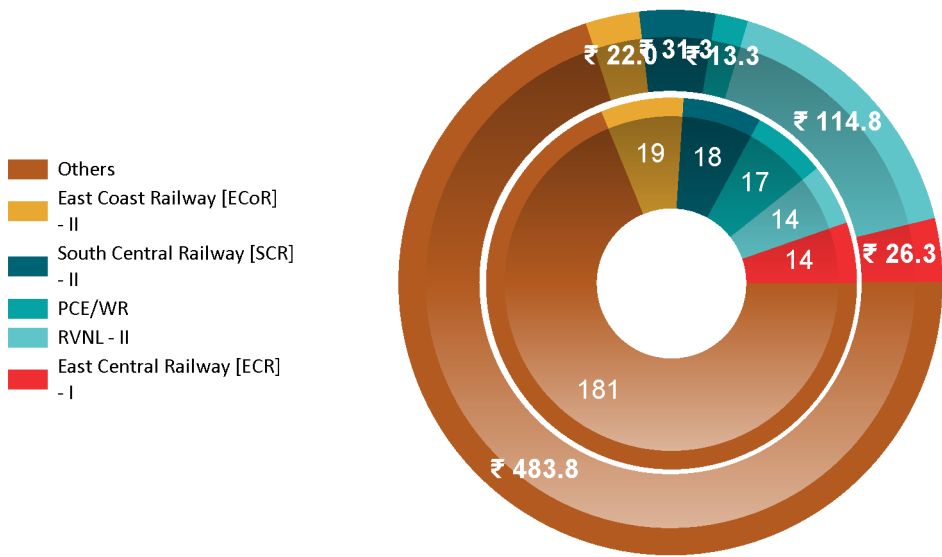


Sectoral Comparison : Major Sectors*
[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Physical & Financial progress (%) : Project count

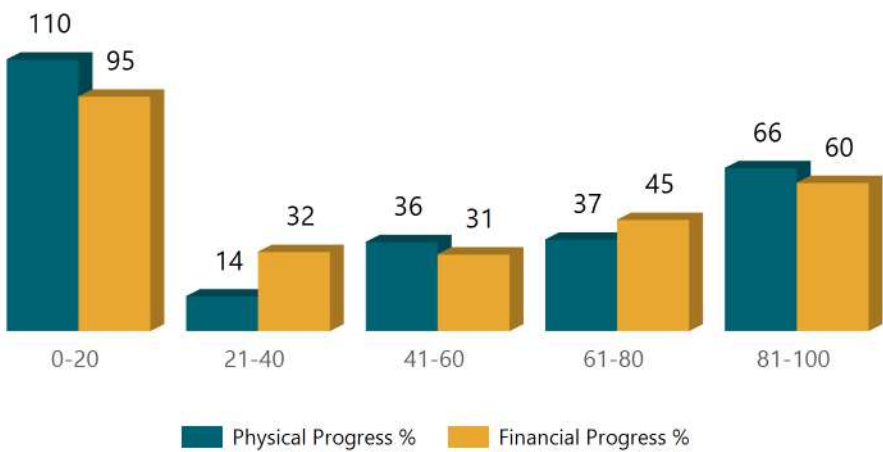

Cost Analytics : Major Sectors*

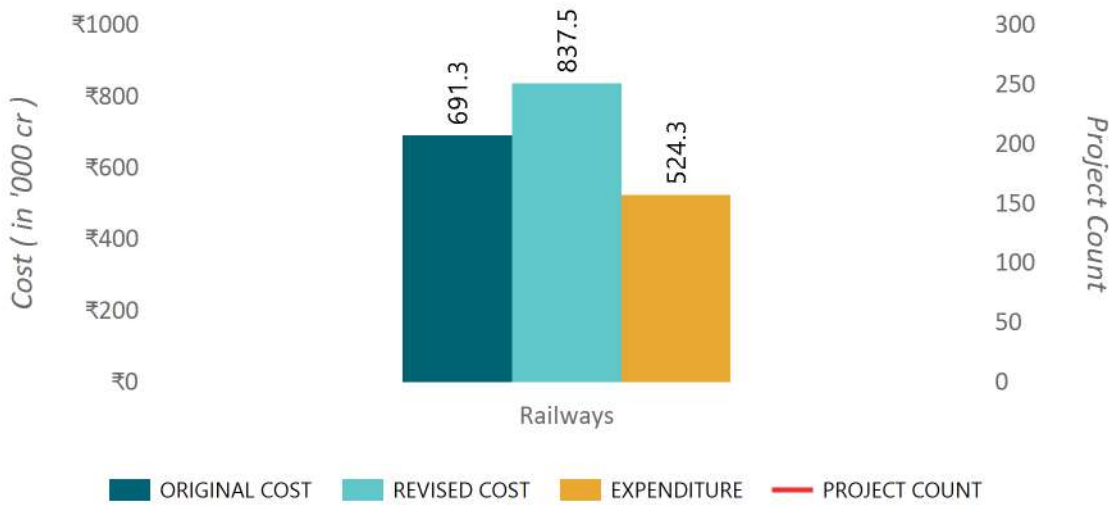

State Comparison : Major States*

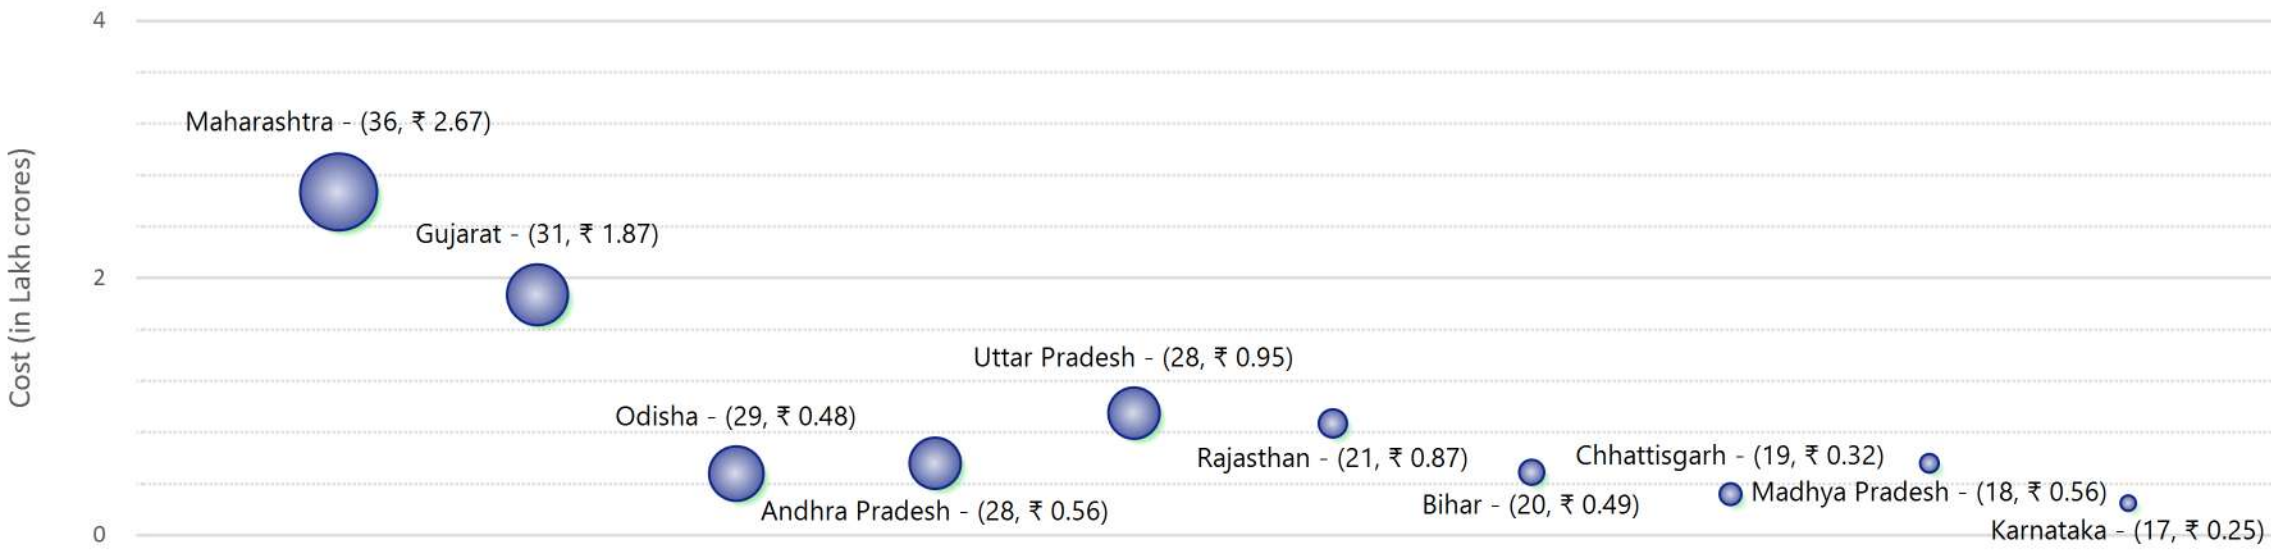

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705728	MUMBAI-AHMEDABAD HIGH SPEED RAIL PROJECT- 508 KM	108,000	108,000	79,919	53
2	705237	WESTERN DEDICATED FREIGHT CORRIDOR	51,101	124,005	124,623	96
3	705429	RISHIKESH-KARNAPRAYAG NEW RAIL LINE- 125 KM	38,953	38,953	24,645	65
4	706780	MUMBAI URBAN TRANSPORT PROJECT [MUTP] PHASE-IIIA	33,690	33,690	2,303	16
5	705391	JIRIBAM-IMPHAL NEW LINE PROJECT	14,323	21,886	15,598	69



Ministry of Coal

AUGUST 2025

124

Ongoing Projects

₹ 2,17,158

Original Cost
(crores)

₹ 2,19,157

Revised Cost
(crores)

₹ 78,643

(35.88% of Revised Cost)
Expenditure
(crores)

39 | ₹ 175,401


Mega Projects
Count | Original Cost (crores)

85 | ₹ 41,757

Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

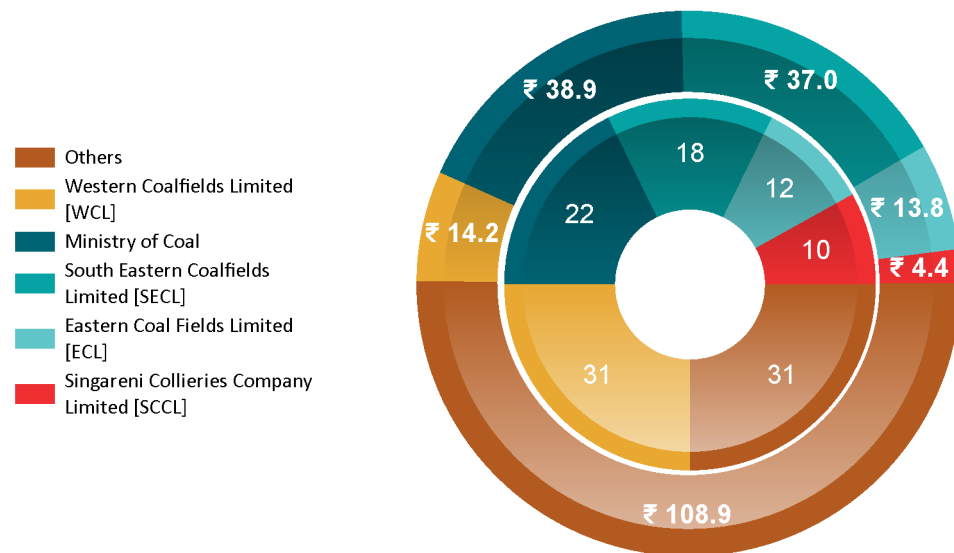


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

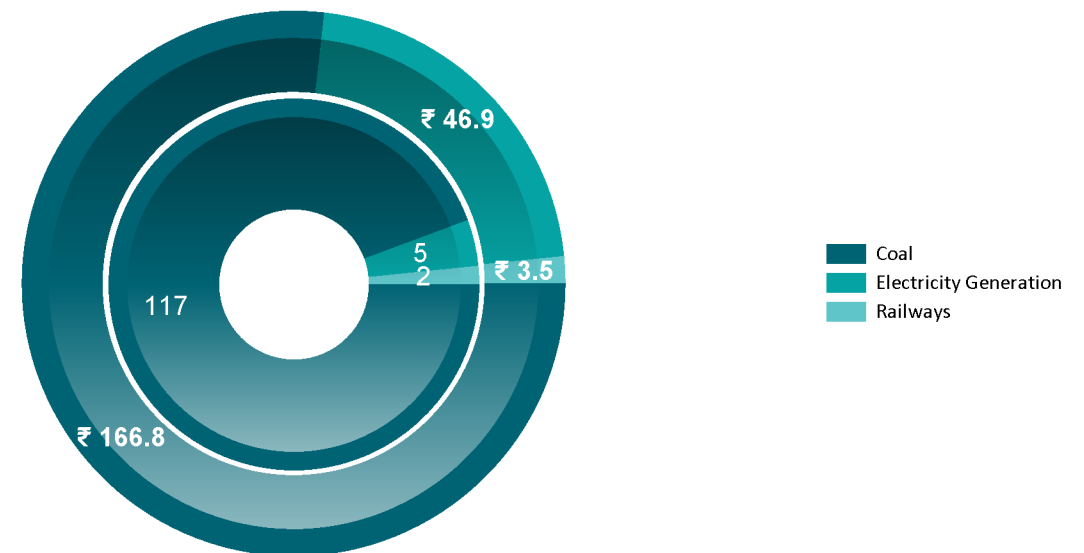


Physical & Financial progress (%) : Project count

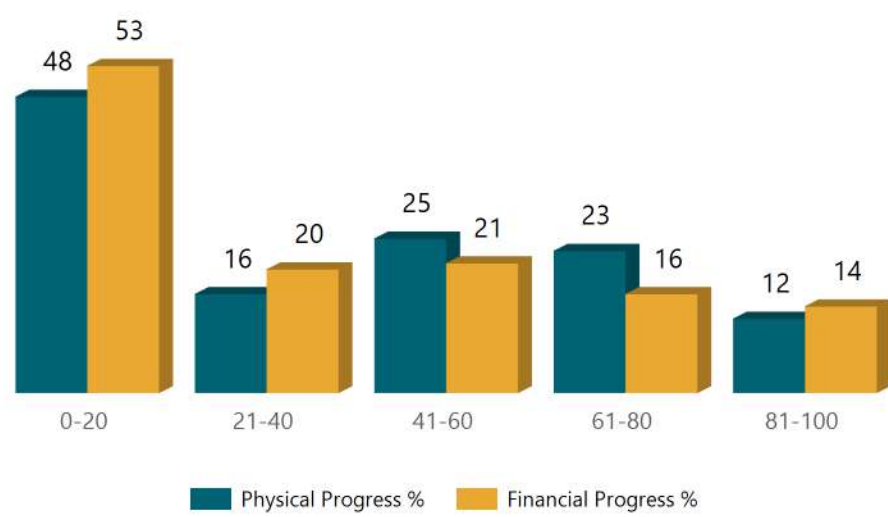

Cost Analytics : Major Sectors*

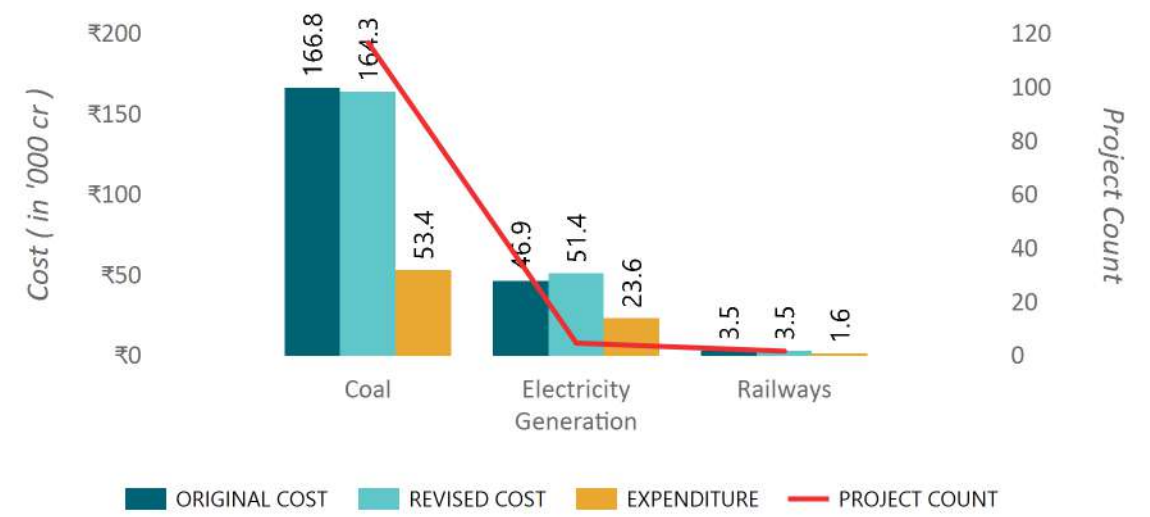

State Comparison : Major States*

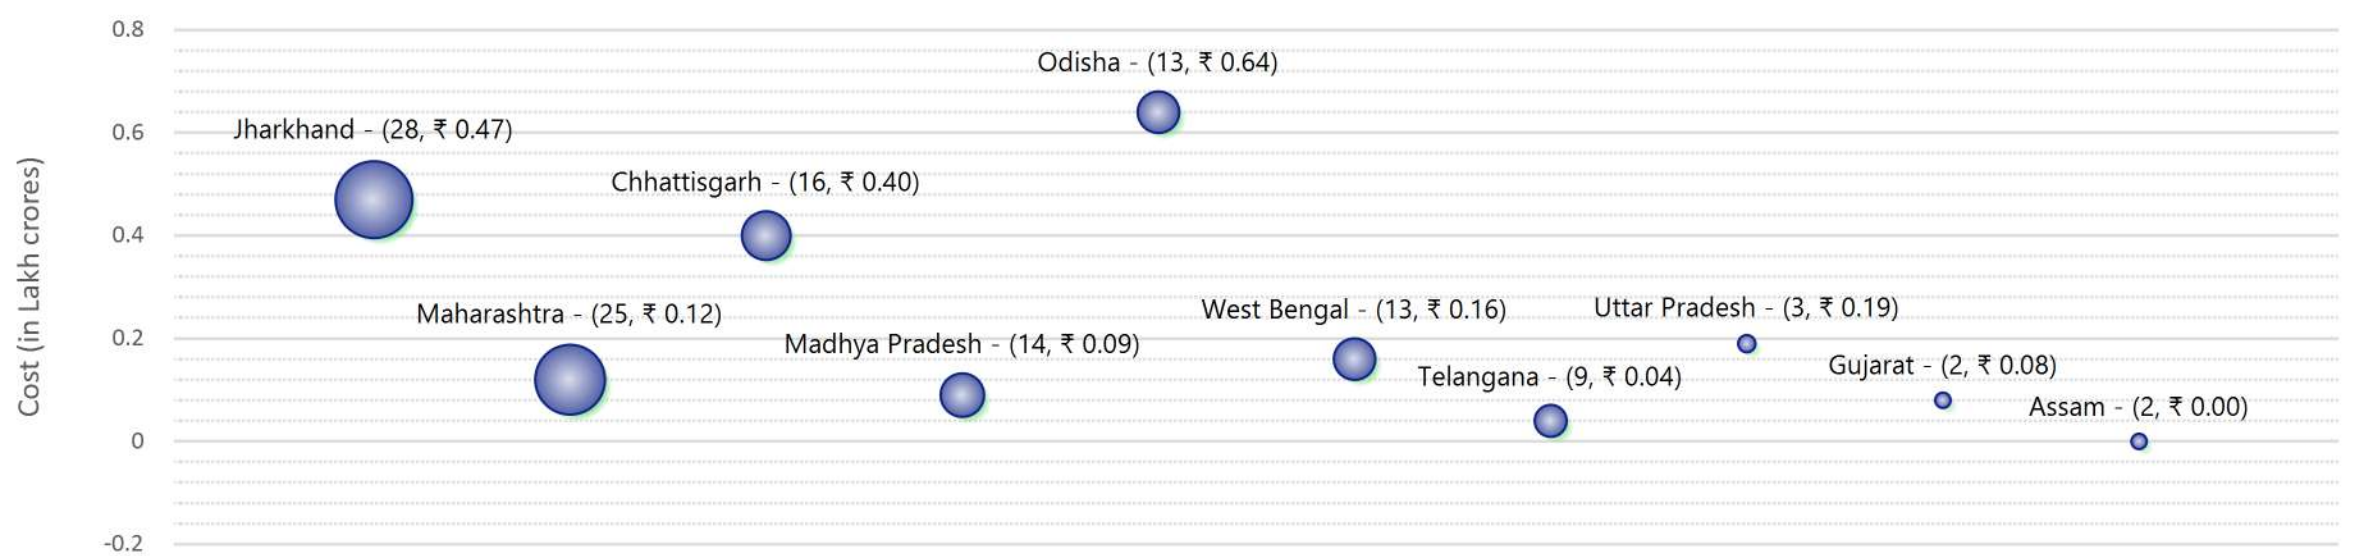

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400231	NLC TALABIRA THERMAL POWER PROJECT	27,213	27,213	1,954	1
2	400259	GHATAMPUR THERMAL POWER PLANT 3 X 660 MW	17,238	21,781	20,270	92
3	400424	GEVRA OC [70 MTY]	11,816	11,816	5,329	77
4	400185	GOPALJI KANIHA OCP [10 TO 30 M	8,416	6,108	1,709	17
5	400147	KUSMUNDA OC EXPANSION [15 TO 50 MTY]	7,612	7,612	4,698	81

Ministry of Petroleum & Natural Gas

AUGUST 2025

106
Ongoing Projects


₹ 4,32,550
Original Cost
(crores)

₹ 5,03,665
Revised Cost
(crores)

₹ 2,74,530
(54.51% of Revised Cost)
Expenditure
(crores)

49 | ₹ 407,305
Mega Projects
Count | Original Cost (crores)

57 | ₹ 25,245
Major Projects
Count | Original Cost

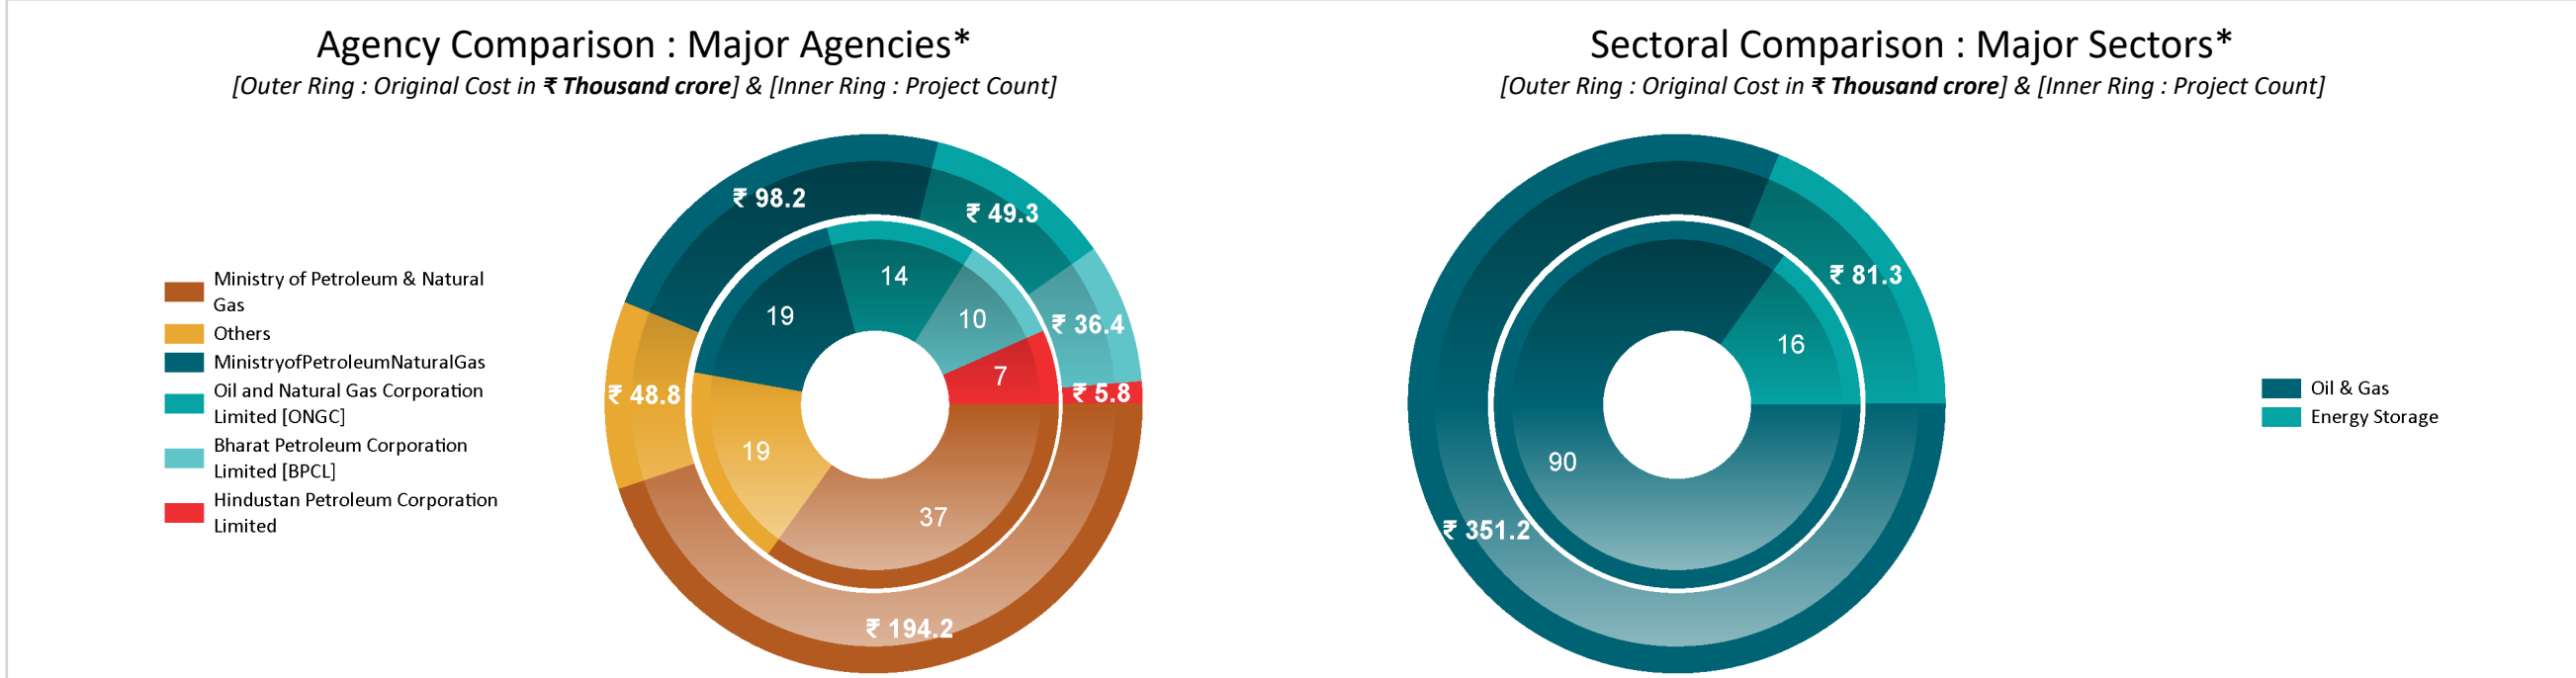

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA						
S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	1,856	14
2	701263	RAJASTHAN REFINERY PROJECT	43,129	79,459	60,295	88
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	24,355	89
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	33,238	96
5	604795	CBR 9 MMTPA PROJECT	31,580	36,354	1,342	10



Ministry of Power

AUGUST 2025

93

Ongoing Projects

₹ 3,68,478

Original Cost
(crores)

₹ 4,30,084

Revised Cost
(crores)

₹ 1,85,464

(43.12% of Revised Cost)

Expenditure
(crores)

63 | ₹ 355,654


Mega Projects
Count | Original Cost (crores)

30 | ₹ 12,824

Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

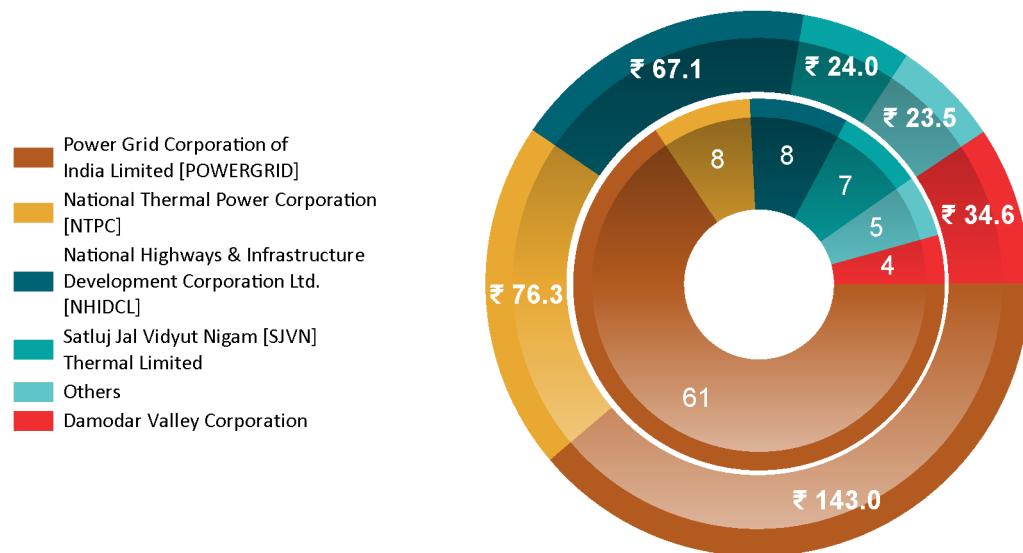


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

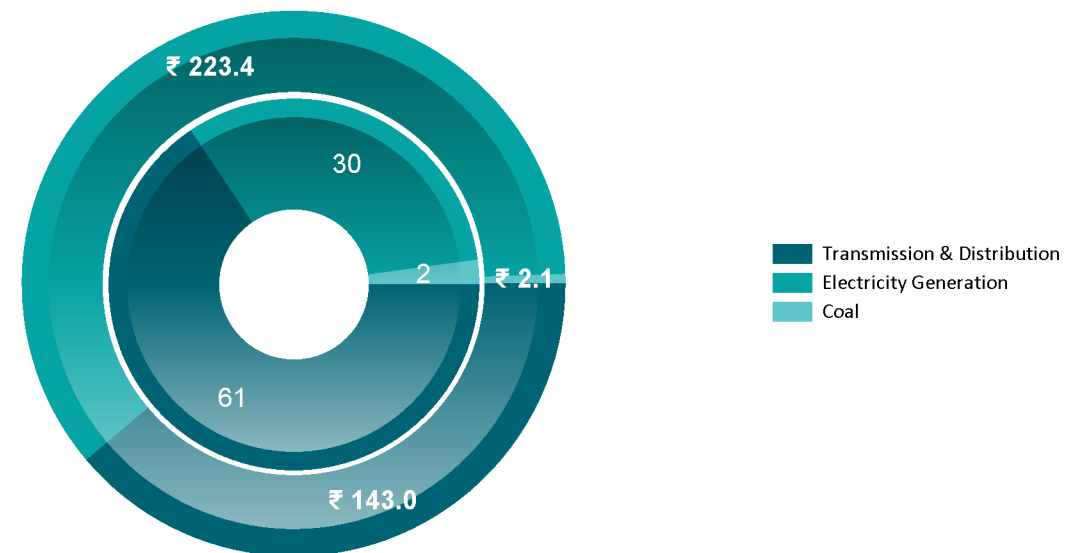


Physical & Financial progress (%) : Project count

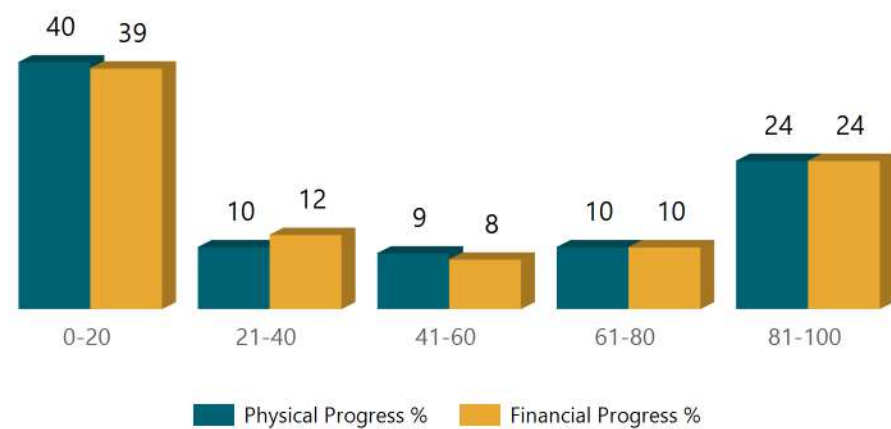

Cost Analytics : Major Sectors*

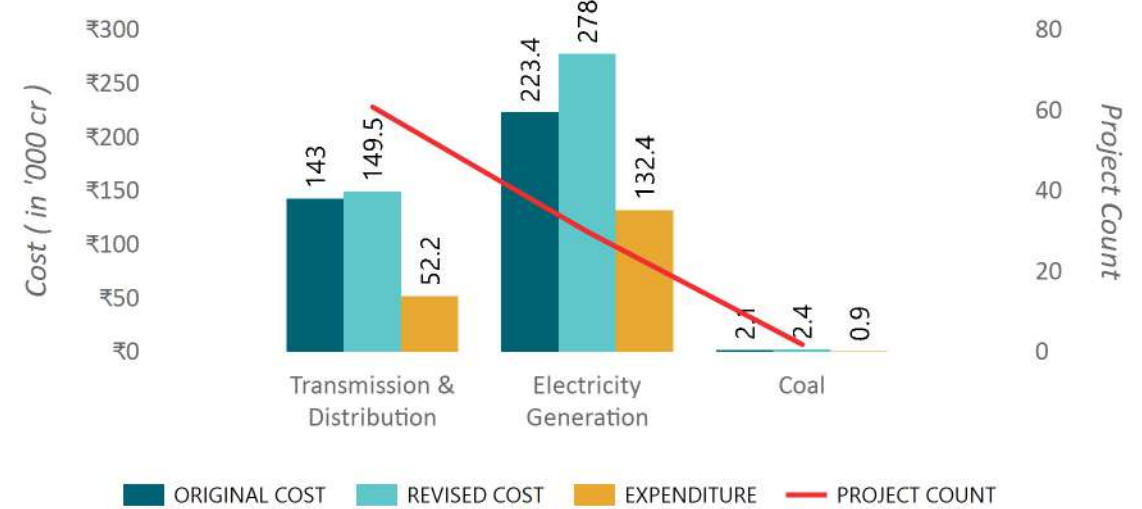

State Comparison : Major States*

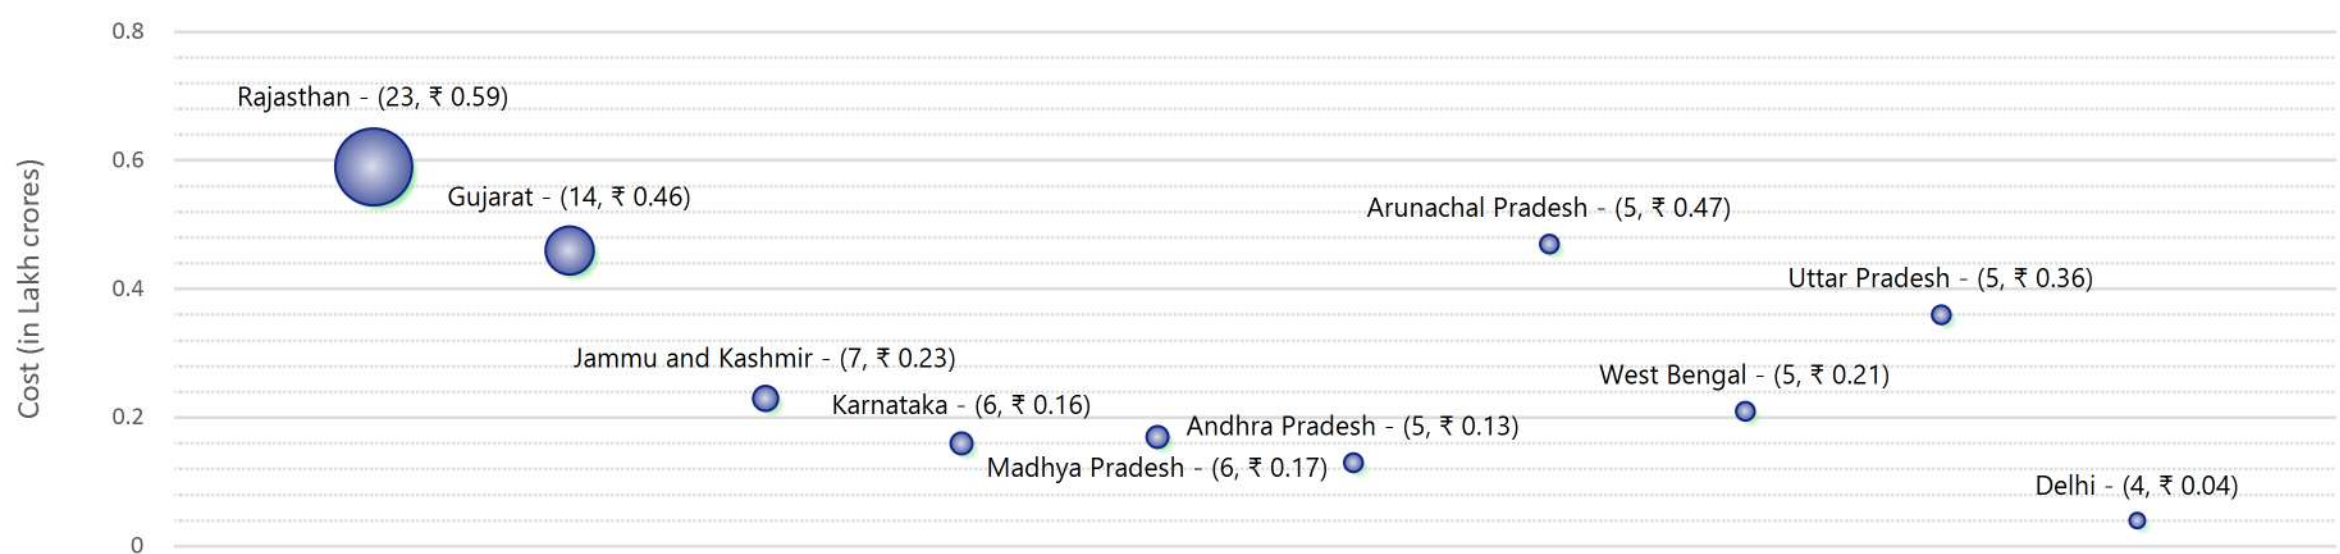

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)

Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRES (%)S
1	602182	DIBANG MULTIPURPOSE PROJECT	31,876	31,876	3,554	16
2	615347	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV NAME POWERGRID WEST CENTRAL TRANSMISSION LIMITED]	24,819	24,819	1,796	1
3	400062	RAGHUNATHPUR THERMAL POWER STATION PHASE II [2X660 MW] AT RAGHUNATHPUR, PURULIA, WEST BENGAL	17,673	17,673	1,193	1
4	612142	SINGRAULI SUPER THERMAL POWER PROJECT, STAGE-III [2X800 MW]	17,195	17,195	1,739	9
5	400261	PATRATU THERMAL POWER STATION EXPANSION PROJECT PHASE-I [3X800 MW]	17,112	20,302	17,475	85



Ministry of Housing & Urban Affairs

AUGUST 2025

52

Ongoing Projects

₹ 3,26,745

Original Cost
(crores)

₹ 3,47,326

Revised Cost
(crores)

₹ 2,05,635

(59.21% of Revised Cost)

Expenditure
(crores)

20 | ₹ 317,340


Mega Projects
Count | Original Cost (crores)

32 | ₹ 9,405

Major Projects
Count | Original Cost


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

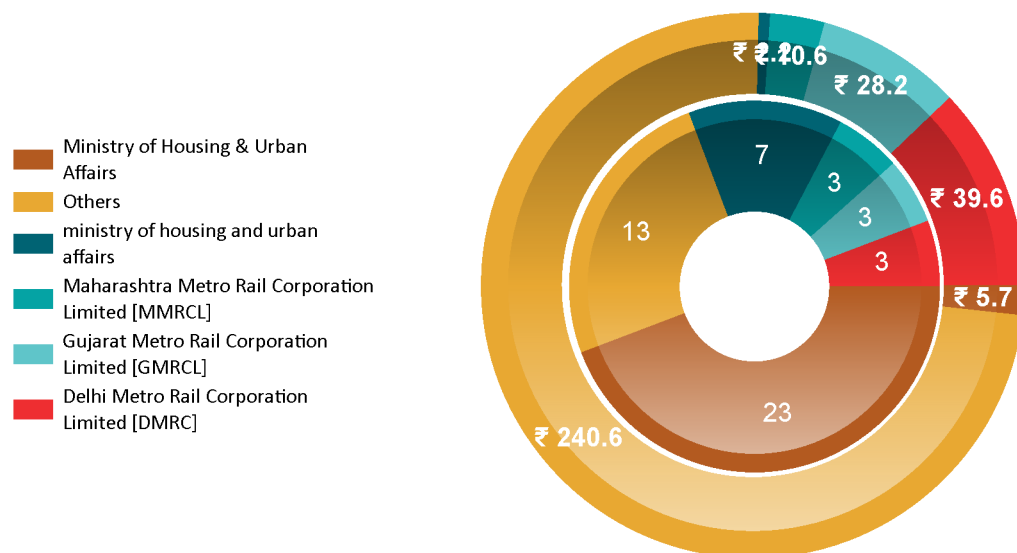


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

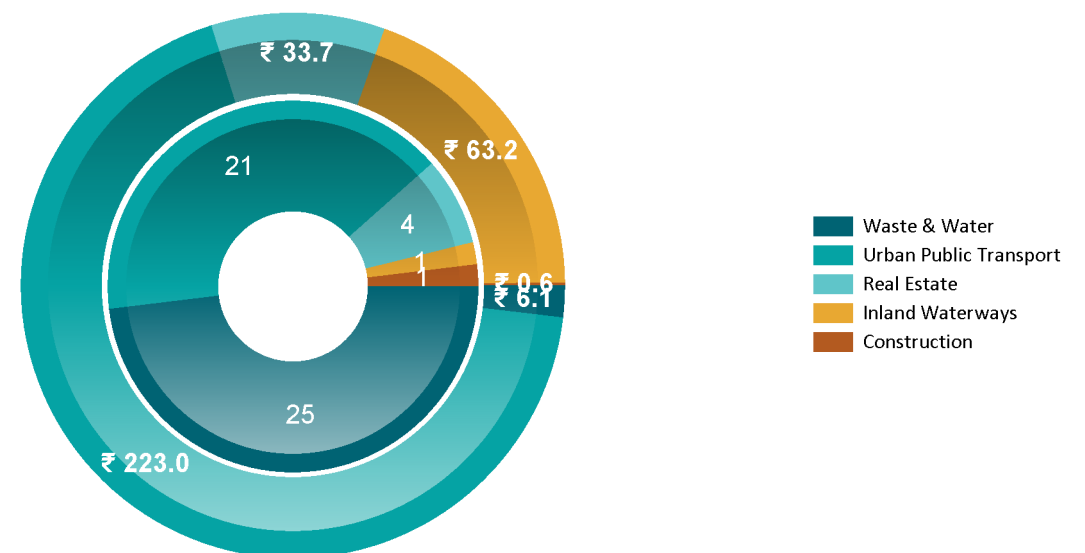


Physical & Financial progress (%) : Project count

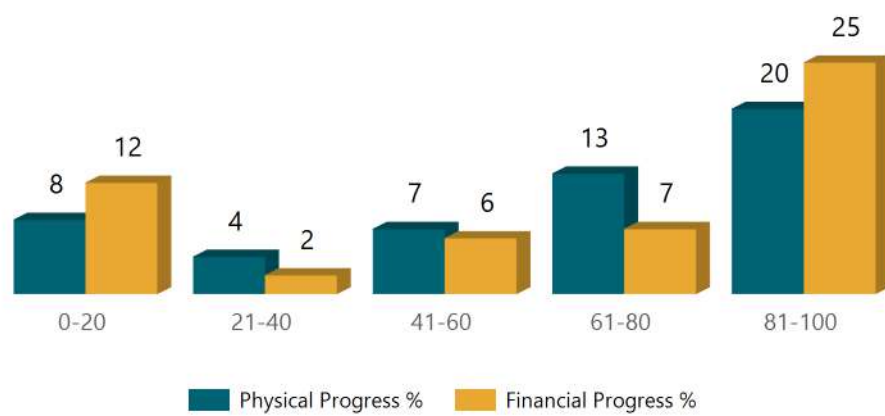

Cost Analytics : Major Sectors*

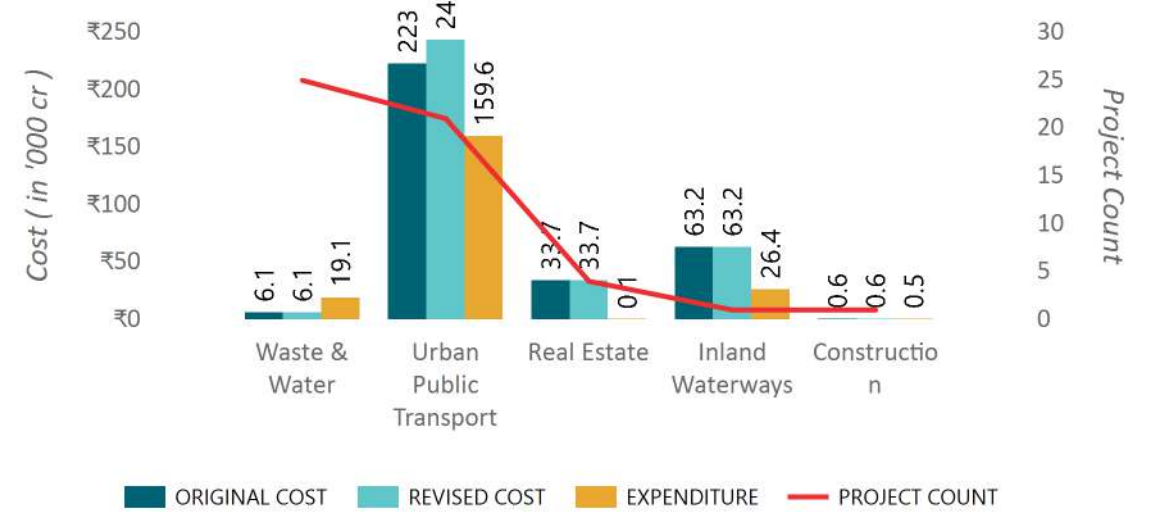

State Comparison : Major States*

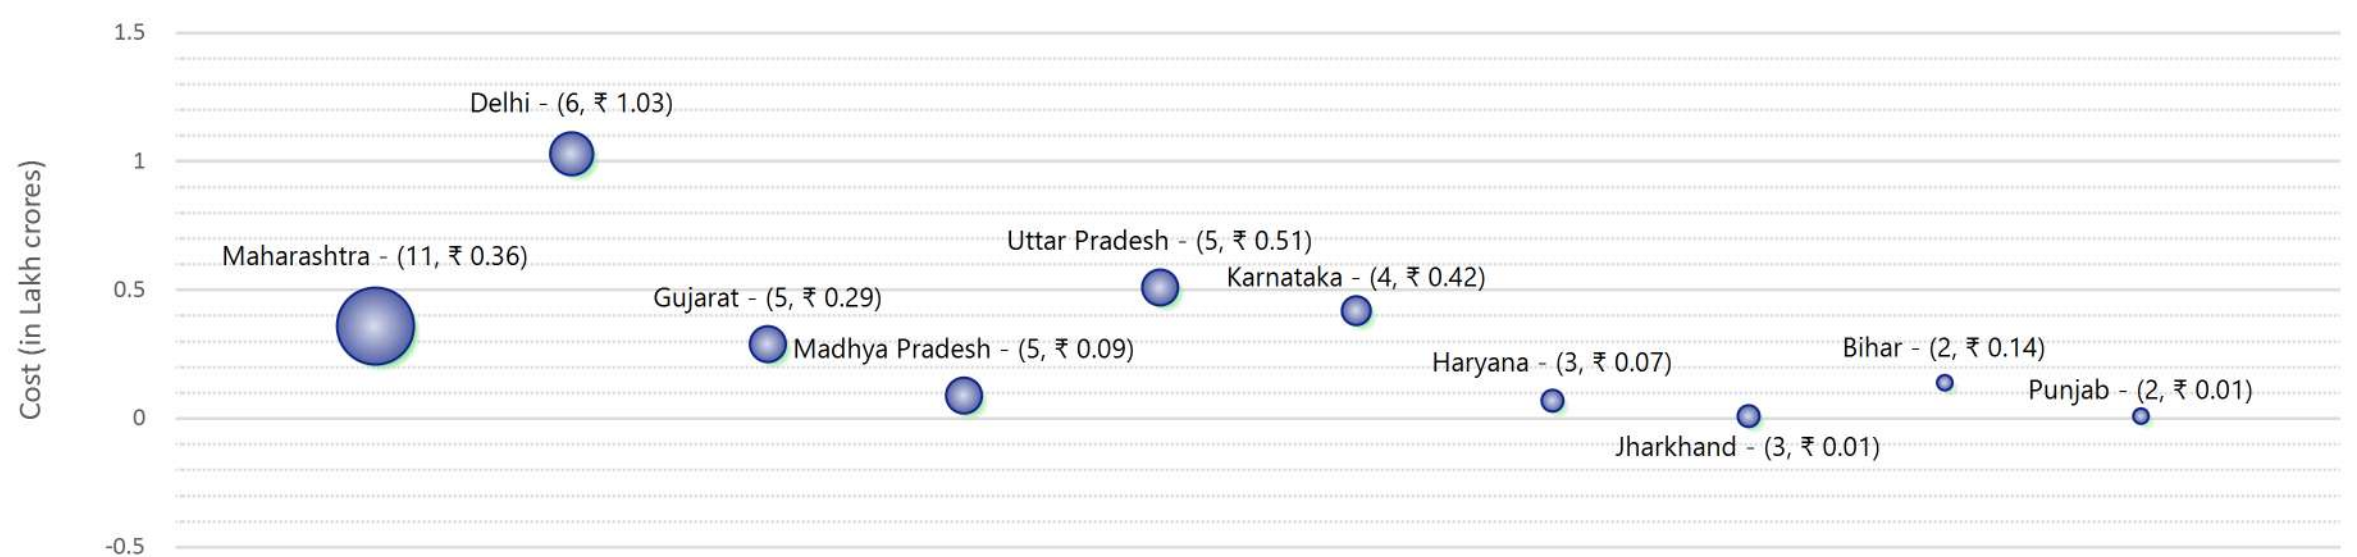

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246	63,246	26,410	45
2	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850	32,850	0	0
3	702633	DELHI-GHAZIABAD-MEERUT REGIONAL RAPID TRANSIT SYSTEM [RRTS] CORRIDOR	30,274	30,274	26,326	95
4	702635	CONSTRUCTION OF BANGALORE METRO RAIL PROJECT PHASE 2.	26,405	30,695	29,478	94
5	702632	DMRTS PHASE - IV [3 PRIORITY CORRIDORS]	24,949	24,949	15,785	69



List of Tables



Table 1: Ministry-wise Ongoing Projects





Ministry-wise Ongoing Projects

AUGUST 2025

Sl.No	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Department for Promotion of Industry & Internal Trade	Real Estate	2	3841.25 3841.25	494.3
2	Department of Higher Education	Education	30	12754.41 12685.5	8159.38
3	Department of Telecommunications	Telecommunication	14	150849.85 272942	72122.5
4	Department of Water Resources, River Development & GR	Waste & Water	8	4039.12 4039.12	1643.05
		Water Resources	40	93248.95 195108	138397
5	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	26	23049.84 23511	24879.8
6	Ministry of Coal	Coal	117	166806.82 164263	53439.3
		Electricity Generation	5	46865.63 51408.8	23562.4
		Railways	2	3485.86 3485.86	1641.67
7	Ministry of Health & Family Welfare	Healthcare	3	4155 4492.95	2694.22
8	Ministry of Housing & Urban Affairs	Construction	1	646.53 646.52	533.12
		Inland Waterways	1	63246 63246	26410.2
		Real Estate	4	33749.85 33749.8	58.58
		Urban Public Transport	21	223016.77 243598	159570
		Waste & Water	25	6085.6 6085.6	19062.9
9	Ministry of Mines	Construction	1	255.37 255.37	79.34
		Metals & Mining	9	12736.35 15116.5	6124.59
10	Ministry of Petroleum & Natural Gas	Energy Storage	16	81301.48 120185	90497.5
		Oil & Gas	90	351248.78 383480	184032
11	Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58
		Inland Waterways	2	9612.82 9304.79	3876.92
		Shipping	5	4823.34 4823.34	2020.93
		Tourism, Hospitality & Wellness	1	573 1238.05	496.63
12	Ministry of Power	Coal	2	2083 2365	910.82
		Electricity Generation	30	223418.07 278228	132370
		Transmission & Distribution	61	142976.51 149491	52183.1
13	Ministry of Railways	Railways	263	691320.92 837521	524256
14	Ministry of Steel	Metals & Mining	1	1700 1756.2	65.44
		Steel	19	16748.25 19986.5	7969.76
Total			800	2,375,332.37	1,537,609.45



Table 2: State-wise Ongoing Projects

Ongoing Projects State-Wise

AUGUST 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1		Ministry of Housing & Urban Affairs	Urban Public Transport	1	6941.4 6941.4	3164.15
	Offshore	Ministry of Petroleum & Natural Gas	Oil & Gas	6	19714.58 22972.8	10210.97
		Ministry of Railways	Railways	2	1311.83 1311.83	583.60
	PAN India	Department of Telecommunications	Telecommunication	6	141891.67 264213	69165.67
	Total			15	169859.48	83124.39
2	Andaman & Nicobar	Ministry of Housing & Urban Affairs	Real Estate	1	209.88 209.88	0.00
	Total			1	209.88	0.00
3	Andhra Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	1	2139.44 2139.44	406.05
		Department of Higher Education	Education	1	305 305	83.33
		Department of Telecommunications	Telecommunication	2	5262.57 5262.57	1699.75
		Department of Water Resources, River Development & GR	Water Resources	3	10901.5 57269.5	25827.76
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1224.86 1224.86	613.89
		Ministry of Housing & Urban Affairs	Waste & Water	1	172.22 172.22	622.02
		Ministry of Petroleum & Natural Gas	Energy Storage	2	2898.34 3050	2242.80
			Oil & Gas	5	37997 38057	33498.29
		Ministry of Power	Transmission & Distribution	5	13395.24 13395.2	4512.61
		Ministry of Railways	Railways	28	56255.53 63480.7	32347.60
	Total			51	130551.7	101854.10
4	Arunachal Pradesh	Department of Higher Education	Education	1	592.61 592.61	549.96
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	284.04
		Ministry of Petroleum & Natural Gas	Energy Storage	1	43129 79459	60295.14
			Oil & Gas	1	9265 9265	6393.85
		Ministry of Power	Electricity Generation	4	41850.64 61640.8	28586.95
			Transmission & Distribution	1	4754.42 9129.32	7462.20
		Ministry of Railways	Railways	1	435 1250	901.00
	Total			10	101282.16	104473.14
5	Assam	Department of Higher Education	Education	1	153.71 153.71	54.05
		Department of Telecommunications	Telecommunication	1	1255.49 1255.49	284.04
		Department of Water Resources, River Development & GR	Water Resources	1	256.16 256.16	0.00
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1712 1712	2335.44
		Ministry of Coal	Coal	2	449.23 449.23	186.31
		Ministry of Housing & Urban Affairs	Waste & Water	1	186.8 186.8	1291.55
		Ministry of Petroleum & Natural Gas	Energy Storage	3	10768.4 11947.4	9941.27
			Oil & Gas	13	28019.15 41554	30591.24
		Ministry of Power	Electricity Generation	1	6285.33 26075.5	24880.95
			Transmission & Distribution	1	5111.33 6700	5277.24
		Ministry of Railways	Railways	7	14593.57 16308.6	10302.48
	Total			32	68791.17	85144.57
6	Bihar	Department of Higher Education	Education	1	499.21 499.21	425.47
		Department of Telecommunications	Telecommunication	3	2336.11 2107.64	960.21
		Department of Water Resources, River Development & GR	Waste & Water	5	2351.43 2351.43	1303.45
			Water Resources	3	2884.49 4060.84	1590.27
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3541.56 3541.56	1256.71
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	13365.77 13365.8	4039.77
			Waste & Water	1	158.78 158.78	48.61
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9766.72



Ongoing Projects State-Wise

AUGUST 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
6	Bihar	Ministry of Petroleum & Natural Gas	Oil & Gas	7	24636.5 26501.2	13258.37
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3510.72
		Ministry of Power	Electricity Generation	1	10439.09 13756.6	12148.46
			Transmission & Distribution	2	751.63 751.63	0.90
		Ministry of Railways	Railways	20	48815.69 52817.3	22483.47
	Total			49	125377.44	70793.13
7	Chhattisgarh	Department of Telecommunications	Telecommunication	2	5262.57 5262.57	1699.75
		Department of Water Resources, River Development & GR	Water Resources	2	842.26 1109.33	616.93
		Ministry of Coal	Coal	15	38654.89 38654.9	15480.40
			Railways	1	1686.22 1686.22	347.96
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	10056.25 10467	6509.05
		Ministry of Power	Electricity Generation	2	25321 25321	2480.00
			Transmission & Distribution	1	385.84 385.84	378.17
		Ministry of Railways	Railways	19	32162 34222.7	18291.67
		Ministry of Steel	Metals & Mining	1	1700 1756.2	65.44
	Steel		6	7530.14 10050.1	5270.32	
Total			51	123601.17	51139.69	
8	Dadra & Nagar Haveli and Daman & Diu	Ministry of Housing & Urban Affairs	Waste & Water	1	210 210	0.00
		Ministry of Power	Transmission & Distribution	1	4546.26 4546.26	4172.96
		Ministry of Railways	Railways	1	108000 108000	79918.89
	Total			3	112756.26	84091.85
9	Delhi	Department of Higher Education	Education	2	706.49 706.49	300.98
		Department of Telecommunications	Telecommunication	1	248.2 248.2	236.91
		Ministry of Housing & Urban Affairs	Construction	1	646.53 646.52	533.12
			Real Estate	1	32850 32850	0.00
			Urban Public Transport	4	69853.45 69853.4	42116.99
		Ministry of Power	Transmission & Distribution	4	4356.47 4908.47	3923.11
		Ministry of Railways	Railways	14	28176.96 28177	5356.29
	Total			27	136838.1	52467.40
10	Goa	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	255.69 255.69	130.00
		Ministry of Railways	Railways	2	5804.49 6182.62	5976.87
	Total			3	6060.18	6106.87
11	Gujarat	Department of Higher Education	Education	1	490.63 490.63	301.44
		Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Department of Water Resources, River Development & GR	Water Resources	2	25739.93 40082.8	36722.58
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1305 1551	1348.78
		Ministry of Coal	Coal	1	7580 7580	3091.00
			Electricity Generation	1	383.84 383.84	303.50
		Ministry of Housing & Urban Affairs	Real Estate	1	539 539	39.63
			Urban Public Transport	3	28177.49 30329	23950.31
			Waste & Water	1	200 200	100.00
		Ministry of Petroleum & Natural Gas	Energy Storage	3	62245 98575	75103.78
			Oil & Gas	11	32704.12 32178.7	22879.89
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	4243.64 4243.64	366.20
			Tourism, Hospitality & Wellness	1	573 1238.05	496.63
	Ministry of Power	Electricity Generation	1	339.35 339.35	317.59	

Ongoing Projects State-Wise

AUGUST 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
11	Gujarat	Ministry of Power	Transmission & Distribution	13	45319.41 45318.9	12842.82
		Ministry of Railways	Railways	31	187430.66 262112	216423.66
		Total		73	397607.96	394515.63
12	Haryana	Ministry of Health & Family Welfare	Healthcare	1	1299 1299	349.41
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	6230.99 6230.99	0.29
			Waste & Water	2	491.2 491.2	2617.89
		Ministry of Petroleum & Natural Gas	Energy Storage	1	9028 9028	7136.41
			Oil & Gas	5	45925.07 49596.1	33666.90
		Ministry of Power	Transmission & Distribution	4	13362 13914	2619.30
		Ministry of Railways	Railways	4	53464 126368	125567.23
		Total		18	129800.26	171957.43
13	Himachal Pradesh	Department of Higher Education	Education	3	811.15 921.89	579.09
		Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Ministry of Power	Electricity Generation	4	7728.04 12252.1	4137.13
		Ministry of Railways	Railways	3	17005 17005.1	9366.44
		Total		11	25881.08	14310.48
14	Jammu and Kashmir	Department of Higher Education	Education	1	424.93 500.91	484.52
		Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	861.37 861.37	177.69
		Ministry of Health & Family Welfare	Healthcare	1	1828 1828	1531.86
		Ministry of Petroleum & Natural Gas	Energy Storage	1	676.89 676.89	526.10
			Oil & Gas	2	1059.9 1059.9	193.82
		Ministry of Power	Electricity Generation	4	22207.77 27945.1	12525.60
			Transmission & Distribution	3	825.43 825.43	496.12
		Total		14	28221.18	16163.53
15	Jharkhand	Department of Telecommunications	Telecommunication	2	5262.57 5262.57	1699.75
		Department of Water Resources, River Development & GR	Water Resources	2	5430.04 12010.3	5704.07
		Ministry of Coal	Coal	27	45414.48 45178.8	10417.02
			Railways	1	1799.64 1799.64	1293.71
		Ministry of Housing & Urban Affairs	Waste & Water	3	654.14 654.14	2532.48
		Ministry of Mines	Metals & Mining	2	3370.02 3370.02	16.57
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9766.72
			Oil & Gas	3	2010.07 2010.07	595.56
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3510.72
		Ministry of Power	Coal	2	2083 2365	910.82
			Electricity Generation	2	31470 34660	18606.57
		Ministry of Railways	Railways	12	43352.74 43746.7	14874.38
		Ministry of Steel	Steel	6	2854.58 3572.87	1284.99
		Total		64	159298.46	71213.36
16	Karnataka	Department for Promotion of Industry & Internal Trade	Real Estate	1	1701.81 1701.81	88.25
		Department of Higher Education	Education	1	420.41 420.41	360.72
		Department of Water Resources, River Development & GR	Water Resources	1	770.16 1606.07	1511.22
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1143.4 1143.4	515.77
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	41193.24 45483.2	37902.51
			Waste & Water	2	337.69 337.69	1278.27
		Ministry of Petroleum & Natural Gas	Energy Storage	1	678 1732	713.86

Ongoing Projects State-Wise

AUGUST 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
16	Karnataka	Ministry of Petroleum & Natural Gas	Oil & Gas	5	9662 12693.6	8749.96
		Ministry of Power	Transmission & Distribution	6	15682.01 15682	2815.76
		Ministry of Railways	Railways	17	25363.59 31532.2	17702.61
		Ministry of Steel	Steel	1	1043.63 1043.63	229.77
		Total		40	97995.94	71868.70
17	Kerala	Department of Higher Education	Education	1	1006.45 1217.4	623.60
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	484.57 484.57	83.95
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	1957.05 1957.05	329.94
		Ministry of Petroleum & Natural Gas	Oil & Gas	3	7996.87 10990.9	4912.37
		Ministry of Railways	Railways	3	2846 5199	3026.15
		Total		9	14290.94	8976.01
18	Ladakh	Department of Telecommunications	Telecommunication	1	336.89 301.13	227.82
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	480 640	434.79
		Ministry of Power	Transmission & Distribution	1	288.71 288.71	207.80
		Total		3	1105.6	870.41
19	Madhya Pradesh	Department of Higher Education	Education	1	496.28 496.28	143.95
		Department of Telecommunications	Telecommunication	2	1999.22 1806.51	732.39
		Department of Water Resources, River Development & GR	Water Resources	3	2628.27 2941.14	2725.95
		Ministry of Coal	Coal	14	8634.02 8634.02	3368.12
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	7500.8 7500.8	3931.40
			Waste & Water	4	1243.05 1243.05	6956.60
		Ministry of Mines	Metals & Mining	1	1856.36 1856.36	935.32
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10088 10088	7672.23
			Oil & Gas	2	51211.25 51622	8351.10
		Ministry of Power	Transmission & Distribution	6	17446 17446	2930.65
		Ministry of Railways	Railways	18	56050.78 67640.2	42750.83
		Total		53	159154.03	80498.54
20	Maharashtra	Department of Higher Education	Education	2	250.33 446.26	154.70
		Department of Telecommunications	Telecommunication	3	5723.99 5723.99	1865.77
		Department of Water Resources, River Development & GR	Water Resources	10	20736.55 30421.9	31303.79
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	332.26
		Ministry of Coal	Coal	25	12455.88 12455.9	3084.72
		Ministry of Housing & Urban Affairs	Urban Public Transport	6	34571.47 48711.5	28993.92
			Waste & Water	5	1088.72 1088.72	2313.41
		Ministry of Petroleum & Natural Gas	Energy Storage	1	281.35 389.67	230.76
			Oil & Gas	13	34264.24 37660.4	20702.79
		Ministry of Ports, Shipping and Waterways	Healthcare	1	693 693	58.00
			Shipping	2	1266.8 1266.8	441.86
		Ministry of Power	Transmission & Distribution	3	29589.67 29589.7	5993.74
		Ministry of Railways	Railways	36	267281.11 358733	262133.68
		Total		108	408703.59	357609.40
21	Manipur	Department of Water Resources, River Development & GR	Water Resources	1	1449.44 1822.24	1837.91
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	499 499	154.43
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6393.85
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5277.24



Ongoing Projects State-Wise

AUGUST 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
21	Manipur	Ministry of Railways	Railways	1	14323 21885.9	15598.11
		Total		5	30647.77	29261.54
22	Meghalaya	Department of Higher Education	Education	1	494.52 494.52	413.57
		Department of Telecommunications	Telecommunication	1	971.96 971.96	208.25
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6393.85
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5277.24
		Total		4	15842.81	12292.91
23	Mizoram	Department of Higher Education	Education	1	474.23 474.23	167.55
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6393.85
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5277.24
		Total		3	14850.56	11838.64
24	Nagaland	Department of Higher Education	Education	1	275.63 275.63	260.10
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	9492.62 9492.62	6402.97
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5277.24
		Ministry of Railways	Railways	2	8786.7 8786.7	5326.00
		Total		6	23666.28	17266.31
25	Odisha	Department of Higher Education	Education	1	1229.32 773.76	837.04
		Department of Telecommunications	Telecommunication	2	5262.57 5262.57	1699.75
		Department of Water Resources, River Development & GR	Water Resources	2	1556.46 5291.33	5193.30
		Ministry of Coal	Coal	12	36526.28 34218	13335.92
			Electricity Generation	1	27212.96 27213	1953.52
		Ministry of Mines	Metals & Mining	5	7343.97 9724.14	5037.70
		Ministry of Petroleum & Natural Gas	Energy Storage	2	12886.34 14217	11970.70
			Oil & Gas	5	25285.44 23768.5	15778.36
		Ministry of Ports, Shipping and Waterways	Shipping	1	3004.63 3004.63	1149.79
		Ministry of Power	Electricity Generation	1	11843.75 12543	4161.68
			Transmission & Distribution	1	342.69 342.69	0.60
		Ministry of Railways	Railways	28	47401.37 52133.4	31907.65
			Railways	1	267.61 267.61	0.00
		Ministry of Steel	Steel	1	1105.23 1105.23	769.08
		Total		63	181268.62	93795.09
26	Puducherry	Department of Higher Education	Education	1	618.34 544.34	509.55
		Ministry of Railways	Railways	1	713 981	598.38
		Total		2	1331.34	1107.93
27	Punjab	Department of Higher Education	Education	2	559.3 559.3	290.39
		Department of Water Resources, River Development & GR	Water Resources	2	3727.07 5177.86	5072.69
		Ministry of Housing & Urban Affairs	Waste & Water	2	545.53 545.53	612.96
		Ministry of Petroleum & Natural Gas	Oil & Gas	6	13060.36 13090.4	8374.98
		Ministry of Power	Transmission & Distribution	1	5969 5969	218.47
		Ministry of Railways	Railways	3	15702.64 15702.6	8977.71
		Total		16	39563.9	23547.20
28	Rajasthan	Department of Telecommunications	Telecommunication	2	758.54 530.07	361.90
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1367 1367	634.54
		Ministry of Coal	Electricity Generation	1	1813 1813	874.14
		Ministry of Petroleum & Natural Gas	Energy Storage	3	52618.05 88948.1	67548.03
			Oil & Gas	2	10599 10599	6647.57

Ongoing Projects State-Wise

AUGUST 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
28	Rajasthan	Ministry of Power	Electricity Generation	1	5491.89 5491.89	4805.16
			Transmission & Distribution	22	53646.51 54198.2	16979.78
		Ministry of Railways	Railways	21	86599.15 162169	139520.05
		Total		54	212893.14	237371.17
29	Sikkim	Department of Higher Education	Education	2	999.82 924.82	359.78
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	323.26 323.26	29.70
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	9265 9265	6393.85
		Ministry of Power	Electricity Generation	2	6686.33 7576.15	6161.06
			Transmission & Distribution	1	4754.42 9129.32	7462.20
		Ministry of Railways	Railways	1	7877 12133	9039.91
		Total		8	29905.83	29446.50
30	Tamil Nadu	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1207 1207	149.21
		Ministry of Coal	Electricity Generation	1	218.03 218.03	161.73
		Ministry of Housing & Urban Affairs	Inland Waterways	1	63246 63246	26410.15
		Ministry of Mines	Metals & Mining	1	166 166	135.00
		Ministry of Petroleum & Natural Gas	Energy Storage	3	2334 3448.71	1641.58
			Oil & Gas	4	38385 46153	6060.57
		Ministry of Power	Transmission & Distribution	1	548 548	14.68
		Ministry of Railways	Railways	8	8730 11599	5805.89
		Total		20	114834.03	40378.81
31	Telangana	Department of Higher Education	Education	1	262 262	177.09
		Department of Telecommunications	Telecommunication	2	2038.99 2038.99	764.33
		Department of Water Resources, River Development & GR	Water Resources	4	11670.14 24129.6	11830.43
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 500.48	332.26
		Ministry of Coal	Coal	9	3890.03 3890.03	2462.36
		Ministry of Health & Family Welfare	Healthcare	1	1028 1365.95	812.95
		Ministry of Power	Transmission & Distribution	2	5694.56 5694.56	4337.14
		Ministry of Railways	Railways	11	22284.15 26048.2	9009.21
		Total		31	47368.35	29725.77
32	Tripura	Ministry of Petroleum & Natural Gas	Energy Storage	1	656 656	478.11
			Oil & Gas	2	9474.33 9396.51	6462.73
		Ministry of Power	Transmission & Distribution	1	5111.33 6700	5277.24
		Total		4	15241.66	12218.08
33	Uttar Pradesh	Department of Higher Education	Education	1	246 246	193.38
		Department of Telecommunications	Telecommunication	3	2336.11 2107.64	960.21
		Department of Water Resources, River Development & GR	Waste & Water	2	1532.96 1532.96	243.43
			Water Resources	4	3694.65 8775.49	7633.54
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	5	7268.31 7323.51	16971.73
		Ministry of Coal	Coal	2	1328.09 1328.09	1017.31
			Electricity Generation	1	17237.8 21780.9	20269.54
		Ministry of Housing & Urban Affairs	Urban Public Transport	3	49730.1 49730.1	41466.62
			Waste & Water	2	797.47 797.47	689.15
		Ministry of Petroleum & Natural Gas	Energy Storage	2	11068.45 11068.5	7888.89
			Oil & Gas	3	17824.68 18213.1	1578.44
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3510.72
		Ministry of Power	Electricity Generation	2	28284.42 30471.2	14511.21

Ongoing Projects State-Wise

AUGUST 2025

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
33	Uttar Pradesh	Ministry of Power	Transmission & Distribution	3	8114.81 8114.81	1650.63
		Ministry of Railways	Railways	28	95245.3 169871	148169.27
		Total		62	250078.33	266754.07
34	Uttarakhand	Department of Higher Education	Education	1	650.85 650.85	195.52
		Department of Water Resources, River Development & GR	Water Resources	1	2584.1 2584.1	968.52
		Ministry of Housing & Urban Affairs	Real Estate	1	150.97 150.97	18.95
		Ministry of Power	Electricity Generation	3	11663.95 26070	20361.54
		Ministry of Railways	Railways	1	38953 38953	24645.15
		Total		7	54002.87	46189.68
35	West Bengal	Department of Higher Education	Education	2	787.2 729.2	693.60
		Department of Telecommunications	Telecommunication	1	1577.57 1577.57	598.31
		Department of Water Resources, River Development & GR	Waste & Water	1	154.73 154.73	96.17
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1877.3 1877.3	375.40
		Ministry of Coal	Coal	13	15863.74 15863.7	2802.30
		Ministry of Mines	Construction	1	255.37 255.37	79.34
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10228 11407	9766.72
			Oil & Gas	8	18159.65 19007.2	11294.42
		Ministry of Ports, Shipping and Waterways	Inland Waterways	1	5369.18 5061.15	3510.72
			Shipping	2	551.91 551.91	429.28
		Ministry of Power	Electricity Generation	3	20091.84 20160.8	3566.83
			Transmission & Distribution	2	751.63 751.63	0.90
		Ministry of Railways	Railways	16	49682.05 60254	33496.35
		Ministry of Steel	Steel	5	4214.67 4214.67	415.60
		Total		58	129564.84	67125.94



Table 3: Ongoing Projects North Eastern Region



Ongoing Projects of North-East Region							
AUGUST 2025							
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Ministry of Civil Aviation						
	Aviation & Aviation Infrastructure						
1	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	03/2018	03/2025 11/2025	1712 (1712)	2335.44	91
2	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	07/2022	07/2024 12/2026	499 (499)	154.43	41
3	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	12/2023	02/2026 (-)	323.26 (323.26)	29.7	12
	Total (3)				2534.26	2519.57	
	Ministry of Coal						
	Coal						
4	TIKAK EXTENSION OCP (MIS MoCoal Integration Logins) (615820)	Assam	07/2022	07/2031 (-)	159.77 (159.77)	80.84	0
5	TIRAP OCP (MIS MoCoal Integration Logins) (615821)	Assam	11/2022	11/2030 (-)	289.46 (289.46)	105.47	0
	Total (2)				449.23	186.31	
	Department of Higher Education						
	Education						
6	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	03/2013	08/2026 (-)	592.61 (592.61)	549.96	75
7	Tezpur University Projects (Tezpur University) (606112)	Assam	06/2021	11/2023 08/2025	153.71 (153.71)	54.05	95
8	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2014	03/2022 07/2025	494.52 (494.52)	413.57	86
9	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (Ministry of Education) (612876)	Mizoram	05/2014	12/2029 12/2029	474.23 (474.23)	167.55	4
10	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2012	12/2025 (-)	275.63 (275.63)	260.1	95
11	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	01/2022	01/2025 09/2025	314.06 (314.06)	238.22	82
12	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (Ministry of Education) (612883)	Sikkim	03/2024	02/2028 12/2026	685.76 (610.76)	121.56	9
	Total (7)				2990.52	1805.01	
	Ministry of Power						
	Electricity Generation						
13	Dibang Multipurpose Project (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602182)	Arunachal Pradesh	02/2023	02/2032 02/2032	31876.39 (31876.4)	3553.9	16
14	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	05/2025	07/2029 (-)	1938.85 (1938.85)	49.31	3
15	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	05/2025	07/2029 (-)	1750.07 (1750.07)	102.79	2
16	Subansiri Lower HE Project [2000 MW] (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003	09/2010 05/2026	6285.33 (26075.5)	24880.95	96
17	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (602181)	Sikkim	03/2019	03/2024 12/2027	5748.04 (5748.04)	4576.93	69
18	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (605156)	Sikkim	03/2021	05/2024 12/2025	938.29 (1828.11)	1584.13	91
	Total (6)				48536.97	34748.01	
	Transmission & Distribution						
19	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	01/2016	12/2018 03/2027	4754.42 (9129.32)	7462.2	81
20	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	03/2016	12/2018 12/2025	5111.33 (6700)	5277.24	96

Ongoing Projects of North-East Region

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Total (2)				9865.75	12739.44	
	Ministry of Petroleum & Natural Gas						
	Energy Storage						
21	Rajasthan Refinery Project (MinistryofPetroleumNaturalGas) (701263)	Arunachal Pradesh	10/2017	10/2022 03/2026	43129 (79459)	60295.14	88
22	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (Ministry of Petroleum & Natural Gas) (701349)	Assam	01/2019	07/2024 09/2025	10228 (11407)	9766.72	87
23	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	03/2023	07/2027 07/2027	156.36 (156.36)	54.15	46
24	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited [HPCL]) (709755)	Assam	03/2023	07/2027 07/2027	384.04 (384.04)	120.4	52
25	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (Indian Oil Corporation Limited [IOCL]) (400035)	Tripura	06/2022	09/2025 06/2026	656 (656)	478.11	86
	Total (5)				54553.4	70714.52	
	Oil & Gas						
26	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791)	Assam	07/2020	07/2024 12/2025	12366 (22494)	16764.09	76
27	Assam Bio Refinery, ABRPL (Ministry of Petroleum & Natural Gas) (604792)	Assam	02/2018	09/2021 09/2025	1750 (4930)	4710	99
28	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863)	Assam	01/2018	02/2020 12/2025	682.9 (726.93)	489.3	94
29	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery (Ministry of Petroleum & Natural Gas) (607701)	Assam	05/2021	10/2023 05/2026	412.3 (577)	430.83	85
30	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858)	Assam	12/2020	03/2024 12/2025	430.76 (430.76)	327.27	85
31	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA (Ministry of Petroleum & Natural Gas) (701350)	Assam	06/2021	12/2024 10/2025	860 (860)	584.76	98
32	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (MinistryofPetroleumNaturalGas) (709776)	Assam	04/2022	09/2026 09/2026	277 (323.09)	185.18	68
33	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (MinistryofPetroleumNaturalGas) (709779)	Assam	06/2022	03/2026 03/2026	768 (740)	107.72	39
34	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847)	Assam	01/2023	04/2026 04/2026	344.99 (344.99)	211.05	47
35	Borholla GGS Life Extension Project [BLEP] (Ministry of Petroleum & Natural Gas) (709850)	Assam	09/2023	05/2026 05/2026	198.7 (198.7)	36.8	30
36	DCU Revamp Project (NRL) (709864)	Assam	08/2021	07/2024 10/2025	370 (370)	253.17	60
37	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (NRL) (709865)	Assam	04/2023	12/2024 10/2025	293.5 (293.5)	97.22	94
38	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura)	04/2020	03/2024 03/2026	9265 (9265)	6393.85	85
39	Augmentation/ Revamping of Dimapur Depot, Dimapur (MinistryofPetroleumNaturalGas) (709786)	Nagaland	08/2023	11/2027 11/2027	227.62 (227.62)	9.12	22
40	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837)	Tripura	03/2022	05/2024 12/2025	209.33 (131.51)	68.88	62
	Total (15)				28456.1	30669.24	
	Ministry of Railways						
	Railways						
41	Doubling of New Bongaigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016	03/2026 03/2026	4060 (4961)	3683.75	93
42	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2018	09/2020 06/2024	890.36 (889.36)	391.73	89
43	Mariani-Jorhat, Tinsukia-Dangri and Makum -TirapTrack Electrification Project (GM/C/ NFR) (706940)	Assam	01/2022	05/2024 (-)	183.99 (183.99)	0	0
44	Harmuty-Murkongselek Branch Line Electrification Project (GM/C/ NFR) (706942)	Assam	01/2022	05/2024 (-)	237.52 (237.52)	0	0

Ongoing Projects of North-East Region							AUGUST 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
45	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391)	Manipur	12/2007	12/2026 06/2029	14323 (21885.9)	15598.11	69
46	Murkongselek-Pasighat (Northeast Frontier Railway (NFR) - II) (705401)	Multi-States (Arunachal Pradesh, Assam)	03/2012	03/2025 12/2025	435 (1250)	901	56
47	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	01/2025	02/2028 (-)	2123.7 (2123.7)	13.74	0
48	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR]) (705392)	Multi-States (Assam, Nagaland)	02/2016	03/2025 12/2025	6663 (6663)	5312.26	80
49	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Sikkim	05/2010	05/2015 12/2027	7877 (12133)	9039.91	84
Total (9)					36793.57	34940.5	
Department of Telecommunications							
Telecommunication							
50	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications [DoT]) (701598)	Meghalaya	09/2020	03/2022 09/2025	971.96 (971.96)	208.25	99
51	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications [DoT]) (701597)	Multi-States (Arunachal Pradesh, Assam)	10/2021	04/2023 09/2025	1255.49 (1255.49)	284.04	89
Total (2)					2227.45	492.29	
Ministry of Housing & Urban Affairs							
Waste & Water							
52	Dibrugarh Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702682)	Assam	01/2020	03/2023 12/2025	186.8 (186.8)	1291.55	98
Total (1)					186.8	1291.55	
Department of Water Resources, River Development & GR							
Water Resources							
53	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370)	Assam	12/1996	12/2022 03/2026	256.16 (256.16)	0	55
54	Thoubal Multipurpose Project (Water Resources Department-MN) (701400)	Manipur	04/1997	12/2019 03/2026	1449.44 (1822.24)	1837.91	98
Total (2)					1705.6	1837.91	




Table 4: All Ongoing Projects



All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Ministry of Civil Aviation							
Aviation & Aviation Infrastructure							
1	Construction of New Domestic Terminal Building Building and miscellaneous works including maintenance, operations and AICMC at Kadapa Airport (Airport Authority of India [AAI]) (612786)	Andhra Pradesh	01/2024	01/2026 03/2026	265.91 (265.91)	50.06	34
2	Construction of New Integrated Terminal Building and associated works including apron to park 3 code E type of aircraft or 6 code C type of aircraft at Vijayawada Airport. (Airport Authority of India [AAI]) (701107)	Andhra Pradesh	09/2020	09/2022 12/2025	611.8 (611.8)	473.27	79
3	Construction of New Domestic Terminal Building at Rajahmundry Airport. (Airport Authority of India [AAI]) (701121)	Andhra Pradesh	08/2023	08/2025 12/2025	347.15 (347.15)	90.56	51
4	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	03/2018	03/2025 11/2025	1712 (1712)	2335.44	91
5	Development of New Civil Enclave at Bihta (Airport Authority of India [AAI]) (612183)	Bihar	03/2025	09/2027 (-)	1413 (1413)	0	1
6	Development of New Civil Enclave and associated works at Darbhanga Airport (Airport Authority of India [AAI]) (612194)	Bihar	07/2024	01/2026 (-)	911.66 (911.66)	160.2	26
7	Construction of New Domestic Terminal Building [Phase-I and II] and other allied structures at JPNI Airport, Patna (Airport Authority of India [AAI]) (701101)	Bihar	10/2018	07/2023 11/2025	1216.9 (1216.9)	1096.51	94
8	Goa Airport Terminal Building Extension Project (Airport Authority of India [AAI]) (701105)	Goa	12/2019	12/2021 09/2025	255.69 (255.69)	130	90
9	Development of Dholera International Greenfield Airport , Gujarat (Airport Authority of India [AAI]) (701126)	Gujarat	07/2022	06/2026 06/2026	1305 (1551)	1348.78	64
10	Construction of NTB complex including apron, taxi track and other associated civil works and electrical & mechanical installations towards Tawi River side at CA Jammu. (Airport Authority of India [AAI]) (611047)	Jammu and Kashmir	07/2023	06/2026 06/2026	861.37 (861.37)	177.69	35
11	Construction of New Domestic Terminal Building and Miscellaneous works at Hubli Airport (Airport Authority of India [AAI]) (612787)	Karnataka	01/2024	01/2026 03/2026	320.47 (320.47)	61.79	38
12	Construction of New Domestic Terminal Building and Miscellaneous Works at Belagavi Airport. (Airport Authority of India [AAI]) (612788)	Karnataka	02/2024	01/2026 01/2026	322.45 (322.45)	121.72	52
13	Development of additional RESA on either end on Runway 10-28 at Calicut Airport. Construction of embankment with slope protection, drainage system and associated works for additional RESA on either end on Runway 10-28 (Airport Authority of India [AAI]) (612789)	Kerala	02/2024	09/2025 03/2026	484.57 (484.57)	83.95	21
14	Construction of Terminal Building & Associated works at Leh Airport, Ladakh (Airport Authority of India [AAI]) (400010)	Ladakh	09/2018	09/2021 10/2025	480 (640)	434.79	71
15	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	07/2022	07/2024 12/2026	499 (499)	154.43	41
16	SITC of ATM Automation System and ASMGCS [Including SMR & MLAT] for Mumbai, Navi Mumbai, Jewar [earlier MOPA, without ASMGCS], HIAL & BIAL (Airport Authority of India [AAI]) (611570)	Multi-States (Karnataka, Maharashtra, Telangana, Uttar Pradesh)	10/2022	09/2025 08/2026	500.48 (500.48)	332.26	75
17	Construction of New Passenger Terminal Building for Domestic Operations at Jodhpur Airport. (Airport Authority of India [AAI]) (701127)	Rajasthan	04/2023	11/2024 10/2025	480 (480)	281.72	84
18	Construction of New Integrated Passenger Terminal Building at Udaipur Airport (Airport Authority of India [AAI]) (701128)	Rajasthan	11/2022	03/2026 10/2026	887 (887)	352.82	49
19	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	12/2023	02/2026 (-)	323.26 (323.26)	29.7	12
20	Modernization of Chennai Airport, Phase II, Part 2 (Airport Authority of India [AAI]) (611602)	Tamil Nadu	06/2023	07/2025 03/2026	1207 (1207)	149.21	22
21	Construction of New Terminal Building, Second Link Taxi Track, Apron Expansion, and associated works at Prayagraj Airport- On Design & Build Basis. (Airport Authority of India [AAI]) (612063)	Uttar Pradesh	08/2023	11/2024 08/2025	219.18 (274.38)	215.19	100
22	Lucknow Airport-Terminal 3- Phase 1 & Other Associated Works (Adani Airport Holdings Limited) (701091)	Uttar Pradesh	09/2018	03/2026 (-)	3100 (3100)	16024.42	100
23	Development of Lal Bahadur Shastri International airport, Varanasi including C/o New Terminal Building, Apron Extension, Runway Extension, PTT and allied works. (Airport Authority of India [AAI]) (701113)	Uttar Pradesh	07/2024	07/2027 07/2027	2869.65 (2869.65)	322.98	16
24	Development of New Integrated Civil Enclave at Agra Airport (Airport Authority of India [AAI]) (701122)	Uttar Pradesh	07/2024	07/2026 (-)	579 (579)	76.88	16
25	Development of New Civil Enclave at Bagdogra Airport (Airport Authority of India [AAI]) (611495)	West Bengal	10/2023	01/2027 01/2027	1549 (1549)	274.14	11

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
26	Re-Construction of Rigid portions of Secondary Runway, K and A Taxiway and Strengthening of C Taxiway at NSCB I Airport Kolkata. <i>(Airport Authority of India [AAI])</i> (612791)	West Bengal	12/2023	02/2025 08/2026	328.3 (328.3)	101.26	45
	Total (26)				23049.84	24879.77	
	Ministry of Coal						
	Coal						
27	TIKAK EXTENSION OCP <i>(MIS MoCoal Integration Logins)</i> (615820)	Assam	07/2022	07/2031 (-)	159.77 (159.77)	80.84	0
28	TIRAP OCP <i>(MIS MoCoal Integration Logins)</i> (615821)	Assam	11/2022	11/2030 (-)	289.46 (289.46)	105.47	0
29	PORDA CHINTAPANI OCP [10 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400144)	Chhattisgarh	12/2020	03/2029 (-)	2310.12 (2310.12)	83.66	10
30	CHHAL OC SEAM III [6 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400145)	Chhattisgarh	12/2013	03/2022 09/2025	610.63 (610.63)	577.46	85
31	KUSMUNDA OC EXPANSION [15 TO 50 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400147)	Chhattisgarh	08/2013	03/2023 03/2030	7612.33 (7612.33)	4697.95	81
32	BAROUD OC EXPANSION [3.0-10.0M] <i>(South Eastern Coalfields Limited [SECL])</i> (400149)	Chhattisgarh	08/2020	03/2029 (-)	2309.8 (2309.8)	926.11	48
33	DIPKA EXPANSION OCP [40 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400354)	Chhattisgarh	12/2020	03/2029 (-)	5241.4 (5241.4)	2830.01	37
34	GEVRA OC [70 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (400424)	Chhattisgarh	03/2016	03/2023 03/2026	11816.4 (11816.4)	5328.96	77
35	JAMPALI OC RCE [2.0 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613795)	Chhattisgarh	05/2020	03/2025 06/2025	278.64 (278.64)	210.07	82
36	AMERA OC RCE [1.0 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613798)	Chhattisgarh	02/2015	03/2026 (-)	335.97 (335.97)	88.21	42
37	AMGAON OC RCE [1.0 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613799)	Chhattisgarh	07/2015	03/2026 (-)	316.11 (316.11)	188.6	72
38	JAGANNATHPUR OC RCE PROJECT[3 <i>(South Eastern Coalfields Limited [SECL])</i> (613800)	Chhattisgarh	07/2016	03/2025 03/2026	459.49 (459.49)	274.35	92
39	MAHAMAYA OCP [1.50 MTY] <i>(South Eastern Coalfields Limited [SECL])</i> (613801)	Chhattisgarh	05/2018	03/2026 (-)	410.26 (410.26)	181.23	38
40	KATKONA RO UG MINE <i>(South Eastern Coalfields Limited [SECL])</i> (615191)	Chhattisgarh	01/2023	03/2029 (-)	329.21 (329.21)	60.3	2
41	PELMA OC MDO <i>(South Eastern Coalfields Limited [SECL])</i> (616234)	Chhattisgarh	10/2022	03/2033 (-)	1725.04 (1725.04)	15.66	17
42	KUSMUNDA OC EXPANSION PROJECT 50-75 MTY <i>(SECL - CIL)</i> (617287)	Chhattisgarh	11/2024	03/2030 (-)	4516.88 (4516.88)	16.97	3
43	MANIKPUR OC EXPANSION PROJECT 7 MTY <i>(South Eastern Coalfields Limited [SECL])</i> (617288)	Chhattisgarh	01/2025	03/2029 (-)	382.61 (382.61)	0.86	1
44	DIPKA OC <i>(SECL - CIL)</i> (612838)	Gujarat	01/2017	03/2025 (-)	7580 (7580)	3091	65
45	HURA C OCP <i>(ECL - CIL)</i> (400018)	Jharkhand	08/2022	03/2029 (-)	859.41 (859.41)	450.76	62
46	KONAR EXPANSION OCP <i>(Ministry of Coal)</i> (400073)	Jharkhand	01/2022	03/2032 (-)	799.34 (799.34)	424.01	45
47	KARO EXPANSION OCP <i>(Ministry of Coal)</i> (400074)	Jharkhand	01/2022	03/2029 (-)	908.47 (908.47)	269.18	22
48	SANGHMITRA OC <i>(Ministry of Coal)</i> (400136)	Jharkhand	03/2027	03/2032 (-)	2660 (2660)	0	0
49	CHANDRAGUPT OCP <i>(Ministry of Coal)</i> (400138)	Jharkhand	08/2020	03/2032 (-)	973.5 (973.5)	440.56	25
50	KOTRE BASANTPUR PACHMO OCP <i>(Ministry of Coal)</i> (400139)	Jharkhand	08/2020	03/2032 (-)	861.06 (625.4)	455.95	42
51	Pachwara South Coal Block <i>(NLC India Limited [NLCIL])</i> (400142)	Jharkhand	12/2019	09/2028 (-)	2242.9 (2242.9)	1170.75	74
52	RPR MAGADH EXP OCP <i>(Ministry of Coal)</i> (400150)	Jharkhand	08/2020	03/2028 (-)	7254.37 (7254.37)	1535.31	38
53	NORTH URIMARI EXPANSION OCP <i>(Ministry of Coal)</i> (400151)	Jharkhand	07/2021	03/2029 (-)	778.8 (778.8)	695.99	67
54	EPR ROHINI - KARKETTA OCP <i>(Central Coalfields Limited [CCL])</i> (400153)	Jharkhand	01/2021	03/2028 (-)	1020.42 (1020.42)	83.95	20



All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
55	EPR PUNDI OCP (Ministry of Coal) (400154)	Jharkhand	11/2020	03/2027 (-)	713.35 (713.35)	236.58	10
56	EPR ASHOK OC (Ministry of Coal) (400155)	Jharkhand	05/2021	03/2028 (-)	2898.28 (2898.28)	178.51	22
57	EPR AMRAPALI OCP (Ministry of Coal) (400156)	Jharkhand	02/2020	03/2028 (-)	5136.15 (5136.15)	1154.6	43
58	RAJRAPPA RCE OCP (Ministry of Coal) (400160)	Jharkhand	12/2009	03/2016 03/2027	510.85 (510.85)	488.67	76
59	CHITRA EAST OC (Eastern Coal Fields Limited [ECL]) (400172)	Jharkhand	08/2018	03/2026 (-)	513.99 (513.99)	229.01	51
60	JHARKHAND-LAIYO OCP (Ministry of Coal) (400352)	Jharkhand	08/2020	03/2031 (-)	764.57 (764.57)	145.81	29
61	MOONIDIH XV SEAM UG (Ministry of Coal) (400425)	Jharkhand	08/2011	03/2019 05/2026	1230.27 (1230.27)	626.63	81
62	2.5 MTPA PATHERDIH NLW WASHERY (Ministry of Coal) (611017)	Jharkhand	04/2016	04/2018 03/2026	334.27 (334.27)	140.51	48
63	AMALAGAMATED NTST KUJAMA OCP 8.5MTY (Ministry of Coal) (611864)	Jharkhand	01/2023	03/2030 (-)	4011.85 (4011.85)	398.5	28
64	MURAI DIH UG PROJECT (Ministry of Coal) (613808)	Jharkhand	02/2011	04/2014 12/2026	339.87 (339.87)	191	70
65	TAPIN SOUTH EXPN (Ministry of Coal) (615349)	Jharkhand	11/2020	03/2028 (-)	230.41 (230.41)	22.02	20
66	SIRKA OC (Ministry of Coal) (615822)	Jharkhand	05/2020	03/2028 (-)	222.82 (222.82)	139.31	53
67	TETARIAKHAR OC (Ministry of Coal) (615843)	Jharkhand	11/2019	03/2025 03/2027	243.52 (243.52)	44.64	30
68	CHUPERBHITA SIMLONG OCP MDO 6 MTY (Eastern Coal Fields Limited [ECL]) (616225)	Jharkhand	12/2023	03/2037 (-)	979.08 (979.08)	0	0
69	JARANGDIH EXPN. OCP 1.5 MTY (CCL - CIL) (616236)	Jharkhand	02/2020	03/2029 (-)	414.37 (414.37)	85.6	33
70	BLOCK E OCP (Ministry of Coal) (616253)	Jharkhand	03/2024	03/2029 (-)	5850.83 (5850.83)	20.32	3
71	AMADAND OCP[4.0MTY] (South Eastern Coalfields Limited [SECL]) (400148)	Madhya Pradesh	03/2016	03/2021 03/2027	869.44 (869.44)	273.45	75
72	RAMPUR BATURA OCP [4.0MTY] (South Eastern Coalfields Limited [SECL]) (400152)	Madhya Pradesh	07/2019	03/2026 (-)	1248.93 (1248.93)	495.4	44
73	BLOCK B EXPANSION [3.5 TO 8.0 (Northern Coalfields Limited [NCL]) (400162)	Madhya Pradesh	07/2019	03/2023 03/2027	998.71 (998.71)	457.2	47
74	NIGAHI EXPANSION [15 TO 25 MTP (Northern Coalfields Limited [NCL]) (400321)	Madhya Pradesh	11/2020	03/2025 03/2028	1729.68 (1729.68)	804.11	48
75	KANCHAN OC EXP (South Eastern Coalfields Limited [SECL]) (613802)	Madhya Pradesh	12/2014	03/2026 (-)	371.04 (371.04)	144.61	47
76	JHIRIA WEST OCP [1.5 MTY] (South Eastern Coalfields Limited [SECL]) (613803)	Madhya Pradesh	01/2024	03/2026 (-)	366.94 (366.94)	34.05	41
77	RPR TAWA-III UG 0.84 MTY (Western Coalfields Limited [WCL]) (613804)	Madhya Pradesh	12/2021	03/2027 (-)	314.09 (314.09)	5.79	17
78	AMALGAMATED DHANKASA & JAMUNIA (Western Coalfields Limited [WCL]) (615185)	Madhya Pradesh	09/2022	03/2027 (-)	399.2 (399.2)	91.67	66
79	RPR OF VISHNUPURI UG TO OC (Western Coalfields Limited [WCL]) (615187)	Madhya Pradesh	11/2022	03/2029 (-)	220.62 (220.62)	0	11
80	URDHAN EXPANSION OC COST PLUS (Western Coalfields Limited [WCL]) (615194)	Madhya Pradesh	01/2023	03/2031 (-)	206.88 (206.88)	27.19	1
81	SHARDA UG MINE (Western Coalfields Limited [WCL]) (615195)	Madhya Pradesh	09/2023	03/2028 (-)	166.25 (166.25)	3.96	9
82	GANDHIGRAM UG MINE (Western Coalfields Limited [WCL]) (615206)	Madhya Pradesh	08/2019	03/2026 (-)	414.15 (414.15)	13.38	57
83	BHATADI EXPANSION OC (Western Coalfields Limited [WCL]) (400033)	Maharashtra	05/2022	03/2028 (-)	580.61 (580.61)	69.73	26
84	AMALGAMATED YEKONA I & YEKONA (Western Coalfields Limited [WCL]) (400177)	Maharashtra	08/2015	03/2025 03/2026	727.28 (727.28)	535.96	80
85	DINESH[MAKARDHOKRA-III] OC (Western Coalfields Limited [WCL]) (400178)	Maharashtra	02/2020	03/2027 (-)	822.88 (822.88)	621.73	35



All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
86	DHUPTALA OC [SASTI UG TO OC] <i>(Western Coalfields Limited [WCL])</i> (400353)	Maharashtra	10/2021	03/2028 (-)	711.01 (711.01)	80.61	17
87	SAONER UG MINE -1 EXPANSION 1. <i>(Western Coalfields Limited [WCL])</i> (615184)	Maharashtra	01/2022	03/2028 (-)	228.64 (228.64)	141.21	68
88	SASTI EXPANSION OPENCAST <i>(Western Coalfields Limited [WCL])</i> (615186)	Maharashtra	08/2020	03/2026 (-)	319.04 (319.04)	90.31	20
89	NEW MAJRI UG TO OC 3 MTY COST <i>(Western Coalfields Limited [WCL])</i> (615188)	Maharashtra	09/2022	03/2027 (-)	402.27 (402.27)	55.44	24
90	MAKARDHOKRA EXPN OC 4.9 MTY <i>(Western Coalfields Limited [WCL])</i> (615189)	Maharashtra	06/2022	03/2026 (-)	361.87 (361.87)	70.22	12
91	SINGHORI DEEP OC MIN 2.0 MTY <i>(Western Coalfields Limited [WCL])</i> (615190)	Maharashtra	05/2022	03/2029 (-)	335.75 (335.75)	26.79	6
92	GOKUL EXTENSION OC MINE <i>(Western Coalfields Limited [WCL])</i> (615192)	Maharashtra	04/2021	03/2026 (-)	309.58 (309.58)	40.06	8
93	KOLGAON EXPANSION DEEP OC MINE 0.80 MTY <i>(Western Coalfields Limited [WCL])</i> (615199)	Maharashtra	09/2023	03/2027 (-)	198.71 (198.71)	0.71	3
94	BALLARPUR NORTH WEST OC MINE <i>(Western Coalfields Limited [WCL])</i> (615330)	Maharashtra	12/2022	03/2029 (-)	360.81 (360.81)	0.02	4
95	GADEGAON OC 3 MTY <i>(Western Coalfields Limited [WCL])</i> (615331)	Maharashtra	10/2023	03/2030 (-)	497.41 (497.41)	0.08	0
96	GHONSA EXPANSION DEEP OC MINE <i>(Western Coalfields Limited [WCL])</i> (615914)	Maharashtra	03/2021	03/2029 (-)	184.71 (184.71)	11.48	6
97	AMLG GAURI PAUNI EXPANSION OC <i>(Western Coalfields Limited [WCL])</i> (615916)	Maharashtra	04/2024	03/2030 (-)	1225.21 (1225.21)	78.87	1
98	GAURIDEEP/GAURI CENTRAL OCP 7. <i>(Western Coalfields Limited [WCL])</i> (615917)	Maharashtra	06/2024	03/2030 (-)	973.07 (973.07)	0.24	0
99	RPR OF BHANEGAON OC <i>(Western Coalfields Limited [WCL])</i> (615918)	Maharashtra	09/2022	03/2028 (-)	405.2 (405.2)	12.36	8
100	N. EXTN. MUNGOLI NIRGUDA D OCP <i>(Western Coalfields Limited [WCL])</i> (615919)	Maharashtra	06/2024	03/2030 (-)	1024.91 (1024.91)	168.59	0
101	NILJAI EXPANSION DEEP OCP <i>(Western Coalfields Limited [WCL])</i> (615982)	Maharashtra	08/2016	03/2022 03/2026	319.75 (319.75)	367.6	79
102	UKNI DEEP OC MINE -COST PLUS <i>(Western Coalfields Limited [WCL])</i> (616044)	Maharashtra	01/2019	03/2021 03/2026	237.06 (237.06)	165.57	87
103	AMALGAMATED INDER-KAMPTEE DEEP OC <i>(Western Coalfields Limited [WCL])</i> (616050)	Maharashtra	09/2018	03/2024 03/2026	235.9 (235.9)	237.12	98
104	ADASA UG TO OC MINE <i>(Western Coalfields Limited [WCL])</i> (616223)	Maharashtra	11/2018	03/2024 03/2026	316 (316)	308.84	86
105	AMAL GONDEGAON GHATROHANA EXPN <i>(Western Coalfields Limited [WCL])</i> (616229)	Maharashtra	09/2024	03/2030 (-)	668.54 (668.54)	1.18	0
106	WAGHODA UG MINE [1.02 MTY] <i>(Western Coalfields Limited [WCL])</i> (617233)	Maharashtra	01/2025	03/2030 (-)	379.3 (379.3)	0	0
107	KOLARPIMPRI EXPANSION OC [2.5 MTY] <i>(Western Coalfields Limited [WCL])</i> (617278)	Maharashtra	02/2025	03/2030 (-)	630.37 (630.37)	0	0
108	Master Plan for Jharia and Raniganj Coalfields <i>(Bharat Coking Coal Limited [BCCL])</i> (400313)	Multi-States (Jharkhand, West Bengal)	08/2009	08/2019 12/2028	2661.73 (2661.73)	788.85	43
109	BINA KAKRI AMALGAMATION EXPANS <i>(Northern Coalfields Limited [NCL])</i> (400369)	Multi-States (Madhya Pradesh, Uttar Pradesh)	08/2020	03/2024 03/2027	836.42 (836.42)	786.99	89
110	KHADIA EXPANSION [10 TO 16 MTP <i>(Northern Coalfields Limited [NCL])</i> (615183)	Multi-States (Madhya Pradesh, Uttar Pradesh)	06/2021	03/2025 03/2027	491.67 (491.67)	230.32	45
111	SUBHADRA OCP <i>(Mahanadi Coalfields Limited [MCL])</i> (400165)	Odisha	05/2021	04/2032 (-)	1693.81 (1693.81)	1321.15	42
112	SIARMAL OCP <i>(Mahanadi Coalfields Limited [MCL])</i> (400166)	Odisha	02/2021	03/2029 (-)	5194.95 (5194.95)	3456.05	55
113	BALARAM EXPANSION OCP <i>(Mahanadi Coalfields Limited [MCL])</i> (400183)	Odisha	08/2020	03/2029 (-)	3504.21 (3504.21)	1028.92	52
114	GOPALJI KANIHA OCP [10 TO 30 M <i>(MCL - CIL)</i> (400185)	Odisha	04/2022	03/2030 (-)	8416.19 (6107.87)	1708.88	17
115	INTEGRATED LAKHANPUR-BELPAHAR- <i>(Mahanadi Coalfields Limited [MCL])</i> (400187)	Odisha	05/2018	03/2027 (-)	2434.75 (2434.75)	1813.26	69
116	BHARATPUR RE-ORGANIZATION OCP <i>(Mahanadi Coalfields Limited [MCL])</i> (400392)	Odisha	11/2018	03/2029 (-)	2838.86 (2838.86)	1748.41	47

All Ongoing Projects

AUGUST 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
117	BASUNDHARA WEST EXTENSION OPEN (MCL - CIL) (615193)	Odisha	05/2014	03/2019 03/2029	479.15 (479.15)	281.01	64
118	Naini Coal Mine (Singareni Collieries Company Limited [SCCL]) (615857)	Odisha	03/2020	03/2026 (-)	494.3 (494.3)	491.33	80
119	INTEGRATED KULDA GARJANBAHAL O (Mahanadi Coalfields Limited (MCL)) (616226)	Odisha	04/2023	03/2033 (-)	3563.5 (3563.5)	540.62	4
120	BHUBANESWARI EXPN OCP 50 MTY (MCL - CIL) (616231)	Odisha	03/2024	03/2033 (-)	5366.27 (5366.27)	465.31	14
121	HINGULA II OC EXPN PH III 15 M (MCL - CIL) (616232)	Odisha	11/2022	03/2029 (-)	1561.85 (1561.85)	269.61	23
122	BALABHADRA OCP (MCL - CIL) (616233)	Odisha	04/2023	03/2030 (-)	978.44 (978.44)	211.37	11
123	Jawahar Khani Open Cast Mine (Singareni Collieries Company Limited [SCCL]) (615818)	Telangana	12/2021	03/2025 03/2027	297.88 (297.88)	46.39	20
124	Kalyanikhani Opencast Project (Singareni Collieries Company Limited [SCCL]) (615858)	Telangana	05/2017	03/2026 (-)	384.32 (384.32)	281.83	75
125	Kakathiya Khani Opencast - III Project Phase - I (Singareni Collieries Company Limited [SCCL]) (615859)	Telangana	05/2017	03/2026 (-)	413.84 (413.84)	397.55	79
126	Godavarikhani Coal Mine - 5 (Singareni Collieries Company Limited [SCCL]) (615860)	Telangana	05/2019	03/2025 03/2026	607.04 (607.04)	188.15	71
127	Indaram Opencast Project (Singareni Collieries Company Limited [SCCL]) (615861)	Telangana	12/2022	03/2025 03/2026	424.81 (424.81)	402.64	80
128	Goleti Opencast Mine (Singareni Collieries Company Limited [SCCL]) (615862)	Telangana	08/2021	03/2026 (-)	345.6 (345.6)	74.59	20
129	Venkatesh Khani Coal Mine (Singareni Collieries Company Limited [SCCL]) (615863)	Telangana	06/2020	03/2026 (-)	484.5 (484.5)	460.67	95
130	Ramagundam OC-II Extension Project (Singareni Collieries Company Limited [SCCL]) (615864)	Telangana	06/2015	03/2026 (-)	489.62 (489.62)	405.54	77
131	Kakatiyakhani OC - 2 Project (Singareni Collieries Company Limited [SCCL]) (615865)	Telangana	09/2017	03/2025 03/2026	442.42 (442.42)	205	63
132	MOHANPUR EXPANSION OC -PHASE II (Eastern Coal Fields Limited [ECL]) (400173)	West Bengal	11/2020	03/2026 (-)	888.99 (888.99)	93	30
133	BONJEMEhari EXPANSION OCP (Eastern Coal Fields Limited [ECL]) (400180)	West Bengal	08/2021	03/2026 03/2026	570.11 (570.11)	81.95	16
134	NAKRAKONDA KUMARDIH- B OCP (Eastern Coal Fields Limited [ECL]) (400181)	West Bengal	08/2018	03/2029 (-)	502.68 (502.67)	67.61	26
135	SIDULI [OC & UG] (ECL - CIL) (400182)	West Bengal	05/2018	03/2027 (-)	535.18 (535.17)	5.05	14
136	TILABONI UG (Eastern Coal Fields Limited [ECL]) (400186)	West Bengal	03/2023	03/2029 03/2029	749.08 (749.08)	52.18	10
137	JHANJRA EXPANSION UG (Eastern Coal Fields Limited [ECL]) (400312)	West Bengal	04/2020	03/2029 (-)	1210.12 (1210.12)	527.67	41
138	SONEPUR BAZARI EXPANSION OCP [12 MTY] (Eastern Coal Fields Limited [ECL]) (400315)	West Bengal	07/2021	03/2029 (-)	5365.88 (5365.88)	565.26	17
139	2.0 MTPA BHOJUDIH NLW WASHERY (Ministry of Coal) (611016)	West Bengal	03/2019	09/2020 10/2025	384.57 (384.57)	353.21	97
140	ITAPARA OCP (Eastern Coal Fields Limited [ECL]) (612816)	West Bengal	12/2023	03/2030 (-)	929.1 (929.1)	67.6	7
141	SHYAMSUNDARPUR UG INCLUDING SA (Eastern Coal Fields Limited [ECL]) (613793)	West Bengal	04/2020	03/2026 (-)	483.65 (483.65)	59.04	12
142	PARASEA-BELBAID UG PROJECT (Eastern Coal Fields Limited [ECL]) (613794)	West Bengal	01/2023	03/2028 (-)	389.1 (389.1)	131.42	17
143	PARASCOLE JAMBAD OCP (Eastern Coal Fields Limited [ECL]) (616230)	West Bengal	11/2024	03/2037 (-)	1193.55 (1193.55)	9.46	0
Total (117)					166806.82	53439.3	
Electricity Generation							
144	50 MW Wind Power Project (NLC India Limited [NLCIL]) (617299)	Gujarat	02/2024	06/2025 01/2026	383.84 (383.84)	303.5	41
145	NLC Talabira Thermal Power Project (NLC India Limited [NLCIL]) (400231)	Odisha	01/2024	03/2030 (-)	27212.96 (27213)	1953.52	1
146	300 MW SPP part of 510 MW CPSU scheme (NLC India Limited [NLCIL]) (612819)	Rajasthan	03/2023	09/2024 09/2025	1813 (1813)	874.14	70

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
147	50 MW Solar PP Minedout Area (<i>NLC India Limited [NLCIL]</i>) (615327)	Tamil Nadu	02/2024	03/2025 09/2025	218.03 (218.03)	161.73	50
148	Ghatampur Thermal Power Plant 3 X 660 MW (<i>NLC India Limited [NLCIL]</i>) (400259)	Uttar Pradesh	08/2016	11/2020 10/2025	17237.8 (21780.9)	20269.54	92
Total (5)					46865.63	23562.43	
Railways							
149	Dharamjaigarh-Korba (<i>Railway</i>) (400203)	Chhattisgarh	03/2017	12/2026 08/2026	1686.22 (1686.22)	347.96	41
150	Shivpur-Kathautia New Rail [BG] Line [49 km] [Package II of Tori-Shivpur-Kathautia line] (<i>Ministry of Coal</i>) (400416)	Jharkhand	05/2022	06/2025 (-)	1799.64 (1799.64)	1293.71	60
Total (2)					3485.86	1641.67	
Ministry of Power							
Coal							
151	Tubed Coal Mine (<i>Damodar Valley Corporation</i>) (400192)	Jharkhand	10/2016	05/2026 05/2026	1581 (1581)	596.94	34
152	Badam Coal Mining project of NTPC (<i>National Thermal Power Corporation [NTPC]</i>) (603293)	Jharkhand	09/2019	12/2056 04/2027	502 (784)	313.88	59
Total (2)					2083	910.82	
Electricity Generation							
153	Dibang Multipurpose Project (<i>National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]</i>) (602182)	Arunachal Pradesh	02/2023	02/2032 02/2032	31876.39 (31876.4)	3553.9	16
154	240MW Heo HE Project (<i>North Eastern Electric Power Corporation Limited</i>) (611698)	Arunachal Pradesh	05/2025	07/2029 (-)	1938.85 (1938.85)	49.31	3
155	186 MW Tato-I H E Project (<i>North Eastern Electric Power Corporation Limited</i>) (611699)	Arunachal Pradesh	05/2025	07/2029 (-)	1750.07 (1750.07)	102.79	2
156	Buxar Thermal Power Project [1320 MW] (<i>Satluj Jal Vidyut Nigam [SJVN] Thermal Limited</i>) (602579)	Bihar	06/2019	01/2024 12/2025	10439.09 (13756.6)	12148.46	92
157	Lara Super Thermal Power Project Stage-II [2 x 800 MW] (<i>National Thermal Power Corporation [NTPC]</i>) (611930)	Chhattisgarh	08/2023	06/2028 (-)	15530 (15530)	2480	16
158	Sipat Super Thermal Power Project, Stage-III [1x800 MW] (<i>National Thermal Power Corporation [NTPC]</i>) (617188)	Chhattisgarh	09/2024	09/2029 (-)	9791 (9791)	0	0
159	Bagodara Solar Power Project (<i>Satluj Jal Vidyut Nigam [SJVN] Thermal Limited</i>) (709747)	Gujarat	05/2021	12/2025 12/2025	339.35 (339.35)	317.59	51
160	Dhauilasidh Hydro Electric Project [66 MW] (<i>Satluj Jal Vidyut Nigam [SJVN] Thermal Limited</i>) (602582)	Himachal Pradesh	05/2021	11/2025 03/2027	687.97 (1511.87)	927.3	68
161	Luhri Stage-I Hydro Electric Project [210 MW] (<i>Satluj Jal Vidyut Nigam [SJVN] Thermal Limited</i>) (602593)	Himachal Pradesh	11/2020	01/2026 10/2029	1810.56 (3584.53)	1751.6	51
162	382 MW Sunni Dam HEP (<i>Satluj Jal Vidyut Nigam [SJVN] Thermal Limited</i>) (602633)	Himachal Pradesh	04/2018	03/2027 (-)	2615 (2615)	495.57	0.5
163	Sunni Dam Hydro Electric Project [382 MW] (<i>Satluj Jal Vidyut Nigam [SJVN] Thermal Limited</i>) (611586)	Himachal Pradesh	01/2023	04/2028 12/2029	2614.51 (4540.71)	962.66	29
164	Pakal Dul [Drangdhuran] Hydroelectric Project, 1000 MW (<i>National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]</i>) (602525)	Jammu and Kashmir	02/2018	04/2020 12/2026	8112.12 (12728)	7238.73	72
165	Kiru HE Project (<i>National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]</i>) (602532)	Jammu and Kashmir	03/2019	09/2023 12/2026	4287.59 (5409)	3157.49	68
166	Rattle HE Project - 850 MW, Rattle Hydroelectric Power Corporation Limited. (<i>National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]</i>) (602535)	Jammu and Kashmir	02/2021	02/2026 08/2029	5281.94 (5281.94)	1009.79	24
167	Kwar HE Project (<i>National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]</i>) (605155)	Jammu and Kashmir	05/2022	11/2026 03/2028	4526.12 (4526.12)	1119.59	23
168	Patratu Thermal Power Station Expansion Project Phase-I [3x800 MW] (<i>National Thermal Power Corporation [NTPC]</i>) (400261)	Jharkhand	11/2017	03/2023 11/2026	17112 (20302)	17475	85
169	Koderma Thermal Power Station Phase II [2X800 MW] At Koderma, Jharkhand (<i>Damodar Valley Corporation</i>) (611509)	Jharkhand	11/2024	03/2029 (-)	14358 (14358)	1131.57	3
170	Subansiri Lower HE Project [2000 MW] (<i>National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]</i>) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003	09/2010 05/2026	6285.33 (26075.5)	24880.95	96
171	Talcher Thermal Power Station Stage III [2 x 660 MW] Expansion (<i>National Thermal Power Corporation [NTPC]</i>) (602961)	Odisha	09/2022	05/2027 03/2028	11843.75 (12543)	4161.68	32
172	BIKANER SOLAR POWER PROJECT (<i>Satluj Jal Vidyut Nigam [SJVN] Thermal Limited</i>) (709748)	Rajasthan	05/2022	04/2024 12/2025	5491.89 (5491.89)	4805.16	84
173	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (<i>National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]</i>) (602181)	Sikkim	03/2019	03/2024 12/2027	5748.04 (5748.04)	4576.93	69

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
174	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] -A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (605156)	Sikkim	03/2021	05/2024 12/2025	938.29 (1828.11)	1584.13	91
175	Khurja super Thermal Power Plant [2X660 MW] (THDC India Limited) (602194)	Uttar Pradesh	08/2019	02/2024 09/2025	11089.42 (13276.2)	12772.21	97
176	Singrauli Super Thermal Power Project, Stage-III [2x800 MW] (National Thermal Power Corporation [NTPC]) (612142)	Uttar Pradesh	03/2024	02/2030 (-)	17195 (17195)	1739	9
177	Tapovan-Vishnugad HEP [4x130 MW] (National Thermal Power Corporation [NTPC]) (602185)	Uttarakhand	11/2006	03/2013 04/2029	2978 (10907.3)	7195.58	77
178	Tehri Pumped Storage Plant Project [4x250 MW] (THDC India Limited) (602193)	Uttarakhand	06/2011	06/2022 11/2025	4825.6 (8339)	8064.9	98
179	Vishnugad Pipalkoti Hydro Electric Project [444 MW] (THDC India Limited) (602195)	Uttarakhand	01/2014	12/2022 03/2027	3860.35 (6823.72)	5101.06	72
180	Raghunathpur Thermal Power Station Phase II [2X660 MW] at Raghunathpur, Purulia, West Bengal (Damodar Valley Corporation) (400062)	West Bengal	02/2025	06/2029 (-)	17673 (17673)	1192.71	1
181	Rammam-III HEPP [3x40 MW] (National Thermal Power Corporation [NTPC]) (602184)	West Bengal	09/2014	09/2019 03/2029	1381.84 (1381.84)	1281.85	47
182	Installation of FGD for 4x210 & 2x250 MW MTPS U 1-6 (Damodar Valley Corporation) (602538)	West Bengal	02/2021	01/2024 12/2025	1037 (1106)	1092.27	92
Total (30)					223418.07	132369.78	
Transmission & Distribution							
183	Transmission Scheme for Solar Energy Zone in Ananthpuram 2500MW and Kurnool 1000MW (Power Grid Corporation of India Limited [POWERGRID]) (611967)	Andhra Pradesh	09/2023	09/2025 04/2026	1248.69 (1248.69)	860.97	82
184	Augmentation of 1x1500 MVA 3rd 765/400 kV transformation capacity at Kurnool New Substation (Power Grid Corporation of India Limited [POWERGRID]) (612856)	Andhra Pradesh	12/2023	09/2025 11/2025	163.61 (163.61)	60.53	42
185	Transmission system strengthening at Kurnool- III PS for integration of additional RE generation projects [POWERGRID Kurnool III PS RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617183)	Andhra Pradesh	03/2025	12/2027 (-)	2886 (2886)	117.86	0
186	Western Region Expansion Scheme-XXV (Power Grid Corporation of India Limited [POWERGRID]) (611737)	Chhattisgarh	02/2023	11/2023 12/2025	385.84 (385.84)	378.17	97
187	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan 8.1 GW under Phase II- Part- G1 (Power Grid Corporation of India Limited [POWERGRID]) (608301)	Delhi	02/2022	09/2023 11/2025	359.47 (359.47)	330.91	93
188	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part B (Power Grid Corporation of India Limited [POWERGRID]) (611656)	Gujarat	03/2023	03/2025 10/2025	1167.55 (1167)	1050.41	93
189	Transmission scheme for evacuation of 4.5GW RE injection at Khavda PS under Phase II- Part C (Power Grid Corporation of India Limited [POWERGRID]) (611657)	Gujarat	03/2023	03/2025 11/2025	2820.99 (2820.99)	2570.25	84
190	Establishment of Khavda Pooling Station-2 KPS2 in Khavda RE Park KPS2 TRANSMISSION SYSTEM LIMITED (Power Grid Corporation of India Limited [POWERGRID]) (611660)	Gujarat	03/2023	12/2024 10/2025	966.79 (966.79)	904.52	95
191	Transmission system for Evacuation of Additional 7 GW RE power from Khavda RE park under Phase-III Part B [Vataman Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (612139)	Gujarat	12/2023	12/2025 06/2026	3751.82 (3751.82)	1575.72	22
192	Transmission System for Evacuation of Power from potential Renewable Energy zone in Khavda Area of Gujarat under Phase IV [7 GW] Part E3 (Power Grid Corporation of India Limited [POWERGRID]) (612151)	Gujarat	07/2023	07/2025 12/2025	334 (334)	73.48	30
193	Transmission System for Evacuation of Power from Potential Energy Renewable Zone in Khavda Area of Gujarat under Ph-IV [7GW] Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (612855)	Gujarat	05/2024	05/2026 02/2026	679 (679)	97.23	19
194	Augmentation of Transformation Capacity at jam Khambhaliya PS [GIS] [SPV Name POWERGRID Jam Khambhaliya Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615342)	Gujarat	10/2024	07/2026 (-)	329 (329)	10.07	1
195	Provision of Dynamic Reactive Compensation at Khavda pooling Station 1 [KPS1] and Khavda Pooling station 3 [KPS3] (Power Grid Corporation of India Limited [POWERGRID]) (615343)	Gujarat	11/2024	11/2026 (-)	501 (501)	6.01	1
196	Transmission System for Evacuation of Power from Potential Renewable Energy Zone in Khavda area of Gujarat under Phase-IV [7GW] Part B [SPV Name POWERGRID South Olpad Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615345)	Gujarat	10/2024	10/2026 (-)	4766 (4766)	564.77	7
197	Augmentation of Transformation Capacity at KPS1 [GIS] and KPS2 [GIS] [Phase-V Part B1 and Part B2 Scheme] [SPV Name- POWERGRID KPS1 and 2 Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617069)	Gujarat	02/2025	02/2027 (-)	466 (466)	13.99	1

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
198	Augmentation of Banaskantha [Raghanesda] PS [GIS] [POWERGRID Banaskantha Transco Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617182)	Gujarat	03/2025	03/2027 (-)	172 (172)	7.27	3
199	Implementation of LILO of both circuits of 400KV vindhyachal PS-Sasan D/C Line at Hindalco Switchyard (Power Grid Corporation of India Limited [POWERGRID]) (617272)	Haryana	06/2024	12/2026 (-)	370 (370)	3.7	1
200	Transmission system for evacuation of Power from Pakaldul HEP in Chenab Valley HEPs - LTA System (Power Grid Corporation of India Limited [POWERGRID]) (608302)	Jammu and Kashmir	02/2022	04/2025 09/2025	318.12 (318.12)	287.31	99
201	Transmission Scheme for evacuation of Power from Rattle HEP [850 MW] & kiru [624 MW] Part B (Power Grid Corporation of India Limited [POWERGRID]) (617179)	Jammu and Kashmir	07/2024	07/2026 (-)	218.6 (218.6)	1.01	0
202	Transmission Scheme for Integration of Renewable Energy Zone [Phase II] in Koppal II [Phase A&B] and gadag II[Phase A] in Karnataka [POWERGRID KOPPAL GADAG TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (612140)	Karnataka	12/2023	12/2025 03/2026	2889.39 (2889.39)	1332.21	46
203	System Strengthening at Koppal-II and GadagII for integration of RE generation projects [SPV Name POWERGRID Koppal Gadag Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616672)	Karnataka	01/2025	06/2027 (-)	1354 (1354)	17.73	0
204	Augmentation of Transformation Capacity by 3x500 MVA, 400/220 KV ICTS [6th-8th] and 1x1500 MVA, 765/400 KV ICT [4th] at Bidar PS [SPV Name- POWERGRID Bidar Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617068)	Karnataka	02/2025	06/2027 (-)	288 (288)	6.79	0
205	Transmission Scheme for integration of Davanagere/ Chitradurga and Bellary REZ in Karnataka [POWERGRID Chitradurga Bellary REZ Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617184)	Karnataka	03/2025	09/2027 (-)	3453 (3453)	33.14	0
206	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5GW] [Jaisalmer/Barmer Complex] Part H1 [POWERGRID KURAWAR TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615344)	Madhya Pradesh	10/2024	10/2026 (-)	3674 (3674)	495.18	14
207	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part C [SPV Name POWERGRID Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615346)	Madhya Pradesh	08/2024	08/2026 (-)	2708 (2708)	812.4	35
208	Transmission System for evacuation of power from Mahan Energen Limited Generating Station in Madhya Pradesh [SPV Name - POWERGRID MEL Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617279)	Madhya Pradesh	06/2025	12/2027 (-)	558 (558)	16.74	0
209	Transmission System for Evacuation of power from Potential RE Zone in Khavda Area of Gujarat under phase IV 7GW-Part E4 (Power Grid Corporation of India Limited [POWERGRID]) (611966)	Maharashtra	11/2023	07/2025 12/2025	224.41 (224.41)	24.64	10
210	Transmission System for Integration of Kurnool-IV REZ Phase-I [for 4.5 GW] [POWERGRID Kurnool-IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617185)	Multi-States (Andhra Pradesh, Karnataka)	03/2025	03/2027 (-)	5550 (5550)	281	0
211	Transmission System for Kurnool Wind Energy Zone/ Solar Energy Zone Part-A and Part-B (Power Grid Corporation of India Limited [POWERGRID]) (900808)	Multi-States (Andhra Pradesh, Telangana)	03/2023	11/2024 12/2025	3546.94 (3546.94)	3192.25	95
212	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Arunachal Pradesh, Sikkim)	01/2016	12/2018 03/2027	4754.42 (9129.32)	7462.2	81
213	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	03/2016	12/2018 12/2025	5111.33 (6700)	5277.24	96
214	Eastern Region Expansion Scheme-43 [ERES-43] (Power Grid Corporation of India Limited [POWERGRID]) (617271)	Multi-States (Bihar, Odisha, West Bengal)	09/2024	03/2026 (-)	342.69 (342.69)	0.6	0
215	Eastern Region Expansion Scheme-44 [ERES-44] (Power Grid Corporation of India Limited [POWERGRID]) (617270)	Multi-States (Bihar, West Bengal)	11/2024	05/2026 (-)	408.94 (408.94)	0.3	0
216	Transmission Network Expansion in Gujarat to increase its ATC from ISTS Part B (Power Grid Corporation of India Limited [POWERGRID]) (400005)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	07/2022	06/2023 12/2025	4546.26 (4546.26)	4172.96	93
217	Transmission System Strengthening Scheme for evacuation of power from SEZ in Rajasthan 8.1 GW under Phase II Part G (Power Grid Corporation of India Limited [POWERGRID]) (608922)	Multi-States (Delhi, Haryana, Rajasthan)	05/2022	11/2023 11/2025	1666 (2218)	2129.28	95
218	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part J (Power Grid Corporation of India Limited [POWERGRID]) (611735)	Multi-States (Delhi, Rajasthan)	12/2022	03/2025 04/2026	331 (331)	82.72	29
219	Transmission Scheme for Evacuation of power from REZ in Rajasthan [20 GW] under Phase-III Part D [Sikar Khetri Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612132)	Multi-States (Delhi, Rajasthan)	02/2024	08/2025 05/2026	2000 (2000)	1380.2	62

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
220	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV Name POWERGRID West Central Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615347)	Multi-States (Gujarat, Maharashtra)	11/2024	05/2029 (-)	24819 (24819)	1796.14	1
221	Transmission system for evacuation of power from Rajasthan REZ Ph-IV [Part-3/6GW] [Bikaner complex] Part A [SPV Name POWERGRID Bikaner IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615339)	Multi-States (Haryana, Punjab, Rajasthan)	11/2024	11/2026 (-)	5969 (5969)	218.47	5
222	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3/ 6 GW] [BIKANER COMPLEX] PART B [SPV Name POWERGRID Siwani Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615340)	Multi-States (Haryana, Rajasthan)	11/2024	11/2026 (-)	5357 (5357)	267.85	9
223	Transmission System for Strengthening of Srinagar-Leh Tr. System (Power Grid Corporation of India Limited [POWERGRID]) (606781)	Multi-States (Jammu and Kashmir, Ladakh)	03/2022	12/2024 10/2025	288.71 (288.71)	207.8	75
224	Transmission Scheme for Solar Energy Zone in Bidar [2500 MW], Karnataka [Bidar Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612138)	Multi-States (Karnataka, Telangana)	02/2024	02/2026 (-)	2147.62 (2147.62)	1144.89	61
225	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part D [SPV Name POWERGRID Beawar Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615333)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024	08/2026 (-)	2227 (2227)	622.89	20
226	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part E [SPV Name POWERGRID Mewar Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615334)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024	08/2026 (-)	3251 (3251)	780.24	18
227	Rajasthan REZ Ph-V [Part-1- 4 GW] [Sirohi/Nagaur] Complex [Rajasthan V Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617186)	Multi-States (Madhya Pradesh, Rajasthan)	03/2025	03/2027 (-)	5028 (5028)	203.2	1
228	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part D [Neemrana Bareilly Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612133)	Multi-States (Rajasthan, Uttar Pradesh)	12/2023	12/2025 06/2026	2056 (2056)	1356.96	58
229	Transmission System for evacuation of Power from Rajasthan REZ Ph-IV [Part-4 3.5 GW] Part A [SPV name POWERGRID Ghiror Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616670)	Multi-States (Rajasthan, Uttar Pradesh)	12/2024	12/2026 (-)	5846 (5846)	293.47	4
230	Transmission system strengthening scheme for evacuation of power from solar energy zones in Rajasthan[8.1 GW] under phase-II- Part E (Power Grid Corporation of India Limited [POWERGRID]) (611659)	Rajasthan	03/2023	09/2024 10/2025	1433.28 (1433)	1359.63	95
231	Transmission System for Evacuation of Power from REZ in Rajasthan 20GW under Phase III- Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (611947)	Rajasthan	11/2023	06/2025 12/2025	428.3 (428.3)	179.89	51
232	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part H (Power Grid Corporation of India Limited [POWERGRID]) (611948)	Rajasthan	10/2023	04/2025 12/2025	2211.29 (2211.29)	1817.46	80
233	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part C1 (Power Grid Corporation of India Limited [POWERGRID]) (611949)	Rajasthan	10/2023	04/2025 10/2025	1796.02 (1796.02)	1247.87	83
234	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part B1 (Power Grid Corporation of India Limited [POWERGRID]) (611950)	Rajasthan	09/2023	04/2025 12/2025	2190.54 (2190.54)	1870.72	83
235	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part E1 (Power Grid Corporation of India Limited [POWERGRID]) (611951)	Rajasthan	08/2023	02/2025 09/2025	688.74 (688.74)	587.42	96
236	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part A [Bikaner Neemrana Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612134)	Rajasthan	12/2023	12/2025 03/2026	2998.34 (2998.34)	1703.11	51
237	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW][Jaisalmer/Barmer Complex] Part B [SPV Name POWERGRID Sirohi Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615332)	Rajasthan	08/2024	08/2026 (-)	3279 (3279)	688.59	21
238	Transmission System Strengthening for Interconnections of Bhadla-III & Bikaner III Complex [SPV Name POWERGRID BHADLA BIKANER TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615335)	Rajasthan	08/2024	08/2026 (-)	1382 (1382)	41.46	4
239	Additional Transmission System for evacuation of Power from Bhadla-III PS as part of Rajasthan REZ Phase III Scheme [20 GW] [SPV Name POWERGRID Bhadla-III Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615337)	Rajasthan	08/2024	02/2026 (-)	369 (369)	58.26	16
240	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BARMER COMPLEX] PART F [SPV Name POWERGRID BARMER I TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615338)	Rajasthan	11/2024	11/2026 (-)	2735 (2735)	82.05	8
241	Augmentation at Fatehgarh-II PS, Fatehgarh-IV PS [Section-II] and Barmer-I PS [POWERGRID Fatehgarh Barmer Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617181)	Rajasthan	03/2025	12/2026 (-)	404 (404)	8.04	0

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
242	Transmission System under ISTS for evacuation of Power from Kudankulam Unit-3&4 [2x1000 MW] [SPV Name POWERGRID Kudankulam Tarnsmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616671)	Tamil Nadu	01/2025	12/2026 12/2026	548 (548)	14.68	6
243	Transmission System for Strengthening to facilitate evacuation of power from Bhadla/Bikaner Complex (Power Grid Corporation of India Limited [POWERGRID]) (617269)	Uttar Pradesh	12/2024	06/2026 (-)	212.81 (212.81)	0.2	0
	Total (61)				142976.51	52183.05	
	Ministry of Housing & Urban Affairs						
	Construction						
244	C/o 184 MS Flats for Hon'ble MPs at BKS Marg, New Delhi (Central Public Works Department [CPWD]) (617282)	Delhi	05/2022	05/2025 08/2025	646.53 (646.52)	533.12	99
	Total (1)				646.53	533.12	
	Inland Waterways						
245	Chennai Metro Rail Phase-II Development Project (Chennai Metro Rail Limited [CMRL]) (702668)	Tamil Nadu	11/2020	08/2029 (-)	63246 (63246)	26410.15	45
	Total (1)				63246	26410.15	
	Real Estate						
246	Integrated Command control Center [ICCC] - Construction and Development of Integrated Command Control Center with Security, Surveillance, ITMS, Connecting Port, Ship Service, Smart Solid Waste Management, Smart Public Transport System (ministry of housing and urban affairs) (707229)	Andaman & Nicobar	11/2021	05/2023 (-)	209.88 (209.88)	0	70
247	Redevelopment of Seven General Pool Residential Accommodation [GPRA] Colonies in Delhi (National Buildings Construction Corporation [NBCC]) (400188)	Delhi	05/2018	12/2025 12/2025	32850 (32850)	0	0
248	Rehabilitation in Junavadaj Area Smart City Project (ministry of housing and urban affairs) (701719)	Gujarat	06/2016	07/2022 (-)	539 (539)	39.63	50
249	Green Building Development Project (ministry of housing and urban affairs) (701766)	Uttarakhand	08/2019	11/2023 (-)	150.97 (150.97)	18.95	31
	Total (4)				33749.85	58.58	
	Urban Public Transport						
250	Bhopal Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702625)		11/2018	11/2022 06/2028	6941.4 (6941.4)	3164.15	43
251	Patna Metro Rail Project (Patna Metro Rail Corporation Ltd. [PMRCL]) (702627)	Bihar	02/2019	02/2024 06/2027	13365.77 (13365.8)	4039.77	40.07
252	Delhi Metro Rail Phase-IV [2 Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (617207)	Delhi	03/2024	03/2029 (-)	8399.81 (8399.81)	5.58	0
253	DMRTS Phase - IV [3 Priority Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (702632)	Delhi	07/2019	03/2025 03/2026	24948.65 (24948.7)	15785.39	69
254	Surat Metro Rail Project (Gujarat Metro Rail Corporation Limited [GMRCL]) (702630)	Gujarat	04/2019	03/2024 06/2026	12020.32 (12020.3)	7595.47	70
255	Ahmedabad Metro Rail Project, Phase-II (Gujarat Metro Rail Corporation Limited [GMRCL]) (702631)	Gujarat	03/2019	03/2024 12/2025	5384.17 (5384.17)	4180.43	88
256	Ahmedabad Metro Rail Project [Phase-I] (Gujarat Metro Rail Corporation Limited [GMRCL]) (702639)	Gujarat	02/2015	03/2018 10/2025	10773 (12924.5)	12174.41	99
257	Construction of Bangalore Metro Rail Project Phase 2. (Bengaluru Metro Rail) (702635)	Karnataka	02/2016	03/2021 09/2026	26405.14 (30695.1)	29477.97	94
258	Construction Bangalore Metro Rail Project Phase-2A & 2B (Bengaluru Metro Rail) (702665)	Karnataka	01/2019	06/2026 06/2026	14788.1 (14788.1)	8424.54	53
259	Kochi Metro Rail Phase 2 Development Project (CSPCC Projects) (702664)	Kerala	11/2022	11/2026 11/2026	1957.05 (1957.05)	329.94	12
260	Indore Metro Rail Project (Madhya Pradesh Metro Rail Co Limited [MPMRCL]) (702626)	Madhya Pradesh	11/2018	11/2022 12/2028	7500.8 (7500.8)	3931.4	55
261	PCMC To Nigdi- Extension Of North South Corridor Of Phase-1 (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617225)	Maharashtra	10/2023	01/2027 (-)	910.18 (910.18)	119.88	22
262	Pune Metro Phase-1 Extension line towards south from Swargate to Katraj (Maharashtra Metro Rail Corporation Limited [MMRCL]) (617226)	Maharashtra	09/2024	03/2029 (-)	2954.53 (2954.53)	19.61	3
263	New Suburba Station Development Project (ministry of housing and urban affairs) (701745)	Maharashtra	03/2019	07/2022 (-)	262.76 (262.76)	17.62	6
264	Kalyan Station Precinct Imporvement Project (ministry of housing and urban affairs) (701991)	Maharashtra	07/2020	07/2023 (-)	600 (600)	272.42	70
265	Mumbai Metro Line 3 (Mumbai Metro Rail Corporation Limited [MMRC]) (702637)	Maharashtra	06/2016	03/2023 08/2025	23136 (37276)	27519.07	91.9
266	Nagpur Metro Rail Phase II Development Project (Maharashtra Metro Rail Corporation Limited [MMRCL]) (702658)	Maharashtra	12/2022	12/2027 (-)	6708 (6708)	1045.32	25

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
267	Delhi Metro Rail Phase-IV [Rithala - Kundli Corridor] (Delhi Metro Rail Corporation Limited [DMRC]) (617206)	Multi-States (Delhi, Haryana)	01/2025	01/2029 (-)	6230.99 (6230.99)	0.29	0
268	Delhi-Ghaziabad-Meerut Regional Rapid Transit System [RRTS] corridor (National Capital Region Transport Corporation [NCRTC]) (702633)	Multi-States (Delhi, Uttar Pradesh)	03/2019	06/2025 08/2025	30274 (30274)	26325.73	95
269	Kanpur Metro Rail Project (Uttar Pradesh metro rail corporation [UPMRC]) (702628)	Uttar Pradesh	11/2019	05/2024 03/2027	11076.48 (11076.5)	9083.27	73
270	Agra Metro Rail Project (Uttar Pradesh metro rail corporation [UPMRC]) (702629)	Uttar Pradesh	12/2020	05/2024 06/2027	8379.62 (8379.62)	6057.62	62
Total (21)					223016.77	159569.88	
Waste & Water							
271	ESR - 8 nos., distribution system - 216 Km, new house service connections - 38760 nos. upgrading of feeder mains, pumping station etc. - Phase II (Ministry of Housing & Urban Affairs) (702674)	Andhra Pradesh	07/2018	03/2023 12/2025	172.22 (172.22)	622.02	82
272	Dibrugarh Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702682)	Assam	01/2020	03/2023 12/2025	186.8 (186.8)	1291.55	98
273	Muzaffarpur Storm Water Drainage Phase-I Project (Ministry of Housing & Urban Affairs) (702699)	Bihar	02/2019	10/2023 03/2024	158.78 (158.78)	48.61	51
274	Storm water drainag Development Project (ministry of housing and urban affairs) (702355)	Dadra & Nagar Haveli and Daman & Diu	12/2021	03/2024 (-)	210 (210)	0	20
275	Upgradation of Sewerage system in Gandhinagar City (ministry of housing and urban affairs) (707267)	Gujarat	03/2021	06/2023 (-)	200 (200)	100	10
276	Sewerage Management Scheme Part-3 Implementation (Ministry of Housing & Urban Affairs) (702734)	Haryana	11/2017	09/2023 03/2026	278.01 (278.01)	1548.15	88
277	Sewerage Management Scheme Part-3 Implementation (Ministry of Housing & Urban Affairs) (702735)	Haryana	10/2018	03/2023 12/2025	213.19 (213.19)	1069.74	91
278	Dhanbad Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702741)	Jharkhand	12/2018	03/2023 03/2026	216.55 (216.55)	696.48	72
279	SAAP-3 Water Supply Infrastructure SAAP-3 Project (Ministry of Housing & Urban Affairs) (702742)	Jharkhand	12/2018	10/2023 03/2026	159.31 (159.31)	612.5	65
280	Augmentation and Strenghthning of Urban Water Supply Phase 1 - SAAP 3 (Ministry of Housing & Urban Affairs) (702746)	Jharkhand	12/2018	03/2023 03/2026	278.28 (278.28)	1223.5	78
281	Belgavi Improvement in Sewerage System Project (Ministry of Housing & Urban Affairs) (702760)	Karnataka	10/2016	07/2023 12/2025	162.73 (162.73)	562.71	80
282	24/7 water supply under AMRUT for Davanagere (Ministry of Housing & Urban Affairs) (702764)	Karnataka	01/2018	03/2023 12/2025	174.96 (174.96)	715.56	65
283	Indore Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702793)	Madhya Pradesh	11/2017	03/2023 12/2025	287.17 (287.17)	1766	99
284	Jabalpur Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702798)	Madhya Pradesh	12/2017	03/2023 12/2025	362.31 (362.31)	2264.18	93
285	Satna Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702808)	Madhya Pradesh	12/2016	03/2024 12/2025	191.56 (191.56)	501.71	86
286	Singrauli Sewerage Management and Treatment Infrastructure Project (Ministry of Housing & Urban Affairs) (702810)	Madhya Pradesh	11/2017	03/2023 12/2025	402.01 (402.01)	2424.71	90
287	Kalyan-Dombivali Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702833)	Maharashtra	09/2019	10/2023 12/2025	194.2 (194.2)	375.32	70
288	Mira-Bhayandar Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702840)	Maharashtra	08/2018	03/2023 12/2025	204.55 (204.55)	581.09	99
289	Nagpur Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702842)	Maharashtra	08/2018	03/2023 09/2025	273.78 (273.78)	266.11	99
290	Pune Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (702851)	Maharashtra	07/2017	03/2023 10/2025	235.95 (235.95)	614.06	92
291	Solapur Sewerage Management Infrastructure Project (Ministry of Housing & Urban Affairs) (702854)	Maharashtra	04/2018	03/2023 12/2025	180.24 (180.24)	476.83	91
292	Jalandhar Water Supply Infrastructure Project (Ministry of Housing & Urban Affairs) (703021)	Punjab	08/2020	08/2023 03/2026	258.53 (258.53)	161.02	58
293	Patiala Water Supply Infrastructure Part-2 Project (Ministry of Housing & Urban Affairs) (703057)	Punjab	08/2020	10/2023 12/2025	287 (287)	451.94	74
294	Jaunpur Sewerage Management Infrastructure Project (Ministry of Housing & Urban Affairs) (702948)	Uttar Pradesh	08/2019	06/2023 12/2025	235.73 (235.73)	166	87
295	Jhansi Water Supply Infrastructure Phase-II Project (Ministry of Housing & Urban Affairs) (702949)	Uttar Pradesh	06/2019	07/2023 09/2025	561.74 (561.74)	523.15	100
Total (25)					6085.6	19062.94	

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Ministry of Mines							
Construction							
296	Construction of Basement + Ground Floor+ 10 Storeyed building for State of the Art Director General, GSI Building at plot No.GN-40, Sector-V, Salt Lake, Kolkata (Central Public Works Department (CPWD)) (617280)	West Bengal	02/2020	08/2026 (-)	255.37 (255.37)	79.34	79
Total (1)					255.37	79.34	
Metals & Mining							
297	Rakha Underground Mining Project (Hindustan Copper Limited [HCL]) (611798)	Jharkhand	03/2024	03/2033 (-)	2705 (2705)	0	0
298	Surda Underground Copper Mining Project (Hindustan Copper Limited [HCL]) (611800)	Jharkhand	03/2024	03/2028 (-)	665.02 (665.02)	16.57	1
299	Expansion of Malanjkhanda Copper Project (Hindustan Copper Limited [HCL]) (400426)	Madhya Pradesh	04/2015	04/2020 04/2026	1856.36 (1856.36)	935.32	80
300	Expansion of Alumina Refinery Plant with addition of 5th Stream having capacity enhancement of 1.0 Million Tonne Per Annum (National Aluminium Company Limited [NALCO]) (400141)	Odisha	04/2017	12/2022 09/2025	4103 (5677.4)	3984.99	76
301	Pottangi Bauxite Mines Project (National Aluminium Company Limited [NALCO]) (400299)	Odisha	05/2018	03/2025 05/2026	1381 (1960.77)	650.04	51
302	UTKAL D AND E COAL BLOCK (National Aluminium Company Limited [NALCO]) (709829)	Odisha	02/2016	03/2025 (-)	1021.97 (1021.97)	0	0
303	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND (Ministry of Mines) (709830)	Odisha	04/2017	11/2026 (-)	355 (581)	0	0
304	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PANCHPATMAILI MINES (National Aluminium Company Limited [NALCO]) (709831)	Odisha	11/2019	05/2025 06/2026	483 (483)	402.67	90
305	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (National Aluminium Company Limited [NALCO]) (709832)	Tamil Nadu	12/2017	03/2025 03/2026	166 (166)	135	65
Total (9)					12736.35	6124.59	
Department of Higher Education							
Education							
306	Construction of Permanent Campus of Central Tribal University of Andhra Pradesh Phase-1 (Central Tribal University of Andhra Pradesh) (613008)	Andhra Pradesh	12/2023	06/2027 (-)	305 (305)	83.33	24
307	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	03/2013	08/2026 (-)	592.61 (592.61)	549.96	75
308	Tezpur University Projects (Tezpur University) (606112)	Assam	06/2021	11/2023 08/2025	153.71 (153.71)	54.05	95
309	Additional Campus of NIT Patna (NIT Patna) (606013)	Bihar	08/2022	07/2024 01/2026	499.21 (499.21)	425.47	91
310	Phase 1B - Construction of Academic Block, Hostel, Residential Tower, Directors Residence and External Development works at National Institute of Technology, Delhi Campus on Engineering, Procurement and Construction basis (Ministry of Education) (612851)	Delhi	11/2022	09/2025 (-)	333.49 (333.49)	277.75	91
311	Delhi University Eastern Campus at Surajmal Vihar (Delhi University) (616886)	Delhi	01/2025	10/2026 (-)	373 (373)	23.23	15
312	Construction of permanent campus of Central University of Gujarat at Village kundhela, Dist. Vadodara, Gujarat. (Gujarat) (612916)	Gujarat	02/2021	03/2025 03/2026	490.63 (490.63)	301.44	76
313	Establishment of Permanent campus Phase 1 of IIM Sirmaur (Indian Institute of Management, Sirmaur) (602099)	Himachal Pradesh	08/2020	10/2023 02/2026	392.51 (454.78)	323.64	92
314	Hostel blocks & dining hall block (Indian Institute of Technology, Mandi) (612128)	Himachal Pradesh	03/2024	03/2026 03/2026	166.66 (166.66)	72.09	65
315	Construction of Permanent Campus of Central University of Himachal Pradesh at Dehra, District - Kangra, [H.P.] on Engineering. Procurement and Construction [EPC Mode 1] Basis. (Central University, Himachal Pradesh) (612894)	Himachal Pradesh	08/2022	11/2024 11/2025	251.98 (300.45)	183.36	78
316	Construction of Permanent Campus for IIM Jammu Phase-1 at Jagti, Nagrota, Jammu, J&K (Indian Institute of Management, Jammu) (602098)	Jammu and Kashmir	10/2020	06/2023 09/2025	424.93 (500.91)	484.52	96
317	Additional Infrastructure at IISc Bangalore-RCC Monolithic for Men Hostel S14, Women Hostel S11, Postdoctoral Hostel S12 2 Block, International Hostel S 12, D&E Block S 12 2 Block FR. (IISc Bangalore) (610940)	Karnataka	08/2021	03/2024 09/2025	420.41 (420.41)	360.72	99
318	CONSTRUCTION OF PERMANENT CAMPUS FOR IIT PALAKKAD UNDER PHASE 1A (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (606431)	Kerala	03/2020	06/2022 11/2026	1006.45 (1217.4)	623.6	71

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
319	Phase III A works at IIT Indore [03 Hostels, 01 Studio Apartment, 01 Housing, Heavy & Sophisticated lab complex, Academic POD and Infrastructure for center of excellence] <i>(Indian Institute of Technology, Indore)</i> (611957)	Madhya Pradesh	11/2023	12/2026 (-)	496.28 (496.28)	143.95	35
320	Hostel 4 -Earlier Known as Hostel 20 <i>(Indian Institute of Technology, Bombay)</i> (612135)	Maharashtra	05/2022	09/2025 (-)	182.33 (182.33)	132.44	95
321	Academic Block 1 & 2 <i>(Indian Institute of Technology, Bombay)</i> (612203)	Maharashtra	01/2023	07/2026 03/2027	68 (263.93)	22.26	18
322	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra <i>(National Institute of Technology, Meghalaya)</i> (612885)	Meghalaya	09/2014	03/2022 07/2025	494.52 (494.52)	413.57	86
323	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl <i>(Ministry of Education)</i> (612876)	Mizoram	05/2014	12/2029 12/2029	474.23 (474.23)	167.55	4
324	Establishment of NIT Nagaland <i>(NIT Nagaland)</i> (613013)	Nagaland	09/2012	12/2025 (-)	275.63 (275.63)	260.1	95
325	IISER BERHAMPUR <i>(Indian Institutes of Science Education and Research, Behrampur)</i> (610315)	Odisha	09/2019	03/2021 12/2025	1229.32 (773.76)	837.04	97
326	Establishment of NIT Puducherry Permanent Campus [Phase-I and Phase-II] <i>(National Institute of Technology, Puducherry)</i> (612877)	Puducherry	07/2013	12/2024 08/2025	618.34 (544.34)	509.55	94
327	Construction of Permanent Campus of Indian Institute of Management [IIM] Amritsar, Punjab, Phase-I <i>(Indian intitue of Management, Amritsar)</i> (605292)	Punjab	07/2020	06/2023 12/2025	348.31 (348.31)	290.39	91
328	Construction of Girls Hostel 400 seater, Boys Hostel 600 seater, Academic Block, International Hostel 100 seater, VC Residence and Purchase of Equipment <i>(Central University of Punjab)</i> (617221)	Punjab	04/2025	10/2027 (-)	210.99 (210.99)	0	0
329	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim <i>(Sikkim University)</i> (609736)	Sikkim	01/2022	01/2025 09/2025	314.06 (314.06)	238.22	82
330	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District <i>(Ministry of Education)</i> (612883)	Sikkim	03/2024	02/2028 12/2026	685.76 (610.76)	121.56	9
331	Construction of Precast housing and hostels at IIT Hyderabad <i>(Indian Institute of Technology, Hyderabad)</i> (609996)	Telangana	11/2022	10/2024 01/2026	262 (262)	177.09	73
332	Banaras Hindu University [Kayakalp of Institute of Medical Sciences] <i>(Banaras Hindu University)</i> (606479)	Uttar Pradesh	06/2020	09/2022 03/2026	246 (246)	193.38	95
333	Construction & Development of Infrastructural Facilities in the main campus of NIT Uttarakhand at Sumari, Pauri Garhwal <i>(National Institute of Technology Uttarakhand)</i> (611963)	Uttarakhand	04/2024	09/2027 (-)	650.85 (650.85)	195.52	24
334	HEFA projects on development of student hostels, playgrounds, departmental buildings, class room complex and other campus facilities in IIT Kharagpur <i>(Indian Institute of Technology, Kharagpur)</i> (609019)	West Bengal	04/2019	03/2023 03/2026	500 (442)	383.6	87
335	IoE Projects [Civil Works], IIT Kharagpur <i>(Indian Institute of Technology, Kharagpur)</i> (609041)	West Bengal	04/2019	03/2023 12/2026	287.2 (287.2)	310	86
Total (30)					12754.41	8159.38	
Ministry of Petroleum & Natural Gas							
Energy Storage							
336	Construction of Aviation Fuel farm Facilities at Bhogapuram Airport <i>(Ministry of Petroleum & Natural Gas)</i> (616235)	Andhra Pradesh	08/2024	03/2026 03/2026	240 (240)	38.82	59
337	Construction of LPG Facilities at Kamardanga, Assam <i>(Hindustan Petroleum Corporation Limited)</i> (709754)	Assam	03/2023	07/2027 07/2027	156.36 (156.36)	54.15	46
338	Setting up of new rail fed POL facility at Kamardanga, Assam <i>(Hindustan Petroleum Corporation Limited [HPCL])</i> (709755)	Assam	03/2023	07/2027 07/2027	384.04 (384.04)	120.4	52
339	Setting up a common user Petroleum Terminal at Jammu, J&K for resitement of existing PSU OMC's Depots from Jammu City <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (400235)	Jammu and Kashmir	04/2023	03/2025 01/2026	676.89 (676.89)	526.1	79
340	Andheri Residential Towers, Mumbai <i>(Ministry of Petroleum & Natural Gas)</i> (604833)	Maharashtra	06/2017	05/2025 06/2026	281.35 (389.67)	230.76	50
341	Srikakulam Angul Gas Pipeline Project <i>(Ministry of Petroleum & Natural Gas)</i> (701343)	Multi-States (Andhra Pradesh, Odisha)	09/2019	07/2022 12/2025	2658.34 (2810)	2203.98	95
342	Rajasthan Refinery Project <i>(MinistryofPetroleumNaturalGas)</i> (701263)	Multi-States (Arunachal Pradesh, Gujarat, Rajasthan)	10/2017	10/2022 03/2026	43129 (79459)	60295.14	88
343	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip <i>(Ministry of Petroleum & Natural Gas)</i> (701349)	Multi-States (Assam, Bihar, Jharkhand, Odisha, West Bengal)	01/2019	07/2024 09/2025	10228 (11407)	9766.72	87
344	New Mundra Panipat Crude Oil Pipeline <i>(Ministry of Petroleum & Natural Gas)</i> (400078)	Multi-States (Gujarat, Haryana, Rajasthan)	12/2021	12/2024 12/2025	9028 (9028)	7136.41	85

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
345	Kandla Gorakhpur LPG Pipeline (Ministry of Petroleum & Natural Gas) (400012)	Multi-States (Gujarat, Madhya Pradesh, Uttar Pradesh)	12/2018	12/2021 12/2025	10088 (10088)	7672.23	92
346	Multi Product Pipeline from Irugur to Devangonchi (Department of Water Resources, River Development & GR) (400301)	Multi-States (Karnataka, Tamil Nadu)	11/2012	02/2017 10/2025	678 (1732)	713.86	69
347	Petrochemical evacuation marketing terminal at Barmer, Rajasthan (Hindustan Petroleum Corporation Limited [HPCL]) (709759)	Rajasthan	12/2023	12/2026 12/2026	461.05 (461.05)	116.48	54
348	Laying of POL Pipelines in Common Corridor for proposed grass root terminal at Vallur [Chennai] (Ministry of Petroleum & Natural Gas) (400043)	Tamil Nadu	01/2022	05/2026 05/2026	829 (829)	301.71	63
349	Grass root POL Terminal at Vallur, Chennai (Indian Oil Corporation Limited [IOCL]) (400077)	Tamil Nadu	01/2022	12/2024 03/2026	827 (887.71)	626.01	88
350	Grass Root Rail-fed Depot at Sekerkote, Agartala as resitement of existing Dharmanagar Depot (Indian Oil Corporation Limited [IOCL]) (400035)	Tripura	06/2022	09/2025 06/2026	656 (656)	478.11	86
351	Grass-root Terminal at Mirzapur, Uttar Pradesh (Ministry of Petroleum & Natural Gas) (604852)	Uttar Pradesh	09/2022	11/2026 11/2026	980.45 (980.45)	216.66	52
	Total (16)				81301.48	90497.54	
	Oil & Gas						
352	KG-DWN-98/2 Cluster - II Development Project - NELP Block (Oil and Natural Gas Corporation Limited [ONGC]) (400120)	Andhra Pradesh	03/2016	06/2020 06/2026	34012 (34012)	33238.47	96
353	HP-COAT [Crude to Olefins and Aromatics Technology] demo unit at Visakh Refinery (Hindustan Petroleum Corporation Limited) (709752)	Andhra Pradesh	09/2021	06/2024 03/2026	160 (220)	80.29	69
354	HP Trijet Unit in Visakh Refinery (Hindustan Petroleum Corporation Limited) (709761)	Andhra Pradesh	07/2024	07/2027 07/2027	193 (193)	0.43	23
355	City Gas Distribution Project at Kurnool, Guntur & Prakasam Districts (Ministry of Petroleum & Natural Gas) (709766)	Andhra Pradesh	03/2022	03/2030 03/2030	1420 (1420)	165.65	6
356	Numaligarh Refinery Expansion Project (Ministry of Petroleum & Natural Gas) (604791)	Assam	07/2020	07/2024 12/2025	12366 (22494)	16764.09	76
357	Assam Bio Refinery, ABRPL (Ministry of Petroleum & Natural Gas) (604792)	Assam	02/2018	09/2021 09/2025	1750 (4930)	4710	99
358	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Ministry of Petroleum & Natural Gas) (604863)	Assam	01/2018	02/2020 12/2025	682.9 (726.93)	489.3	94
359	Guwahati Refinery Expansion [1.0 to 1.2 MMTPA] along with installation of CRU, Guwahati Refinery (Ministry of Petroleum & Natural Gas) (607701)	Assam	05/2021	10/2023 05/2026	412.3 (577)	430.83	85
360	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Ministry of Petroleum & Natural Gas) (616858)	Assam	12/2020	03/2024 12/2025	430.76 (430.76)	327.27	85
361	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (Ministry of Petroleum & Natural Gas) (709776)	Assam	04/2022	09/2026 09/2026	277 (323.09)	185.18	68
362	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (Ministry of Petroleum & Natural Gas) (709779)	Assam	06/2022	03/2026 03/2026	768 (740)	107.72	39
363	Pipeline Network Project Rudrasagar (Ministry of Petroleum & Natural Gas) (709847)	Assam	01/2023	04/2026 04/2026	344.99 (344.99)	211.05	47
364	Borholla GGS Life Extension Project [BLEP] (Ministry of Petroleum & Natural Gas) (709850)	Assam	09/2023	05/2026 05/2026	198.7 (198.7)	36.8	30
365	DCU Revamp Project (NRL) (709864)	Assam	08/2021	07/2024 10/2025	370 (370)	253.17	60
366	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (NRL) (709865)	Assam	04/2023	12/2024 10/2025	293.5 (293.5)	97.22	94
367	City Gas Distribution Project at Khagaria, Saharsa and Madhepura (Ministry of Petroleum & Natural Gas) (617303)	Bihar	03/2019	03/2030 03/2030	163 (163)	96.07	40
368	Setting up of LPG Plant with Rail Unloading Facility at Hathua, Dist. Gopalganj, Bihar (Ministry of Petroleum & Natural Gas) (617304)	Bihar	10/2023	03/2027 03/2027	340.15 (340.15)	91.32	26
369	Barauni Refinery Capacity Expansion from 6.0 to 9.0 MMTPA (Ministry of Petroleum & Natural Gas) (701324)	Bihar	01/2020	04/2023 08/2026	14810 (16724)	11880.66	87
370	Installation of Bitumen Manufacturing Unit along with allied facilities at Barauni Refinery (Ministry of Petroleum & Natural Gas) (709777)	Bihar	01/2022	04/2025 10/2026	389.35 (340)	50.48	40
371	City Gas Distribution Projects at Darbhanga, Madhubani, Supaul, Sitamarhi and Sheohar districts (Bharat Petroleum Corporation Limited [BPCL]) (709792)	Bihar	12/2022	03/2030 03/2030	3638 (3638)	407.18	29

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
372	City Gas Distribution Projects at Gopalganj, Siwan, West Champaran, East Champaran and Deoria districts (Bharat Petroleum Corporation Limited [BPCL]) (709793)	Bihar	12/2022	06/2030 06/2030	3919 (3919)	400.92	18
373	Redevelopment of Sobhasan Complex (Oil and Natural Gas Corporation Limited [ONGC]) (400087)	Gujarat	08/2021	02/2026 02/2026	885.63 (1286.67)	789.49	78
374	Redevelopment of Santhal Field [Onshore-Mehsana Asset] (Oil and Natural Gas Corporation Limited [ONGC]) (400167)	Gujarat	02/2017	03/2026 03/2026	1162.56 (1162.56)	1157	94
375	Redevelopment of Linch Field (Oil and Natural Gas Corporation Limited [ONGC]) (400169)	Gujarat	04/2021	03/2025 10/2025	631.03 (860.04)	505.15	79
376	Petrochemical and Lube Integration Project at Gujarat Refinery (Ministry of Petroleum & Natural Gas) (701329)	Gujarat	09/2020	08/2024 12/2025	18936 (17825)	12327.91	83
377	Installation of new Biturox Unit along with allied facilities at Gujarat Refinery (MinistryofPetroleumNaturalGas) (709778)	Gujarat	01/2022	08/2025 09/2026	328.29 (287)	151.53	58
378	Commercial Polymer Flooding Project in Bechraji field (Oil and Natural Gas Corporation Limited [ONGC]) (709838)	Gujarat	01/2022	11/2024 11/2025	621.4 (621.4)	137.71	21
379	Restoration of Gas Terminal, Phase-I [Part-A], Hazira (Oil and Natural Gas Corporation Limited [ONGC]) (709840)	Gujarat	05/2022	02/2025 12/2025	249.43 (249.43)	209.45	94
380	Old Pipe Line Replacement [OPRP] Group-A (Oil and Natural Gas Corporation Limited [ONGC]) (709841)	Gujarat	07/2021	07/2025 03/2026	173.03 (169.84)	147.02	87
381	Kalol Redevelopment Project, Ahmedabad Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709842)	Gujarat	08/2022	03/2027 03/2027	1487.41 (1487.41)	927.5	62
382	Revamping of SV Stations, Gas Terminal & Kribhco Terminal (Oil and Natural Gas Corporation Limited [ONGC]) (709845)	Gujarat	11/2022	08/2026 08/2026	837.34 (837.34)	219.13	52
383	Indian Oil Technology Development and Deployment Centre at R&D Campus-II, Faridabad (Ministry of Petroleum & Natural Gas) (604853)	Haryana	06/2019	12/2022 03/2026	2281.94 (3200)	1800.61	63
384	Poly Butadiene Rubber plant at Panipat (Indian Oil Corporation Limited [IOCL]) (611917)	Haryana	03/2022	03/2025 06/2026	1459 (2531.44)	1072.59	70
385	Capacity Expansion of Panipat Refinery from 15 to 25 MMTPA (Ministry of Petroleum & Natural Gas) (701289)	Haryana	02/2021	09/2024 12/2025	34627 (36225)	24355.1	89
386	Installation of Multiple Effect Evaporator [MEE] for ETP-1, 2 & 4 of Panipat Refinery and Petrochemical Complex. (MinistryofPetroleumNaturalGas) (709783)	Haryana	12/2020	06/2023 06/2026	165.13 (247.69)	130.6	72
387	City Gas Distribution Project at Jammu, Udhampur, Reasi, Samba and Kathua Districts (MinistryofPetroleumNaturalGas) (709773)	Jammu and Kashmir	03/2022	03/2032 03/2032	538 (538)	3.72	0
388	Development of Jharia CBM Block [Phase-1] (Oil and Natural Gas Corporation Limited [ONGC]) (610984)	Jharkhand	11/2019	01/2024 11/2025	431 (431)	211.4	59
389	Laying of Natural Gas Pipeline from Hazaribagh to Ranchi [HRPL] (MinistryofPetroleumNaturalGas) (709785)	Jharkhand	02/2023	02/2026 02/2026	202.07 (202.07)	52.42	45
390	Power System Upgradation Project (Mangalore Refinery and Petrochemicals Limited) (612790)	Karnataka	10/2023	11/2025 05/2026	385 (385)	137	64
391	Demo Bio-ATF Project (Ministry of Petroleum & Natural Gas) (616879)	Karnataka	03/2024	01/2027 01/2027	364 (364)	27.02	12
392	Revamping/ Augmentation of facilities at existing port terminal at Mangalore (Ministry of Petroleum & Natural Gas) (709774)	Karnataka	01/2022	12/2025 12/2025	463 (500.62)	271.16	82
393	Replacement and Extension of Jetty Pipelines [REJP] at KR (Bharat Petroleum Corporation Limited [BPCL]) (709790)	Kerala	03/2023	03/2026 03/2026	621.87 (621.87)	193.19	85
394	Setting up Polypropylene Unit at Kochi Refinery (MinistryofPetroleumNaturalGas) (709799)	Kerala	12/2023	10/2027 10/2027	4460 (4460)	265.89	13
395	Ethylene Cracker Project at Bina Refinery including downstream Petrochemical Plants and expansion of Refinery (MinistryofPetroleumNaturalGas) (709798)	Madhya Pradesh	05/2023	05/2028 05/2028	43367 (43367)	1855.5	14
396	Debottlenecking and Augmentation of Cryogenic facilities at Uran LPG Import Terminal (Department of Water Resources, River Development & GR) (400158)	Maharashtra	04/2021	02/2024 12/2025	1164.69 (1629.86)	932.25	86
397	500 KTA PDHPP Project, Usar (Ministry of Petroleum & Natural Gas) (400168)	Maharashtra	04/2021	04/2025 10/2025	8797 (11256)	6877.59	85
398	Construction of lube oil blending plant at Rasayani (Ministry of Petroleum & Natural Gas) (610985)	Maharashtra	05/2022	12/2023 12/2025	423.39 (526.26)	301.01	80
399	Lube Modernization & Bottom Upgradation Project at Mumbai Refinery (Ministry of Petroleum and Natural Gas) (616933)	Maharashtra	12/2024	03/2028 03/2028	4679 (4679)	194.44	5
400	HP TDAE Unit in Mumbai Refinery (Hindustan Petroleum Corporation Limited) (709760)	Maharashtra	06/2024	04/2026 04/2026	240 (240)	34.42	40

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
401	City Gas Distribution Project at Beed, Jalgaon and Jalna Districts (Ministry of Petroleum & Natural Gas) (709771)	Maharashtra	03/2022	09/2031 09/2031	865 (865)	69.15	2
402	Construction of Additional Tankages and Allied Facilities at JNPT Terminal (Ministry of Petroleum & Natural Gas) (709780)	Maharashtra	04/2022	08/2026 08/2026	341.43 (436.14)	282.95	51
403	ATF Pipeline from Jawaharlal Nehru Port Trust to Navi Mumbai International Airport (Indian Oil Corporation Limited [IOCL]) (709782)	Maharashtra	08/2022	08/2025 03/2026	165 (165)	90.75	74
404	Installation of Independent De- Aromatized Solvents [DAS] production facilities at MR (Bharat Petroleum Corporation Limited [BPCL]) (709789)	Maharashtra	03/2023	07/2025 12/2025	405 (343)	205.63	86
405	POL & LOBS Installations with Receipt Pipelines at Rasayani (Bharat Petroleum Corporation Limited [BPCL]) (709797)	Maharashtra	05/2023	05/2026 05/2026	2585 (2585)	612.7	61
406	Part Replacement Pipeline Project [PRPP] (Oil and Natural Gas Corporation Limited [ONGC]) (709846)	Maharashtra	11/2022	05/2024 11/2025	1219.48 (1145.1)	744.81	90
407	Visakh Raipur Pipeline Project (Ministry of Petroleum & Natural Gas) (616254)	Multi-States (Andhra Pradesh, Chhattisgarh, Odisha)	09/2024	09/2027 09/2027	2212 (2212)	13.45	8
408	North East Gas Grid (Ministry of Petroleum & Natural Gas) (701346)	Multi-States (Arunachal Pradesh, Assam, Manipur, Meghalaya, Mizoram, Nagaland, Sikkim, Tripura, West Bengal)	04/2020	03/2024 03/2026	9265 (9265)	6393.85	85
409	Upgradation of Facilities of Numaligarh-Siliguri Product Pipeline [NSPL] for transportation of additional products from existing 1.72 MMTPA to 5.5 MMTPA (Ministry of Petroleum & Natural Gas) (701350)	Multi-States (Assam, West Bengal)	06/2021	12/2024 10/2025	860 (860)	584.76	98
410	CGD Project in Banka, Dumka, Godda, Jamtara, Pakur, Sahibganj GA ID 11A.02 (Hindustan Petroleum Corporation Limited) (709757)	Multi-States (Bihar, Jharkhand)	06/2022	06/2030 06/2030	1377 (1377)	331.74	27
411	Mumbai Nagpur Jharsuguda Pipeline Project (Ministry of Petroleum & Natural Gas) (701354)	Multi-States (Chhattisgarh, Madhya Pradesh, Maharashtra, Odisha)	06/2020	05/2023 09/2025	7844.25 (8255)	6495.6	96
412	Mehsana-Bhatinda & Bhatinda-Jammu Natural Gas Pipeline (Ministry of Petroleum & Natural Gas) (701330)	Multi-States (Gujarat, Haryana, Punjab, Rajasthan)	07/2011	06/2024 12/2025	7392 (7392)	6308	90
413	Gurdaspur Jammu Pipeline (Gas Authority of India Limited [GAIL]) (612853)	Multi-States (Jammu and Kashmir, Punjab)	07/2023	07/2026 07/2026	521.9 (521.9)	190.1	36
414	Kochi - Kootanad - Bangalore - Mangalore Pipeline Phase-II (Ministry of Petroleum & Natural Gas) (701228)	Multi-States (Karnataka, Kerala, Tamil Nadu)	06/2009	12/2012 12/2025	2915 (5909)	4453.29	94
415	City Gas Distribution Maharashtra Natural Gas Limited (Ministry of Petroleum & Natural Gas) (701338)	Multi-States (Karnataka, Maharashtra)	01/2006	06/2031 06/2031	5535 (5535)	3861.49	0
416	Dhamra Haldia Pipeline Project (Ministry of Petroleum & Natural Gas) (701344)	Multi-States (Odisha, West Bengal)	03/2020	11/2022 12/2025	1030.65 (1125)	854.6	87
417	City Gas Distribution Projects at Fazilka [except area already authorized], Ganganagar and Hanumangarh districts (Bharat Petroleum Corporation Limited [BPCL]) (709794)	Multi-States (Punjab, Rajasthan)	12/2022	06/2030 06/2030	3207 (3207)	339.57	24
418	Augmentation/ Revamping of Dimapur Depot, Dimapur (Ministry of Petroleum & Natural Gas) (709786)	Nagaland	08/2023	11/2027 11/2027	227.62 (227.62)	9.12	22
419	Integrated Para Xylene [PX] and Purified Terephthalic Acid [PTA] Project at Paradip Refinery (Ministry of Petroleum & Natural Gas) (604859)	Odisha	07/2020	01/2024 08/2026	13805 (11783)	8310.16	90
420	CUF POL Depot at Sadashibpur [Meramundali], Odisha (Ministry of Petroleum & Natural Gas) (709800)	Odisha	04/2021	03/2026 03/2026	393.54 (393.54)	104.55	44
421	Life Extension of 48 well platforms of Mumbai High & Heera Fields (Oil and Natural Gas Corporation Limited [ONGC]) (400119)	Offshore	12/2015	04/2018 12/2025	3190.69 (3375.9)	3074.25	89
422	PRP-VIII [Group-A] (Ministry of Petroleum & Natural Gas) (616950)	Offshore	09/2024	02/2026 02/2026	1486.4 (1486.4)	272.3	19
423	Daman Upside Development Project (Oil and Natural Gas Corporation Limited [ONGC]) (709839)	Offshore	06/2022	10/2025 02/2026	4144.41 (6406.9)	3894.53	85
424	MHN TCPG PGC BGC Project [MTPBP] (Ministry of Petroleum & Natural Gas) (709848)	Offshore	06/2022	05/2026 05/2026	2329.45 (2354.23)	820.24	53
425	PRP-VIII Group B [NH & BS Asset] (Ministry of Petroleum & Natural Gas) (709849)	Offshore	06/2024	02/2026 02/2026	2379.84 (3165.53)	1675.65	62
426	Integrated Development of 4 Contract Areas under DSF-II (Ministry of Petroleum & Natural Gas) (709851)	Offshore	05/2023	04/2027 04/2027	6183.79 (6183.79)	474	20
427	2G Ethanol Biorefinery at Bathinda (Hindustan Petroleum Corporation Limited [HPCL]) (400171)	Punjab	05/2020	02/2023 03/2026	1421.46 (1421.46)	1182.4	95

All Ongoing Projects

AUGUST 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
428	Bathinda Sangrur Pipeline (Ministry of Petroleum and Natural Gas) (612998)	Punjab	11/2021	05/2024 09/2025	367 (397)	346.18	93
429	City Gas Distribution Project at Pathankot District (Ministry of Petroleum and Natural Gas) (709770)	Punjab	03/2022	09/2033 09/2033	151 (151)	8.73	2
430	CBR 9 MMTPA Project (Chennai Petroleum Corporation Limited [CPCL]) (604795)	Tamil Nadu	09/2021	06/2025 10/2028	31580 (36354)	1342.27	10
431	Laying of new 28 inch Desal Water Pipeline and 10 inch Reject Water Pipeline between CPCL Manali Refinery and CPCL Desalination plant at Ennore (Chennai Petroleum Corporation Limited [CPCL]) (709750)	Tamil Nadu	01/2024	09/2025 12/2025	205 (205)	38.14	42
432	City Gas Distribution Projects at the Nilgiris and Erode districts (Bharat Petroleum Corporation Limited [BPCL]) (709796)	Tamil Nadu	12/2022	03/2030 03/2030	3685 (3685)	226.87	17
433	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837)	Tripura	03/2022	05/2024 12/2025	209.33 (131.51)	68.88	62
434	PP Project, Pata (Gas Authority of India Limited [GAIL]) (400161)	Uttar Pradesh	03/2019	01/2024 09/2025	910.56 (1299.02)	1019	97
435	Revamping / Augmentation of Facilities at Mathura Bitumen Plant (Ministry of Petroleum and Natural Gas) (709781)	Uttar Pradesh	04/2022	06/2027 12/2026	260.12 (260.12)	1.11	26
436	City Gas Distribution Projects at Lakhimpur Kheri, Sitapur, Bahraich, Shravasti, Balrampur, Siddharth Nagar & Maharajganj districts (Bharat Petroleum Corporation Limited [BPCL]) (709795)	Uttar Pradesh	12/2022	06/2030 06/2030	16654 (16654)	558.33	11
437	Durgapur - Haldia Pipeline [Section-3B of JHBDPL Project] (Ministry of Petroleum & Natural Gas) (617302)	West Bengal	03/2017	12/2020 12/2025	1740 (2493.15)	2239.7	90
438	Haldia Panagarh Pipeline Project (Hindustan Petroleum Corporation Limited) (709753)	West Bengal	11/2022	11/2025 11/2025	1010 (1010)	645.07	82
439	CGD Project in Malda, Birbhum, Murshidabad, Dakshin Dinajpur GA ID 11A.03 (Hindustan Petroleum Corporation Limited) (709758)	West Bengal	06/2022	06/2030 06/2030	2628 (2628)	335.96	27
440	City Gas Distribution Project at East Mednipore, West Mednipore & Jhargram Districts (Ministry of Petroleum and Natural Gas) (709772)	West Bengal	03/2022	06/2031 06/2031	609 (609)	56.35	2
441	City Gas Distribution Projects at Alipurduar and Cooch Behar (Bharat Petroleum Corporation Limited [BPCL]) (709791)	West Bengal	12/2022	03/2030 03/2030	1017 (1017)	184.13	39
Total (90)					351248.78	184032.26	
Ministry of Health & Family Welfare							
Healthcare							
442	AIIMS Majra Rewari Haryana (Ministry of Health & Family Welfare) (701173)	Haryana	02/2019	02/2023 12/2026	1299 (1299)	349.41	28
443	AIIMS Kashmir at Awantipora Jammu & Kashmir (Central Public Works Department [CPWD]) (701167)	Jammu and Kashmir	01/2019	01/2025 12/2025	1828 (1828)	1531.86	66
444	AIIMS Bibinagar (Ministry of Health & Family Welfare) (701171)	Telangana	12/2018	09/2022 12/2025	1028 (1365.95)	812.95	84
Total (3)					4155	2694.22	
Ministry of Ports, Shipping and Waterways							
Healthcare							
445	Establishment of 600 bed super specialty hospital with optional development of Medical college and further expansion on PPP basis. (Mumbai Port Trust [MPT]) (708662)	Maharashtra	01/2022	06/2026 12/2027	693 (693)	58	0
Total (1)					693	58	
Inland Waterways							
446	Development of Container Terminal at Tuna-Tekra, Deendayal Port on BOT Basis Under PPP Mode (Deendayal Port Trust [DPT]) (609424)	Gujarat	12/2023	12/2026 (-)	4243.64 (4243.64)	366.2	10
447	Jal Marg Vikas Project (Inland Waterways Authority of India [IWAI]) (701565)	Multi-States (Bihar, Jharkhand, Uttar Pradesh, West Bengal)	02/2018	12/2023 12/2025	5369.18 (5061.15)	3510.72	71
Total (2)					9612.82	3876.92	
Shipping							
448	Setting up of a Floating Storage and Regasification Unit [FSRU] - Mumbai (Mumbai Port Trust [MPT]) (701586)	Maharashtra	04/2021	11/2026 11/2026	900 (900)	65	0
449	Operationalization of Coastal Berth & Shallow Water Berth through PPP (Jawaharlal Nehru Port Authority [JNPA]) (708655)	Maharashtra	07/2021	01/2026 (-)	366.8 (366.8)	376.86	25
450	Deepening and Optimization of Inner Harbour facilities including development of Western Dock on BOT basis to handle Cape size vessels (Paradip Port Trust [PPT]) (701574)	Odisha	01/2023	12/2027 10/2028	3004.63 (3004.63)	1149.79	40
451	Berth No. 2 [previously Berth 3] of HDC Mechanization Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701576)	West Bengal	03/2023	09/2025 01/2026	298.26 (298.26)	420	91

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
452	Shalukkhali Liquid Cargo Handling Facility Development Project (Haldia Dock Complex, Syama Prasad Mookerjee Port Authority) (701577)	West Bengal	08/2022	08/2025 (-)	253.65 (253.65)	9.28	0
	Total (5)				4823.34	2020.93	
	Tourism, Hospitality & Wellness						
453	National Maritime Heritage Complex [NMHC] Phase-I (Indian Port Rail & Ropeway Corporation Ltd. [IPRCL]) (707215)	Gujarat	01/2022	03/2024 09/2025	573 (1238.05)	496.63	66
	Total (1)				573	496.63	
	Ministry of Steel						
	Metals & Mining						
454	Capacity expansion of Deposit-14 and 14 NMZ at Kirandul (National Mineral Development Corporation Limited [NMDC]) (615202)	Chhattisgarh	07/2022	12/2028 03/2028	1700 (1756.2)	65.44	3
	Total (1)				1700	65.44	
	Steel						
455	Replacement of Hot Leveller No.1 of Plate Mill at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617243)	Chhattisgarh	08/2024	07/2026 (-)	198.62 (198.62)	10.9	10
456	Replacement of Converter Vessels, Trunnion Rings, Support System & Installation of Secondary Emission at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617255)	Chhattisgarh	12/2023	06/2026 (-)	471.83 (471.83)	130.66	40
457	Rebuilding of Coke Oven Battery No.7 & 8 at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617256)	Chhattisgarh	01/2024	10/2025 (-)	884.1 (884.1)	466.31	77
458	NMDC Slurry Pipeline Project Phase-1 (National Mineral Development Corporation Limited [NMDC]) (706811)	Chhattisgarh	09/2020	06/2023 12/2025	2907 (5427)	3038.85	85
459	SCREENING PLANT-III AT KIRANDUL (National Mineral Development Corporation Limited [NMDC]) (709826)	Chhattisgarh	10/2021	01/2026 (-)	2718.84 (2718.84)	1341.08	72
460	CONSTRUCTION OF RESIDENTIAL TOWERS AT BIOM KIRANDUL COMPLEX (National Mineral Development Corporation Limited [NMDC]) (709827)	Chhattisgarh	10/2022	12/2025 (-)	349.75 (349.75)	282.52	88
461	New Sinter Plant at BSL, SAIL (Steel Authority of India Limited [SAIL]) (400174)	Jharkhand	05/2015	10/2017 06/2027	1034.01 (1752.3)	883.44	51
462	Replacement of existing Grinders in CRM-I & II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617249)	Jharkhand	02/2025	01/2027 (-)	211.94 (211.94)	15.04	10
463	Secondary Emission Control in Converters of SMS-II at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617250)	Jharkhand	02/2025	10/2026 (-)	207.13 (207.13)	15.76	8
464	Revamping of old sub-systems of Blast Furnace 3 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617253)	Jharkhand	10/2023	07/2025 11/2025	513.82 (513.82)	234.54	71
465	Replacement of remaining 04 sets of Battery Cyclones with 04 Nos. of ESPs in Sinter Plant-1 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617254)	Jharkhand	04/2024	06/2026 (-)	260.37 (260.37)	44.25	22
466	Rebuilding of Coke Oven Battery No.6 at Bokaro Steel Plant (Steel Authority of India Limited [SAIL]) (617257)	Jharkhand	12/2023	11/2026 (-)	627.31 (627.31)	91.96	38
467	Construction of Screening Plant-II for Donimalai and Kumaraswamy Iron Ore Mining Complex of NMDC Limited at Ballari Dt, Karnataka. (National Mineral Development Corporation Limited [NMDC]) (400121)	Karnataka	06/2024	08/2026 (-)	1043.63 (1043.63)	229.77	29
468	Installation of 4th Slab Caster along with its Auxiliaries and a New Ladle Furnace in SMS-II at Rourkela Steel Plant (Steel Authority of India Limited [SAIL]) (400065)	Odisha	02/2022	05/2025 09/2025	1105.23 (1105.23)	769.08	97
469	Rebuilding of COB 4 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (612781)	West Bengal	12/2023	12/2026 (-)	916.78 (916.78)	126.25	14
470	Installation of New Bar Mill at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617242)	West Bengal	10/2024	06/2027 (-)	2115.44 (2115.44)	209.11	27
471	Up-gradation of Blast Furnace No. 3 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617246)	West Bengal	10/2024	06/2026 (-)	758.09 (758.09)	63.81	4
472	Third Ladle Furnace in Secondary Refinery Unit at IISCO Steel Plant (Steel Authority of India Limited [SAIL]) (617248)	West Bengal	12/2024	07/2026 (-)	227.96 (227.96)	16.24	29
473	Revamping of Air Pollution Control Systems of SP-1 at Durgapur Steel Plant (Steel Authority of India Limited [SAIL]) (617251)	West Bengal	12/2024	05/2026 (-)	196.4 (196.4)	0.19	3
	Total (19)				16748.25	7969.76	
	Ministry of Railways						
	Railways						
474	Khurda Road - Balangir Electrification of Railway Track Project (Ministry of Railways) (706898)		09/2019	03/2021 (-)	267.61 (267.61)	0	0
475	Nadikudi - Srikalahasti New Line (South Central Railway [SCR] - II) (400298)	Andhra Pradesh	12/2016	05/2027 03/2028	2312 (5200)	2179	54

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
476	Malugur- Palasamudram New Line Project [17.975 Km] (South Western Railway [SWR] - II) (611615)	Andhra Pradesh	11/2025	11/2027 12/2027	342 (342.14)	0	0
477	GOOTY-PENDEKALLU DOUBLING 29.225 Km (South Central Railway [SCR] - II) (611752)	Andhra Pradesh	06/2023	03/2027 03/2027	351.83 (351.83)	18	25
478	GUNTAKAL WEST-MALLAPPA GATE RAIL OVER RAIL - ROR TRACK (South Central Railway [SCR] - II) (611754)	Andhra Pradesh	07/2023	07/2026 (-)	293.3 (293.3)	0	0
479	Kurnool - Setting up facilities for coach midlife rehabilitation workshop (WPO/Patna) (611927)	Andhra Pradesh	10/2017	12/2023 (-)	560.72 (560.72)	276.66	65
480	Flyover between Pendurthi and Simhachalam North to avoid surface crossing at Simhachalam 7.135 km PB 73 of 2023 24 NR (East Coast Railway [ECor] - II) (612827)	Andhra Pradesh	05/2024	04/2027 (-)	183.65 (183.65)	4.2	11
481	3rd & 4th line between Vadlapudi -Gate Jn. cabin and Tie line between Gate Junction to Gangavaram port (East Coast Railway [ECor] - II) (616697)	Andhra Pradesh	03/2024	06/2026 (-)	154.28 (154.28)	10.98	16
482	Tiupati Katpadi 104.39 kms (South Central Railway [SCR] - II) (617210)	Andhra Pradesh	04/2025	03/2029 (-)	1215.56 (1215.56)	0	0
483	3rd Line between Gudur Renigunta 83.17 Km (South Central Railway [SCR] - II) (617216)	Andhra Pradesh	10/2024	03/2027 (-)	877.34 (877.34)	2.97	0
484	Kurnool Coach Midlife Rehabilitation Project (WPO/Patna) (705253)	Andhra Pradesh	07/2014	12/2020 (-)	563 (563)	120	0
485	Kotapalli - Narasapur New Line (South Central Railway [SCR] - II) (705436)	Andhra Pradesh	09/2013	03/2028 03/2028	2501 (2501)	1303.41	29
486	Guntur-Guntakal Doubling Project (South Central Railway [SCR] - II) (705633)	Andhra Pradesh	11/2017	12/2025 12/2026	3733 (4295)	4213.01	92
487	Vijaywada-Gudur 3rd Line (RVNL - II) (705648)	Andhra Pradesh	04/2018	11/2024 12/2025	6654 (6654)	5922	90
488	Penukonda - Dharmavaram Doubling Project [41.5 Km] (South Western Railway [SWR] - II) (705789)	Andhra Pradesh	12/2018	03/2026 03/2026	307.66 (307.66)	270.52	61
489	Doubling of New Bonggigaon to Kamakhya via Goalpara - 176 km (Northeast Frontier Railway [NFR]) (705572)	Assam	09/2016	03/2026 03/2026	4060 (4961)	3683.75	93
490	Guwahati-Dibrugarh via Tinsukia & Simaluguri-Dibrugarh (Central Organisation for Railway Electrification [CORE]) (706922)	Assam	09/2018	09/2020 06/2024	890.36 (889.36)	391.73	89
491	Mariani-Jorhat, Tinsukia-Dangri and Makum -TirapTrack Electrification Project (GMIC/ NFR) (706940)	Assam	01/2022	05/2024 (-)	183.99 (183.99)	0	0
492	Harmuty-Murkongselek Branch Line Electrification Project (GMIC/ NFR) (706942)	Assam	01/2022	05/2024 (-)	237.52 (237.52)	0	0
493	Sakri -Hasanpur [via Harnagar - Kusheshwar Asthan] New Railway line (East Central Railway [ECR] - I) (400254)	Bihar	08/1997	12/2024 03/2027	735.2 (735.2)	585.84	82
494	Khagaria-Kusheshwar Asthan [42Km] new line project (East Central Railway [ECR] - I) (705364)	Bihar	12/1998	12/2024 03/2027	614 (1384)	484.29	55
495	Hajipur-Sagauli New line (East Central Railway [ECR] - I) (705366)	Bihar	10/2004	03/2020 12/2026	2067 (2087)	1968.45	74
496	Araria Supaul New BG Line (East Central Railway [ECR] - I) (705368)	Bihar	03/2009	03/2024 01/2027	1605 (2514)	1490.2	35
497	Fatuha-Islampur incl. MM for extn.of NL from Neora to Daniawan , Daniawan to Biharsharif, Biharsharif to Barbigha , Barbigha to Shekhpura (East Central Railway [ECR] - I) (705373)	Bihar	03/2002	03/2023 08/2025	1473 (2882)	2522.41	94
498	Jogbani-Biratnagar New Rail Line project (Indian Railway Construction International Limited [IRCON]) (705450)	Bihar	01/2011	03/2022 12/2026	402 (486)	367.54	86
499	Samastipur-Darbhanga Doubling Railway Project (East Central Railway [ECR] - I) (705526)	Bihar	12/2015	03/2025 10/2025	519 (519)	344.23	84
500	Sagauli-Valmiknagar (East Central Railway [ECR] - I) (705527)	Bihar	03/2017	12/2025 12/2025	1216 (2222)	2044.54	91
501	Muzaffarpur-Sugauli (East Central Railway [ECR] - I) (705528)	Bihar	03/2017	06/2024 08/2025	1586 (1586)	1463.45	99
502	Rampur Dumra-Tal-Rajendrapul Additional Bridge and Railway Line Doubling (Indian Railway Construction International Limited [IRCON]) (706759)	Bihar	05/2017	12/2024 12/2025	2373.64 (1700.24)	1402.95	95
503	Barauni-Bachwara [16 km] - 3rd & 4th line incl. Barauni yard remodelling [32 km] (East Central Railway [ECR] - I) (706860)	Bihar	08/2025	08/2025 10/2026	645 (645)	0.77	55
504	Kharsia-Dharamjaygarh with Spur line [East Corridor-Phase 1] (Indian Railway Construction International Limited [IRCON]) (400220)	Chhattisgarh	01/2014	09/2018 03/2026	3055 (3438)	2574.54	94
505	Doubling of Kirandul-Jagdulpur Line [150 km] (East Coast Railway [ECor] - II) (400291)	Chhattisgarh	03/2013	03/2020 12/2025	1589 (1798)	1542.79	92

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
506	Gauge Conversion of Kendri-Dhamtari including Abhanpur - Rajim Branch line 67.20 Kms - 2nd Material Modification to Raipur Titlagarh doubling. (SECR) (602792)	Chhattisgarh	05/2021	02/2025 11/2025	1171 (1171)	848	82
507	4th line between Nipania Bhatapara 14.4 Km (South East Central Railway [SECR] - II) (612815)	Chhattisgarh	05/2024	03/2027 (-)	170.49 (170.49)	0	0
508	Dharamjaigarh-Korba 63 km (CERL) (613003)	Chhattisgarh	07/2022	08/2026 (-)	1686.26 (1686.26)	288.83	18.5
509	KHARSIA- NAYA RAIPUR-PARMALKASA 5th and 6th Line [278KM] (CAO/C/SECR) (617200)	Chhattisgarh	04/2025	03/2031 (-)	7853.84 (7853.84)	0	0
510	Dallirajhra- Rowghat New Railway Line - Phase I [95 km] (RVNL - II) (705433)	Chhattisgarh	12/2009	09/2025 12/2025	1628 (1628)	1440.85	82
511	Gevra Road-Pendra Road New Railway Line [135 km] (Indian Railway Construction International Limited [IRCON]) (705444)	Chhattisgarh	04/2014	03/2022 12/2025	4970 (4970)	4346.55	73
512	Chirimiri-Nagpur Halt New Railway Line Project (South East Central Railway [SECR] - II) (705756)	Chhattisgarh	06/2020	06/2030 06/2030	241 (656.52)	71	0
513	Boridand - Ambikapur Doubling Line Project (South East Central Railway [SECR] - II) (706854)	Chhattisgarh	04/2022	06/2030 06/2030	1376 (1576.23)	218	18
514	NIPANIA-BHATAPRA [14.4 KM] 4TH LINE [PB-72/NR/2022-23] (SECR) (709814)	Chhattisgarh	05/2024	12/2026 12/2026	170 (184)	0	0
515	4TH LINE - BHATAPARA-HATHBAND [8.8 KM] [PB-72/NR/2022-23] (SECR) (709815)	Chhattisgarh	05/2024	01/2027 12/2027	177.03 (177.03)	0	2
516	4TH LINE - BHILAI-BHILAI NAGAR [8.8 KM] [PB-72/NR/2022-23] (SECR) (709816)	Chhattisgarh	05/2024	02/2027 02/2027	177.34 (177.34)	1.16	2
517	4TH LINE - DADHAPARA-BELHA [9.2 KM] [PB-72/NR/2022-23] (SECR) (709817)	Chhattisgarh	05/2024	11/2026 11/2026	169.06 (169.06)	14.42	60
518	4TH LINE RAJNANDGAON-DONGARHGARH [31.2 KM] [PB-72/NR/2022-23] (SECR) (709818)	Chhattisgarh	05/2024	01/2027 01/2027	328.34 (328.34)	50.58	25
519	3RD AND 4TH LINE - SARAGBUNDIA AND MADWARANI (SECR) (709819)	Chhattisgarh	05/2025	12/2026 12/2026	167.64 (167.64)	0	2
520	Redevelopment of New Delhi Railway Station and construction of associated infrastructure (Ministry of Railways) (613785)	Delhi	06/2024	12/2028 (-)	4744 (4744)	35.09	0
521	North Region Video Surveillance Project (RCIL) (705298)	Delhi	04/2023	03/2024 (-)	274.39 (274.39)	0	0
522	Anand Vihar-Tilak Bridge 3rd & 4th line (CAO/C/NR) (705583)	Delhi	03/2013	03/2023 12/2027	667 (667)	285.44	62
523	Provision of Work-site Tampers [WST] Railway Project (EDTK[MC]/RB) (705694)	Delhi	01/2016	12/2023 01/2026	187.72 (187.72)	141.91	100
524	WST Machine Procurement Project (EDTK[MC]/RB) (705708)	Delhi	06/2018	03/2024 12/2027	176 (176)	0	0
525	PCT Machine Procurement Project (EDTK[MC]/RB) (705710)	Delhi	04/2019	04/2024 06/2027	336 (336)	74.32	85
526	RBMV Machine Procurement Project (EDTK[MC]/RB) (705712)	Delhi	10/2019	06/2024 12/2027	480 (480)	0.33	7
527	SRGM Machine Procurement Project (EDTK[MC]/RB) (705717)	Delhi	10/2019	12/2023 03/2026	440 (440)	390.03	90
528	WST Machine Procurement Project (EDTK[MC]/RB) (705720)	Delhi	12/2019	04/2024 12/2026	384 (384)	0	0
529	DTS Machine Procurement Project (EDTK[MC]/RB) (705721)	Delhi	12/2019	12/2024 12/2026	447.6 (447.6)	0	0
530	BRM Machine Procurement Project (EDTK[MC]/RB) (705722)	Delhi	09/2019	06/2024 12/2027	210 (210)	0.02	0
531	Track Machine Procurement Project (EDTK[MC]/RB) (705726)	Delhi	04/2020	03/2025 01/2028	6339 (6339)	4166.47	41
532	Kosamba Umarpada 70 Km (PCE/WR) (611918)	Gujarat	07/2022	03/2027 (-)	468 (468)	20	8
533	Adraj Moti Vijapur 40 Kms (Western Railway [WR] - II) (611937)	Gujarat	05/2022	05/2026 05/2026	417.53 (417.53)	223	86
534	Vijapur Ambliyan 42 km (PCE/WR) (611938)	Gujarat	05/2022	05/2026 05/2026	415.38 (415.38)	364	96
535	Himatnagar Khedbrahma 55 km (Railway) (611939)	Gujarat	04/2017	06/2001 06/2026	482.42 (482.42)	461	96



All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
536	New broad gauge line between Naliya Jakhau Port 25 Kms (PCE/WR) (611943)	Gujarat	02/2023	01/2028 01/2028	410.26 (410.26)	6	4
537	Quadrupling between Gandhidham Adipur with Y connection at Adipur for providing direct entry towards Mundra Port and Bhuj and high level platform at Gopalpur 11Kms (PCE/WR) (611944)	Gujarat	02/2023	03/2026 03/2026	152.44 (152.44)	20	68
538	Petlad Bhadran 23 Kms (PCE/WR) (611945)	Gujarat	05/2022	05/2030 05/2030	307.11 (307.11)	82	17
539	Choranda Motikoral 18 Kms (PCE/WR) (611969)	Gujarat	08/2023	10/2026 (-)	246 (246)	0	0
540	Samlaya Timba Road 54 km (PCE/WR) (611970)	Gujarat	02/2023	03/2030 03/2030	670.17 (670.17)	102	12
541	Samni Jambusar 24 km (PCE/WR) (611971)	Gujarat	05/2022	03/2030 03/2030	350 (349.93)	87	31
542	Jambusar Kavi 26 Kms (PCE/WR) (611972)	Gujarat	04/2023	12/2026 (-)	318 (318)	0	0
543	miyagam karjan Choranda maalsar 37 kms (PCE/WR) (611973)	Gujarat	06/2023	12/2026 (-)	450 (450)	0	0
544	Western Railway Samakhiali Gandhidham Quadrupiling 53 Kms (PCE/WR) (611974)	Gujarat	08/2023	12/2026 (-)	1430 (1430)	0	0
545	Dahod Creation of Infrastructure facilities for 9000 HP Electric locomotives Manufacturing at (PCE/WR) (611977)	Gujarat	02/2023	02/2025 (-)	487 (487)	108.69	0
546	Dahod Rolling Stock Workshop Provision of Infrastructure for CBS at (PCE/WR) (611978)	Gujarat	03/2023	03/2025 (-)	158 (158)	47.31	0
547	Sabarmati Setting up of Maintenance Facilities for Train Sets Phase ii (PCE/WR) (611979)	Gujarat	04/2023	06/2025 (-)	250 (250)	0	0
548	4th LINE BETWEEN BAREJADI NANDEJ-SANAND-AHMEDABAD BYPASS (Western Railway) (612072)	Gujarat	02/2023	03/2027 03/2027	961.67 (961.67)	327.53	17
549	Redevelopment of Ahmedabad railway station and associated infrastructure on engineering, procurement and construction mode (Ministry of Railways) (613786)	Gujarat	11/2023	03/2028 (-)	2379 (2379)	656.84	16
550	Miyagam-Karjan-Dabhoi-Samlaya [GC] (Western Railway [WR] - II) (705458)	Gujarat	01/2017	03/2021 12/2026	483.88 (844.1)	620.98	41
551	Modasa-Shamlaji Road Railway Line Project (SECR) (706757)	Gujarat	04/2008	03/2025 03/2027	262 (262)	203	58
552	Rajkot - Kanalus Doubling Project [111.2 Kms] (Western Railway [WR] - II) (706763)	Gujarat	12/2021	10/2026 10/2026	1080.58 (1080.58)	787.69	76
553	NADIAD-PETLAD [37.26 KM] (Railway) (709812)	Gujarat		06/2030 06/2030	461.91 (461.91)	75	7
554	NEW BG LINE INTERSECTION [5 NOS] BETWEEN GERATPUR-SANAND & BOTAD-AHMEDABAD [16.51 KM] [PB#29/NR/202] (SECR) (709813)	Gujarat		10/2027 10/2027	437.21 (437.21)	43	15
555	Bhiwani - Dobh Bahali Doubling Project [42.30 Km] (North Western Railway [NWR]) (611884)	Haryana	02/2023	02/2028 02/2028	471 (471)	191.39	59
556	Gomoh - Flyover for DN trains (East Central Railway [ECR] - I) (705765)	Jharkhand	01/2018	03/2026 03/2026	686 (686)	538.66	59
557	Lodhma - Piska - Link Line bypassing Hatia/Ranchi with Y connection (South Eastern Railway [SER] - I) (705785)	Jharkhand	03/2019	06/2026 05/2027	473 (473)	284.34	4
558	Pradhan Kuntha Jn Line Doubling Project (East Central Railway [ECR] - I) (706837)	Jharkhand	11/2022	11/2027 11/2027	349.22 (349.22)	90.64	60
559	Construction of New BG line between Hassan to Belur [27 Km] (South Western Railway [SWR] - II) (400023)	Karnataka	12/2025	04/2028 04/2027	749 (749)	0	0
560	Yeshvanthpur - Channasandra Doubling Project [21.70 Km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703585)	Karnataka	10/2019	03/2024 08/2025	314.1 (683.57)	151.11	52
561	New Railway Line between Ginigera and Raichur [165.57 km] (South Western Railway [SWR] - II) (705434)	Karnataka	05/2009	03/2019 03/2027	2565 (3034.98)	2073.98	66
562	Gadag-Wadi New Railway Line [257 km] (South Western Railway [SWR] - II) (705490)	Karnataka	08/2017	03/2027 12/2027	2842 (6700)	1735.22	30
563	Kadur - Chickamagalur - Sakleshpur [93km] (South Western Railway [SWR] - II) (705492)	Karnataka	11/2016	06/2025 12/2025	825 (825)	788.13	83
564	Bagalkot-Kudachi New Railway Line [142 km] (South Western Railway [SWR] - II) (705495)	Karnataka	11/2012	03/2027 01/2027	1378 (1649)	683.48	35
565	Tumkur-Chitradurga-Davangere New Rail Line Project [191 km] (South Western Railway [SWR] - II) (705496)	Karnataka	01/2017	03/2019 12/2027	1876 (1876)	523.07	13

All Ongoing Projects

AUGUST 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
566	Bangalore-Whitefield-Bangalore City-Krishnarajapuram [23.08 km] - Quadrupling (South Western Railway [SWR] - II) (705663)	Karnataka	06/2022	02/2026 02/2026	493 (493)	252.45	82
567	SHIMOGA - SHIKARIPURA - RANEBENNUR [96 Km] (South Western Railway [SWR] - II) (705761)	Karnataka	02/2023	12/2027 06/2028	1454 (1454)	69.82	11
568	Belgaum-Dharwad via Kittur [73.10Km] (South Western Railway [SWR] - II) (706835)	Karnataka	03/2025	12/2027 03/2029	1591 (1591)	0.75	0
569	Kumbalam-Turavur doubling project [15.59 Km] (Southern Railway [SR] - II) (705638)	Kerala	04/2023	03/2027 03/2027	813 (813)	292.15	15
570	Ernakulam-Kumbalam doubling project [7.71 Km] (SR-ERS) (705639)	Kerala	04/2023	03/2028 03/2028	601 (601)	283	17
571	Lalitpur-Satna, Rewa-Singrauli & Mahoba-Khajuraho (North Central Railway) (705480)	Madhya Pradesh	03/1998	03/2027 12/2027	8914 (8914)	5013.49	72
572	Katni - Bina Third Railway Line [279 km] (West Central Railway WCR I) (705651)	Madhya Pradesh	01/2017	03/2022 12/2025	2478.23 (4127.23)	3301.89	90
573	Satna-Rewa Railway Line Doubling Project (West Central Railway [WCR] - II) (705659)	Madhya Pradesh	08/2017	03/2026 03/2026	500 (584)	561.38	80
574	Doubling of Katni - Singrauli Railway Line [261 km] (Indian Railway Construction International Limited [IRCON]) (705660)	Madhya Pradesh	03/2017	12/2025 12/2025	2445 (4377)	3201.67	100
575	Katni Grade Separator/Bye Pass (Indian Railway Construction International Limited [IRCON]) (705661)	Madhya Pradesh	09/2017	09/2024 03/2026	1248 (1248)	1587.21	94
576	Indore - Budni New Railway Line [198 kms] (RVNL - II) (705763)	Madhya Pradesh	10/2020	09/2030 09/2030	7474 (7474)	1685.25	23
577	Nimach-Ratlam Doubling [133 Km] (Western Railway [WR] - II) (705933)	Madhya Pradesh	10/2021	10/2027 10/2027	1095.88 (1095.88)	1067.49	89
578	DHULE [BORVIHIR] - NARDANA NEW LINE [50.60 KMS] (CR) (400019)	Maharashtra	04/2023	12/2026 09/2027	492.76 (1170.83)	245.11	16
579	Wardha-Nanded Via Yavatmal New BG Line (Central Railway [CR] - II) (400271)	Maharashtra	04/2008	03/2028 03/2028	3445 (3445)	3002.93	50
580	AURANGABAD-ANKAI - DOUBLING PROJECT 98.25 Km (South Central Railway [SCR] - II) (611751)	Maharashtra	05/2023	03/2027 (-)	960.64 (960.64)	0	0.01
581	Western Railway Vasai bypass double line between Naigaon Juchandra 6 km (PCE/WR) (611975)	Maharashtra	07/2023	03/2026 (-)	176 (176)	0	0
582	Jogeshwari AT Development of JOS-AT as Trainset Maintenance Depot for energy efficient Vande Bharat Sleeper Trains (PCE/WR) (611976)	Maharashtra	06/2023	10/2025 (-)	221 (221)	0	0
583	Redevelopment of Chhatrapati Shivaji Maharaj Terminus [CSMT] and construction of associated infrastructure (Ministry of Railways) (613015)	Maharashtra	07/2023	03/2027 (-)	1813 (1813)	569.08	13
584	Gondia-Balharshah [Chanda Fort] Doubling [240 Km] (South East Central Railway) (617201)	Maharashtra	04/2025	04/2030 (-)	4373.04 (4373.04)	0	0
585	Doubling between Parbhani Parli Vaijanath stations 64.71 Km (South Central Railway [SCR] - II) (617215)	Maharashtra	12/2023	03/2028 (-)	769.93 (769.93)	0	0
586	Western Region Video Surveillance Project (RCIL) (705300)	Maharashtra	04/2023	12/2023 (-)	227.59 (227.59)	0	0
587	Ahmednagar - Beed - Parli - Vajinath New Broad Gauge Line Railway Project [261.3 km] (Central Railways) (705356)	Maharashtra	10/2002	03/2026 03/2026	2538.67 (4957.27)	4975.74	98
588	Baramati Lonand New Line Project (Central Railway [CR] - II) (705357)	Maharashtra	03/1999	03/2027 03/2027	138.48 (1843.9)	735.33	51
589	Wadsa-Gadchiroli (South East Central Railway) (705479)	Maharashtra	03/2012	03/2027 03/2027	1886 (1886)	925.28	50
590	3rd Line Kalyan - Kasara [67.35 Kilometres] (Central Railway [CR] - II) (705498)	Maharashtra	09/2015	12/2026 12/2026	792.89 (1395.79)	899.47	51
591	3rd Line Wardha - Sewagram - Nagpur (Central Railway [CR] - II) (705500)	Maharashtra	05/2016	12/2025 12/2025	540.02 (944.24)	754.27	81
592	3rd Line Wardha - Ballarshah [132 Kilometres] (Central Railway [CR] - II) (705502)	Maharashtra	12/2016	12/2025 02/2026	1384.72 (2033.59)	1655.88	68
593	Pune - Miraj-Londa [467 Kilometres] (Central Railway [CR] - II) (705503)	Maharashtra	06/2016	02/2025 08/2025	4027.53 (4872.52)	4833.04	85
594	Doubling of Daund Manmad Line [247.6 km] (Central Railway [CR] - II) (705504)	Maharashtra	03/2017	12/2025 03/2026	2081.27 (3267.06)	2816.46	88
595	4th Line Wardha - Nagpur [78.7 Kilometres] (Central Railway [CR] - II) (705505)	Maharashtra	05/2018	12/2025 02/2026	637.95 (1341.28)	983.16	81

All Ongoing Projects

AUGUST 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
596	3rd Line Manmad - Jalgaon [160 Kilometres] (Central Railway [CR] - II) (705506)	Maharashtra	04/2018	12/2024 08/2025	1035.16 (1558.75)	1726.94	95
597	Solapur-tuljapur-Osmanabad (Railway) (705735)	Maharashtra	12/2023	03/2027 03/2028	904.92 (3295.74)	1127.14	12
598	Nagpur- Nagbhir Railway Line Gauge Conversion Project (MRIDC) (705799)	Maharashtra	04/2020	12/2025 12/2025	1400 (1400)	1472	80
599	Mumbai Urban Transport Project [MUTP] - PHASE II (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706779)	Maharashtra	04/2008	03/2014 12/2027	8087 (8087)	7364	87
600	Mumbai Urban Transport Project [MUTP] Phase-III A (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706780)	Maharashtra	04/2019	12/2027 12/2027	33690 (33690)	2303.4	16
601	Mumbai Urban Transport Project Phase-III (Mumbai Rail Vikas Corporation Ltd.[MRVC]) (706781)	Maharashtra	12/2016	03/2022 12/2026	10947 (10947)	5152.7	60
602	PACHORA-JAMNER WITH EXTENSION UPTO MALKAPUR NG TO BG (CR) (709808)	Maharashtra	01/2022	08/2027 03/2028	955.39 (2093.82)	130.42	11
603	KALYAN-MURBAD VIA ULHASNAGAR [UMBRELLA WORK] (Central Railway [CR] - II) (709809)	Maharashtra	04/2023	03/2027 03/2027	726.46 (836.12)	9.29	0
604	Jiribam-Imphal new line project (Northeast Frontier Railway [NFR]) (705391)	Manipur	12/2007	12/2026 06/2029	14323 (21885.9)	15598.11	69
605	Marikuppam - Kuppam New Line Project [23.70 Km] (South Western Railway [SWR] - II) (705491)	Multi-States (Andhra Pradesh, Karnataka)	10/2018	06/2026 06/2026	297 (297)	123.38	15
606	Rayadurg-Tumkur via Kalyandurg New Line [207 km] (South Western Railway [SWR] - II) (705494)	Multi-States (Andhra Pradesh, Karnataka)	07/2010	09/2015 02/2028	2496 (2496)	1706.31	68
607	Renigunta, Wadi & Gooty Bypass Railway Project (South Central Railway [SCR] - I) (705610)	Multi-States (Andhra Pradesh, Karnataka)	04/2016	12/2025 12/2025	302 (543)	381	50
608	Doubling between Mudkhed Medchal & Mahbubnagar Dhone section 417.88 Km (South Central Railway [SCR] - II) (617212)	Multi-States (Andhra Pradesh, Maharashtra, Telangana)	08/2023	03/2029 (-)	4686.09 (4686.09)	0	0
609	Vizianagaram - Titlagarh 3rd line [272 Km including By - pass line of 7.68 KM] (RVNL - II) (400253)	Multi-States (Andhra Pradesh, Odisha)	11/2016	12/2026 12/2026	4803 (6670)	5722.01	89
610	Doubling of Kottavalasa-Koraput Rail Line [189 KM] (East Coast Railway [ECOR] - II) (705512)	Multi-States (Andhra Pradesh, Odisha)	01/2016	03/2022 03/2028	2500 (2500)	1987.17	70
611	Vizianagaram-Sambhalpur 3rd Line Project (RVNL) (705520)	Multi-States (Andhra Pradesh, Odisha)	12/2016	03/2025 (-)	4803.16 (4803.16)	2979.23	0
612	Malkangiri Pandurangapuram new railway line project (Indian Railways) (616702)	Multi-States (Andhra Pradesh, Odisha, Telangana)	01/2027	11/2031 (-)	3591.76 (3591.76)	0	0
613	Tindivanam-Nagari New Line Project [184.5 km] (Southern Railway [SR] - II) (400275)	Multi-States (Andhra Pradesh, Tamil Nadu)	10/2008	09/2016 03/2028	3631 (3631)	1113.53	18
614	Doubling between Motumari Vishnupuram - 88.81 Km and Rail over Rail - RoR at Motumari - 10.877 Km (South Central Railway [SCR] - II) (616857)	Multi-States (Andhra Pradesh, Telangana)	03/2025	03/2029 (-)	1595.55 (1595.55)	7.69	1
615	Doubling of Guntur Bibinagar 239 Km (South Central Railway [SCR] - II) (617211)	Multi-States (Andhra Pradesh, Telangana)	08/2023	03/2029 (-)	2853.23 (2853.23)	43.88	1
616	Rail Connectivity to Errupalem Amravati Namburu 57 Km (South Central Railway [SCR] - II) (617214)	Multi-States (Andhra Pradesh, Telangana)	11/2024	03/2027 (-)	2047.4 (2047.4)	0	0
617	Kazipet-Vijayawada 3rd line with electrification [220 km] (South Central Railway [SCR] - II) (705612)	Multi-States (Andhra Pradesh, Telangana)	08/2014	02/2025 12/2025	1953 (3363)	3073.74	91
618	Vijayawada - Kazipet Bypass line (South Central Railway [SCR] - II) (705632)	Multi-States (Andhra Pradesh, Telangana)	04/2016	01/2025 12/2025	647 (904)	888.91	91
619	Murkongselek-Pasighat (Northeast Frontier Railway [NFR] - II) (705401)	Multi-States (Arunachal Pradesh, Assam)	03/2012	03/2025 12/2025	435 (1250)	901	56
620	Lumding Furkating Doubling Project 140 km (Northeast Frontier Railway [NFR]) (616701)	Multi-States (Assam, Nagaland)	01/2025	02/2028 (-)	2123.7 (2123.7)	13.74	0
621	Dimapur [Dhansiri]-Sukhobi Kohima [Zubza] NL [82.5 Km] (Northeast Frontier Railway [NFR]) (705392)	Multi-States (Assam, Nagaland)	02/2016	03/2025 12/2025	6663 (6663)	5312.26	80
622	New Delhi- Howrah Speed Booster[160Kmph] Project (PCE/NCR) (705794)	Multi-States (Bihar, Delhi, Jharkhand, Uttar Pradesh, West Bengal)	09/2019	03/2024 (-)	6684.81 (6684.81)	127.03	0
623	Third Railway Line between Patratu-Sonnagar [281 kms] (RVNL - II) (400234)	Multi-States (Bihar, Jharkhand)	08/2018	03/2026 07/2026	8975 (8975)	4950	88
624	Multi tracking of Son Nagar-Andal 374.53 rkm & 814.38 tkm (East Central Railway [ECR] - I) (616699)	Multi-States (Bihar, Jharkhand)	08/2023	03/2028 (-)	12333.57 (12333.6)	467.55	11

All Ongoing Projects

AUGUST 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
625	Koderma-Tilaiya New Line (East Central Railway [ECR] - I) (705375)	Multi-States (Bihar, Jharkhand)	03/2002	02/2025 02/2026	1626 (2020)	2000.4	95
626	Pirpainti - Jasidih [100.52 Km] New BG line (Eastern Railway [ER] - I) (705385)	Multi-States (Bihar, Jharkhand)	03/2022	03/2028 03/2028	2555 (2555)	767.04	48
627	NER Provision of Automatic Block Signalling on Gorakhpur Cantt[Excl] Chhapra Gramin & Burhwal Jn [Excl] Sitapur Jn section of high density routes (North Eastern Railway [NER]) (611669)	Multi-States (Bihar, Uttar Pradesh)	06/2023	03/2027 (-)	380.47 (380.47)	24.53	0
628	Gorakhpur-Valmikinagar Doubling project (NER) (617224)	Multi-States (Bihar, Uttar Pradesh)	03/2024	12/2027 (-)	1120 (1120)	204.59	20
629	Chhapra-Ballia Patch Doubling (North Eastern Railway [NER]) (705562)	Multi-States (Bihar, Uttar Pradesh)	11/2015	02/2025 03/2025	963 (1046)	911.66	95
630	Katihar - Kumedpur Doubling Line Project (GM/C/ NFR) (706844)	Multi-States (Bihar, West Bengal)		08/2027 08/2027	942 (942)	356	45
631	Rajnandgaon - Nagpur [Kalumna] Third Railway Line [228.30 km] (South East Central Railway [SECR] - II) (705617)	Multi-States (Chhattisgarh, Maharashtra)	12/2016	12/2024 06/2026	3545 (3545)	3428.26	95
632	Jagdalpur-Koraput (East Coast Railway [ECoR] - II) (705511)	Multi-States (Chhattisgarh, Odisha)	03/2016	03/2024 12/2026	1547 (1547)	1323.05	90
633	Jharsuguda-Bilaspur Fourth Railway Line [206 km] (SECR) (705616)	Multi-States (Chhattisgarh, Odisha)	09/2016	10/2024 12/2025	2140 (2979)	2143.64	89
634	Mumbai-Ahmedabad High Speed Rail Project- 508 km (National High Speed Rail Corporation [NHSRC]) (705728)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	09/2017	08/2027 12/2029	108000 (108000)	79918.89	53
635	New Delhi- Mumbai Speed Booster[160Kmph] Project (PCE/WR) (705793)	Multi-States (Delhi, Gujarat, Madhya Pradesh, Maharashtra, Rajasthan)	09/2019	03/2024 (-)	6806.44 (6806.44)	135.65	0
636	Hospet - Tinaighat - Vasco Rail Doubling Project (RVNL - II) (705650)	Multi-States (Goa, Karnataka)	07/2012	03/2027 12/2027	5060 (5060)	5007.82	86
637	Hospet-Hubli-Vasco da Gama Line Electrification Project (RVNL) (706950)	Multi-States (Goa, Karnataka)	05/2018	03/2023 03/2024	744.49 (1122.62)	969.05	95
638	Western Dedicated Freight Corridor (DFCCIL) (705237)	Multi-States (Gujarat, Haryana, Maharashtra, Rajasthan, Uttar Pradesh)	01/2012	03/2022 12/2025	51101 (124005)	124623	96
639	New line Dahod-Indore via Sardarpur, Jabuwa and Dhar (Western Railway [WR] - II) (705453)	Multi-States (Gujarat, Madhya Pradesh)	06/2012	02/2027 02/2027	456.07 (1873.1)	3412.33	46
640	Chhota Udaipur - Dhar New Line Project [157 km] (Western Railway [WR] - II) (705454)	Multi-States (Gujarat, Madhya Pradesh)	01/2014	12/2025 12/2025	1794 (1794)	1804.05	80
641	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM (Western Railway) (611452)	Multi-States (Gujarat, Maharashtra)	03/2023	12/2025 06/2025	311 (311)	208	92
642	Taranga Hill-Abu Road via Ambaji (North Western Railway [NWR]) (400022)	Multi-States (Gujarat, Rajasthan)	07/2022	07/2030 07/2030	2798 (2798)	1915.38	15
643	LUNI- SAMDARI- BHILDI DOUBLING (North Western Railway [NWR]) (616842)	Multi-States (Gujarat, Rajasthan)	02/2024	07/2027 (-)	3085.59 (3085.59)	171.32	7
644	Chandigarh-Baddi New Rail Line- 36 km (Northen Railway [NR]) (705424)	Multi-States (Haryana, Himachal Pradesh)	02/2018	12/2026 12/2026	1540 (1540.13)	506.73	31
645	Rewari - Kathuwas Doubling Project [27.72 Km] (North Western Railway [NWR]) (611861)	Multi-States (Haryana, Rajasthan)	12/2022	06/2027 06/2027	352 (352)	246.11	63
646	Nangal Dam-Talwara New Broad Gauge Line [84 KM] and Taking Over Siding Mukerian-Talwara [29 KM] (Northen Railway [NR]) (705410)	Multi-States (Himachal Pradesh, Punjab)	05/1985	12/2025 01/2027	2018 (2018)	2053.9	45
647	Bhanupalli-Bilaspur-Beri New Railway Line Project (RVNL - II) (705428)	Multi-States (Himachal Pradesh, Punjab)	04/2015	12/2026 12/2027	13447 (13447)	6805.81	60
648	Doubling of Hatia [Ranchi]-Bondamunda Rail Line - 159 km (South Eastern Railway - JH) (705628)	Multi-States (Jharkhand, Odisha)	02/2017	06/2025 06/2026	3029 (3029)	2470.12	85
649	Buramara-Chakulia new line [59.96 km] (South Eastern Railway [SER] - I) (616588)	Multi-States (Jharkhand, Odisha, West Bengal)	12/2024	12/2029 (-)	1459.13 (1459.13)	2.11	0
650	Chandil - Anara - Damodar - 3rd line [121.26 km] (CAO/C/SER) (616227)	Multi-States (Jharkhand, West Bengal)	07/2025	09/2029 (-)	1932.01 (1932.01)	0.03	0
651	KHARAGPUR-ADITYAPUR THIRD RAIL LINE- 132 KM (RVNL - II) (705668)	Multi-States (Jharkhand, West Bengal)	01/2018	03/2025 12/2025	3250 (3250)	3176.46	97
652	Hotgi-Kudgi-Gadag Doubling Project (South Western Railway [SWR] - II) (705662)	Multi-States (Karnataka, Maharashtra)	01/2016	12/2024 03/2026	1878 (2459)	2642.04	92

All Ongoing Projects

AUGUST 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
653	Baiyyappanahalli - Hosur Doubling Project [48 km] (Karnataka Rail Infrastructure Development Company Limited [K-RIDE]) (703586)	Multi-States (Karnataka, Tamil Nadu)	02/2019	12/2024 01/2026	499 (499)	595	97
654	Trivandrum- Kanyakumari (Southern Railway (SR) - I) (705635)	Multi-States (Kerala, Tamil Nadu)	03/2016	03/2024 12/2027	1432 (3785)	2451	46
655	Ratlam-Mhow-Khandwa-Akola Gauge Conversion (Western Railway [WR] - II) (705457)	Multi-States (Madhya Pradesh, Maharashtra)	03/2010	03/2027 09/2028	1656.25 (5735.88)	4428.77	80
656	Itarsi - Nagpur Third Railway Line [280 km] (Central Railway [CR] - II) (705507)	Multi-States (Madhya Pradesh, Maharashtra)	09/2016	03/2027 03/2027	2449.91 (2506.68)	1843.76	51
657	Gwalior - Seopurkala with extension to Kota [Gauge Conversion] (North Central Railway) (705419)	Multi-States (Madhya Pradesh, Rajasthan)	07/2018	03/2025 02/2026	2913 (2913)	2097.51	78
658	Ramganjmandi-Bhopal New Line Project [262 km] (West Central Railway [WCR] - II) (705481)	Multi-States (Madhya Pradesh, Rajasthan)	10/2004	12/2025 12/2027	3032 (5073)	3621.79	70
659	Nimach-Badi Sadri New Rail Line Project (Western Railway [WR] - II) (705764)	Multi-States (Madhya Pradesh, Rajasthan)	09/2021	03/2026 06/2026	495 (825)	79.55	53
660	Mathura-Jhansi Third Railway Line [274 Km] (RVNL - II) (705667)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	03/2018	12/2024 12/2026	5961 (5961)	4928.62	94
661	Jhansi - Bina Third Railway Line [153 Km] (CAO/C/NCR) (705598)	Multi-States (Madhya Pradesh, Uttar Pradesh)	03/2018	03/2022 03/2026	2002 (2002)	1795.86	93
662	Jhansi-Khairar-Manikpur & Khirar-Bhimsen (North Central Railway) (705608)	Multi-States (Madhya Pradesh, Uttar Pradesh)	03/2017	03/2026 03/2026	4330 (4330)	2184.56	55
663	Third Line [new] between Kazipet - Balharshah with electrification [201.04 Km] (South Central Railway [SCR] - II) (705613)	Multi-States (Maharashtra, Telangana)	10/2016	01/2025 11/2025	2595 (3071)	3223.67	93
664	Narayangarh-Bhadrak 3rd line (South Eastern Railway [SER] - I) (705629)	Multi-States (Odisha, West Bengal)	03/2017	12/2025 06/2026	2400 (2400)	2236.9	65
665	Nagapattinam-Tiruturaipundi and Karaikal-Peralam New Line (Southern Railway [SR] - II) (400223)	Multi-States (Puducherry, Tamil Nadu)	01/2019	03/2026 03/2027	713 (981)	598.38	80
666	Sivok-Rangpo New Rail Line (Indian Railway Construction International Limited [IRCON]) (705432)	Multi-States (Sikkim, West Bengal)	05/2010	05/2015 12/2027	7877 (12133)	9039.91	84
667	Sainthia, Sitarampur, Mughalsarai, Allahabad & Etawah - Bypass Line Project (Eastern Railway [ER] - I) (602797)	Multi-States (Uttar Pradesh, West Bengal)	12/2017	03/2027 03/2027	461.64 (461.64)	186.03	7
668	Proposed 6 nos Road Over Bridge [ROB] at different locations under MCL Talcher Under Deposit Scheme. (East Coast Railway [ECoR] - II) (400045)	Odisha	07/2022	03/2025 01/2025	168.32 (168.32)	69.85	82
669	Brundamal-Jharsuguda- flyover connection for joining downline (East Coast Railway [ECoR] - II) (400232)	Odisha	01/2014	12/2026 12/2026	297 (297)	193.22	30
670	3rd & 4th line between Sarla - Sason [8 km] [PB 73/2023-24/NR] (East Coast Railway [ECoR] - II) (612834)	Odisha	04/2023	12/2025 (-)	252 (252)	79.55	45
671	Bangriposi-Gorumahisani new line [85.60 km] (CAO/C/SER) (616586)	Odisha	09/2025	12/2029 (-)	2269.49 (2269.49)	2.31	0
672	Badampahar-Kendujhargarh new line [82.06 km] (CAO/C/SER) (616587)	Odisha	09/2025	12/2029 (-)	1875.72 (1875.72)	0.53	0
673	Flyover between Siju and Paradeep coaching Yard to avoid Surface crossing of trains (East Coast Railway [ECoR] - II) (616694)	Odisha	10/2025	07/2028 (-)	200.77 (200.77)	0	0
674	Paradeep - Badabandha 3rd & 4th Line / 18.51kms (East Coast Railway [ECoR] - II) (616695)	Odisha	04/2025	11/2028 (-)	300.15 (300.15)	0.01	0
675	Khurda-Bolangir New Broad Gauge Rail Link [301km] (East Coast Railway [ECoR] - II) (705358)	Odisha	03/2001	12/2026 12/2026	3792 (5089)	5027.62	89
676	Talcher-Bimlagarh New Railway Line (East Coast Railway [ECoR] - II) (705359)	Odisha	12/2004	03/2025 03/2027	1928 (1928)	1934.28	48
677	Bhadrak-Nergundi Third Line (East Coast Railway [ECoR] - II) (705510)	Odisha	04/2015	11/2024 01/2026	1284 (1284)	1298	80
678	Koraput - Singapur Railway Doubling (East Coast Railway [ECoR] - II) (705513)	Odisha	12/2015	12/2027 03/2028	2362 (2362)	1798.71	68
679	Jarapada- Budhapank with flyover at Talcher road 3rd and 4th Line (East Coast Railway [ECoR] - II) (705514)	Odisha	12/2015	11/2018 03/2026	1000 (810.02)	401.61	36
680	3rd & 4th Railway Line Project from Salegaon to Budhapank via Rajathgarh. (East Coast Railway [ECoR] - II) (705515)	Odisha	12/2015	03/2026 03/2026	1173 (2092)	1971	80
681	Jeypore-Navarangpur New Rail Line Project (East Coast Railway [ECoR] - II) (705741)	Odisha	04/2023	07/2028 12/2029	748 (748)	10.56	1
682	Jeypore-Malkanagiri New Railway Line Project (East Coast Railway [ECoR] - II) (705742)	Odisha	12/2023	07/2033 07/2033	2344 (2344)	225.84	8

All Ongoing Projects

AUGUST 2025

SI.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
683	Talcher-Angul New Line with Y-Connection at Talcher (CAO/C/ECoR) (705743)	Odisha		05/2027 05/2028	495 (495)	29.5	1
684	Baghuapal Flyover Construction Project (CAO/C/ECoR) (705767)	Odisha	10/2022	03/2028 03/2028	257.97 (258)	0.83	0
685	KODINGAMALI BAUXITE MINES TO SINGARAM RAILWAY STATION (Indian Railway) (709810)	Odisha	01/2026	08/2027 08/2027	190.9 (190.9)	0	0
686	GANDHAMARDAN IRON ORE MINES TO GOALDIH STATION/12.76kms (East Coast Railway [ECoR] - II) (709811)	Odisha	05/2025	09/2027 09/2027	190 (190)	0	0
687	Junagarh Visavadar 42 Kms (Railway) (611980)	Offshore	02/2023	09/2028 09/2028	492.83 (492.83)	3	1
688	Jaynagar-Bijalpura, incl. extn. Bet, Bijalpura-Bardibas [Nepal] (East Central Railway [ECR] - I) (705362)	Offshore	03/2011	03/2022 03/2026	819 (819)	580.6	75
689	Ludhiana- Killa Raipur Railway Doubling Project (Railway) (705783)	Punjab	12/2022	03/2025 03/2026	237.64 (237.64)	118	55
690	Dedicated Test Track for RDSO Phase II (North Western Railway [NWR]) (611614)	Rajasthan	11/2021	11/2026 11/2026	819.48 (967.06)	471	86
691	Devgarh Madariya - Nathdwara Gauge Conversion [82.54 Km] part of Marwar - Mavli Gauge Conversion [152 Km] (North Western Railway [NWR]) (611849)	Rajasthan	01/2023	06/2028 06/2028	968.92 (968.92)	98.62	51
692	Maintenance cum workshop depot for Vande Bharat Sleeper Trains as per conditions under WTA 527 (WPO/Patna) (611929)	Rajasthan	06/2023	12/2024 (-)	166.86 (166.86)	0	0
693	RINGUS KHATUSHYAMJI NEW LINE (North Western Railway [NWR]) (616696)	Rajasthan	03/2024	03/2028 (-)	254.06 (254.06)	2.94	0
694	RAS- MERTA CITY NEW LINE INCL BYPASS AT MERTA ROAD (North Western Railway [NWR]) (616840)	Rajasthan	02/2024	03/2028 (-)	947 (947)	1.36	0
695	PUSHKAR- MERTA CITY NEW LINE (North Western Railway [NWR]) (616841)	Rajasthan	02/2024	12/2026 (-)	799.64 (799.64)	14.5	4
696	AJMER- CHANDERIYA DOUBLING (North Western Railway [NWR]) (616843)	Rajasthan	02/2024	06/2027 (-)	1634.79 (1634.79)	74.43	6
697	Dholpur - Sirmuttra Gauge Conversion (North Central Railway) (705482)	Rajasthan	04/2020	02/2019 02/2027	747 (747)	355.13	43
698	Gudha-Thatha Mithri Construction of Railway Track Project (North Western Railway [NWR]) (705752)	Rajasthan	04/2019	11/2026 11/2026	819.48 (967.06)	471	98
699	Sawai Madhopur-Jaipur Railway Line Project (North Western Railway [NWR]) (705912)	Rajasthan	04/2023	03/2027 (-)	1203.89 (1203.89)	46.07	7
700	Agra Fort-Bandikui Doubling Line Project (CAO/C/NCR) (705919)	Rajasthan	02/2021	06/2027 06/2027	1390 (1390)	123	25
701	Sawaimadhopur Bye Pass Line Project (North Western Railway [NWR]) (706866)	Rajasthan	01/2023	03/2026 05/2027	304 (304)	43.07	44
702	Ph II extension of MRTS from Velachery to St Thomas Mount (Southern Railways [SR] - construction) (400280)	Tamil Nadu	11/2008	07/2024 08/2025	734 (982)	475.73	99
703	Redevelopment of Chennai Egmore Station (Railway) (613002)	Tamil Nadu	10/2022	03/2026 (-)	842 (842)	340	0
704	Coach Production Factory Upgradation Project (CPM/ICF) (705244)	Tamil Nadu	07/2018	12/2021 (-)	520 (520)	192.25	0
705	Morappur - Dharpuri New Railway Line Project (Southern Railway [SR] - I) (705755)	Tamil Nadu	12/2016	03/2028 03/2028	359 (359)	40	1
706	Doubling between Bhadrachalam Road and Dornakal (South Central Railway [SCR] - II) (616856)	Telangana	04/2025	04/2029 (-)	770.12 (770.12)	0	0
707	Kazipet Wagon Overhauling Project (RVNL) (705252)	Telangana	07/2017	12/2023 (-)	385 (385)	0	0
708	Manoharabad-Kothapalli New Rail Line [151 km] (South Central Railway [SCR] - II) (705437)	Telangana	01/2017	03/2027 12/2027	1160 (2781)	1771.32	71
709	Bahraich-Shravasti-Balrampur-Siddharthnagar -Santkabir nagar (North Eastern Railway [NER]) (400204)	Uttar Pradesh	03/2017	10/2030 10/2030	4939.78 (4939.78)	1232.64	8
710	Sahjanwa-Dohrighat (North Eastern Railway [NER]) (400205)	Uttar Pradesh	03/2017	03/2029 03/2029	1319.75 (1319.75)	460.2	3
711	Anandnagar - Ghugli via Maharajganj New line 52.7 km (Construction NER) (617252)	Uttar Pradesh	11/2023	03/2028 (-)	958.27 (958.27)	436.95	23
712	Chunar-Chopan doubling project (North Central Railway) (617284)	Uttar Pradesh	01/2025	03/2028 (-)	1423.96 (1423.96)	49.57	2

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
713	Domingarh-Gorakhpur-Gorakhpur Cantt.-Kusumhi - 3rd Railway Line Project (North Eastern Railway [NER]) (705566)	Uttar Pradesh	06/2018	02/2025 09/2025	351 (521.47)	495.86	98
714	Burhwal Gonda 3rd line (North Eastern Railway [NER]) (705567)	Uttar Pradesh	07/2019	03/2025 09/2025	1016 (1118)	1373.8	73
715	Janghai-Pratapgarh- Amethi (CAO/C/II/INR) (705588)	Uttar Pradesh	03/2017	03/2025 03/2026	722 (1194)	1550	70
716	Lalitpur-Birari with flyover at Lalitpur- 16 Km (North Central Railway) (705766)	Uttar Pradesh	03/2017	12/2024 11/2025	304.44 (356)	220.8	72
717	Allahabad-Bamhrauli Flyover Construction & 4th Railway Line Project (North Central Railway) (705771)	Uttar Pradesh	10/2020	03/2026 03/2026	494 (494)	333	70
718	Mughalsarai-Allahabad, 3rd line (North Central Railway) (705772)	Uttar Pradesh	03/2016	12/2026 03/2027	2649 (2649.44)	1561.89	62
719	Aligarh -Daud Khan Flyover Construction & 3rd Railway Line Project (CAO/C/INCR) (705774)	Uttar Pradesh	09/2020	01/2025 03/2027	758 (779.49)	315.37	55
720	Bhandai - Flyover for Etawah bound down train- 10 Km (North Central Railway [NCR] - II) (705777)	Uttar Pradesh	04/2021	02/2026 02/2027	250.18 (250.18)	113.94	3
721	Phephna-Indara, Mau-Shahganj doubling excluding Indara-Mau (South Eastern Railway [SER] - I) (705779)	Uttar Pradesh	03/2017	12/2024 03/2026	1178 (1777)	1489.5	85
722	Bhatni-Aurnihar with electrification excluding Indara-Mau (RVNL - II) (705780)	Uttar Pradesh	03/2017	12/2024 10/2025	2529 (2529.46)	2051.69	94
723	Barabanki-Malhaur 3rd & 4th Railway Line Project (CAO/C/INR) (705782)	Uttar Pradesh	04/2017	03/2025 03/2026	407 (407)	317	75
724	Janghai-Phaphamau Doubling Rail Line Project (RVNL) (705784)	Uttar Pradesh	03/2020	03/2025 03/2025	357 (978.77)	579	95
725	Bahraich - Nanpara - Nepalganj Road Gauge Conversion (North Eastern Railway [NER]) (705863)	Uttar Pradesh	04/2021	07/2025 09/2025	950 (550)	511.18	90
726	Allahabad division - Aligarh - Harduaganj Flyover (North Central Railway) (705918)	Uttar Pradesh	02/2021	06/2026 03/2027	1457 (1457)	50	14
727	DOUBLING BETWEEN JAUNPUR JN-ZAFFARABAD [6.28 KM] (Northen Railway [NR]) (900872)	Uttar Pradesh		01/2027 12/2028	177 (177)	41	10
728	Rishikesh-Karnaprayag New Rail Line- 125 km (RVNL - II) (705429)	Uttarakhand	08/2018	12/2025 03/2027	38953 (38953)	24645.15	65
729	Kalinarayanpur-Krishnanagar Doubling Alongwith Krishnanagar - Chapra New Line. And Naihati-Ranaghat 3rd Line. (Eastern Railway [ER] - I) (400247)	West Bengal	11/2005	02/2027 02/2027	1000 (1000)	1031.21	67
730	Tarakeshwar-Bishnupur New Line [82.47 km] (Eastern Railway [ER] - I) (400273)	West Bengal	02/2008	03/2019 02/2026	1189 (1542)	1307.52	90
731	Dum Dum Airport-New Garia via Rajarhat-Construction of Metro Railway (RVNL - II) (400277)	West Bengal	10/2011	12/2025 03/2026	8964 (8964)	8097.47	80
732	Construction of Balurghat-Hilli new BG Line (Northeast Frontier Railway [NFR]) (612096)	West Bengal	12/2010	03/2027 03/2025	1209 (1209)	405.31	9
733	Kalipahari Bakhtarnagar 5th line (Eastern Railway [ER] - I) (617322)	West Bengal	07/2025	06/2027 06/2027	350.46 (350.46)	0	0
734	Joka-BBD Bag new metro project (RVNL - II) (705730)	West Bengal	04/2010	12/2026 12/2028	4835 (10362)	4373.24	60
735	Noapara-Barasat via Bimanbandar - Construction of Metro railway [18 km] (Metro Railway, Kolkata) (706776)	West Bengal	03/2010	08/2026 03/2029	4830 (4830)	2764.13	32
736	Baranagar-Barrackpore and Dakshineshwar- Construction of Metro Railway (RVNL - II) (706777)	West Bengal	03/2010	12/2026 12/2025	2298 (2734)	393	17
Total (263)					691320.92	524256.16	
Department for Promotion of Industry & Internal Trade							
Real Estate							
737	Krishnapatnam Node - Phase 1 - Roads and Services Development (National Industrial Corridor Development Corporation) (701658)	Andhra Pradesh	02/2024	02/2028 (-)	2139.44 (2139.44)	406.05	17
738	Tumakuru Node - Phase 1 - Roads and Services Development (National Highways & Infrastructure Development Corporation Ltd. [NHIDCL]) (701657)	Karnataka	02/2023	09/2026 (-)	1701.81 (1701.81)	88.25	8
Total (2)					3841.25	494.3	
Department of Telecommunications							
Telecommunication							
739	SETTING UP OF PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE [NICF] AT GHITORNI (National Communication Academy - Finance (Erstwhile NICF)) (709859)	Delhi	04/2018	02/2020 10/2025	248.2 (248.2)	236.91	98

All Ongoing Projects							
							AUGUST 2025
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
740	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya <i>(Department of Telecommunications [DoT])</i> (701598)	Meghalaya	09/2020	03/2022 09/2025	971.96 (971.96)	208.25	99
741	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase2 <i>(Department of Telecommunications [DoT])</i> (701599)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	09/2021	03/2023 11/2025	1577.57 (1577.57)	598.31	87
742	Provision of 4G based mobile services in 7,287 uncovered villages of 44 Aspirational District across 5 states of Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra & Odisha <i>(Department of Telecommunications [DoT])</i> (701602)	Multi-States (Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra, Odisha)	05/2022	11/2023 11/2025	3685 (3685)	1101.44	79
743	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam <i>(Department of Telecommunications [DoT])</i> (701597)	Multi-States (Arunachal Pradesh, Assam)	10/2021	04/2023 09/2025	1255.49 (1255.49)	284.04	89
744	354 Uncovered Villages Scheme <i>(Department of Telecommunications [DoT])</i> (701600)	Multi-States (Bihar, Gujarat, Himachal Pradesh, Jammu and Kashmir, Ladakh, Rajasthan, Uttar Pradesh)	04/2020	10/2021 08/2025	336.89 (301.13)	227.82	97
745	502 Aspirational District Scheme in Four states - Bihar, Madhya Pradesh, Rajastha and Uttar Pradesh <i>(Department of Telecommunications [DoT])</i> (704495)	Multi-States (Bihar, Madhya Pradesh, Rajasthan, Uttar Pradesh)	03/2021	03/2022 12/2025	421.65 (228.94)	134.08	96
746	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART <i>(BSNL)</i> (709749)	Multi-States (Maharashtra, Telangana)	03/2020	06/2021 12/2025	461.42 (461.42)	166.02	81
747	Saturation 4G mobile coverage of Uncovered Villages through USOF <i>(Department of Telecommunications [DoT])</i> (400013)	PAN India	07/2022	06/2024 03/2026	26316 (30620)	9791.8	73
748	4G Services by BSNL <i>(Department of Telecommunications [DoT])</i> (701593)	PAN India	11/2020	03/2024 03/2026	28466 (19592)	8390.32	96
749	BharatNet <i>(Department of Telecommunications [DoT])</i> (706775)	PAN India	10/2011	08/2023 03/2027	61109 (188000)	41486.14	81
750	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT <i>(BSNL)</i> (709856)	PAN India	05/2023	08/2024 10/2025	645.13 (645.13)	364.34	91
751	Planning, Engineering, Supply, Installation, Testing, Commissioning, Integration & Annual Maintenance of 4G mobile network at 1 Lakh sites on PAN India basis including Mumbai & Delhi LSA on turnkey basis under Phase IX.2 Project. <i>(BSNL)</i> (709857)	PAN India	06/2023	06/2025 03/2026	24544.55 (24544.5)	8391.17	96
752	OPTICAL TRANSPORT NETWORK [OTN] PH-4 IN BSNL <i>(BSNL)</i> (709858)	PAN India	02/2024	08/2025 10/2025	810.99 (810.99)	741.9	100
	Total (14)				150849.85	72122.54	
	Department of Water Resources, River Development & GR						
	Waste & Water						
753	Interception and Diversion and STP works in Bhagalpur under Hybrid annuity based PPP mode-Namami Gange Programme <i>(National Mission for Clean Ganga)</i> (616600)	Bihar	03/2022	02/2025 12/2025	413.29 (413.29)	126.67	97
754	Sewage Treatment Plant 100MLD and Sewerage Network 288 km in Digha-Patna under Hybrid annuity based PPP mode-Namami Gange Programme <i>(National Mission for Clean Ganga)</i> (616611)	Bihar	07/2019	12/2025 (-)	824 (824)	396.71	56
755	Sewage Treatment Plant 50MLD and Sewerage Network 150 km in Kankarbagh-Patna under Hybrid annuity based PPP mode-Namami Gange Programme <i>(National Mission for Clean Ganga)</i> (616612)	Bihar	07/2019	12/2025 (-)	578.89 (578.89)	171.79	54
756	Sewer Network, SPS and STP at Begusarai <i>(National Mission for Clean Ganga)</i> (616615)	Bihar	03/2018	04/2025 12/2025	230.06 (230.06)	261.82	97
757	Sewer Networks, SPS and STP at Hajipur <i>(National Mission for Clean Ganga)</i> (616616)	Bihar	03/2018	06/2025 12/2025	305.19 (305.19)	346.46	95
758	Interception & Diversion with Rehabilitation of sewerage scheme at Agra under Hybrid annuity based PPP model-Namami Gange Programme <i>(National Mission for Clean Ganga)</i> (616594)	Uttar Pradesh	04/2023	04/2025 12/2025	842.25 (842.25)	208.64	73
759	Pollution Abatement Works for River Kali Meerut under Meerut Municipality Interception & Diversion with STP <i>(National Mission for Clean Ganga)</i> (616605)	Uttar Pradesh	11/2024	12/2024 05/2027	690.71 (690.71)	34.79	27
760	Pollution Abatement works for River Ganga at Hooghly Chinsurah- Municipal Town Interception & Diversion with STP <i>(National Mission for Clean Ganga)</i> (616604)	West Bengal	12/2021	03/2025 12/2025	154.73 (154.73)	96.17	92

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Total (8)				4039.12	1643.05	
	Water Resources						
761	Sardar Gouthu Latchanna Thotapalli Barrage Project (Water Resources-AP) (400100)	Andhra Pradesh	01/2006	12/2019 06/2026	353.05 (1023.24)	869.11	95
762	Gundlakamma project (Water Resources-AP) (400101)	Andhra Pradesh	04/2005	12/2019 03/2027	397.41 (697.39)	610.89	98
763	Polavaram Irrigation Project (Water Resources-AP) (701415)	Andhra Pradesh	11/2004	04/2022 03/2026	10151.04 (55548.9)	24347.76	83
764	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370)	Assam	12/1996	12/2022 03/2026	256.16 (256.16)	0	55
765	Punpun Barrage Project (Water Resources-BR) (400104)	Bihar	04/2007	12/2019 03/2026	571.07 (658.12)	469.66	44
766	Durgawati Reservoir Project (Irrigation and CAD-TG) (701371)	Bihar	04/1997	12/2019 12/2024	691.15 (971.96)	978.51	87
767	Kelo Irrigation Project (Water Resources-CT) (400111)	Chhattisgarh	04/2008	12/2019 06/2026	459.97 (727.04)	616.93	71
768	Kudali Irrigation Project (Department of Water Resources, River Development & GR) (701399)	Chhattisgarh	12/2009	12/2025 (-)	382.29 (382.29)	0	86
769	Sardar Sarovar CADWM Project (Narmada and Water Resources, Water Supply and Kalpsar Department-GJ) (400097)	Gujarat	04/2004	12/2019 03/2025	5021.76 (6670.31)	4954.99	90.3
770	Sardar Sarovar Project (Narmada and Water Resources, Water Supply and Kalpsar Department-GJ) (701372)	Gujarat	04/1996	12/2019 12/2025	20718.17 (33412.5)	31767.59	93
771	Subernarekha Multipurpose Project, Jharkhand (Department of Water Resources-JH) (701376)	Jharkhand	01/2012	12/2019 03/2026	3807.77 (9579.58)	5561.97	69
772	Upper Tunga Irrigation Project (Water Resources-KA) (701377)	Karnataka	04/2014	12/2019 12/2025	770.16 (1606.07)	1511.22	99
773	Omkarashwar CADWM Project (Water resource-mp) (400096)	Madhya Pradesh	04/2015	12/2019 03/2026	648.09 (648.09)	172.56	3
774	Bargi Diversion Project Phase - IV [km. 154 to km 197] (Water Resources-MP) (400115)	Madhya Pradesh	01/2009	12/2019 03/2025	751.03 (893.35)	746.19	75
775	Bargi Diversion Project Phase - III [km. 104 to km 154] (Water Resources-MP) (400116)	Madhya Pradesh	04/2007	12/2019 12/2025	1229.15 (1399.7)	1807.2	79
776	Gosikhurd CADWM Project (Department of water resources-MH - II) (400095)	Maharashtra	04/2017	12/2019 06/2026	743.73 (743.73)	252	50
777	Urmodi Irrigation Project (Department of water resources-MH - II) (400105)	Maharashtra	04/2018	06/2022 12/2026	580.79 (895.81)	713.46	76
778	Sulwade-Jamphal-Kanoli Lift Irrigation Scheme (Department of water resources-MH - II) (400107)	Maharashtra	02/2019	06/2023 06/2027	2407.67 (2407.67)	2436.43	80
779	Purna Barrage-2 [Ner Dhamana] Medium Irrigation Project (Department of water resources-MH - II) (400109)	Maharashtra	04/2018	06/2020 06/2026	848.07 (888.43)	690.49	69
780	Jigaon Irrigation Project (Department of water resources-MH - II) (400112)	Maharashtra	04/2018	06/2028 (-)	7222.95 (7222.95)	8501.45	90
781	Waghur Project (Department of water resources-MH - II) (701383)	Maharashtra	04/1996	12/2019 03/2026	1058.99 (1758.51)	1530.45	89
782	Gosikhurd Project (Department of water resources-MH - II) (701386)	Maharashtra	04/2008	12/2019 06/2026	7196.47 (12770.1)	13533.29	72
783	Aruna Medium Irrigation Project (Department of water resources-MH - II) (701391)	Maharashtra	01/2010	12/2019 12/2025	210.45 (1472.14)	1697.94	97
784	Lower Pedhi Project (Department of water resources-MH - II) (701396)	Maharashtra	04/2008	12/2019 06/2026	255.97 (1480.7)	1324.78	64
785	Nardave Medium Irrigation Project (Department of water resources-MH - II) (701398)	Maharashtra	04/2009	12/2019 06/2026	211.46 (781.85)	623.5	72
786	Thoubal Multipurpose Project (Water Resources Department-MN) (701400)	Manipur	04/1997	12/2019 03/2026	1449.44 (1822.24)	1837.91	98
787	North Koel Reservoir Project (Department of Water Resources, River Development & GR) (701412)	Multi-States (Bihar, Jharkhand)	01/2021	03/2021 03/2026	1622.27 (2430.76)	142.1	32
788	Integrated Anandpur Barrage Project (Water Resources-OR) (603945)	Odisha	01/1998	12/2019 06/2026	567.03 (2990.05)	2629.74	62
789	Kanupur Irrigation Project (Irrigation and CAD-TG) (701404)	Odisha	01/2004	12/2019 12/2024	989.43 (2301.28)	2563.56	79
790	Relining of Rajasthan feeder and Sirhind Feeder canal (Department of Water Resources-PB) (701410)	Punjab	04/2018	06/2021 06/2026	1441.26 (2462.16)	3000.36	80

All Ongoing Projects

AUGUST 2025

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
791	Shahpur Kandi Dam Project (Department of Water Resources-PB) (701411)	Punjab	04/2018	06/2022 10/2025	2285.81 (2715.7)	2072.33	80
792	Sri Ram Sagar Project Stage - II (Irrigation and CAD-TG) (400102)	Telangana	04/2005	12/2019 03/2026	736.13 (949.87)	940.7	96
793	Indiramma Flood Flow Canal Project (Irrigation and CAD-TG) (400103)	Telangana	01/2006	12/2019 12/2026	1331.3 (5940.09)	4491.08	92
794	J. Chokka Rao Devadula Lift Irrigation Scheme (Irrigation and CAD-TG) (701405)	Telangana	04/2006	12/2019 12/2025	8200.71 (14730)	4558.89	87
795	Rajiv Bhima Lift Irrigation Scheme (Irrigation and CAD-TG) (701406)	Telangana	01/2008	12/2019 03/2026	1402 (2509.66)	1839.76	100
796	Saryu Nahar CADWM Project (Irrigation & Water Resources-UP) (400093)	Uttar Pradesh	04/2017	12/2019 03/2026	1672.7 (1672.7)	0	0
797	Arjun Sahayak Project (Irrigation & Water Resources-UP) (400117)	Uttar Pradesh	04/2009	12/2019 12/2019	741.38 (2465.68)	3218.3	100
798	Morna [Gureghar] Irrigation Project (Department of Water Resources, River Development & GR) (701395)	Uttar Pradesh	12/2007	12/2025 (-)	219.9 (219.9)	0	0
799	Madhya Ganga canal Phase-II (Irrigation & Water Resources-UP) (701408)	Uttar Pradesh	07/2007	12/2019 12/2025	1060.67 (4417.21)	4415.24	82
800	Jamrani Dam Multipurpose Project (Irrigation-UK) (613787)	Uttarakhand	04/2023	06/2029 (-)	2584.1 (2584.1)	968.52	16
Total (40)					93248.95	138396.86	



सत्यमेव जयते

Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <http://www.ipm.mospi.gov.in>
